FY 2016

Educational Facilities MASTER PLAN

and Amendments to the FY 2015–2020 Capital Improvements Program







Montgomery County Public Schools

ROCKVILLE, MARYLAND

FY 2016 Educational Facilities Master Plan and the Amendments to the FY 2015–2020 Capital Improvements Program

Montgomery County Public Schools
Rockville, Maryland

Published by:
the Department of Materials Management
for the Department of Facilities Management and the Division of Long-range Planning
45 West Gude Drive, Suite 4100
Rockville, Maryland 20850
http://www.montgomeryschoolsmd.org/departments/planning

MCPS
MONTGOMERY COUNTY PUBLIC SCHOOLS
www.montgomeryschoolsmd.org
MARYLAND

Malcolm Baldrige
National Quality Award
2010 Award Recipient

June 30, 2015

Dear Citizens:

The *FY 2016 Educational Facilities Master Plan* (Master Plan) reviews the issues that influenced the formulation and adoption of the Fiscal Year (FY) 2016 Capital Budget and Amendments to the FY 2015–2020 Capital Improvements Program (CIP). The Master Plan also sets forth the agenda for future facilities planning and provides information that the community and the Board of Education need as they work toward resolving facilities-related issues and setting school system priorities. Montgomery County Board of Education Policy FAA, *Long-range Educational Facilities Planning*, and the state of Maryland require that the Educational Facilities Master Plan be updated annually.

A two-year capital programming cycle was approved in a referendum by Montgomery County citizens in November 1996. The biennial process for the six-year CIP mandates that the entire program be reviewed and approved for each odd-numbered fiscal year. Accordingly, the FY 2015–2020 CIP was comprehensively reviewed and approved in May 2014. In even-numbered fiscal years, such as FY 2016, the county executive and County Council consider only amendments to the approved six-year CIP. In addition, the County Council must approve an annual capital budget outlining appropriations for projects approved in the CIP each year. Therefore, this Master Plan reflects the funding implications of the adopted FY 2015–2020 CIP, as amended and adopted by the County Council in May 2015.

In May 2014, the County Council adopted the FY 2015–2020 CIP that totaled $1.528 billion, $214 million less than the Board of Education's request. This reduction in funding resulted in a one-year delay of all individual school projects—not currently under design or construction—but maintained the planning funds as requested by the Board of Education. The reduction also resulted in a one-year delay, beyond the Board of Education's request, for elementary school revitalization/expansion projects and a one-year delay of secondary revitalization/expansion projects.

The *Board of Education's Requested FY 2016 Capital Budget and Amendments to the FY 2015–2020 Capital Improvements Program* totaled $1.751 billion, an increase of $223.3 million more than the previously approved CIP. The requested amendments called for the restoration of the schedule of all individual school projects that were delayed one year in the adopted CIP and the schedule of the elementary and secondary revitalization/expansion projects that were delayed. The Board of Education's request also included a scope change for one existing project, additional funding for two existing projects, and funding for one new project.

The county executive, in his *Recommended FY 2016 Capital Budget and Amendments to the FY 2015–2020 Capital Improvements Program*, supported the Board of Education's request, but in order to fully fund the request, assumed $213.3 million in new state-supported School Financing Bonds for Montgomery County Public Schools (MCPS). Unfortunately, the Maryland General Assembly did not pass the School Financing Bonds legislation, which created a $213.3 million shortfall between the Board of Education's request and the county executive's recommendation.

As a result, the County Council requested that the Board of Education submit a scenario to reduce the *Board of Education's FY 2016 Capital Budget and Amendments to the FY 2015–2020 Capital Improvements Program* to reflect the funding deficit. The Board of Education submitted a scenario to the County Council that delayed elementary and secondary revitalization/expansion projects one year beyond the Board of Education's request, with the exception of 3 elementary revitalization/expansion projects that can begin construction in FY 2016—Brown Station, Wayside, and Wheaton Woods elementary schools; delayed 7 of 16 capacity projects one year; and removed all expenditures for the Shady Grove Transportation Depot Replacement project. Based on the scenario above, the Board of Education's request was reduced by $210.1 million.

On May 14, 2015, during the reconciliation process, the County Council approved the Board of Education's scenario, which delayed all but three elementary school revitalization/expansion projects one year beyond the Board of Education's request and delayed, by one year, all secondary revitalization/expansion projects. The County Council decided to delay all 16 capacity projects by one year. Also, the County Council removed all expenditures for the Shady Grove Transportation Depot, with the exception of $700,000 to be used to conduct feasibility studies to determine the future location of the depot.

The County Council supported an additional $2.5 million for the Planned Life-cycle Asset Replacement project and the $100,000 for the Facility Planning project to conduct feasibility studies for the high schools in the Downcounty Consortium. Also, the County Council programmed an additional $2.0 million in the Technology Modernization project for FY 2016. The County Council approved four projects in the CIP to avoid placing certain neighborhoods into residential development moratorium—two at the high school level in the Downcounty Consortium, one at the middle school level in the Downcounty Consortium, and one at the elementary school level in the Gaithersburg Cluster.

The Board of Education's request included a scope change for the Blair G. Ewing Center Improvements project to relocate Alternative Education Programs from the Blair G. Ewing Center to the former English Manor Elementary School site. The County Council did not approve the scope change but, instead, directed the Board of Education to

reevaluate the current Blair G. Ewing site, as well as another site deemed appropriate by the Board of Education. Subsequently, the Board of Education directed MCPS staff to reevaluate the current Blair G. Ewing site, as well as other publicly owned sites. The Board of Education's request also included the acceleration of construction funds for the Blair G. Ewing Center Improvements project. As a result of the actions by the County Council and the Board of Education, the County Council maintained the approved schedule for this project.

In November 2014, as part of its approval of the CIP, the Board of Education approved a roundtable discussion group to review the possibility of collocating Rock Terrace School with Tilden Middle School at the current Tilden Holding Center. Tilden Middle School was identified as the potential site for the collocation due to its upcoming revitalization/expansion project, central location in the Walter Johnson Cluster, and site size, which is able to accommodate these two schools. Rock Terrace School is one of five stand-alone special education schools in Montgomery County and is housed in an aging facility. After careful consideration of the work and input from the Rock Terrace School/Tilden Middle School Roundtable Discussion Group, the interim superintendent of schools recommended, and the Board of Education approved, the collocation of Rock Terrace School and Tilden Middle School on the Tilden Holding Center site.

As a result of the reductions, deferrals, and technical adjustments, the County Council adopted the FY 2016 Capital Budget and Amendments to the FY 2015–2020 CIP for MCPS totaling $1.544 billion for the six-year period, an increase of $15.7 million more than the previously approved CIP and includes an FY 2016 expenditure of $283.3 million.

The construction of new facilities and additions to existing facilities, as well as our revitalization/expansion projects, will help to accomplish the goal of addressing the capacity needs throughout the county. For the 2014–2015 school year, MCPS experienced the seventh straight year of significant enrollment growth. Official September 30, 2014, student enrollment was 153,852—a one-year increase of 2,563 students. Since the 2007–2008 school year, enrollment has increased by 16,107 students, with most of the increase at the elementary school level. This total increase is equivalent to 22 elementary schools. Although numerous school capacity projects recently have been built to address our student enrollment, we need significant additional funds, particularly from the state, to meet our capacity needs.

The large cohort of today's elementary school students has started to enter the secondary level, and many of these buildings quickly will become overutilized in the next six years. By the 2020–2021 school year, middle school enrollment is projected to increase by approximately 4,800 students and high school enrollment by approximately 6,000 students. These increases equate to four middle schools and three high schools.

Total MCPS enrollment is projected to increase by 11,526 students and will reach 165,378 students by the 2020–2021 school year. Adding the projected 11,526 increase to the 16,107 increase since 2007 results in a total increase of 27,633 students spanning the 13-year period from 2007 to 2020. This is a remarkable amount of enrollment growth for our school system to accommodate.

With the need to provide permanent seats in classrooms for our student population and address the aging inventory of older school facilities, funding for the CIP continues to be a complex issue. Local funding sources, such as County General Obligation bonds, current revenue, the County Recordation Tax, and the School Impact Tax, are utilized in conjunction with state aid to fund the CIP.

For FY 2016, the revised state aid request was $147.99 million; however, the state, through the Board of Public Works, only approved $39.84 million. The approved allocation was for the balance of funding for 5 construction projects; funding for 13 systemic roofing and Heating, Ventilation, and Air Conditioning projects; and partial funding for one construction project. The $39.84 million state allocation was approximately $108.15 million less than the amount requested by the Board of Education. MCPS also received an additional $5.9 million in state aid for school construction projects due to the passage of the *Capital Grant Program for Local School Systems with Significant Enrollment Growth or Relocatable Classrooms*. Therefore, our total state aid for school construction totals $45.74 million.

We appreciate the continued support of the citizens of Montgomery County. We know that the county continues to face fiscal challenges; however, we look to the community, including county and state officials, to help us secure the funds necessary for our school system. Public involvement is an important part of the planning process, and we encourage school and community organizations to evaluate the information in this document and offer feedback. We will continue our efforts to increase the capacity of public school facilities, as well as maintain and improve our older school facilities in order to provide seats for every student and programmatic spaces essential for learning.

Sincerely,

Patricia B. O'Neill
President, Board of Education

Larry A. Bowers
Interim Superintendent of Schools

PBO:LAB:AMZ:ak

Maryland Department of Planning

Larry Hogan, Governor
Boyd Rutherford, Lt. Governor

David R. Craig, Secretary
Wendi W. Peters, Deputy Secretary

April 15, 2015

Mr. Larry A. Bowers
Interim Superintendent of Schools
Montgomery County Public Schools
2096 Gaither Road, Suite 201
Rockville, Maryland 20850

Dear Mr. Bowers:

We have received your letter dated March 31, 2015 and the enclosed Montgomery County 2014 Actual Enrollments and 2015 - 2024 enrollment projections.

We compared Montgomery County's projections to those generated by our Department. There is a difference of less than 5 percent for years 2015 – 2024. You may use the local projections (2015-2024) for updating your 2015 Educational Facilities Master Plan (EFMP). We look forward to receiving your updated EFMP in July. A copy of this letter and its attachment should be included in the Plan.

If you have any questions, please do not hesitate to contact me at 410.767.4564.

Sincerely,

Pat Goucher, Director
Director, Infrastructure Planning Division

cc: Ms. Adrienne Karamihas, Capital Budget Manager (w/enclosure)
Dr. David Lever, PSCP (w/enclosure)
Mr. Mark Goldstein, MDP

301 West Preston Street - Suite 1101 - Baltimore - Maryland - 21201
Tel: 410.767.4500 - Toll Free: 1.877.767.6272 - TTY users: Maryland Relay - Planning.Maryland.gov

Jurisdiction	2014	2015	2016	2017	2018	2019	2020	2021	2022	2023	2024
Montgomery	**150,230**	**152,178**	**154,497**	**156,567**	**158,047**	**159,720**	**161,042**	**161,936**	**162,509**	**163,004**	**163,197**
MDP	150,320	152,750	154,870	156,130	156,730	158,040	159,110	159,940	160,540	160,930	160,990
Diff	-90	-572	-373	437	1,317	1,680	1,932	1,996	1,969	2,074	2,207
% Diff	-0.06%	-0.37%	-0.24%	0.28%	0.84%	1.06%	1.21%	1.25%	1.23%	1.29%	1.37%

MONTGOMERY COUNTY PLANNING DEPARTMENT
THE MARYLAND-NATIONAL CAPITAL PARK AND PLANNING COMMISSION

May 1, 2015

Mr. Bruce Crispell, Director
Division of Long Range Planning
Montgomery Public Schools
45 West Gude Drive, Suite 4100
Rockville, Maryland 20850

Subject: FY 2016 Capital Budget and Amendments to the FY 2015-2020 Capital Improvements Program

For Educational Facilities

Dear Mr. Crispell:

In response to your request, the Montgomery Planning Department, on behalf of the M-NCPPC, reviewed the FY 2016 Capital Budget and Amendments to the FY 2015-2020 Capital Improvements Program for Educational Facilities.

The Montgomery County Planning Department finds that the FY 2016 Capital Budget and the FY 2015-2020 Capital Improvements Program for Educational Facilities are consistent with the M-NCPPC approved and adopted master plans.

We appreciate your assistance in the master plans currently underway, including Westbard, Montgomery Village, Greater Lyttonsville and the Bethesda Downtown Plan. We value and look forward to continuing the working relationship between our agencies for the upcoming master plans that will be starting in FY 2016: White Flint II, Rock Spring, Aspen Hill and Vicinity, the MARC Rail Stations Plan and the Shady Grove Minor Master Plan.

Sincerely,

Gwen Wright
Planning Director

GW:cp

Table of Contents

Page

Alphabetical Listing of Schools xi
Countywide Map of Clusters xiii
Introduction xiv

CHAPTER 1
The County Council Adopted FY 2016 Capital Budget and Amendments to the FY 2015–2020 Capital Improvements Program 1-1
The Impact of the Biennial CIP Process 1-1
The County Council Adopted Capital Improvements Program 1-1
Funding the Capital Improvements Program 1-2
General Obligation (GO) Bonds and Spending Affordability Guidelines (SAG) 1-3
Recordation Tax and School Impact Tax 1-3
State Funding 1-3
Current Revenues 1-4
The Relationship between State and Local Funding 1-4
Capital Budget and Operating Budget Relationship 1-5
County Council Adopted FY 2016 Capital Budget and Amendments to the FY 2015–2020 CIP Summary Table 1-6
County Council FY 2016 Capital Budget and Amendments to the FY 2015–2020 CIP Funding Table 1-14
FY 2016 Adopted State CIP for MCPS Table 1-15

CHAPTER 2
The Planning Environment 2-1
Community Trends 2-1
Population 2-1
Economy 2-1
Housing 2-2
Master Plans 2-2
Subdivision Staging Policy 2-3
Student Population Trends 2-3
Student Diversity 2-4
Focus and Non-focus Schools 2-5
MCPS Enrollment Forecast 2-6
Summary 2-6

CHAPTER 3
Facility Planning Objectives 3-1
Capital Improvements Priorities 3-1
Long-range Educational Facilities Planning Policy Guidance 3-1
Preferred Range of Enrollment 3-2
School Capacity Calculations 3-2
School Facility Utilization 3-2
School Site Size 3-2
Objective 1: Implement Facility Plans that Support the Continuous Improvement of Educational Programs in the School System 3-3
Objective 2: Meet Long-Term and Interim Space Needs 3-4
Objective 3: Sustaining and Modernizing Facilities 3-7
Objective 4: Provide Schools that are environmentally Safe, Secure, Functionally Efficient, and Comfortable 3-8
Objective 5: Support Multipurpose Use of Schools 3-8
Objective 6: Meet Special Education Programs Space Needs 3-9

Page

CHAPTER 4
Approve Actions and Planning Issues 4-1
MCPS Clusters for 2015–2016 4-4
Bethesda–Chevy Chase Cluster 4-6
Winston Churchill Cluster 4-14
Clarksburg Cluster 4-20
Damascus Cluster 4-28
Downcounty Consortium 4-34
Gaithersburg Cluster 4-50
Walter Johnson Cluster 4-56
Col. Zadok Magruder Cluster 4-62
Richard Montgomery Cluster 4-68
Northeast Consortium 4-74
Northwest Cluster 4-84
Poolesville Cluster 4-92
Quince Orchard Cluster 4-94
Rockville Cluster 4-100
Seneca Valley Cluster 4-106
Sherwood Cluster 4-112
Watkins Mill Cluster 4-118
Walt Whitman Cluster 4-124
Thomas S. Wootton Cluster 4-130
Special Education Centers 4-136
Other Educational Facilities 4-142

CHAPTER 5
Countywide Projects 5-1

CHAPTER 6
Project Description Forms 6-1

APPENDICES
A: Projected Enrollment A-1
B: Special Program Enrollment B-1
C: School Enrollment and Capacity C-1
D: Relocatable Classrooms Placements D-1
E: Modernization Schedule for Assessed Schools E-1
F: Assessing Schools for Modernization F-1
G: Restroom Renovations Schedule G-1
H: Head Start and Prekindergarten Locations H-1
I: Growth Policy I-1
J: State and Local Capacities Table J-1
K: Reopened Schools K-1
L: Closed Schools L-1
M: Catchment Area Maps M-1
N: Political District Maps and Tables N-1
O: Priority Funding Areas and Hot Spots O-1
P: Land Use, Growth Policy, and MCPS Enrollment Forecasting P-1
Q: Capacity Calculation Q-1
R: Planned Life-cycle Asset Replacement (PLAR) Projects R-1
S: Special Education Program Descriptions S-1
T: Long-range Facilities Planning Policy and Interim Regulation T-1
U: Quality Integrated Education Policy U-1
V: Sustaining and Modernizing Montgomery County Public Schools Facilities Policy V-1
W: Transfer of Students Policy W-1
X: Student Transportation Policy X-1
School Addresses and Phone Numbers
Planning Calendar

Alphabetical Listing of Schools

Page

Arcola ES—Downcounty Consortium....4-34
Argyle MS—Downcounty Consortium....4-34
Ashburton ES—Walter Johnson Cluster....4-56
John T. Baker MS—Damascus Cluster....4-28
Benjamin Banneker MS—Northeast Consortium....4-74
Bannockburn ES—Walt Whitman Cluster....4-124
Lucy V. Barnsley ES—Rockville Cluster....4-100
Beall ES—Richard Montgomery Cluster....4-68
Bel Pre ES—Downcounty Consortium....4-34
Bells Mill ES—Winston Churchill Cluster....4-14
Belmont ES—Sherwood Cluster....4-112
Bethesda ES—Bethesda-Chevy Chase Cluster....4-6
Bethesda-Chevy Chase HS—Bethesda-Chevy Chase Cluster....4-6
Beverly Farms ES—Winston Churchill Cluster....4-14
Montgomery Blair HS—Downcounty Consortium....4-34
James Hubert Blake HS—Northeast Consortium....4-74
Bradley Hills ES—Walt Whitman Cluster....4-124
Briggs Chaney MS—Northeast Consortium....4-74
Broad Acres ES—Northeast Consortium....4-74
Brooke Grove ES—Sherwood Cluster....4-112
Brookhaven ES—Downcounty Consortium....4-34
Brown Station ES—Quince Orchard Cluster....4-94
Burning Tree ES—Walt Whitman Cluster....4-124
Burnt Mills ES—Northeast Consortium....4-74
Burtonsville ES—Northeast Consortium....4-74
Cabin John MS—Winston Churchill and Thomas S. Wootton Clusters....4-14, 4-130
Candlewood ES—Col. Zadok Magruder Cluster....4-62
Cannon Road ES—Northeast Consortium....4-74
Carderock Springs ES—Walt Whitman Cluster....4-124
Rachel Carson ES—Quince Orchard Cluster....4-94
Cashell ES—Col. Zadok Magruder Cluster....4-62
Cedar Grove ES—Clarksburg and Damascus Clusters....4-20, 4-28
Chevy Chase ES—Bethesda-Chevy Chase Cluster....4-6
Winston Churchill HS—Winston Churchill Cluster....4-14
Clarksburg ES—Clarksburg Cluster....4-20
Clarksburg HS—Clarksburg Cluster....4-20
Clearspring ES—Damascus Cluster....4-28
Roberto Clemente MS—Northwest and Seneca Valley Clusters....4-84, 4-106
Clopper Mill ES—Northwest Cluster....4-84
Cloverly ES—Northeast Consortium....4-74
Cold Spring ES—Thomas S. Wootton Cluster....4-130
College Gardens ES—Richard Montgomery Cluster....4-68
Cresthaven ES—Northeast Consortium....4-74
Capt. James E. Daly ES—Clarksburg Cluster....4-20
Damascus ES—Damascus Cluster....4-28
Damascus HS—Damascus Cluster....4-28
Darnestown ES—Northwest Cluster....4-84
Diamond ES—Northwest Cluster....4-84
Dr. Charles R. Drew ES—Northeast Consortium....4-74
DuFief ES—Thomas S. Wootton Cluster....4-130
East Silver Spring ES—Downcounty Consortium....4-34
Eastern MS—Downcounty Consortium....4-34

Page

Thomas Edison High School of Technology....4-142
Albert Einstein HS—Downcounty Consortium....4-34
Blair Ewing Center....4-142
Fairland ES—Northeast Consortium....4-74
Fallsmead ES—Thomas S. Wootton Cluster....4-130
Farmland ES—Walter Johnson Cluster....4-56
William H. Farquhar MS—Northeast Consortium and Sherwood Cluster....4-74, 4-112
Fields Road ES—Quince Orchard Cluster....4-94
Flower Hill ES—Col. Zadok Magruder Cluster....4-62
Flower Valley ES—Rockville Cluster....4-100
Forest Knolls ES—Downcounty Consortium....4-34
Forest Oak MS—Gaithersburg Cluster....4-50
Fox Chapel ES—Clarksburg Cluster....4-20
Robert Frost MS—Thomas S. Wootton Cluster....4-130
Gaithersburg ES—Gaithersburg Cluster....4-50
Gaithersburg HS—Gaithersburg Cluster....4-50
Gaithersburg MS—Gaithersburg Cluster....4-50
Galway ES—Northeast Consortium....4-74
Garrett Park ES—Walter Johnson Cluster....4-56
Georgian Forest ES—Downcounty Consortium....4-34
Germantown ES—Northwest Cluster....4-84
William B. Gibbs, Jr. ES—Clarksburg Cluster....4-20
Glen Haven ES—Downcounty Consortium....4-34
Glenallan ES—Downcounty Consortium....4-34
Goshen ES—Gaithersburg Cluster....4-50
Great Seneca Creek ES—Northwest Cluster....4-84
Greencastle ES—Northeast Consortium....4-74
Greenwood ES—Sherwood Cluster....4-112
Harmony Hills ES—Downcounty Consortium....4-34
Highland ES—Downcounty Consortium....4-34
Highland View ES—Downcounty Consortium....4-34
Herbert Hoover MS—Winston Churchill Cluster....4-14
Jackson Road ES—Northeast Consortium....4-74
Walter Johnson HS—Walter Johnson Cluster....4-56
Jones Lane ES—Quince Orchard Cluster....4-94
Kemp Mill ES—Downcounty Consortium....4-34
John F. Kennedy HS—Downcounty Consortium....4-34
Kensington-Parkwood ES—Walter Johnson Cluster....4-56
Francis Scott Key MS—Northeast Consortium....4-74
Martin Luther King, Jr. MS—Seneca Valley Cluster....4-106
Kingsview MS—Northwest Cluster....4-84
Lake Seneca ES—Seneca Valley Cluster....4-106
Lakelands Park MS—Northwest and Quince Orchard Clusters....4-84, 4-94
Lakewood ES—Thomas S. Wootton Cluster....4-130
Laytonsville ES—Gaithersburg Cluster....4-50
Col. E. Brooke Lee MS—Downcounty Consortium....4-34
Little Bennett ES—Clarksburg Cluster....4-20
A. Mario Loiederman MS—Downcounty Consortium....4-34
Longview—Special Education Centers....4-136
Luxmanor ES—Walter Johnson Cluster....4-56
Col. Zadok Magruder HS—Col. Zadok Magruder Cluster....4-62
Thurgood Marshall ES—Quince Orchard Cluster....4-94


Page

Maryvale ES—Rockville Cluster....4-100
Spark M. Matsunaga—Northwest Cluster....4-84
S. Christa McAuliffe ES—Seneca Valley Cluster....4-106
Ronald McNair ES—Northwest Cluster....4-84
Meadow Hall ES—Rockville Cluster....4-100
Mill Creek Towne ES—Col. Zadok Magruder Cluster....4-62
Monocacy ES—Poolesville Cluster....4-92
Richard Montgomery HS—Richard Montgomery Cluster....4-68
Montgomery Knolls ES—Downcounty Consortium....4-34
Montgomery Village MS—Watkins Mill Cluster....4-118
Neelsville MS—Clarksburg and Watkins Mill Clusters.. 4-20, 4-118
New Hampshire Estates ES—Downcounty Consortium....4-34
Newport Mill MS—Downcounty Consortium....4-34
Roscoe R. Nix ES—Northeast Consortium....4-74
North Bethesda MS—Walter Johnson Cluster....4-56
North Chevy Chase ES—Bethesda-Chevy Chase Cluster....4-6
Northwest HS—Northwest Cluster....4-84
Northwood HS—Downcounty Consortium....4-34
Oak View ES—Downcounty Consortium....4-34
Oakland Terrace ES—Downcounty Consortium....4-34
Olney ES—Sherwood Cluster....4-112
William Tyler Page ES—Northeast Consortium....4-74
Paint Branch HS—Northeast Consortium....4-74
Parkland MS—Downcounty Consortium....4-34
Rosa Parks MS—Sherwood Cluster....4-112
Pine Crest ES—Downcounty Consortium....4-34
Piney Branch ES—Downcounty Consortium....4-34
John Poole MS—Poolesville Cluster....4-92
Poolesville ES—Poolesville Cluster....4-92
Poolesville HS—Poolesville Cluster....4-92
Potomac ES—Winston Churchill Cluster....4-14
Thomas W. Pyle MS—Walt Whitman Cluster....4-124
Quince Orchard HS—Quince Orchard Cluster....4-94
Redland MS—Col. Zadok Magruder Cluster....4-62
Judith A. Resnik ES—Col. Zadok Magruder Cluster....4-62
RICA—Special Education Centers....4-136
Dr. Sally K. Ride ES—Seneca Valley Cluster....4-106
Ridgeview MS—Quince Orchard Cluster....4-94
Ritchie Park ES—Richard Montgomery Cluster....4-68
Rock Creek Forest ES—Bethesda-Chevy Chase Cluster....4-6
Rock Creek Valley ES—Rockville Cluster....4-100
Rock Terrace—Special Education Centers....4-136
Rock View ES—Downcounty Consortium....4-34
Rockville HS—Rockville Cluster....4-100
Lois P. Rockwell ES—Damascus Cluster....4-28
Rocky Hill MS—Clarksburg and Damascus clusters.... 4-20, 4-28
Rolling Terrace ES—Downcounty Consortium....4-34
Rosemary Hills ES—Bethesda-Chevy Chase Cluster....4-6
Rosemont ES—Gaithersburg Cluster....4-50
Carl Sandburg—Special Education Centers....4-136
Seneca Valley HS—Seneca Valley Cluster....4-106
Sequoyah ES—Col. Zadok Magruder Cluster....4-62
Seven Locks ES—Winston Churchill Cluster....4-14
Shady Grove MS—Col. Zadok Magruder Cluster....4-62
Sherwood ES—Northeast Consortium and
Sherwood Cluster.... 4-74, 4-112
Sherwood HS—Sherwood Cluster....4-112

Page

Sargent Shriver ES—Downcounty Consortium....4-34
Flora M. Singer ES—Downcounty Consortium....4-34
Silver Spring International MS—Downcounty Consortium....4-34
Sligo MS—Downcounty Consortium....4-34
Sligo Creek ES—Downcounty Consortium....4-34
Somerset ES—Bethesda-Chevy Chase Cluster....4-6
South Lake ES—Watkins Mill Cluster....4-118
Springbrook HS—Northeast Consortium....4-74
Stedwick ES—Watkins Mill Cluster....4-118
Stephen Knolls—Special Education Centers....4-136
Stone Mill ES—Thomas S. Wootton Cluster....4-130
Stonegate ES—Northeast Consortium....4-74
Strathmore ES—Downcounty Consortium....4-34
Strawberry Knoll ES—Gaithersburg Cluster....4-50
Summit Hall ES—Gaithersburg Cluster....4-50
Takoma Park ES—Downcounty Consortium....4-34
Takoma Park MS—Downcounty Consortium....4-34
Tilden MS—Walter Johnson Cluster....4-56
Travilah ES—Thomas S. Wootton Cluster....4-130
Twinbrook ES—Richard Montgomery Cluster....4-68
Viers Mill ES—Downcounty Consortium....4-34
Washington Grove ES—Gaithersburg Cluster....4-50
Waters Landing ES—Seneca Valley Cluster....4-106
Watkins Mill ES—Watkins Mill Cluster....4-118
Watkins Mill HS—Watkins Mill Cluster....4-118
Wayside ES—Winston Churchill Cluster....4-14
Weller Road ES—Downcounty Consortium....4-34
Julius West MS—Richard Montgomery Cluster....4-68
Westbrook ES—Bethesda-Chevy Chase Cluster....4-6
Westland MS—Bethesda-Chevy Chase Cluster....4-6
Westover ES—Northeast Consortium....4-74
Wheaton HS—Downcounty Consortium....4-34
Wheaton Woods ES—Downcounty Consortium....4-34
Whetstone ES—Watkins Mill Cluster....4-118
White Oak MS—Northeast Consortium....4-74
Walt Whitman HS—Walt Whitman Cluster....4-124
Wilson Wims ES—Clarksburg Cluster....4-20
Earle B. Wood MS—Rockville Cluster....4-100
Wood Acres ES—Walt Whitman Cluster....4-124
Woodfield ES—Damascus Cluster....4-28
Woodlin ES—Downcounty Consortium....4-34
Thomas S. Wootton HS—Thomas S. Wootton Cluster....4-130
Wyngate ES—Walter Johnson Cluster....4-56

Cluster Service Areas and Quad Clusters 2014-2015

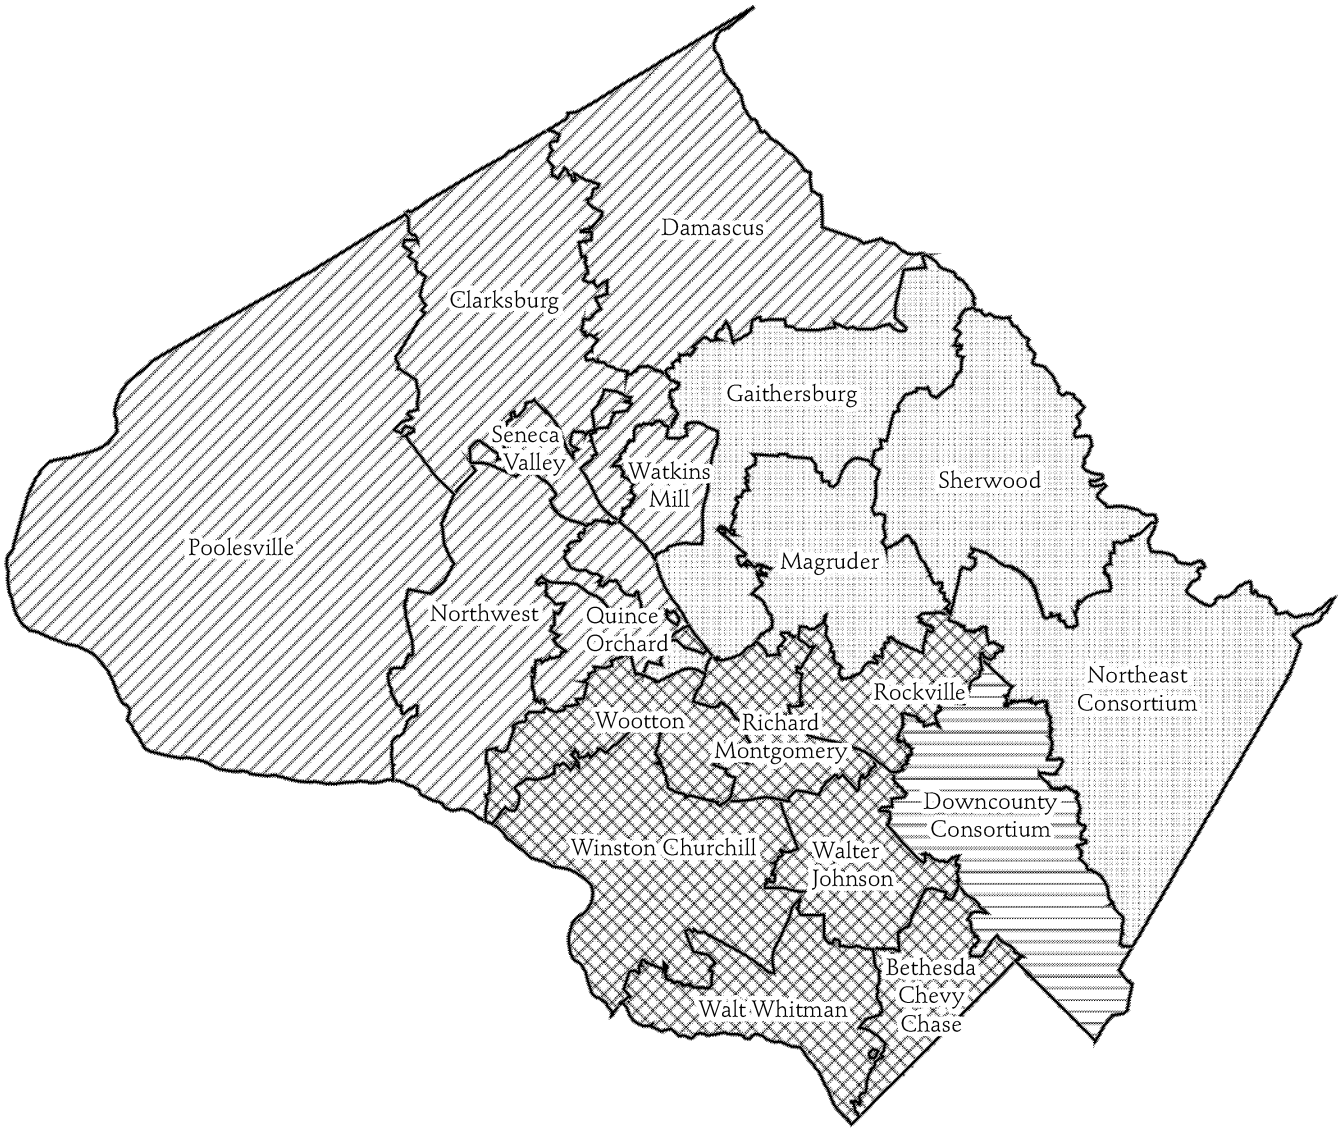

Office of School Support and Improvement
Associate Superintendents and
Directors of School Support and Improvement
Dr. Kimberly A. Statham, Deputy Superintendent

	Associate Superintendent	Director of School Support and Improvement
Elementary Schools	Dr. Donna S. Hollingshead	Mr. Pat D. Abrunzo
		Mr. Michael D. Bayewitz
	Dr. Laverne G. Kimball	Mr. Greg S. Edmundson
	Ms. Bronda L. Mills	Mr. Matthew A. Devan
	Dr. Myra J. Smith	Ms. Audra M. Fladung
Middle Schools	Dr. Darrly L. Williams	Mrs. Diane D. Morris
		Mrs. Elizabeth L. Thomas
		Dr. Michael J. Zarchin
High Schools	Dr. Christopher S. Garran	Mr. Kevin E. Lowndes
		Dr. Debra S. Munk
		Mr. Brian W. Scriven

Montgomery County Public Schools - Division of Long-range Planning - June, 2015

Introduction

In November 1996, the voters of Montgomery County approved by referendum an amendment to the County Charter that changed the County Council's review and approval cycle of the six-year Capital Improvements Program (CIP) from an annual to biennial cycle. The referendum specified that in odd-numbered fiscal years (on-years) the County Council would conduct a full review of the six-year CIP and in even-numbered fiscal years (off-years), the County Council only would consider amendments to the adopted CIP. The Approved FY 2016 Capital Budget and Amendments to the FY 2015–2020 CIP provides the approved appropriation authority for funds needed to implement CIP projects during FY 2016 as well as proposed amendments to the Adopted FY 2015–2020 CIP.

This document contains the following sections:

Chapter 1, "The Approved FY 2016 Capital Budget and Amendments to the FY 2015–2020 Capital Improvements Program (CIP)," is a review of the major factors that have influenced the development of approved projects to the FY 2016 Capital Budget and Amendments to the FY 2015–2020 CIP. This chapter includes a table summarizing approved Amendments to the FY 2015–2020 CIP.

Chapter 2, "The Planning Environment," describes the demographic, economic, and enrollment trends in Montgomery County that form the context for reviewing facility plans and addressing long-range system needs.

Chapter 3, "Facility Planning Objectives," outlines six facility planning objectives that guide the school system as it moves to accommodate enrollment growth and program changes. The objectives are discussed and placed in the context of the recommended CIP actions.

Chapter 4, "Approved Actions and Planning Issues," is arranged by high school cluster and high school consortium. This chapter provides maps depicting school boundaries and locations, a bar graph that indicates school utilization within each cluster, tables with enrollment projections, school demographic profiles, building room use, capacity data, and other facility information. Planning issues are identified, and adopted actions and recommended actions to this CIP are discussed.

Chapter 5, "Countywide Projects," provides a brief summary description of the CIP projects that are programmed to meet the needs of many schools across the county. These projects involve multiyear plans with different schools scheduled each year. (Referred to as countywide projects).

Chapter 6, 'Project Description Forms,' contain the individual MCPS Project Description Forms (PDFs) adopted by the County Council for the Amended FY 2015–2020 CIP. Montgomery County uses the PDFs as the official capital budget documentation for all county agencies.

Several appendices, at the end of the document, contain information on a variety of topics including enrollment information, state-rated capacities, Board of Education policies, modernization schedules, available school sites, closed schools and their current use, and relocatable classroom placements. Also included are maps for identifying Board of Education, council manic, and legislative election districts. It is important to note that this is a planning document for the school system as a whole and that while cluster organization is used for presentation of information, planning decisions often cross cluster boundaries to meet program and facility needs for students.

Chapter 1

The County Council Adopted FY 2016 Capital Budget and Amendments to the FY 2015–2020 Capital Improvements Program

The Impact of the Biennial CIP Process

In November 1996, the Montgomery County charter was amended by referendum to require a biennial, rather than annual, Capital Improvements Program (CIP) review and approval process. The total six-year CIP is now reviewed and approved for each odd-numbered fiscal year. For even-numbered fiscal years, only amendments are considered where changes are needed in the second year of the six-year CIP. In FY 1998, the county executive developed a set of criteria to identify and prioritize project requests that would qualify as amendments.

Fiscal Year (FY) 2015 was a full CIP review year and resulted in the County Council adopting the FY 2015–2020 CIP in May 2014. Fiscal Year 2016 is an off-budget or amendment year. As a result, the biennial CIP process requires the county executive and County Council to consider amendments to the adopted FY 2015–2020 CIP that request appropriations for the FY 2016 Capital Budget and that changes expenditures for the FY 2016–2020 out-years of the adopted CIP.

In an off-budget year, such as FY 2016, the following criteria are applied to MCPS amendment requests (in priority order):

1. Urgent school capacity need (i.e., Growth Policy (GP) considerations, unusually high utilization rate or seat deficit)
2. Urgent public safety concerns
3. Leveraging of state aid involved
4. Inflationary increases above 2.5 percent in projects that address school capacity
5. Inflationary increases above 2.5 percent in revitalization/expansion and other projects

The County Council must still approve a capital budget in the off-budget fiscal year that includes appropriations for all projects. In a typical off-budget year, it is anticipated that very few changes will be made to the projects and amounts approved by the County Council for FYs 2016–2020.

The County Council Adopted Capital Improvements Program

This document contains the adopted FY 2016 Capital Budget appropriation amounts and the FY 2015–2020 CIP expenditure schedules approved by the County Council in May 2015.

In May 2014, the County Council adopted FY 2015 Capital Budget and FY 2015–2020 CIP was $1.528 billion, $214 million less than the Board of Education's request. This reduction in funding resulted in a one-year delay of all individual school projects—not under design or construction—but maintained the planning funds as requested by the Board of Education. The reduction also resulted in a one-year delay, beyond the Board of Education's request, for elementary school revitalization/expansion projects and a one-year delay of secondary revitalization/expansion projects beginning with Tilden Middle School and Seneca Valley High School.

The *Board of Education's Requested FY 2016 Capital Budget and Amendments to the FY 2015–2020 Capital Improvements Program* totaled $1.751 billion, an increase of $223.3 million more than the previously approved CIP. The requested amendments restored the schedules of all the individual school projects that were delayed one year in the adopted CIP; restored the schedule of the elementary school revitalization/expansion projects that were delayed one year beyond the Board of Education's request; and, restored the schedule for secondary revitalization/expansion projects that were delayed one year. The Board of Education's request also included a scope change for one existing project, additional funding for two existing projects, and funding for one new project.

The county executive, in his Recommended FY 2016 Capital Budget and Amendments to the FY 2015–2020 Capital Improvements Program supported the Board of Education's request, but in order to fully fund the request, assumed $213.3 million in new state supported School Financing Bonds for MCPS. The Maryland General Assembly did not pass the School Financing Bonds legislation; therefore, a $213.3 million shortfall existed between the Board of Education's request and the county executive's recommendation. Subsequently, the County Council requested that the Board of Education submit a scenario to reduce the Board of Education's FY 2016 Capital Budget and

Amendments to the FY 2015–2020 Capital Improvements Program to more closely align with the funding deficit. The Board of Education submitted a scenario to the County Council that delayed elementary and secondary revitalization/expansion projects one year beyond the Board of Education's request, with the exception of three elementary revitalization/expansion projects that can begin construction in FY 2016—Brown Station, Wayside, and Wheaton Woods elementary schools; delayed 7 of 16 capacity projects one year; and removed all expenditures for the Shady Grove Transportation Depot Replacement project. Based on the scenario above, the Board of Education's request was reduced by $210.1 million.

On May 14, 2015, during the reconciliation process, the County Council approved the Board of Education's scenario which delayed all but three elementary school revitalization/expansion projects one year beyond the Board of Education's request and delayed all secondary revitalization/expansion projects one year beyond the Board of Education's request. The County Council also approved the delay of the seven capacity projects, but in addition, also delayed by one year, the remaining 9 capacity projects. Also, the County Council removed all expenditures for the Shady Grove Transportation Depot, with the exception of $700,000, to be used to conduct feasibility studies to determine the future location of the depot.

The County Council did support the additional $2.5 million for the Planned Life-cycle Asset Replacement project and the $100,000 for the Facility Planning project to conduct feasibility studies for the high schools in the Downcounty Consortium. Also, the County Council programmed an additional $2 million in the Technology Modernization project for FY 2016. The County Council included four projects to avoid residential moratoria—two at the high school level in the Downcounty Consortium, one at the middle school level in the Downcounty Consortium, and one at the elementary school level in the Gaithersburg Cluster.

The Board of Education's request included a scope change for the Blair G. Ewing Center Improvements project to relocate the Alternative Education Programs from the Ewing Center site to the former English Manor Elementary School site. The County Council did not approve the scope change, but instead, directed the Board of Education to reevaluate the current Blair G. Ewing site, as well as another site deemed appropriate by the Board of Education. Subsequently, the Board of Education directed MCPS staff to reevaluate the current Blair G. Ewing site, as well as other publicly owned sites. The Board of Education's request also included the acceleration of construction funds for the Blair G. Ewing Center Improvements project. As a result of the actions by the County Council and the Board of Education, the County Council maintained the approved schedule for this project.

The summary table at the end of this chapter, titled "County Council Adopted FY 2016 Capital Budget and Amendments to the FY 2015–2020 Capital Improvements Program," (page 1-6) summarizes the County Council action for all projects. The first column in the table shows the projects grouped by high school cluster. The second column shows the Board of Education's request and the third column shows the County Council's action for the Amended FY 2015–2020 CIP. It is important to note that many previously approved projects will be blank since they can proceed on their currently approved schedules. The last column shows the anticipated completion date for each project.

The next summary table includes all of the countywide projects approved by the County Council in the Amended FY 2015–2020 CIP (page 1-12). The final two tables contain summary information regarding the adopted appropriation and expenditure schedule for the FY 2016 Capital Budget and Amendments to the FY 2015–2020 CIP (page 1-14) and the FY 2016 State CIP funding approved for MCPS (page 1-15).

It is important to note that an appropriation differs from an expenditure. Once approved by the County Council, an appropriation gives MCPS the authority to encumber and spend money within a specified dollar limit for a project. If a project extends beyond one fiscal year, a majority of the cost of the project would need to be appropriated in order to award the construction contract. An expenditure, on the other hand, is a multi-year spending plan in the CIP that shows when County resources are expected to be spent over the six-year period.

Funding the Capital Improvements Program

The CIP is funded mainly from four types of revenue sources—county General Obligation (GO) bonds, state aid, current revenue, and Recordation and School Impact taxes. The amount of GO bond funding available for all county CIP projects is governed by Spending Affordability Guidelines (SAG) limits set by the County Council before CIP submissions are prepared. The amount of state aid available is governed by the rules, regulations, and procedures established by the state of Maryland Interagency Committee on School Construction (IAC) and by the amount of state revenues available to support the state school construction program. The amount of current revenue available to fund CIP projects is governed by county tax revenues and the need to balance capital and operating budget requests. And, the amount of Recordation and School Impact taxes is governed by the amount collected by the county from the sale and refinancing of existing homes and, the construction of new residential development. All four types of revenue sources are discussed below.

Fiscal Years	Spending Affordability Guidelines
FY 1999–2004	$714 million
FY 1999–2004 Amended	$743 million*
FY 2001–2006	$798 million
FY 2001–2006 Amended	$826 million*
FY 2003–2008	$880 million
FY 2003–2008 Amended	$895 million*
FY 2005–2010	$1.14 billion

FY 2005–2010 Amended	$1.22 billion*
FY 2007–2012	$1.44 billion
FY 2007–2012 Amended	$1.65 billion*
FY 2009–2014	$1.8 billion
FY 2009–2014 Amended	$1.84 billion
FY 2011–2016 CIP	$1.95 billion
FY 2011–2016 Amended	$1.91 billion*
FY 2013–2018 CIP	$1.77 billion
FY 2013–2018 Amended	$1.77 billion*
FY 2015–2020 CIP	$1.947 billion
FY 2015–2020 Amended	$1.999 billion*
*Limits set during biennial process	

General Obligation (GO) Bonds and Spending Affordability Guidelines (SAG)

In each fiscal year, the County Council must set Spending Affordability Guidelines (SAG) for the level of bonded debt it believes the county can afford. The guidelines are set following an analysis of fiscal consideration that shape the county's economic health. It is not intended that the County Council consider the extent of the capital needs of the different county agencies at the time it adopts the SAG limits.

As the table above indicates, since FY 1999, the County Council has steadily increased the SAG limits. However, for FY 2012, an off-year of the CIP, the County Council, in February 2011 decreased the SAG limit by $5 million in both FY 2011 and FY 2012 and decreased the six-year total to $1.92 billion, a total reduction of $30 million. This was the first time in nearly 20 years that the six-year total for SAG was reduced. During the County Council's reconciliation process in May 2011, the $320 million programmed for FY 2012 was reduced to $310 million resulting in a six-year total of $1.91 billion.

For FY 2013, the County Council, in October 2011, set the capital budget SAG limits at $295 million for both FY 2013 and FY 2014, with a six-year total of $1.77 billion, a decrease of $140 million from the previously approved SAG limit. The County Council reviewed the SAG limit in February 2012 and upheld the SAG limit that was set in October 2011—$295 million per year and a six-year total of $1.77 billion. For FY 2014, an off-year of the CIP, the County Council, in February 2013, maintained the SAG limit that was approved in FY 2013.

For FY 2015, the County Council, in October 2013, set the capital budget SAG limits at $295 million for both FY 2015 and FY 2016, with a six-year total of $1.77 billion, the same totals for the last two budget cycles. The County Council reviewed the SAG limit in February 2014 and raised the limit to $324.5 million for FY 2015 and FY 2016 and a six-year total of $1.947 billion. The County Council reviewed the SAG limit in February 2015, and increased the limit to $1.999 billion, an increase of $52 million.

Recordation Tax and School Impact Tax

The two bills approved by the County Council in the spring of 2004, Bill 24–03, Recordation Tax—Use of Funds, and Bill 9–03, Development Impact Tax—School Facilities, dedicated and created significant current revenue sources to supplement the GO bond funding of the CIP. Bill 24–03, Recordation Tax—Use of Funds, dedicated the increase in the Recordation Tax adopted in 2002 for use in funding both GO bond eligible and current revenue funded projects in the CIP. Bill 9–03, Development Impact Tax—School Facilities, generates funds used for bond eligible projects that increase school capacity through new schools, additions to schools, or the portion of revitalizations/expansion projects to schools that add capacity. Both of these bills are important because they will continue to provide significant current revenues in addition to GO bonds that will support the MCPS CIP.

State Funding

In the first 22 years of the State Public School Construction Program, from FY 1973 to FY 1994, the amount of state funding received by MCPS averaged $13.7 million per year. In FY 1995 and FY 1996, the state funded approximately $20 million per year, and in FY 1997, the state allocated $36 million for Montgomery County. Using the $36 million level of state funding as a benchmark, the County Council increased the levels of state aid assumed in the CIP. County efforts were again successful in FY 1998 and MCPS was allocated $38 million in state aid for school construction projects. The county was even more successful in FY 1999, FY 2000, and FY 2001 with $50 million, $50.2 million, and $51.2 million being allocated respectively. The following table shows the amount of state aid received each fiscal year since FY 1992.

For FY 2012, the state aid request was $163.7 million. Of the $163.7 million request, the FY 2012 state aid approved for MCPS was $42 million, approximately $121.7 million less than the amount requested, but $2 million more than the $40 million assumed for FY 2012 in the Amended FY 2011–2016 CIP. For FY 2013, the state aid request was $184.5 million. Of the $184.5 million request, the FY 2013 state aid approved for MCPS was $43.1 million, approximately $141.4 million less than the amount requested, but approximately $3 million more than the $40 million assumed for FY 2013 in the FY 2013–2018 CIP. For FY 2014, the state aid request was $149.3 million. Of the $149.3 million request, the FY 2014 state aid approved for MCPS was $35.09 million, approximately $114.2 million less than the amount requested, and $4.9 million less than the $40 million assumed for FY 2014.

For FY 2015, the revised state aid request was $162.9 million. Of the $162.9 million request, the FY 2015 state aid approved for MCPS was $39.95 million, approximately $122.95 million less than the amount requested, and $50,000 less than the $40 million assumed for FY 2015. For FY 2016, the revised state aid request was $147.99 million. This figure is based on current eligibility of projects approved by the County Council in

May 2014. Of the $147.99 million request, $2.6 million was for one project that received partial state funding in a prior year; $94.6 million was for 12 forward-funded construction projects; $5.4 million was for systemic roofing and HVAC projects; $30.8 million was for three construction projects; and $14.6 million was for 7 forward-funded projects that will require state planning approval in addition to construction funds. These projects have already been approved for funding by the County Council and would be eligible for state funding if state planning approval were granted. The FY 2016 state aid approved for MCPS was $39.84 million, approximately, $108.15 million less than the amount requested. MCPS also received an additional $5.9 million in state aid for school construction projects due to the passage of the Capital Grant Program for Local School Systems with Significant Enrollment Growth or Relocatable Classrooms legislation approved by the Maryland General Assembly in April 2015.

Current Revenue


There are some projects that are not bond eligible because the service or improvement covered by the project does not have a life expectancy that would be equal to or exceed the typical 20-year life of the bond funding the project. These projects must be funded with current revenue. There are three such projects in the MCPS CIP—Relocatable Classrooms, Technology Modernization, and Facility Planning. Current revenue-funded projects make up approximately 10 percent of the approved CIP and must be funded with the general current receipts the county receives from its share of all state and local taxes and fees. The same general current receipts are used to fund the county operating budget.

The Relationship Between State and Local Funding

On average, MCPS receives 25 to 30 percent of the cost of eligible project expenditures from state funds. There are, however, many countywide projects in the CIP that are not eligible for state funding. Federal mandates, such as projects to comply with the Americans with Disabilities Act, the Clean Air Act, the Asbestos Hazard Emergency Response Act, and Environmental Protection Agency regulations on fuel tank management are not eligible for state funding. Neither are expenditures for land acquisition, energy conservation, fire safety code upgrades, improved access to schools, indoor air quality improvements, school security systems, and technology modernization. These ineligible projects add approximately $25 million in budget requirements annually.

The amount of state funding received for a new school or addition is approximately 30 percent of the cost of the project, whereas, for a revitalization/expansion project, the amount is approximately 25 percent. The amount varies due to the state formulas used to calculate "eligible" expenditures. The use of the word "eligible" here refers to expenditures the state will reimburse based on state capacity and square foot formulas. The state does not consider what is required to completely fund a construction project. For example, design fees, land acquisition, furniture and equipment, and classroom and support space needs beyond the state square foot formula are not considered eligible for state funding. All of these costs must be borne locally. In addition, the state discounts its contributions to local school systems based on the wealth of each jurisdiction. In the case of Montgomery County, the state will pay only 50 percent of eligible state expenses for MCPS projects.

Capital Budget Expenditures and Funding Sources (FY 1999–2016)

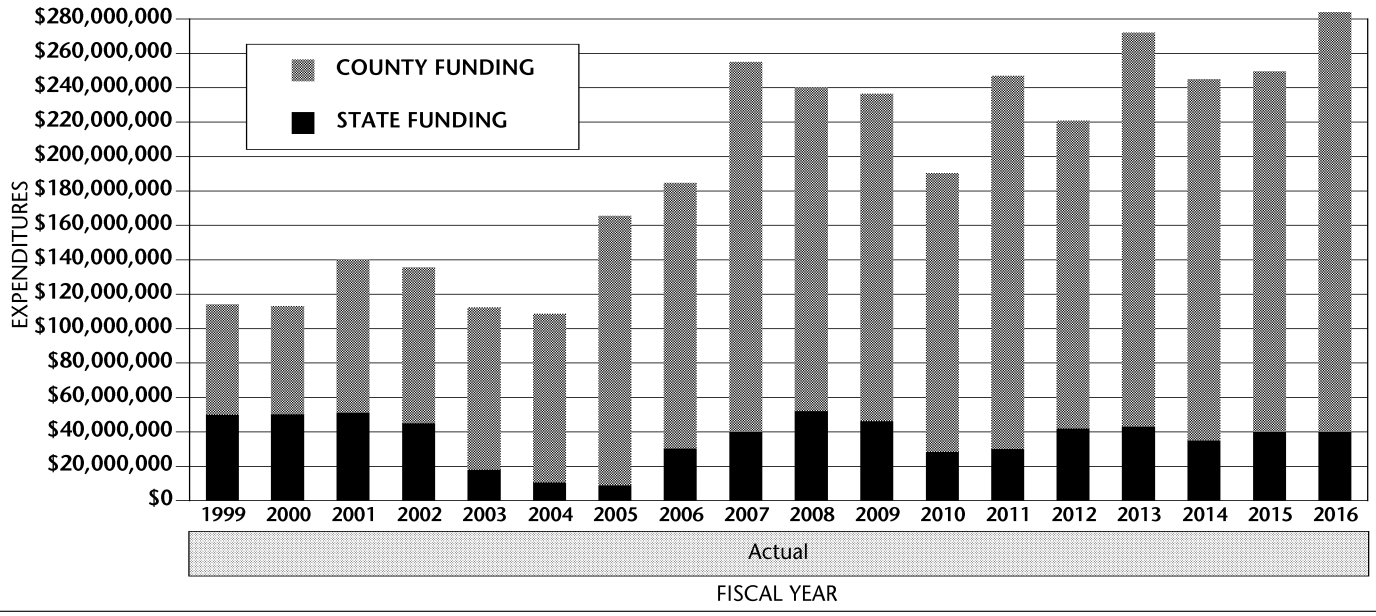

Capital Budget and Operating Budget Relationship

The relationship between the capital and the operating budgets is a critical consideration in the overall fiscal picture for MCPS. The capital budget affects the operating budget in three ways. First, GO bond debt, required for capital projects, creates the need to fund debt service payments in the Montgomery County Government operating budget. The County Council considers this operating budget impact when it approves Spending Affordability Guidelines. Second, a portion of the capital budget request is funded through general current revenue receipts, drawing money from the same sources that fund the operating budget. Finally, decisions in the capital budget to build a new school or add to an existing school create operating budget impacts through additional costs for staff, utilities, and other services. Although the budget process separates the capital and operating budgets by creating different time lines for decision making, checks and balances have been incorporated into the review process to ensure compliance with Spending Affordability Guidelines.

County Council Adopted FY 2016 Capital Budget and Amendments to the FY 2015–2020 Capital Improvements Program Summary Table[1]

Individual Projects	Board of Education Request	County Council Adopted Action May 2015	Anticipated Completion Date
Bethesda-Chevy Chase Cluster			
Bethesda-Chevy Chase HS Addition	Request FY 2016 appropriation for construction funds to restore Board of Education's FY2015–2020 CIP request.	Denied acceleration of capacity projects. Approved FY 2017 expenditures for construction funds.	8/18
Bethesda-Chevy Chase MS #2	Request an FY 2016 appropriation for construction funds.	Approved an FY 2016 appropriation for construction funds.	8/17
Bethesda ES Addition			8/15
North Chevy Chase ES Addition			8/15
Rock Creek Forest ES Revitalization/Expansion			1/15
Rosemary Hills ES Addition			8/15
Rosemary Hills ES Revitalization/Expansion	Request elementary school revitalization/ expansion projects be restored to Board of Education's FY2015–2020 CIP request.	Denied. Approved one year delay of elementary/secondary revitalization/ expansion projects.	1/23
Winston Churchill Cluster			
Potomac ES Revitalization/Expansion	Request elementary school revitalization/ expansion projects be restored to Board of Education's FY2015–2020 CIP request. Request FY 2016 appropriation for planning funds.	Denied. Approved one year delay of elementary/secondary revitalization/ expansion projects. Approved FY 2016 appropriation for planning funds.	1/20
Wayside ES Revitalization/Expansion	**Request elementary school revitalization/ expansion projects be restored to Board of Education's FY2015–2020 CIP request. Request FY 2016 appropriation for construction funds.**	**Approved FY 2016 appropriation for construction funds.**	**8/17**
Clarksburg Cluster			
Clarksburg HS Addition			8/15
Clarksburg/Damascus MS (New)	Request FY 2016 appropriation for balance of funding.	Approved FY 2016 appropriation for balance of funding.	8/16
Neelsville MS Addition			TBD
Clarksburg Cluster ES (Clarksburg Village Site #2) (New)			TBD
Captain James E. Daly ES Addition			TBD
Damascus Cluster			
Clarksburg/Damascus MS (New)	Request FY 2016 appropriation for balance of funding.	Approved FY 2016 appropriation for balance of funding.	8/16
Damascus ES Revitalization/Expansion	Request elementary school revitalization/ expansion projects be restored to Board of Education's FY2015–2020 CIP request.	Denied. Approved one year delay of elementary/secondary revitalization/ expansion projects.	1/23

[1]Bold indicates amendment to the approved FY 2015–2020 CIP. Blank indicates no change from the approved project.

Individual Projects	Board of Education Request	County Council Adopted Action May 2015	Anticipated Completion Date
Downcounty Consortium			
DCC HS Capacity Study	**Request FY 2016 appropriation for facility planning.**	**Approved FY 2016 appropriation for facility planning.**	**TBD**
Wheaton HS Revitalization/Expansion			1/16 Building 8/18 Site
Eastern Middle School Revitalization/Expansion	Request secondary school revitalization/expansion projects be restored to Board of Education's FY2015–2020 CIP request.	Denied. Approved one year delay of elementary/secondary revitalization/ expansion projects.	8/22
Col. E. Brooke Lee MS Addition			TBD
Col. E. Brooke Lee MS Revitalization/Expansion	Request secondary school revitalization/expansion projects be restored to Board of Education's FY2015–2020 CIP request.	Denied. Approved one year delay of elementary/secondary revitalization/ expansion projects.	TBD
A. Mario Loiederman MS Addition			TBD
Parkland MS Addition			TBD
Silver Spring International MS Addition			TBD
Takoma Park MS Addition			TBD
Arcola ES Addition			8/15
Brookhaven ES Addition (DCC Solution)	Request addition projects be restored to Board of Education's FY2015–2020 CIP request. Request FY 2016 appropriation for planning funds.	Denied acceleration of capacity projects. Approved FY 2016 appropriation for planning funds.	8/19
Glen Haven ES Addition (DCC Solution)	Request addition projects be restored to Board of Education's FY2015–2020 CIP request. Request FY 2016 appropriation for planning funds.	Denied acceleration of capacity projects. Approved FY 2016 appropriation for planning funds.	8/19
Highland ES Addition (DCC Solution)	Request addition projects be restored to Board of Education's FY2015–2020 CIP request. Request FY 2016 appropriation for planning funds.	Denied acceleration of capacity projects. Approved FY 2016 appropriation for planning funds.	8/19
Highland View ES Addition			TBD
Kemp Mill ES Addition (DCC Solution)	Request addition projects be restored to Board of Education's FY2015–2020 CIP request. Request FY 2016 appropriation for planning funds.	Denied acceleration of capacity projects. Approved FY 2016 appropriation for planning funds.	8/19
Rolling Terrace ES Addition			TBD
Sargent Shriver ES Addition (DCC Solution)	Request addition projects be restored to Board of Education's FY2015–2020 CIP request. Request FY 2016 appropriation for planning funds.	Denied acceleration of capacity projects. Approved FY 2016 appropriation for planning funds.	8/19
Wheaton Woods ES Revitalization/Expansion	**Request elementary school revitalization/ expansion projects be restored to Board of Education's FY2015–2020 CIP request. Request FY 2016 appropriation for construction funds.**	**Approved FY 2016 appropriation for construction funds.**	**8/17**
Woodlin ES Addition			TBD

[1]Bold indicates amendment to the approved FY 2015–2020 CIP. Blank indicates no change from the approved project.

Individual Projects	Board of Education Request	County Council Adopted Action May 2015	Anticipated Completion Date
Gaithersburg Cluster			
Gaithersburg ES Addition			TBD
Goshen ES Addition			TBD
Strawberry Knoll ES Addition			TBD
Summit Hall ES Revitalization/Expansion	Request elementary school revitalization/ expansion projects be restored to Board of Education's FY2015–2020 CIP request.	Denied. Approved one year delay of elementary/secondary revitalization/ expansion projects.	1/23
Walter Johnson Cluster			
Walter Johnson HS Addition			TBD
North Bethesda MS Addition	Request addition projects be restored to Board of Education's FY2015–2020 CIP request. Request FY 2016 appropriation for construction funds.	Denied acceleration of capacity projects. Approved FY 2017 expenditure for construction funds.	8/18
Tilden MS Revitalization/Expansion	Request secondary school revitalization/expansion projects be restored to Board of Education's FY2015–2020 CIP request. Request FY 2016 appropriation for planning funds.	Denied. Approved one year delay of elementary/secondary revitalization/ expansion projects. Approved FY 2016 appropriation for planning funds.	8/20
Ashburton ES Addition	Request addition projects be restored to Board of Education's FY2015–2020 CIP request.	Denied acceleration of capacity projects. Approved FY 2017 expenditures for planning funds.	8/20
Kensington-Parkwood ES Addition	Request addition projects be restored to Board of Education's FY2015–2020 CIP request. Request FY 2016 appropriation for construction funds.	Denied acceleration of capacity projects. Approved FY 2017 expenditures for construction funds.	8/18
Luxmanor ES Revitalization/Expansion	Request elementary school revitalization/ expansion projects be restored to Board of Education's FY2015–2020 CIP request. Request FY 2016 appropriation for planning funds.	Denied. Approved one year delay of elementary/secondary revitalization/ expansion projects. Approved FY 2016 appropriation for planning funds.	1/20
Col. Zadok Magruder Cluster			
Candlewood ES Revitalization/Expansion			1/15
Judith A. Resnik ES Addition	Request addition projects be restored to Board of Education's FY2015–2020 CIP request.	Denied acceleration of capacity projects. Approved FY 2017 expenditure for planning funds.	8/20
Richard Montgomery Cluster			
Richard Montgomery HS Addition	Request FY 2016 appropriation for facility planning.	Approved FY 2016 appropriation for facility planning.	TBD
Julius West MS Addition	Request FY 2016 appropriation for balance of funding.	Approved FY 2016 appropriation for balance of funding.	8/16
Richard Montgomery ES #5 (Hungerford Park Site)	Request project to be restored to Board of Education's FY2015–2020 CIP request. Request FY 2016 appropriation for construction funds.	Denied acceleration of capacity projects. Approved FY 2017 expenditures for construction funds.	8/18
Twinbrook ES Revitalization/Expansion	Request elementary school revitalization/ expansion projects be restored to Board of Education's FY2015–2020 CIP request.	Denied. Approved one year delay of elementary/secondary revitalization/ expansion projects.	1/23

[1]Bold indicates amendment to the approved FY2015–2020 CIP. Blank indicates no change from the approved project.

Individual Projects	Board of Education Request	County Council Adopted Action May 2015	Anticipated Completion Date
Northeast Consortium			
William Farquhar MS Revitalization/Expansion	Request FY 2016 appropriation for balance of funding.	Approved FY 2016 appropriation for balance of funding.	8/16
JoAnn Leleck ES at Broad Acres Addition			TBD
Burtonsville ES Addition	Request addition projects be restored to Board of Education's FY2015–2020 CIP request.	Denied acceleration of capacity projects. Approved FY 2017 expenditure for planning funds.	8/20
Stonegate ES Revitalization/Expansion	Request elementary school revitalization/ expansion projects be restored to Board of Education's FY2015–2020 CIP request.	Denied. Approved one year delay of elementary/secondary revitalization/ expansion projects.	8/21
Northwest Cluster			
Diamond ES Addition	Request addition projects be restored to Board of Education's FY2015–2020 CIP request. Request FY 2016 appropriation for construction funds.	Denied acceleration of capacity projects. Approved FY 2017 expenditure for construction funds.	8/18
Northwest ES #8	Request project to be restored to Board of Education's FY2015–2020 CIP request. Request FY 2016 appropriation for construction funds.	Denied acceleration of capacity projects. Approved FY 2017 expenditure for construction funds.	8/18
Poolesville Cluster			
Poolesville HS Revitalization/Expansion	Request secondary school revitalization/expansion projects be restored to Board of Education's FY2015–2020 CIP request.	Denied. Approved one year delay of elementary/secondary revitalization/ expansion projects.	8/23 Building 8/24 Site
Quince Orchard Cluster			
Brown Station ES Revitalization/Expansion	**Request elementary school revitalization/ expansion projects be restored to Board of Education's FY2015–2020 CIP request. Request FY 2016 appropriation for construction funds.**	**Approved FY 2016 appropriation for construction funds.**	**8/17**
Jones Lane ES Addition (overutilization at Rachel Carson ES)	Request FY 2015 appropriation for facility planning.		TBD
Fields Road ES Addition	Request FY 2015 appropriation for facility planning.		TBD
Rockville Cluster			
Lucy V. Barnsley ES Addition	Request addition projects be restored to Board of Education's FY2015–2020 CIP request. Request FY 2016 appropriation for construction funds.	Denied acceleration of capacity projects. Approved FY 2017 expenditure for construction funds.	8/18
Maryvale ES Revitalization/Expansion	Request elementary school revitalization/ expansion projects be restored to Board of Education's FY2015–2020 CIP request. Request FY 2016 appropriation for planning funds.	Denied. Approved one year delay of elementary/secondary revitalization/ expansion projects. Approved FY 2016 appropriation for planning funds.	1/20

[1]Bold indicates new project to the approved FY 2015–2020 CIP. Blank indicates no change from the approved project.

Individual Projects	Board of Education Request	County Council Adopted Action May 2015	Anticipated Completion Date
Seneca Valley Cluster			
Seneca Valley HS Revitalization/Expansion	**Request secondary school revitalization/expansion projects be restored to Board of Education's FY2015–2020 CIP request.**	**Denied. Approved one year delay of elementary/secondary revitalization/ expansion projects.**	**8/19 Building 8/20 Site**
Lake Seneca ES Addition			TBD
S. Christa McAuliffe ES Addition	Request addition projects be restored to Board of Education's FY2015–2020 CIP request.	Denied acceleration of capacity projects. Approved FY 2017 expenditure for planning funds.	8/20
Sherwood Cluster			
William Farquhar MS Revitalization/Expansion	Request FY 2016 appropriation for balance of funding.	Approved FY 2016 appropriation for balance of funding.	8/16
Belmont ES Revitalization/Expansion	Request elementary school revitalization/ expansion projects be restored to Board of Education's FY2015–2020 CIP request.	Denied. Approved one year delay of elementary/secondary revitalization/ expansion projects.	8/21
Watkins Mill Cluster			
Neelsville MS Addition	Request FY 2015 appropriation for facility planning.		TBD
South Lake ES Addition			TBD
Walt Whitman Cluster			
Whitman HS Addition			TBD
Thomas S. Pyle MS Addition	Request FY 2016 appropriation for facility planning.	Approved FY 2016 appropriation for facility planning.	TBD
Burning Tree ES Addition			TBD
Wood Acres ES Addition	Request FY 2016 appropriation for balance of funding.	Approved FY 2016 appropriation for balance of funding.	8/16
Thomas S. Wootton Cluster			
Thomas S. Wootton HS Revitalization/Expansion	Request secondary school revitalization/expansion projects be restored to Board of Education's FY2015–2020 CIP request. Request FY 2016 appropriation for planning funds.	Denied. Approved one year delay of elementary/secondary revitalization/ expansion projects. Approved FY 2016 appropriation for planning funds.	8/21 Building 8/22 Site
Cold Spring ES Revitalization/Expansion	Request elementary school revitalization/ expansion projects be restored to Board of Education's FY2015–2020 CIP request.	Denied. Approved one year delay of elementary/secondary revitalization/ expansion projects.	8/21
DuFief ES Revitalization/Expansion	Request elementary school revitalization/ expansion projects be restored to Board of Education's FY2015–2020 CIP request.	Denied. Approved one year delay of elementary/secondary revitalization/ expansion projects.	8/21

[1]Bold indicates amendment to the approved FY 2015–2020 CIP. Blank indicates no change from the approved project.

Individual Projects	Board of Education Request	County Council Adopted Action May 2015	Anticipated Completion Date
Other Educational Facilities			
Thomas Edison High School for Technology Revitalization/Expansion	Request FY 2016 appropriation for construction funds.	Approved FY 2016 appropriation for construction funds.	8/17 Building 8/18 Site
Blair G. Ewing Center Improvements	Request FY 2016 appropriation for construction funds.	Denied acceleration of the construction funds. Approved FY 2017 expenditure for construction funds.	8/18
Rock Terrace School Modifications		Board of Education approved the collocation of Rock Terrace School with Tilden Middle School. Approved FY 2016 appropriation for planning funds.	8/20
Carl Sandburg Revitalization/Expansion (collocation with Maryvale ES)	Request elementary school revitalization/ expansion projects be restored to Board of Education's FY2015–2020 CIP request. Request FY 2016 appropriation for planning funds.	Denied. Approved one year delay of elementary/secondary revitalization/ expansion projects. Approved FY 2016 appropriation for planning funds.	1/20
Stephen Knolls School Modifications			TBD

[1]Bold indicates amendment to the approved FY 2015–2020 CIP. Blank indicates no change from the approved project.

County Council Adopted FY 2016 Capital Budget and Amendments to the FY 2015–2020 Capital Improvements Program Summary Table[1]

Countywide Projects	Board of Education Request	County Council Adopted Action May 2015	Anticipated Completion Date
ADA Compliance	Request FY 2016 appropriation to continue this project.	Approved FY 2016 appropriation.	Ongoing
Asbestos Abatement and Hazardous Materials Remediation	Request FY 2016 appropriation to continue this project.	Approved FY 2016 appropriation.	Ongoing
Building Modifications and Program Improvements	Request FY 2016 appropriation to continue this project.	Approved FY 2016 appropriation.	Ongoing
Current Revitalizations/Expansions	**Request the revitalization/ expansion projects be restored to Board of Education's FY2015–2020 CIP request.**	**Denied. Approved one year delay of elementary/secondary revitalization/ expansion projects, with the exception of three elementary school projects.**	**Ongoing**
Design and Construction Management	Request FY 2016 appropriation to continue this project.	Approved FY 2016 appropriation.	Ongoing
Energy Conservation	Request FY 2016 appropriation to continue this project.	Approved FY 2016 appropriation.	Ongoing
Facility Planning	**Request an amendment to the FY 2015-2020 CIP to increase the FY 2016 expenditure. Request an FY 2016 appropriation.**	**Approved an amendment to the FY 2015-2020 CIP and approved FY 2016 appropriation.**	**Ongoing**
Fire Safety Code Upgrades	Request FY 2016 appropriation to continue this project.	Approved FY 2016 appropriation.	Ongoing
Future Revitalizations/Expansions	Request the revitalization/ expansion projects be restored to Board of Education's FY2015–2020 CIP request.	Denied. Approved one year delay of elementary/secondary revitalization/ expansion projects.	Ongoing
HVAC Replacement	Request FY 2016 appropriation to continue this project.	Approved FY 2016 appropriation.	Ongoing
Improved (SAFE) Access to Schools	Request FY 2016 appropriation to continue this project.	Approved FY 2016 appropriation.	Ongoing
Indoor Air Quality Improvements	Request FY 2016 appropriation to continue this project.	Approved FY 2016 appropriation.	Ongoing
Planned Life Cycle Asset Replacement (PLAR)	**Request an amendment and an FY 2016 appropriation to continue this project.**	**Approved an amendment to the FY2015-2020 CIP and approved an FY 2016 appropriation to continue this project.**	**Ongoing**
Rehab./Reno. of Closed Schools (RROCS)	Request the schedule Richard Montgomery Cluster Elementary School #5 be restored to the Board of Education's FY2015–2020 CIP request. Request FY 2016 appropriation for construction funds.	Denied. Approved one year delay of capacity projects with construction funds in FY 2016.	Ongoing
Relocatable Classrooms	Request FY 2016 appropriation to continue this project.	Approved FY 2016 appropriation.	Ongoing
Restroom Renovations	Request FY 2016 appropriation to continue this project.	Approved FY 2016 appropriation.	Ongoing
Roof Replacement	Request FY 2016 appropriation to continue this project.	Approved FY 2016 appropriation.	Ongoing
School Security Systems			Ongoing

Countywide Projects	Board of Education Request	County Council Adopted Action May 2015	Anticipated Completion Date
Shady Grove Transportation Depot Replacement	**Request the redevelopment of the current Blair Ewing Center site for the replacement transportation depot.**	**Approved $700,000 to conduct feasibility studies to determine the future location of the depot.**	**TBD**
Stormwater Discharge and Water Quality Management	Request FY 2016 appropriation to continue this project.	Approved FY 2016 appropriation.	Ongoing
Technology Modernization	Request FY 2016 appropriation to continue this project.	Approved FY 2016 appropriation.	Ongoing

[1]Bold indicates amendment to the approved FY 2015–2020 CIP. Blank indicates no change from the approved project.

County Council Adopted FY 2016 Capital Budget
and Amendments to the FY 2015–2020 Capital Improvements Program

(figures in thousands)

Project	FY 2016 Approp.	Total	Thru FY 2013	Remaining FY 2014	Total Six-Years	FY 2015	FY 2016	FY 2017	FY 2018	FY 2019	FY 2020	Beyond
Individual School Projects												
Arcola ES Addition		3,841	141	1,096	2,604	1,057	1,547					
Ashburton ES Addition		5,089			5,089			256	192	1,988	2,653	2,132
Lucy Barnsley ES Addition		12,974			12,974	462	347	3,346	7,319	1,500		
Bethesda ES Addition		3,970	143	1,168	2,659	1,082	1,577					
Bethesda-Chevy Chase HS Addition		30,787			30,787	1,123	842	7,754	12,044	9,024		
Bethesda-Chevy Chase MS #2	47,916	52,314		250	52,064	829	13,181	32,674	5,380			
Brookhaven ES Addition (DCC Solution)	481	5,381			5,381		192	144	1,467	2,229	1,349	
Burtonsville ES Addition		9,766			9,766			469	352	3,574	5,371	3,052
Clarksburg Cluster ES (Clarksburg Village Site #1)		28,218	7,194	8,613	12,411	12,411						
Clarksburg HS Addition		11,823	377	3,229	8,217	3,269	4,948					
Clarksburg/Damascus MS (New)	1,400	52,764	200	1,107	51,457	12,633	30,246	8,578				
Diamond ES Addition		8,926			8,926	322	241	2,535	3,390	2,438		
Albert Einstein Cluster HS Solution		**2,334**			**1,639**				**89**	**556**	**994**	**695**
Blair Ewing Center Improvements		16,579			16,579	605	454	3,375	6,274	5,871		
Gaithersburg Cluster ES Solution		**3,888**			**2,730**				**147**	**927**	**1,656**	**1,158**
Glen Haven ES Addition (DCC Solution)	367	4,092			4,092		147	110	1,269	1,394	1,172	
Highland ES Addition (DCC Solution)	713	8,225			8,225		285	214	2,249	3,430	2,047	
Kemp Mill ES Addition (DCC Solution)	774	8,658			8,658		310	232	2,438	3,225	2,453	
Kensington-Parkwood ES Addition		11,156			11,156	399	299	3,145	6,092	1,221		
S. Christa McAuliffe ES Addition		10,171			7,760			364	273	2,868	4,255	2,411
North Bethesda MS Addition		18,610			18,610	676	507	5,155	6,379	5,893		
North Chevy Chase ES Addition		6,820	230	1,921	4,669	1,880	2,789					
Northwest ES #8		32,450			32,450	1,192	894	7,660	13,532	9,172		
Northwood Cluster HS Solution		**3,888**			**2,730**				**147**	**927**	**1,656**	**1,158**
Judith Resnik ES Addition		11,512			8,471			413	310	3,254	4,494	3,041
Rosemary Hills ES Addition		5,708	198	1,668	3,842	1,569	2,273					
Sargent Shriver ES Addition (DCC Solution)	341	3,881			3,881		136	102	1,074	2,103	466	
Waters Landing ES Addition		8,827	1,794	3,487	3,546	3,546						
Julius West MS Addition	688	15,303		409	14,894	4,664	8,554	1,676				
Wheaton Cluster MS Solution		**1,556**			**1,092**				**59**	**370**	**663**	**464**
Wood Acres ES Addition	342	47,916		232	8,374	2,637	4,822	915				
Countywide Projects												
ADA Compliance: MCPS	3,000	24,393	10,393	3,200	10,800	3,000	3,000	1,200	1,200	1,200	1,200	
Asbestos Abatement	1,145	15,520	7,505	1,145	6,870	1,145	1,145	1,145	1,145	1,145	1,145	
Building Modifications and Program Improvements	3,500	28,732	18,132	2,300	8,300	4,800	3,500					
Current Revitalizations/Expansions	**168,639**	**1,315,443**	**507,905**	**121,982**	**685,556**	**99,774**	**120,654**	**113,789**	**104,300**	**132,435**	**114,604**	
Design and Construction Management	4,900	65,775	31,475	4,900	29,400	4,900	4,900	4,900	4,900	4,900	4,900	
Energy Conservation: MCPS	2,057	29,750	15,351	2,057	12,342	2,057	2,057	2,057	2,057	2,057	2,057	
Facility Planning: MCPS	**550**	**11,097**	**6,807**	**600**	**3,690**	**900**	**550**	**770**	**400**	**670**	**400**	
Fire Safety Upgrades	2,000	15,483	6,712	1,503	7,268	2,000	2,000	817	817	817	817	
Future Revitalizations/Expansions		33,140			33,140	0	0	0	3,368	5,532	24,240	
HVAC (Mechanical Systems) Replacement	16,000	165,775	63,415	10,360	92,000	28,000	16,000	12,000	12,000	12,000	12,000	
Improved (Safe) Access to Schools	1,200	10,828	7,228	1,200	2,400	1,200	1,200					
Indoor Air Quality Improvements	2,147	28,061	16,282	1,497	10,282	2,147	2,147	1,497	1,497	1,497	1,497	
Planned Life-Cycle Asset Replacement (PLAR)	**9,750**	**94,516**	**52,199**	**4,741**	**37,576**	**8,862**	**9,750**	**4,741**	**4,741**	**4,741**	**4,741**	
Rehabilitation/Renovation of Closed Schools (RROCS)		110,820	75,439		35,381	1,303	977	8,455	21,065	3,581		
Relocatable Classrooms		45,811	26,811	4,000	15,000	5,000	5,000	5,000				
Restroom Renovations	1,000	13,085	8,735	1,000	3,350	1,000	1,000	1,000	350			
Roof Replacement: MCPS	8,000	78,929	30,589	6,468	41,872	8,000	8,000	6,468	6,468	6,468	6,468	
School Security Systems		18,610	9,614	5,860	3,136	3,136						
Shady Grove Transportation Depot Replacement	**700**	**700**			**700**		**700**					
Stormwater Discharge and Water Quality Management	616	9,367	5,055	616	3,696	616	616	616	616	616	616	
Technology Modernization	23,538	296,215	138,949	22,088	135,178	24,758	25,538	21,358	21,998	20,728	20,798	
Total Adopted CIP	**301,764**	**2,859,477**	**1,048,873**	**218,697**	**1,543,670**	**252,954**	**283,325**	**264,930**	**257,398**	**260,351**	**224,712**	**14,111**

*Bold indicates an amendment to the approved FY 2015–2020 CIP

FY 2016 Approved State Capital Improvements Program for Montgomery County Public Schools

(figures in thousands)

Priority No.	PFA Y/N	Project	Total Estimated Cost	Non PSCP Funds	Prior IAC Funding Thru FY 2015	FY 2016 Request For Funding	State Approved
		Balance of Funding (Forward-Funded)					
1	Y	Weller Road ES Revitalization/Expansion (CSR)	26,077	19,819	3,604	2,654	2,654
		Subtotal	**26,077**	**19,819**	**3,604**	**2,654**	**2,654**
		Construction Funding (Forward-Funded)					
2	Y	Bradley Hills ES Addition	17,949	13,414	0	4,535	4,305
3	N	Darnestown ES Addition	15,400	12,198	0	3,202	2,434
4	Y	Wyngate ES Addition	10,230	7,392	0	2,838	2,838
5	Y	Georgian Forest ES Addition (CSR)	10,620	7,835	0	2,785	1,197
6	Y	Westbrook ES Addition	12,052	9,105	0	2,947	2,068
7	Y	Viers Mill ES Addition (CSR)	11,177	10,320	0	857	336
		Subtotal	**77,428**	**60,264**	**0**	**17,164**	**13,178**
		Systemic Projects					
8	Y	Beall ES HVAC	2,250	1,690	0	560	560
9	Y	Highland ES HVAC	2,200	1,651	0	549	549
10	Y	Quince Orchard HS HVAC	2,200	1,651	0	549	549
11	Y	Rolling Terrace ES HVAC	2,100	1,576	0	524	524
12	Y	Shady Grove MS HVAC	2,050	1,539	0	511	511
13	Y	Captain James E. Daly ES HVAC	1,850	1,389	0	461	461
14	Y	Damascus HS HVAC	1,750	1,314	0	436	436
15	Y	Albert Einstein HS Roof	1,630	1,224	0	406	406
16	Y	Burning Tree ES HVAC	1,500	1,126	0	374	374
17	Y	Walt Whitman HS Roof	1,370	1,029	0	341	341
18	N	Thurgood Marshall ES Roof	1,084	814	0	270	270
19	Y	Washington Grove ES Roof	866	651	0	215	215
20	Y	Newport Mill MS Roof	864	649	0	215	215
		Subtotal	**21,714**	**16,303**	**0**	**5,411**	**5,411**
		Construction Funding (Forward-Funded)					
21	Y	Gaithersburg HS Revitalization/Expansion	109,100	69,514	0	39,586	18,601
22	Y	Clarksburg Cluster ES (New) (Wilson Wims ES)	28,732	19,311	0	9,421	
23	Y	Bel Pre ES Revitalization/Expansion (CSR)	28,872	20,034	0	8,838	
24	Y	Waters Landing ES Addition (CSR)	8,827	6,954	0	1,873	
25	Y	Rock Creek Forest ES Revitalization/Expansion (CSR)	29,100	18,854	0	10,246	
26	Y	Candlewood ES Revitalization/Expansion	24,133	16,692	0	7,441	
		Subtotal	**228,764**	**151,359**	**0**	**77,405**	**18,601**
		Planning and Construction Request (Forward-Funded)					
27/28	Y	Clarksburg HS Addition	11,823	9,198	0	2,625	
29/30	Y	North Chevy Chase ES Addition	6,820	5,301	0	1,519	
31/32	Y	Rosemary Hills ES Addition	5,708	4,428	0	1,280	
33/34	Y	Bethesda ES Addition	3,970	3,096	0	874	
35/36	Y	Arcola ES Addition (CSR)	3,841	2,987	0	854	
		Subtotal	**32,162**	**25,010**	**0**	**7,152**	**0**
		Construction Funding					
37	Y	Clarksburg/Damascus MS (New)*	52,764	36,723	0	8,021	
38	N	William H. Farquhar MS Revitalization/Expansion*	50,892	36,904	0	6,994	
39	Y	Wheaton HS Revitalization/Expansion*	102,507	70,938	0	15,785	
		Subtotal	**206,163**	**144,565**	**0**	**30,800**	**0**
		Planning and Construction Request					
40/41	Y	Julius West MS Addition	15,303	8,942	0	6,361	LP
42/43	Y	Wood Acres ES Addition	8,606	7,557	0	1,049	LP
		Subtotal	**23,909**	**16,499**	**0**	**7,410**	**0**
		Planning Approval Request					
44	Y	Wheaton Woods ES Revitalization/Expansion (CSR)*	LP			LP	LP
45	Y	Brown Station ES Revitalization/Expansion (CSR)*	LP			LP	LP
46	Y	Wayside ES Revitalization/Expansion*	LP			LP	LP
47	Y	Bethesda/Chevy Chase MS (New)*	LP			LP	
48	Y	Seneca Valley HS Revitalization/Expansion*	LP			LP	
49	Y	Thomas Edison HS of Technology Revitalization/Expansion*	LP			LP	
50	Y	Richard Montgomery ES #5 (New)*	LP			LP	
51	Y	Northwest ES #8 (New)*	LP			LP	
52	Y	Bethesda/Chevy Chase HS Addition	LP			LP	
53	Y	North Bethesda MS Addition	LP			LP	
54	Y	Kensington-Parkwood ES Addition	LP			LP	
55	Y	Diamond ES Addition	LP			LP	
56	Y	Lucy V. Barnsley ES Addition (CSR)	LP			LP	
		TOTAL	**616,217**	**433,819**	**3,604**	**147,996**	**39,844**

*Split-FY Funding Request

Chapter 2
The Planning Environment

Facility plans are developed in a dynamic planning environment. The major driver for these plans, since the mid-1980s, has been an enrollment increase of 63,200 students. Integral to this enrollment growth has been increased diversity, as seen in the wide range of cultures, language groups, and racial and ethnic populations that make up our cosmopolitan county.


Enrollment growth since 2007 has been particularly strong. This year, MCPS enrollment totals 153,852 students. Enrollment has increased by 16,107 students in the seven-year period from 2007 to 2014. Most of this enrollment increase, 14,704 students, has occurred at elementary schools. In the next six years, enrollment is projected to increase by 11,526 students, with most of this increase, 10,800 students, at middle schools and high schools. The 16,107 student increase in the past seven years and the 11,526 student increase projected for the next six years total a 27,633 student increase in a 13-year period. This significant enrollment increase is placing great pressure on school facilities and our capital program.

Funding for capital projects has not been sufficient to fully address elementary school enrollment increases, and 86 percent of the 404 relocatable classrooms are at elementary schools this year. The backlog of projects needed to add capacity at elementary schools will be compounded in the coming years as secondary schools receive higher enrollments that will exceed school capacities.

Community Trends

Population

Demographic trends in Montgomery County are part of a national trend in large metropolitan areas where African Americans, Asians, and especially Hispanics, have accounted for most, if not all, of the suburban population growth since 1990. MCPS planners consult various sources to monitor county population trends, including the U.S. Census Bureau, the Maryland Department of Planning, and the Montgomery County Planning Department. According to the U.S. Census, the total population of Montgomery County increased by 273,420 people between 1990, when there were 757,027 people, to 1,030,447 people in 2014. All of the county population growth since 1990 is due to increases in non-White race groups and the Hispanic ethnic group. Since 1990, the White, non-Hispanic population has decreased in the county by 2 percent, while the population of African Americans increased by 75 percent, the population of Asians increased by 118 percent, and the population of Hispanics of any race increased by 197 percent.

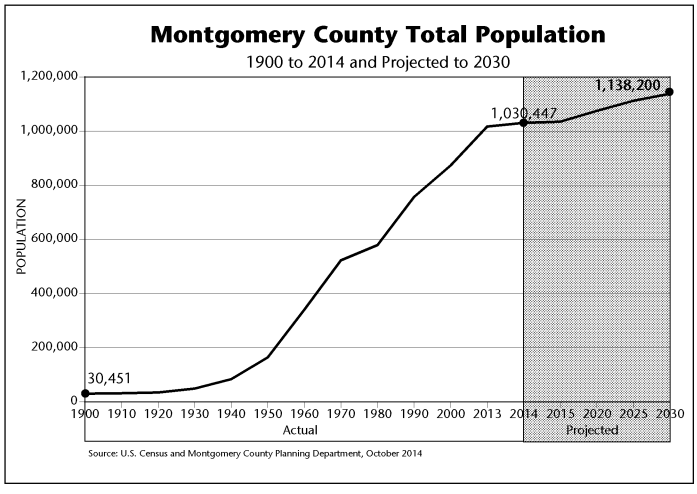

A significant share of the population increase in the county is the result of resident births outnumbering deaths by more than 2 to 1. From 2000 through 2013, there were 187,223 births compared to 77,242 deaths in the county for a net natural increase in population of 109,981 residents. The other major factor in population growth is immigration from outside the United States that has countered the outflow of county population to other places. Between 2000 and 2012, international migration contributed 110,171 residents, while domestic migration resulted in a loss of 68,586 residents. Combined, population migration netted 41,585 more residents between 2000 and 2012. The percent of foreign-born residents in Montgomery County is greater than any other Maryland jurisdiction and second only to Arlington County, Virginia in the Washington metropolitan area. The percent of foreign-born residents in Montgomery County increased from 18.6 percent in 1990 to 32.2 percent in 2010.

Economy

Beginning in the summer of 2007, turmoil in the nation's housing market led to the deepest economic decline since the Great Depression. The burst of the housing "bubble" had devastating implications for banks holding large amounts of mortgage debt. Defaults on mortgages by homeowners who should not have been qualified for loans escalated, led to a credit crisis that rippled through the economy, and resulted in millions of job losses. The credit crisis and related job losses also led to unprecedented federal involvement to contain the financial meltdown and stimulate the economy. In addition to the banking crisis, huge losses in the stock market resulted in a steep reduction in the value of personal investments and retirement accounts, sharply reducing consumer spending patterns.


The National Bureau of Economic Research, considered the arbiter of recessions, declared the recession that began in December 2007 to be over in June 2009. The depth and length of this recession led many to call it the "Great Recession," and to note that it was the longest economic downturn since the Great Depression. Despite the declaration that the recession ended in 2009, full recovery—especially in terms of employment—is proving to be a slow process. Despite recent reports


of lower unemployment, wages have stagnated and income inequality has increased. These factors continue to be a drag on the economy. Moreover, due to the nature of the global economy there are more interdependencies between the U.S. economy and world events than in the past. Because of this, economic uncertainty continues to characterize the recovery.

The impact of the recession was less severe in Montgomery County compared to other parts of the country. In February 2015, the Maryland unemployment rate was 5.5 percent and the Montgomery County unemployment rate was 4.0 percent. Although the 4.0 percent unemployment rate in the county is still above the more typical rates of 2.5 to 3.5 percent, signs of recovery have begun in the county. Resident employment in the county declined during the recession, from 503,400 jobs in 2008 to 493,000 jobs in 2009. Since 2009, resident employment has grown to 507,172 in 2014. Recovery in the county housing market, in terms of price and sales activity, also is evident.

Housing

High construction costs, a decreasing supply of residentially zoned land, and a preference for housing as an investment, led to extreme housing value appreciation, beginning in 2004. The Metropolitan Regional Information System, Inc., reports that the median sales price of homes rose from $355,000 in 2004 to a peak of $444,000 in 2007. After 2007, a market correction and weakened demand resulted in a drop in the median sales price of housing to $340,000 at the low point of the market in 2009. Since 2009, prices have increased gradually and in 2014 the median sale price was $400,000. The year 2009 was not only the low point for sales prices but also was the year with the fewest new residential starts, with only 931 housing units starting construction. Considerable improvement in housing starts has been seen, with 4,936 housing starts recorded in 2014.

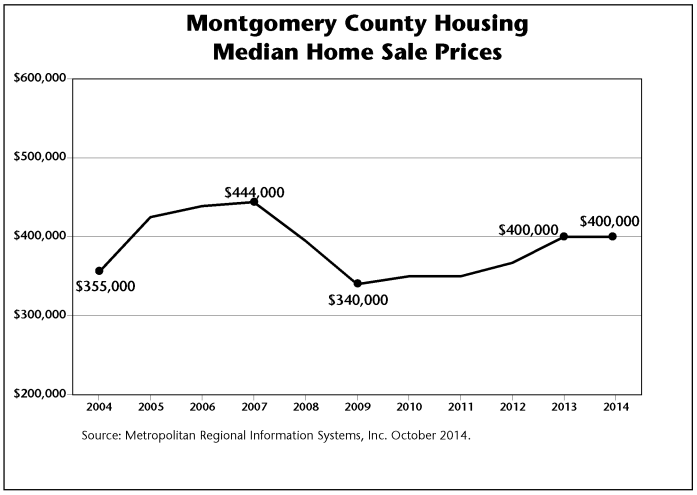

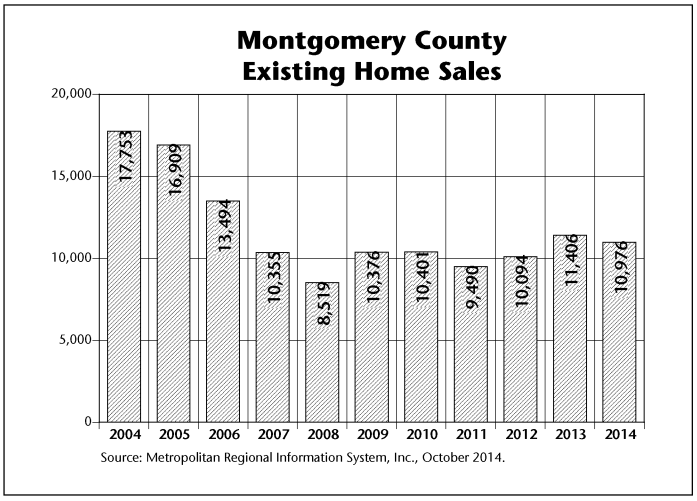

A growing supply of condominiums and apartments are coming on the market. This trend is a response to the high price of single-family units, a reduction in land available for more traditional suburban housing, and the advent of more households without children as baby boomers reach retirement age and the millennial generation seek more urbanized life styles. Seventy percent of residential starts in 2014 were multi-family units. Many of these projects conserve on land by utilizing structured parking garages, an attribute that increases the cost of the units. The number of students that attend school from this mostly high cost, high-density multi-family product has been small. Multi-family housing, both rental and condominium, will dominate the new home market for the foreseeable future.

MCPS monitors housing activity in all school service areas through close coordination with the Development Applications and Regulatory Coordination Unit of the Montgomery County Planning Department. Housing plans are factored into school enrollment projections according to building schedules provided by developers. As the economy improves, demand drives the housing market to renewed growth. Low mortgage interest rates also contribute to renewal of the housing sector.

Master Plans

Traditional suburban residential development is becoming the exception in the county. Clarksburg is the last large suburban community that will be built in the county. A number of large subdivisions in Clarksburg are well underway, and a new school cluster was formed in 2006 when Clarksburg High School opened to accommodate the new communities.

As the availability of land for residential development decreases, infill and redevelopment will characterize new growth. Higher housing densities than seen in the past are needed to increase the supply of housing in this urbanizing county. Areas of the county that already have seen substantial residential development are being revisited in county and city master plans. A desire to increase housing in these areas is driven by a jobs-to-housing imbalance that is believed to worsen traffic congestion.

Plans for high-density residential projects have been adopted in recent years for Germantown, the Great Seneca Science Corridor, the White Oak Science Gateway, and at the Glenmont, Shady Grove, White Flint, and Wheaton METRO stations. In addition, new plans are being developed, including the Bethesda Downtown, Montgomery Village, Westbard, White Flint 2, and Rockville Pike Corridor plans. Most of these new plans are expected to include primarily high density housing units. MCPS participates in county and city land use planning to ensure adequate school sites are identified and impacts on enrollment are considered. (See Appendix P-1 for further information on the role of MCPS in land use plans.)


Subdivision Staging Policy

The Montgomery County Subdivision Staging Policy is the tool the county uses to regulate subdivision approvals commensurate with the availability of adequate transportation and school facilities. The policy includes an annual test of school adequacy that compares projected school enrollment to school capacity in the 25 MCPS school cluster areas. The school test includes capital projects that will open within the Capital Improvements Program (CIP) timeframe. Elementary, middle, and high school capacities are tested separately. For each school level, the total projected enrollment of all schools in the cluster is compared to total school capacity five years in the future. The Subdivision Staging Policy school test is updated annually, using the latest school enrollment projections and capital projects that are funded and add capacity.

The annual school adequacy test has the following two thresholds: clusters where projected enrollment exceeds capacity and results in school utilizations between 105 and 120 percent require a school facility payment in order to obtain building permits; and clusters where projected enrollment exceeds capacity and results in school utilizations exceeding 120 percent are placed in moratorium and no residential subdivisions may be approved. Because school enrollment growth is strong, many clusters exceed the 105 percent threshold for the school facility payment. Sixteen of the 25 MCPS clusters are in this status for FY 2015. No cluster exceeds the 120 percent threshold for moratorium. Results of the FY 2015 school test are summarized in the table below. More detailed cluster tables showing the FY 2015 school test results may be found in Appendix I. Additional information on the role of MCPS in the Subdivision Staging Policy can be found in Appendix P-1. The FY 2016 school test, that will be adopted July 1, 2015, will incorporate the new enrollment projections found in this document and capital projects that are approved by the County Council in May 2015.

Student Population Trends

Resident births, the aging of the student population, and migration are the basic factors that create enrollment change at MCPS. Regarding births, since 2000 steady increases led to a peak of 13,843 births in 2007. Since 2007, births have decreased each year, with 13,022 births recorded in 2013. The decrease in county births is consistent with state and national trends of declining births over the past several years. This trend is attributed to the Great Recession and its impact on household formation and family planning in difficult economic times. The trend of decreasing births since 2007 will result in a plateauing of elementary enrollment in the next few years. However, in the longer term, births are projected to increase as the economy improves and elementary enrollment is expected to grow again beyond the six-year forecast period. The number of births in 2013 equates to an average of 36 children born per day to Montgomery County mothers. Birth trends have a long-range impact—children born in 2013 will reach elementary school in 2018, middle school in 2024, and high school in 2027.

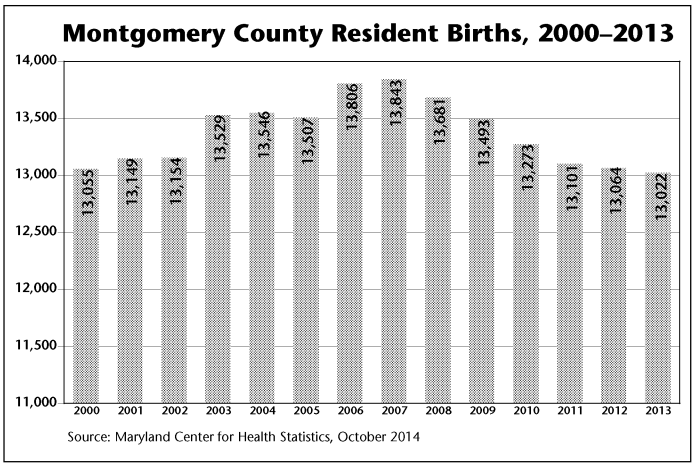

Results of Subdivision Staging Policy School Test for FY 2015

Based on County Council Approved CIP and Cluster Enrollment Forecasts for 2019–2020

See appendix I for more detailed information.

	Cluster Outcomes by Level		
School Test Level	**Elementary Inadequate**	**Middle Inadequate**	**High Inadequate**
Clusters over 105 percent utilization School facility payment required in inadequate clusters to proceed.	Blair Clarksburg Gaithersburg Magruder Northwood Paint Branch Quince Orchard Seneca Valley	Blair Kennedy Northwood Rockville Wheaton Whitman	Clarksburg Einstein Walter Johnson Richard Montgomery Northwest Northwood Quince Orchard Whitman
Clusters over 120 percent utilization Moratorium required in cluster that are inadequate.	None	None	None

Source: Montgomery County Public Schools, Division of Long-range Planning, October 2014

The movement up through the grades by students, termed the "aging of the student population" is the second driver of enrollment change. When the size of the kindergarten is larger than that of Grade 12, then there is a natural increase in total enrollment from one year to the next. During the 2013–2014 school year, there were 11,916 kindergarteners and 10,550 Grade 12 students. The difference between the two grades was 1,366 students. Therefore, in the 2014–2015 school year a large part of the one-year increase in enrollment of 2,941 students was caused by the 1,366 additional students that resulted from the combination of the Grade 12 students aging out of MCPS and the kindergarten class moving into Grade 1. During the next six years the trend of larger kindergarten enrollments and smaller Grade 12 enrollments, will be a major source of enrollment growth in middle schools and high schools.

Migration, the third driver of enrollment change, is driven by the regional economy, housing costs, and international events. All of these factors have a significant degree of volatility and can make movement into and out of MCPS fluctuate from year to year. Records of MCPS student entries and withdrawals show that typically 12,000 to 13,000 new students enter the system each year, while a similar number of students exit the system each year. (These figures do not include students entering kindergarten or students exiting the system at graduation.) In the past five years, entries into MCPS have exceeded withdrawals, resulting in net increases in enrollment.

The impact of the Great Recession on the county housing market made it difficult for residents to sell their homes from 2007 through 2011, thereby reducing household mobility and out migration. In addition, since most areas of the nation continue to have higher unemployment than the Washington region, movement out of the area for job opportunities (labor mobility) has been reduced since the Great Recession. Consequently, more households are "staying put" in the county and fewer MCPS students are moving out to other counties and states. Another contributing factor to enrollment change is the increasing share of county students who are enrolled in public schools. In 2014, 86 percent of students enrolled in Montgomery County schools were enrolled in MCPS, while 14 percent of students were enrolled in county nonpublic schools. This enrollment is up from 82 percent in previous years. Migration—including movement into MCPS from other parts of the world—will continue to be an important driver of enrollment increases throughout the six-year forecast period.


Student Diversity

Records of county resident births show increasing numbers of African American, Asian, and Hispanic births. The share of births to White, non-Hispanic mothers dropped to 36 percent of total county births in 2013. Demographic momentum for further gains in student diversity is building as the median age for the Hispanic, Asian, and African American population is lower than for the White, non-Hispanic population, and household size for these groups exceeds that of White, non-Hispanic households. The growth rate for the Hispanic population exceeds all other groups.


MCPS enrollment for the 2014–2015 school year is 153,852 students. Disaggregation of enrollment by race and ethnic groups reveals the importance of diversity to enrollment growth. In the 10-year period beginning in 2004, MCPS enrollment grew by 14,515 students, an 11 percent increase over the 2004 enrollment of 139,337 students. Over this period, White, non-Hispanic enrollment declined by 12,702 students. The entire enrollment increase, since 2004, is attributed to increases in African American (+1,585) students, Asian (+1,714) students, and Hispanic (+16,750) students. In addition, 7,202 students were recorded this year in the new category of "two or more races." MCPS enrollment is now 21.5 percent African American, 14.2 percent Asian, 28.4 percent Hispanic, 31.0 percent White, non-Hispanic, less than 5 percent two or more races; less than 5 percent Native Hawaiian/Pacific Islander; and less than 5 percent American Indian/Alaskan Native. The accompanying chart illustrates the trend of increasing student diversity since 1970. This chart shows a virtual wave of demographic change from a school system that was 92 percent White, non-Hispanic in 1970 to a school system where there is no longer a majority race/ethnic group. Only the four major race/ethnic groups are shown in this graph for the purpose of presenting long-term trends.


Also shown on accompanying charts are enrollments in the four major race and ethnic groups from 2004 to 2014. These charts show how the greatest amount of enrollment change has been in White, non-Hispanic and Hispanic enrollment. The trend lines for these


MCPS Enrollment by Major Race/Ethnic Groups

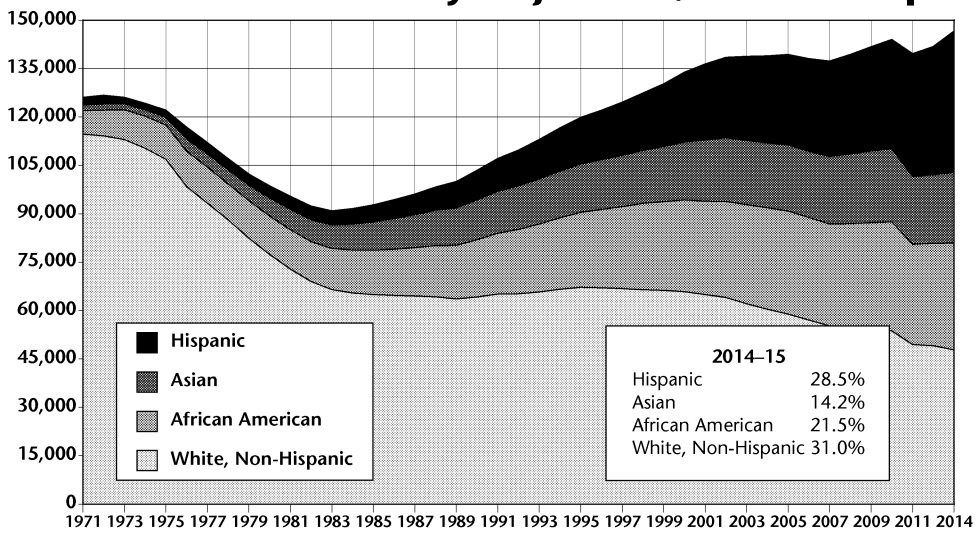

Source: Montgomery County Public Schools, Policy, Records and Reporting, October 2014

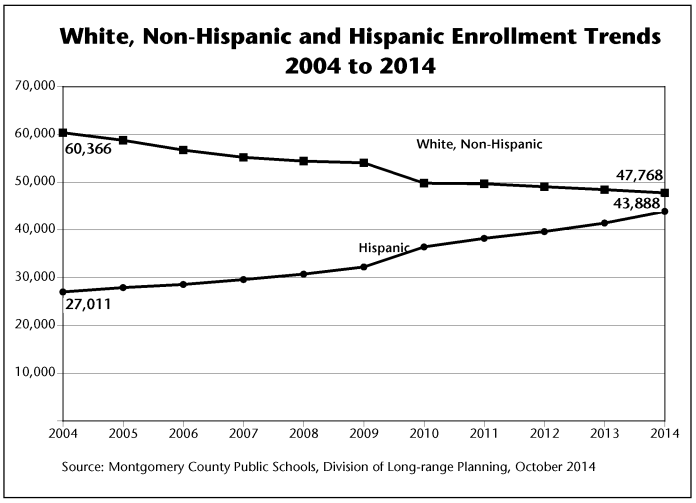

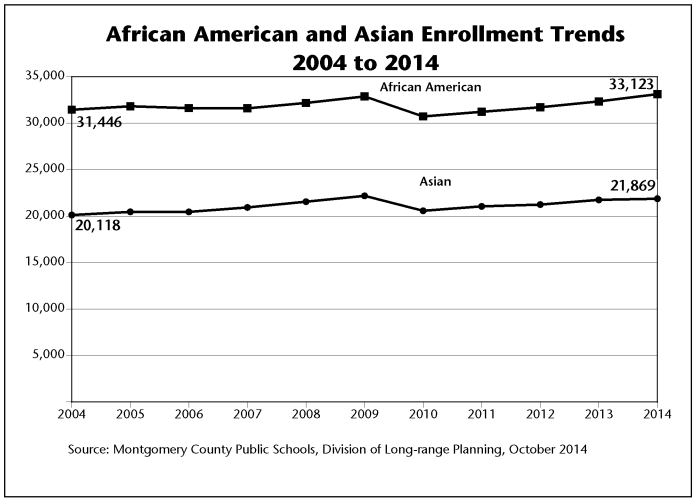

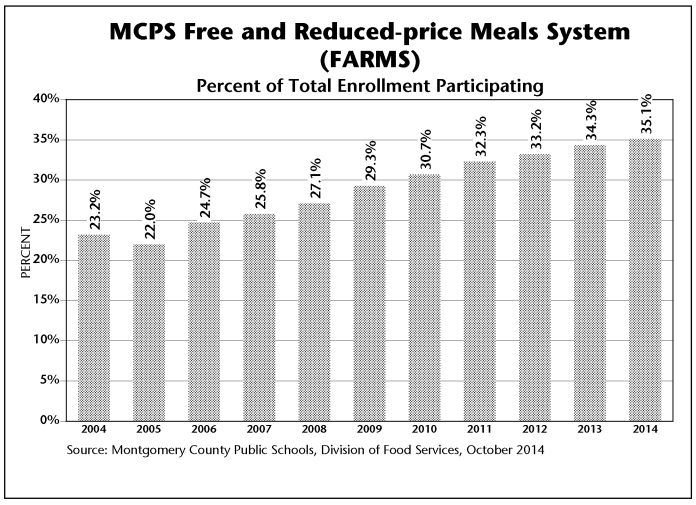



two groups are converging. In the case of Asian and African American enrollment, the increases have been more gradual and the trend lines are running in parallel. Not shown in the charts is enrollment in the "two or more races" category since this category was just established in 2010. However, it can be seen in the accompanying charts how the addition of this new category resulted in a dip in enrollment between 2009 and 2010 in White, non-Hispanic, African American, and Asian students as some members of these groups began to identify with the "two or more races" category. (See Appendices A-3 and A-4 for trends in enrollment by race and ethnic group.)


Enrollment increases in MCPS special programs that serve the diverse student body occurred at higher rates than the total enrollment increases. Student participation in the federal Free and Reduced-price Meals System (FARMS) Program is the school system's best measure of student socioeconomic levels. In 2000, 29,196 students (21.7 percent of enrollment) participated in the program. By 2014, 54,099 students (35.1 percent of enrollment) participated in the program, an increase of 24,903 students. Student enrollment in the English for Speakers of Other Languages (ESOL) Program is a measure of student ethnic and language diversity. In 2000, 10,194 students (7.6 percent of total enrollment) were in this program. By 2014, 21,463 students (14 percent of total enrollment) were in this program, an increase of 11,269 students. In 2014, ESOL students represented 158 countries of origin and spoke 127 different languages. As immigration to the United States has been underway for many years, the share of ESOL students born in the United States has been increasing. These students made up 70 percent of ESOL enrollment in 2014.

Focus and Non-focus Elementary Schools

The greatest concentration of student race and ethnic diversity and participation in the FARMS and ESOL programs is found in areas of the county where two conditions exist—major transportation corridors are present and affordable housing is available. In Silver Spring and Wheaton, these conditions are found in communities bordering New Hampshire Avenue, Georgia Avenue, and Columbia Pike. In Rockville, Gaithersburg, and Germantown, these conditions are found in communities bordering I-270 and Route 355. Affordable communities along these transportation corridors are characterized by apartment communities dating from the 1980s and earlier and neighborhoods with relatively modest townhouses and single-family detached homes. Some of these homes are rented and may be occupied by two or more families who share housing costs. Schools in these areas have reduced class-sizes in Grades K–2 in order to address student needs and prepare the students for success in later grade levels.

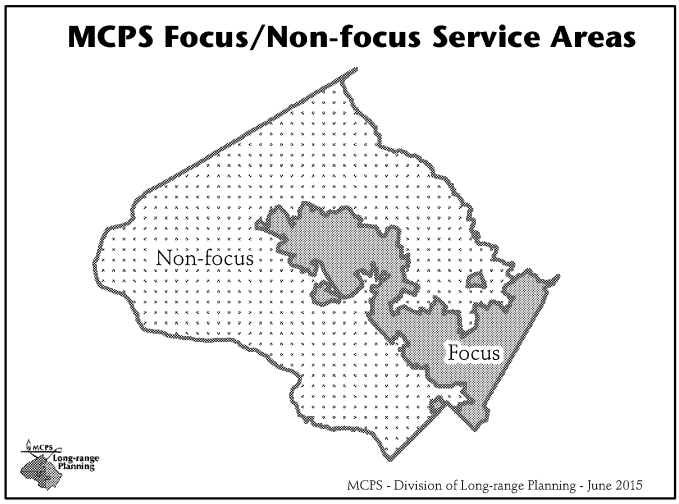

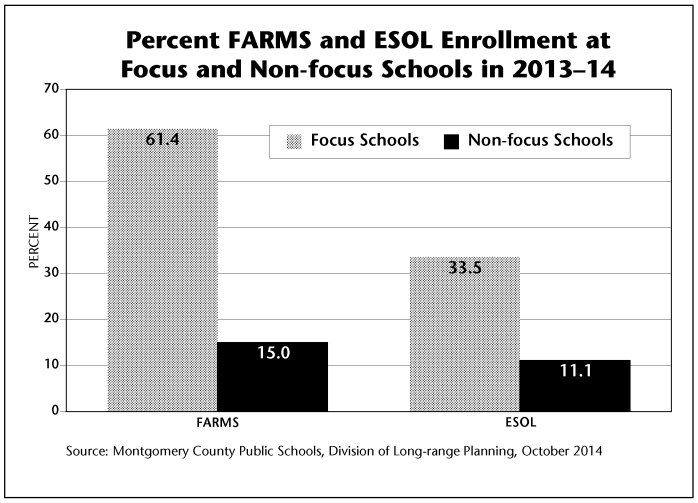

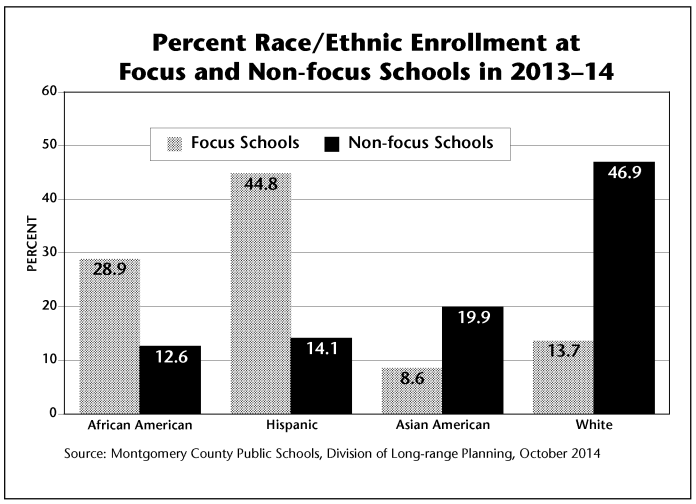

At one time, communities in the "focus" elementary school service areas had little race and ethnic diversity. The wave of immigration over the past three decades has transformed these communities. In these focus school communities, enrollment growth has been driven by turnover of existing housing units. There are currently 67 elementary schools in the focus school group (including the upper schools in the case of paired schools) and 66 elementary schools in the non-focus group. The 2014 demographic composition of focus and non-focus schools is compared in the accompanying charts.


MCPS Enrollment Forecast


The school enrollment forecasts presented in this document are based on county births, aging of the current student population, and migration patterns. As county births increased through 2007, more and more kindergarten students entered MCPS. The advent of full-day kindergarten, countywide since 2006, also has been a major factor in elementary school enrollment increases. Due to the decrease in births from 2007 to 2013, elementary enrollment growth will plateau in the next few years. However, due to the large elementary enrollment increases in the past seven years, MCPS will enter a strong period of growth at secondary schools.

The six-year forecast for Grades K–5 enrollment shows an increase of 136 students from the 2014 enrollment of 71,082 students to the projected 2020 enrollment of 71,218 students. The six-year forecast for Grades 6–8 enrollment shows an increase of 4,799 students from the 2014 enrollment of 33,430 students to the projected 2020 enrollment of 38,229 students. The six-year forecast for Grades 9–12 enrollment shows an increase of 6,001 students from the 2014 enrollment of 45,594 students to the projected 2020 enrollment of 51,595 students. The six-year forecast for total MCPS enrollment shows an increase of 11,526 students from the 2014 enrollment of 153,852 students to the projected 2020 enrollment of 165,378 students. (See appendices A and B for further details on enrollments by grade level and program and Appendix P-2 for a description of the MCPS enrollment forecasting methodology.)

Summary

The last major period of enrollment increases at MCPS occurred during the 1950s, 1960s, and early 1970s, when children from the Baby Boom era, born between 1946 and 1964, enrolled in schools. Enrollment from this wave of births peaked in 1972 at 126,912 students. Thereafter, the so-called Baby Bust era saw births decline and MCPS enrollment decrease to a low of 91,030 students in 1983. Since 1983, a much greater "baby boom" has occurred in the county. During the official Baby Boom years,

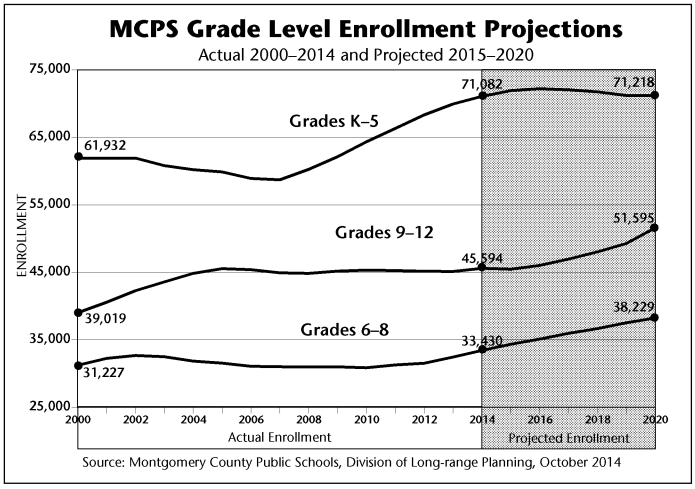

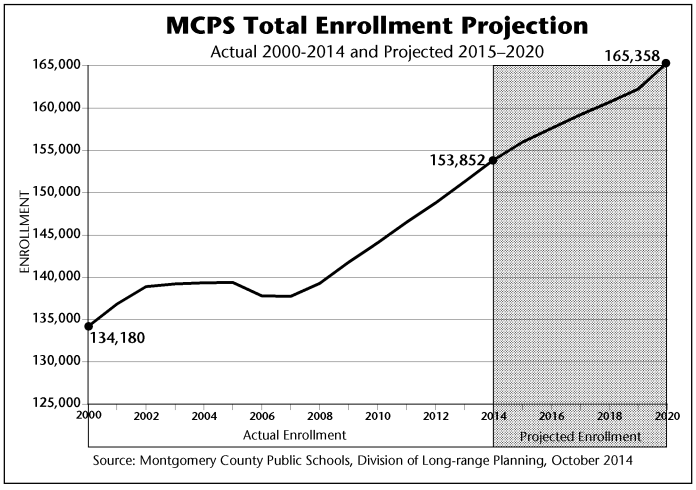

the highest birth year in Montgomery County was 1963 when there were 8,461 resident births. The current baby boom in the county significantly surpasses this figure with births above 13,000 in recent years. Contributing to enrollment increases is the movement of households into the county from other parts of the world and the reduction in out migration of households in more recent years.

The current era of enrollment increases has already seen enrollment grow by 62,822 students since 1983. Keeping pace with enrollment growth, implementing full-day kindergarten at all elementary schools, and accommodating class-size reductions at focus elementary schools have required a major investment in school facilities.

In the 2014–2015 school year, MCPS operates 133 elementary schools, 38 middle schools, 25 high schools, 1 career and technology high school, and 5 special program centers, for a total of 202 facilities. Since 1983, MCPS has opened 34 elementary schools, 17 middle schools, and 6 high schools (including 13 closed schools that were reopened). During the next six years, additional school capacity will be added through new school openings, revitalization/expansion projects, and classroom additions.

Competing with the need for school capacity is the need to preserve our investment in school facilities through a systematic schedule of school revitalization/expansion projects. Since 1983, 66 elementary schools, 13 middle schools, and 13 high schools have been revitalized/expanded. The funding level for school revitalization/expansion projects limits the school system's ability to keep all schools in good condition. Consequently, the school system places a great emphasis on countywide projects to regularly upgrade building systems in aging facilities. Funding for such capital projects as Heating Ventilation and Air Conditioning (HVAC) and Planned Life-cycle Asset Replacement (PLAR) is important to extending the life-cycle of our schools and keeping all schools in good condition. The facility plans and capital projects described in this document enable the school system to add school capacity, systematically revitalize/expand older schools, and maintain all schools in good condition.

Chapter 3

Facility Planning Objectives

The *Approved FY 2016 Capital Budget and Amendments to the FY 2015–2020 Capital Improvements Program (CIP)* are closely aligned with the school system strategic planning framework—*Building Our Future Together*. The Framework is built around three competencies—Academic Excellence, Creative Problem Solving, and Social Emotional Learning. These competencies are what MCPS students will need to compete and thrive in the 21st century. The foundation for the strategic planning framework focuses on organizational effectiveness which states that MCPS will:

- Engage collaboratively and respectfully with all partners, building a self-renewing learning community that reflects our values
- Provide the highest quality business operations and support services that are essential to the educational success of all students
- Organize and optimize resources, including effective use of technology and sustainable practices
- Establish strategic processes for operational excellence, customer service, and shared accountability that support teaching and learning
- Hire for excellence and build capacity of all staff
- Promote effective two-way communication

In addition to the strategic planning framework, Board of Education Policy FAA, *Long-range Educational Facilities Planning* and MCPS Regulation FAA-RA *Long-range Educational Facilities Planning* and the Capital Improvement Priorities, listed below, guide the development of the CIP.

Capital Improvement Priorities

1. Compliance Projects
2. Capital Maintenance Projects
3. Capacity Projects
4. Revitalization/Expansion Projects
5. System Infrastructure Projects
6. Technology Modernization Project

Setting priorities is important in times of fiscal constraints. The CIP includes funding for capital projects in all priority areas and represents a balanced approach to address the many needs of the school system. A brief description of the type of projects that are included in each priority area follows:

- Priority #1—Compliance Projects. This includes funding to address mandates, including American with Disabilities Act (ADA), asbestos abatement, fire safety upgrades, storm water discharge, water quality management, and Washington Suburban Sanitary Commission (WSSC) requirements. These projects must be completed in a timely fashion to be in compliance with laws and regulations.
- Priority #2—Capital Maintenance. This includes funding countywide projects that maintain school facilities in good condition so that they are safe, secure, and comfortable learning environments. In addition, capital projects in this area preserve school assets and can avert more costly repairs or replacements in the future.
- Priority #3—Capacity Projects. This includes funding for new schools and additions so facilities can operate within capacity.
- Priority #4—Revitalization/Expansion Projects. Funding in this area is important to preserve aging facilities and bring schools up to current educational program and building standards.
- Priority #5—System Infrastructure. Funding in this area provides for facilities important to the operation of schools, including transportation depots, maintenance depots, our warehouse, and the upgrading of food services equipment.
- Priority #6—Technology Modernization. Funding in this area enables computers and technology to be upgraded periodically so that student learning is supported by up-to-date technologies.

Long-range Educational Facilities Planning Policy Guidance

On June 17, 2014, the Board of Education adopted a revision to Policy FAA, *Long-range Educational Facilities Planning,* to align Policy FAA with the recent update of Policy ABA, *Community Involvement*. This update was part of an initiative to align all Board policies that have a community involvement component with Policy ABA.

Policy FAA requires that the superintendent of schools include in the CIP recommendations, each fall, a review of certain guidelines involved in facility planning activities. The four guidelines include: preferred range of enrollment, school capacity calculations, desired facility utilization levels, and school site size. Including the guidelines as part of the superintendent's CIP recommendations allows the community an opportunity to provide testimony to the Board of Education on the guidelines and any proposed changes to the guidelines.

On October 15, 2014, the superintendent of schools released Supplement A—Superintendent's Proposed Changes to Regulation FAA-RA, Long-range Educational Facilities Planning. The supplement included several proposed changes to Regulation FAA-RA. One of the proposed changes included an alignment of the community involvement processes described in Regulation FAA-RA with Policy ABA, *Community Involvement*. In addition, since Regulation FAA-RA was issued, roundtable discussion groups have become an important format for community involvement on a variety of facility-related issues.

Therefore, a section on the process to conduct roundtable discussion groups was proposed. Changes to reflect the process for school site selection also were proposed for Regulation FAA-RA. A revised site selection process was developed by a joint working group of Montgomery County Public Schools (MCPS) staff and staff of the Montgomery County departments of Planning and Parks, as well as other county agencies and County Council staff. Important changes to the site selection process include:

- The inclusion of homeowner association representatives from areas surrounding candidate sites on site selection committees;
- Opportunities for the public to comment on school sites recommended by site selection advisory committees; and
- Advisory committee-recommended sites receive review and comment by the Montgomery County Planning Board through the mandatory referral process.

The superintendent of schools also proposed changes to the preferred range of enrollment, school capacity calculations, and school site size. The revised preferred range of enrollment, school capacity calculations, and school site size included in regulation are listed below. See Appendix T for Policy FAA and Regulation FAA-RA.

Preferred Range of Enrollment

The preferred range of enrollment for schools includes all students attending a school. The preferred ranges of enrollment for schools are:

- 450 to 750 students in elementary schools
- 750 to 1,200 students in middle schools
- 1,600 to 2,400 students in high schools
- Enrollment in special and alternative program centers may differ from the above ranges and generally is lower.

The preferred range of enrollment is considered when planning new schools or when changes are made to existing schools. Departures from the preferred ranges may occur if circumstances warrant.

School Capacity Calculations

Unless otherwise specified by Board action, the program capacity of a facility is determined by the space requirements of the educational programs in the facility and student-to-classroom ratios. These ratios should not be confused with staffing ratios that are determined through the annual operating budget process. Program capacity is based on the current ratios shown below:

Head Start and prekindergarten—2 sessions	40:1
Head Start and prekindergarten—1 session	20:1
Grade K—full-day	22:1
Grade K—reduced class size	18:1
Grades 1–2—reduced class size	18:1
Grades 1–5/6 Elementary	23:1
Grades 6–8 Middle	25:1[a]
Grades 9–12 High	25:1[b]
Special Education, ESOL, Alternative Programs[c]	

[a] Program capacity is adjusted at the middle school level to account for scheduling constraints. The regular classroom capacity of 25 is multiplied by .85 to reflect the optimal utilization of a middle school facility (equivalent to 21.25 students per classroom).

[b] Program capacity is adjusted at the high school level to account for scheduling constraints. The regular classroom capacity of 25 is multiplied by .9 to reflect the optimal utilization of a high school facility (equivalent to 22.5 students per classroom).

[c] Special Education, ESOL, alternative programs, and other special programs may require classroom ratios different from those listed.

School Facility Utilization

Unless otherwise specified by Board action, elementary, middle, and high schools should operate in an efficient facility utilization range of 80 to 100 percent of program capacity. If a school is projected to be underutilized (less than 80 percent) or overutilized (over 100 percent), then a boundary study, non-capital action, or a capital project may be considered. Whether a school meets the preferred range of enrollment also is considered. In the case of overutilization, an effort to judge the long-term need for permanent space is made prior to planning for new construction. Underutilization of facilities also is evaluated in the context of long-term enrollment forecasts.

School Site Size

School Site Size is the minimum acreage desired to accommodate the full instructional program, as follows:

- Elementary schools—a minimum useable site size of 7.5 acres that is capable of fitting the instructional program, including site requirements. The 7.5 acres is based on an ideal leveled site, and the size may vary depending on site shapes and surrounding site constraints.
- Middle schools—a minimum useable site size of 15.5 acres that is capable of fitting the instructional program, including site requirements. The 15.5 acres is based on an ideal leveled site, and the size may vary depending on site shapes and surrounding site constraints.
- High schools—a minimum useable site size of 35 acres that is capable of fitting the instructional program, including site requirements. The 35 acres is based on an ideal leveled site, and the size may vary depending on site shapes and surrounding site constraints.

Facility Planning Objectives

Adequate and up-to-date school facilities form the physical infrastructure needed to pursue MCPS goals and priorities. Long-range facility plans, as reflected in this CIP, provide justification for the programming and construction of new school facilities and revitalization/expansion projects. Facility planning and capital programming activities are closely coordinated with educational program delivery approaches. In addition, an emphasis is placed on the inclusion of stakeholders in facility planning processes.

Six objectives guide the facilities planning process and development of each CIP. These objectives are outlined below, with the remainder of this chapter dedicated to providing information on planning within each objective. The CIP also incorporates plans to implement the State of Maryland Bridge to Excellence Master Plan requirement to identify programs

that allow all eligible children admittance, free of charge, to publicly-funded prekindergarten programs.

OBJECTIVE 1: Implement facility plans that support the continuous improvement of educational programs in the school system

OBJECTIVE 2: Meet long-term and interim space needs

OBJECTIVE 3: Sustain and Revitalize Facilities

OBJECTIVE 4: Provide schools that are environmentally safe, secure, functionally efficient, and comfortable

OBJECTIVE 5: Support multipurpose use of schools

OBJECTIVE 6: Meet space needs of special education programs

2014–2015 Class Size Reduction Schools

Arcola	S. Christa McAuliffe
Lucy V. Barnsley	Meadow Hall
***Bel Pre**/Strathmore	Mill Creek Towne
Brookhaven	*Montgomery Knolls/
Brown Station	Pine Crest
Burnt Mills	***New Hampshire**
Burtonsville	**Estates/Oak View**
Cannon Road	***Roscoe Nix/**
Clopper Mill	**Cresthaven**
Capt. James E. Daly	Oakland Terrace
Dr. Charles R. Drew	William T. Page
East Silver Spring	Judith A. Resnik
Fairland	Sally K. Ride
Fields Road	Rock Creek Forest
Flower Hill	Rock Creek Valley
Fox Chapel	Rock View
Forest Knolls	**Rolling Terrace**
Gaithersburg	Rosemont
Galway	Sequoyah
Georgian Forest	**Sargent Shriver**
Glen Haven	Flora M. Singer
Glenallan	**South Lake**
Goshen	Stedwick
Greencastle	Strawberry Knoll
Harmony Hills	**Summit Hall**
Highland	*Takoma Park/Piney Branch
Highland View	Twinbrook
Jackson Road	**Viers Mill**
Kemp Mill	**Washington Grove**
Lake Seneca	Waters Landing
Jody Leleck at Broad Acres	**Watkins Mill**
	Weller Road
Maryvale	**Wheaton Woods**
	Whetstone

Schools receive staffing to reduce class sizes in Grades K–2.
*These schools are paired, Grades K–2/3–5.
Schools in bold are Title I schools in the 2014–2015 school year.

OBJECTIVE 1: Implement Facility Plans that Support the Continuous Improvement of Educational Programs in the School System

As the school system continues to focus program initiatives to improve student performance, facility plans are developed to address the space needs and facility requirements of schools. Implementing school system educational priorities that require more classroom and support space continues to be a challenge, particularly over the past 30 years of steady enrollment growth. With student enrollment increasing rapidly at the secondary schools, the school system will continue to be challenged to provide adequate capacity.

In recent years, several educational program initiatives required more classroom and support space. These initiatives include the reduction in class sizes in Grades K–2 for the 63 schools most heavily affected by poverty and English language deficiency (called "focus schools") and the expansion of full-day kindergarten to all elementary schools in MCPS. Creative uses of existing space in schools, modifications to existing classrooms, and placement of relocatable classrooms are all used to accommodate the additional staff needed to implement these initiatives. At schools with capital improvements in the facility planning or architectural planning phase, additional classrooms are provided to accommodate these initiatives. These initiatives are described in further detail in the following paragraphs.

Class Size Reductions

In the 2000–2001 school year, the Board of Education began a three-year initiative to reduce class size in the primary grades as a key component of the Early Success Performance Plan. Over a three-year period, class size in Grades K–2 in the focus schools most heavily impacted by poverty and language deficiency were reduced for the full instructional day to an average of 17 students per teacher in Grades 1–2 and 15 students per teacher in full-day kindergarten. (See chart on page 3-3.) Reducing class sizes in Grades K–2 had a dramatic impact on utilization levels in elementary schools, creating the need for additional classrooms to accommodate the increased number of teaching positions. Beginning in FY 2012, the staffing guidelines for the focus schools increased to an average of 18 students per teacher in Grades K–2. Beginning in FY 2015, Fields Road Elementary School became a focus school and received staffing to reduce class sizes in Grades K–2. Beginning in FY 2015, Great Seneca Creek Elementary School will become a focus school and receive staffing to reduce class sizes in Grades K–2.

Head Start and Prekindergarten Programs

The Bridge to Excellence in Public Schools Act of 2002 requires that all eligible children "shall be admitted free of charge to publicly funded prekindergarten programs" established by the Board of Education. These programs are located yearly, based on need in the community and transportation travel times. The locations are shown in Appendix H.

Signature and Academy Programs

Most high schools have developed and implemented signature and/or academy programs. Some of these programs are whole school programs, while others are structured as a special program offering at the school. Signature and academy programs have been developed to raise student achievement by matching programs with student interests. Some signature programs require specialized classrooms or laboratories to support the delivery of the educational program. As high schools are revitalized, specialized spaces for the signature programs are designed as part of the revitalization/expansion project. However, some high schools do not have revitalization/expansion projects scheduled in the next six years and may require facility modifications to accommodate signature or academy programs. Minor modifications that are needed to individual classrooms are completed through countywide capital projects.

Information Technologies

MCPS has a strong commitment to prepare today's students for life in the 21st century and to ensure a technologically literate citizenry and an internationally competitive work force. Board of Education Policy IGS, *Educational Technology* strives to ensure that educational technology is appropriately and equitably integrated into instruction and management to increase student learning, enhance the teaching process, and improve the operation of the school system.

The Technology Modernization Project provides the needed technology updates and computers in every school. Funds included in this project update schools' technology hardware, software, and network infrastructure. Up-to-date technology enhance student learning through access to online information and through the ability to use the latest instructional software. MCPS is planning a multiyear effort to provide all students with access to mobile computers and a cloud-based learning platform that will enhance creativity and collaboration in the classroom. These technologies also are critical for implementing online testing strategies.

OBJECTIVE 2: Meet Long-term and Interim Space Needs

Montgomery County has demonstrated a strong commitment to providing sufficient school facilities. Funding capital improvements has been a challenge since 1983 when enrollment began to rise sharply. MCPS enrollment is now 63,200 students greater than it was in 1983, and 34 elementary schools, 17 middle schools, and 6 high schools have been. Numerous additions to existing schools also have been constructed to accommodate the growth in enrollment. This year, MCPS is operating a total of 202 school facilities, including: 133 elementary schools, 38 middle schools, and 25 high schools; 1 career and technology center; and 5 special education program centers.


Long-term Space Needs

A continued commitment to capital projects for the next six years is necessary to address overdue space needs and keep up with rising enrollment. This year's official school enrollment is 154,230 students. Enrollment is projected to be 165,358 students by 2020. The CIP identifies where space deficits are projected to occur and how the school system plans to address them. Due to the high level of school utilization throughout the school system, there are very few opportunities to address school space shortages through boundary changes among existing schools. Therefore, additions to existing schools, the opening of new schools, and the revitalization/expansion projects at schools are all important strategies to address space needs. For a summary of approved capital projects, please see the table in Chapter 1, labeled "County Council Adopted FY 2016 Capital Budget and Amendments to the FY 2015–2020 Capital Improvements Program Summary Table" (page 1–6).

To develop long-term space plans for schools, school planners annually review the space available at schools by comparing the enrollment projections with program capacity in the sixth year of the CIP planning period. When the enrollment exceeds the program capacity of a school planners may consider several strategies to address the overutilization of a school. These strategies range as follow:

- Determine if space is available at adjacent or nearby schools and reassign students to a school(s) with space available;
- Consider an addition at the school to accommodate the enrollment if possible. If the school cannot be expanded to accommodate the projected enrollment, additions could be considered at nearby schools and students reassigned to these schools; For a classroom addition to be considered for funding at an individual school the following thresholds need to be met:

New and Reopened Schools by Type 1985 to 2014
34 Elementary, 17 Middle, and 6 High Schools

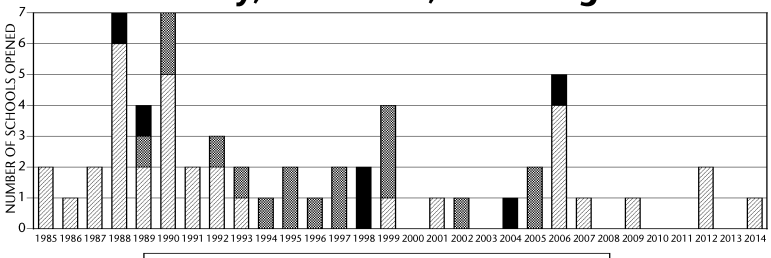

1985 — Flower Hill ES, Lake Seneca ES
1986 — Clopper Mill ES
1987 — Jones Lane ES, S. Christa McAuliffe ES
1988 — Goshen ES, Greencastle ES, Clearspring ES, Stone Mill ES, Strawberry Knoll ES, Waters Landing ES, Quince Orchard HS
1989 — Cloverly ES, Daly ES, Cabin John MS, Watkins Mill HS
1990 — Brooke Grove ES, Burnt Mills ES, Rachel Carson ES, Ronald McNair ES, Sequoyah ES, Briggs Chaney MS, Francis Scott Key MS
1991 — Dr. Charles R. Drew ES, Judith A. Resnik ES
1992 — Dr. Sally K. Ride ES, Lois P. Rockwell ES, Rosa M. Parks MS
1993 — Thurgood Marshall ES, Argyle MS
1994 — Roberto Clemente MS
1995 — Forest Oak MS, Rocky Hill MS
1996 — Neelsville MS
1997 — Kingsview MS, John Poole MS
1998 — James Hubert Blake HS, Northwest HS
1999 — Sligo Creek ES, North Bethesda MS, Shady Grove MS, Silver Spring International MS
2000 — None
2001 — Spark M. Matsunaga ES
2002 — Newport Mill MS
2003 — None
2004 — Northwood HS
2005 — Lakelands Park MS, A. Mario Loiderman MS
2006 — Great Seneca Creek ES, Little Bennett ES Roscoe R. Nix ES, Sargent Shriver ES, Clarksburg HS
2007 — Arcola ES
2008 — None
2009 — William B. Gibbs, Jr. ES
2010 — None
2011 — None
2012 — Flora M. Singer ES, Montessori Charter ES
2013 — None
2014 — Wilson Wims ES

Source: Montgomery County Public Schools, Division of Long-range Planning October 2014.

- Elementary school—the enrollment needs to exceed capacity by four classrooms or more (a minimum of 92 seats) in the sixth year of the CIP period
- Middle school—enrollment needs to exceed capacity by six classrooms or more (a minimum of 150 seats) in the sixth year of the CIP period
- High school by—enrollment needs to exceed capacity by eight classrooms or more (a minimum of 200 seats) in the sixth year of the CIP period

- Consider the opening of a new school if reassignments and increasing capacity of existing schools is not sufficient to address the projected enrollment. Expanding schools to their maximum core capacity is considered before the opening of a new school. A new elementary school may be considered if the clusterwide deficit of space exceeds 500–600 seats. Deficits close to the size of a new secondary school would support a new middle or high school.

School planners also review the impact of school utilization on the county Subdivision Staging Policy. When possible, school facility plans attempt to keep clusters from being placed in a housing moratorium.

To address growing enrollment in the county, funding is approved in the Amendmed to the FY 2015–2020 CIP for four new schools that are listed below:

- Clarksburg/Damascus Middle School (opens August 2016)
- Bethesda-Chevy Chase Middle School #2 (opens August 2018)
- Richard Montgomery Cluster #5 (opens August 2018)
- Northwest Elementary School #8 (opens August 2018)

In addition to new school openings, classroom addition projects are planned to address overutilization at schools. Six classroom addition projects were approved as part of the Amended FY 2013–2018 CIP for completion in the next six years. Planning and/or construction funds were approved for 16 new addition projects as part of the FY 2015–2020 CIP. These schools are listed on the table to the right, along with the number of rooms in the additions, and the completion dates. Prior to requesting funding for a classroom addition project, facility planning funds are requested to conduct a feasibility study to determine the feasibility, scope, and cost of a classroom addition. An FY 2014 appropriation was approved for facility planning funds for the following schools:


- Broad Acres Elementary School
- Burning Tree Elementary School
- Lake Seneca Elementary School
- South Lake Elementary School
- A. Mario Loiederman Middle School
- Walt Whitman High School

An FY 2015 appropriation for facility planning funds was approved to conduct feasibility studies for the following schools:

- Col. E. Brooke Lee Middle School
- Neelsville Middle School
- Parkland Middle School
- Silver Spring International Middle School
- Takoma Park Middle School
- Walter Johnson High School

An FY 2016 appropriation for facility planning funds is approved to conduct feasibility studies for the following schools:

- Fields Road Elementary School
- Thomas W. Pyle Middle School
- Richard Montgomery High School

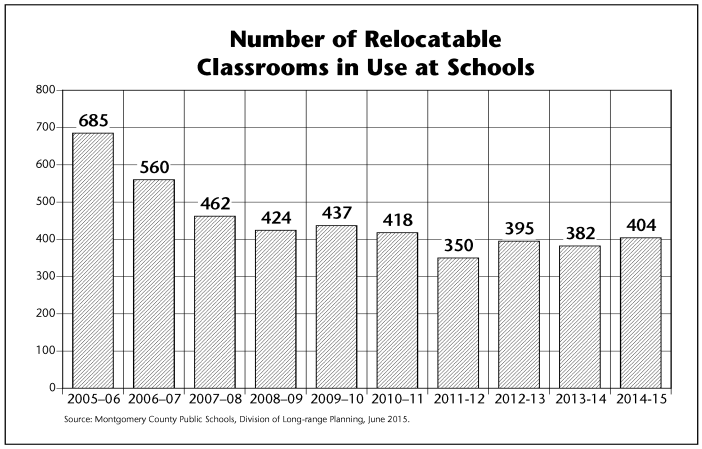

Number of Additional Rooms Planned—Addition Projects

School	Number of Rooms Planned*	Completion Date
Clarksburg HS	18	8/15
Arcola ES	6	8/15
Bethesda ES	8	8/15
North Chevy Chase ES	6	8/15
Rosemary Hills ES	7	8/15
Julius West MS	18	8/16
Wood Acres ES	8	8/16
Bethesda-Chevy Chase HS	33	8/18
North Bethesda MS	17	8/18
Lucy V. Barnsley ES	11	8/18
Diamond ES	7	8/18
Kensington-Parkwood ES	14	8/19
Brookhaven ES	8	8/19
Glen Haven ES	4	8/19
Highland ES	7	8/19
Kemp Mill ES	10	8/19
Sargent Shriver ES	3	8/19
Ashburton ES	14	8/20
Burtonsville ES	9	8/20
S. Christa McAuliffe ES	12	8/20
Judith A. Resnik ES	9	8/20

*The number of rooms includes classrooms that are being added with new construction. These rooms include teaching stations that are counted in capacity as well as teaching stations in the elementary school that are not counted in the capacity—art, music, dual purpose room, and the computer laboratory.

Two comprehensive capacity studies were approved in the Downcounty Consortium and Gaithersburg Cluster to address the overutilization of elementary schools. A comprehensive capacity study was approved for the lower portion of the Downcounty Consortium to address enrollment growth in this area. The comprehensive capacity study for this area was conducted during the 2014–2015 school year and included the following 12 schools: East Silver Spring, Forest Knolls, Highland View, Montgomery Knolls, New Hampshire Estates, Oak View, Pine Crest, Piney Branch, Rolling Terrace, Sligo Creek, and Woodlin elementary schools. A comprehensive capacity study for the Gaithersburg Cluster was approved to address enrollment growth in this cluster. The comprehensive capacity study was conducted during the 2014–2015 school year. This capacity study included all seven of the elementary schools in the cluster.

To address growing enrollment in the Downcounty Consortium high schools, an FY 2016 appropriation for facility planning is approved to conduct a comprehensive capacity study for the Downcounty Consortium high schools. The study will explore the possibility of adding capacity to the Downcounty Consortium through classroom additions at Montgomery Blair, Albert Einstein, John F. Kennedy, and/or Northwood high schools. As part of the revitalization/expansion project at Wheaton High School, the building shell of the master-planned addition will be constructed as part of the ongoing project. Constructing the building shell during ongoing construction will enable classrooms to be built-out in the future when enrollment pressures require additional capacity.

Many schools that are scheduled for revitalization/expansion projects also have increases in capacity as part of the project to accommodate growing enrollment. The table to the right lists the schools that will have revitalization/expansion projects completed in the six-year CIP period and the number of rooms being added as part of the revitalization/expansion projects.

on site at schools, or relocatables located at holding facilities and other facilities throughout the school system.

With the implementation of wireless technology and mobile devices at all schools, the need for computers laboratories has decreased. At some schools with space needs, the school system will be converting computer laboratories to standard classrooms to deliver the educational programs beginning in the 2015–2016 school year.

School	Number of Rooms Planned*	Completion Date
Candlewood ES	6	1/15
Rock Creek Forest ES	16	1/15
Wheaton HS	15	1/16
Brown Station ES	11	8/17
Wheaton Woods ES	17	8/17
Seneca Valley HS	32	8/19
Luxmanor ES	10	1/20
Maryvale ES	7	1/20
Potomac ES	6	1/20
Tilden MS	11	8/20
Wootton HS	12	8/21
DuFief ES	8	8/21
Stonegate ES	8	8/21


Non-Capital Actions

A boundary study was conducted in spring 2015 to determine the service area for Clarksburg/Damascus Middle School. Representatives from Montgomery Village, Neelsville, and Rocky Hill middle schools participated in the boundary advisory study. Board of Education action is scheduled to occur In November 2015. The new middle school opens in August 2016.

Interim Space Needs

The use of relocatable classrooms on a short-term basis has proven to be successful in providing schools the space necessary to deliver educational programs. Relocatable classrooms provide an interim learning environment for students until permanent capacity can be constructed. Relocatable classrooms also enable the school system to avoid significant capital investment where building needs are only short term. The number of relocatable classrooms in use grew dramatically as program initiatives described under Objective 1 were implemented and enrollment increased. The number of relocatable classrooms declined between 2005 and 2008 as enrollment plateaued and capacity projects opened. However, with enrollment increasing again, the number of relocatable classrooms is expected to increase in the future. In the 2014–2015 school year, nearly 9,300 students attended class in 404 relocatable classrooms. This number does not include relocatable classrooms used for daycare, to stage construction

School Revitalized/Expanded by Type, 1985 to 2014
66 Elementary, 3 Middle, and 3 High Schools

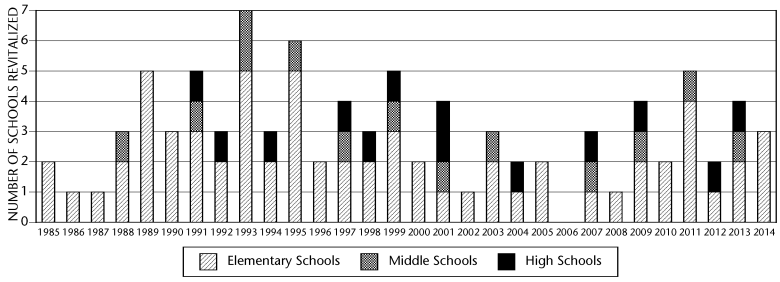

1985 — Oak View ES, Woodfield ES
1986 — Twinbrook ES
1987 — Cedar Grove ES
1988 — Bannockburn ES, Rosemary Hills ES, Gaithersburg MS
1989 — Cloverly ES, Highland ES, Laytonsville ES, Monocacy ES, Montgomery Knolls ES
1990 — Olney ES, Westbrook ES
1991 — Beall ES, Burning Tree ES, Viers Mill ES, Sligo MS, Sherwood HS
1992 — Pine Crest ES, Travilah ES, Walt Whitman HS
1993 — Ashburton ES, Burtonsville ES, Clarksburg ES, Forest Knolls ES, Oakland Terrace ES, Pyle MS, White Oak MS
1994 — Highland View ES, Meadow Hall ES, Springbrook HS
1995 — Brookhaven ES, Georgian Forest ES, Jackson Road ES, North Chevy Chase ES, Rosemont ES, Julius West MS
1996 — Flower Valley ES, Kemp Mill ES
1997 — Ritchie Park ES, Wyngate ES, Westland MS, Albert Einstein HS
1998 — Lucy Barnsley ES, Westover ES, Montgomery Blair HS
1999 — Bethesda ES, Harmony Hills ES, Rock View ES, Takoma Park MS, John F. Kennedy HS
2000 — Mill Creek Towne ES, Chevy Chase ES
2001 — Rock Creek Valley ES, Earle B. Wood MS, Bethesda-Chevy Chase HS
2002 — Wood Acres ES
2003 — Lakewood ES, William Tyler Page ES
2004 — Glen Haven ES, Rockville HS
2005 — Somerset ES, Kensington-Parkwood ES
2006 — None
2007 — College Gardens ES, Parkland MS, Richard Montgomery HS
2008 — Galway ES
2009 — Bells Mill ES, Cashell ES, Francis Scott Key MS, Walter Johnson HS
2010 — Carderock ES, Cresthaven ES
2011 — Cannon Road ES, Farmland ES, Garrett Park ES, Seven Locks ES
2012 — Paint Branch HS and Beverly Farms ES
2013 — Gaithersburg HS, Hoover MS, Glenallan ES, Weller Road ES
2014 — Bel Pre ES, Candlewood ES, Rock Creek Forest ES

Source: Montgomery County Public Schools, Division of Long-range Planning, October 2014

OBJECTIVE 3: Sustaining and Revitalizing Facilities

The Board of Education, superintendent of schools, and school community recognize the necessity to maintain schools in good condition through a range of activities that includes routine daily maintenance to the systematic replacement of building systems. A number of capital projects provide funds for systematic life-cycle asset replacement, including the Roof Replacement Program, the Heating, Ventilation, and Air Conditioning (HVAC) Program, and the Planned Life Cycle Asset Replacement (PLAR) Program. Because schools built or revitalized since 1985 are generally of higher construction quality than schools built prior to 1985, it is possible to extend the useful life through a high level of maintenance and replacement of building systems. In the coming years, more funds will be directed to capital projects that sustain facilities in good condition for longer periods than have been feasible in the past.

The Board of Education, superintendent of schools, and school community also recognize that even well-maintained facilities eventually reach the end of their useful life span and require revitalization. Revitalization/expansion projects update school facilities and provide the variety of instructional spaces necessary to effectively deliver the current curriculum. These projects also bring schools up to current design and code standards. The cost to revitalize/expand an older school so that it is educationally, technologically, and physically up-to-date, is similar to the cost to construct a new school. In most cases, a life cycle cost analysis shows it is more cost effective to replace an older school facility rather than attempt to salvage portions of the old facility.

In recognition of the need to place more emphasis to sustain all schools in good condition, the Board of Education recently updated its policy on school revitalization/expansion projects. The previous policy, called Policy FKB, *Modernization/Renovation*, was adopted in 1992. On December 7, 2010, the Board of Education adopted a new policy, called FKB, *Sustaining and Modernizing Montgomery County Public Schools (MCPS) Facilities*. The policy is found in Appendix V. The updated Policy FKB enacts a long-term view for sustaining MCPS facilities until the point where a full revitalization/expansion project is necessary. The greater emphasis to maintain schools in good condition addresses concerns over the length of time it takes before schools are revitalized/expanded. Although a large number of schools have been revitalized since 1985—*66* elementary schools, 13 middle schools, and 13 high schools—the availability of funds and the limited number of holding centers constrains the pace of revitalization/expansion projects. At the current rate, revitalizations/expansions of elementary schools occur on a 65-year cycle, middle schools occur on a 76-year cycle, and high schools occur on a 50-year cycle. By providing a higher level of maintenance at schools, facilities will be in good condition for a longer period of time.

The original list of schools for revitalization/expansion projects was scheduled using a standardized assessment tool called Facilities Assessment with Criteria and Testing (FACT). Schools beyond a certain age were assessed and scored on a standard set of facility and educational program space criteria. Schools scheduled for revitalization/expansion projects were rank ordered after the assessment. Because the original list of elementary schools in the queue for revitalization/expansion projects is almost complete, it was necessary to prepare for the assessment of additional schools that are aging and in need of revitalization/expansion projects. Therefore, the FACT methodology used to assess schools was updated in the 2010–2011 school year to reflect current educational programs and school design and code standards. The updated FACT methodology describes the following: the criteria used to assess the condition of schools; the measures that define each criterion; and the relative weights applied to the various criteria to obtain an overall score for each facility. The Board of Education adopted the updated FACT methodology on July 8, 2010, and 53 school assessments were completed at the end of June 2011. Appendix F includes the scores and rankings. Schools that have planning or construction funds approved in the six-year CIP period appear in Appendix E with a completion date.

Holding Facility Schedule

Holding Facility	SY 14–15	SY 15–16	SY 16–17	SY 17–18	SY 18–19	SY 19–20	SY 20–21
ELEMENTARY SCHOOLS							
Emory Grove Center	Candlewood		Brown Station				DuFief
Fairland Center							Stonegate
Grosvenor Center			Wayside		Luxmanor		Cold Spring
North Lake Center			Wheaton Woods		Maryvale		Belmont
Radnor Center	Rock Creek Forest	Wood Acres			Potomac		
MIDDLE SCHOOLS							
Tilden Center/ Woodward Center*					*To be revitalized/expanded*		Eastern

** Tilden Middle School is currently located in the Woodward Center. A revitalization/expansion for Tilden Center is scheduled for completion in August 2020 which will house Tilden Middle School. The Woodward Center will then become a secondary holding school facility for school revitalization/expansion projects scheduled after Tilden Middle School.*

OBJECTIVE 4: Provide Schools that Are Environmentally Safe, Secure, Functionally Efficient, and Comfortable

To maintain and extend the useful life of school facilities, MCPS follows a continuum of activities that begins the first day a new school is opened and ends when a school's revitalization/expansion begins. Funding for maintenance activities is found in both the capital and operating budgets. The trend for the past five years has been to provide a level of funding effort in both budgets for building maintenance and systemic renovations. Understanding the full cost of building maintenance is critical to develop a balance between the comprehensive maintenance plan and a revitalization/expansion schedule that reflects the school system's priorities.

MCPS has many projects designed to meet the capital maintenance needs of schools across the county. These countywide projects are described in Chapter 5. Countywide projects work with environmental issues, safety and security, and major building system maintenance in schools. These projects require an assessment of each school relative to the needs of other schools and include scheduled major repairs and replacement activities. The assessment process for most of the countywide projects is carried out through an annual review that involves a team of maintenance professionals, school principals, and consultants. On some projects, local, state, and federal mandates affect the scope and cost of the effort required.

Planned Life-cycle Asset Replacement (PLAR) and other countywide projects that focus on roof and mechanical system rehabilitation are essential to the long-term protection of the county's capital investment in schools. Because the projects to revitalize older schools must compete for funding with projects for building new schools, maintenance and rehabilitation projects for schools and relocatable classrooms take on even greater importance. A list of projects that were completed during summer 2014 can be found in Appendix R.

The Indoor Air Quality (IAQ) Improvements Project funds mechanical retrofits and building modifications to address indoor air quality projects in MCPS schools. An amendment to the FY 2000 Capital Budget created this project and funds improvements, such as major mechanical corrections, carpet removal, floor tile replacement, and minor mechanical retrofits. MCPS staff is required to report periodically to the County Council's Education Committee on the status of this project.

MCPS is committed to sustainability and conservation of resources in the design and operation of all facilities. Several programs exist to support these activities. The School Energy and Recycling Team (SERT) Program promotes efficient and responsible energy use and active recycling in all schools. The SERT Program strives to significantly reduce energy consumption and to increase recycling systemwide by providing training and education; incentives, recognition, and award programs for conservation; accessible energy and recycling data; individual school programs for energy and environmental investigation-based learning opportunities; and conservation operations and procedures. SERT staff works with students, teachers, staff, and the community to practice environmental stewardship and to develop strategies to reduce the carbon footprint of MCPS.

MCPS has implemented measures to reduce the environmental impact of its buildings through a comprehensive revision of its construction design guidelines. This revision incorporates best practices from the widely recognized Leadership in Energy and Environmental Design (LEED) rating system of the United States Green Building Council. Great Seneca Creek Elementary School, which opened in September 2006, was the first public school in Maryland to be "gold" certified under the LEED rating system for green buildings. Beginning in FY 2007, all new schools and revitalization/expansion projects are designed to achieve a LEED for Schools "silver" certification. The following schools have earned LEED for Schools "gold" certification: Cabin John and Francis Scott Key middle schools; and Carderock Springs, Cannon Road, Cashell, Cresthaven, Farmland, William B. Gibbs, Seven Locks, and Flora M. Singer elementary schools. Smaller green technology and conservation pilots have been introduced at several schools to provide a healthy and effective learning environment for students and staff.

The FY 2015–2020 CIP includes funding to implement initiatives in the School Security Program that will enhance the comprehensive security program already in place. The initiative includes: design and installation of Closed Circuit Television (CCTV) camera systems in all middle schools; the replacement of existing outdated analog CCTV camera systems in all high schools; the installation of a visitor management system in all schools; and the installation of a visitor access system at all elementary schools.

OBJECTIVE 5: Support Multipurpose Use of Schools

MCPS recognizes the role schools play as centers of community activity and affiliation. The school system supports multipurpose use of its schools, especially in regard to uses that complement the educational program. Multipurpose uses of schools that promote family and community partnerships also are of great importance. Compatible uses of schools are factored into the facility planning process whenever possible. A prime example of compatible uses in schools is the leasing of available space in elementary schools to childcare providers. Most of the elementary schools in the system provide space for childcare providers through a mixture of full-day centers and before and after school services.

The Montgomery County Department of Health and Human Services (DHHS) Capital Budget includes several projects to provide services in county schools. In the Child Care in Schools Project, DHHS funds the construction of childcare classrooms

in schools undergoing major construction or renovation. MCPS oversees the construction of the childcare classroom while DHHS arranges for the lease of the childcare classroom to a private childcare provider. Funds are included in the DHHS CIP to construct childcare classrooms at Brown Station and Wheaton Woods elementary schools.

Linkages to Learning, a collaborative program between the school system, DHHS, and private community providers, addresses the complex social and mental health needs of an increasingly diverse and economically impacted population in Montgomery County. In order to address possible barriers to learning, a variety of mental health, social, and educational support services are brought together at Linkages to Learning sites. In addition, services are provided at the School Health Services Center at Rocking Horse Road. The long-range plan is to expand the Linkages to Learning programs to additional schools. Funding is included in the DHHS CIP to construct a Linkages to Learning suite at Maryvale and Wheaton Woods elementary schools. Funding was approved in the FY 2015 DHHS Operating Budget to open a Linkages to Learning site at South Lake Elementary School.

Since fall 1997, Linkages to Learning/School-based Health Centers (SBHC) at Broad Acres and Harmony Hills elementary schools have been providing enhanced health resources to students and their families. As part of the Harmony Hills Elementary School revitalization/expansion project in 1999, space was designed to accommodate the Linkages to Learning and the School-based Health Center. In response to the County Council Health and Human Services Committee request for a plan to expand SBHCs to additional school sites, the School-based Health Centers Interagency Planning Group was convened by DHHS. The planning group was an interagency group that developed selection criteria to rank schools and a timeline for constructing new SBHCs at school sites. School-based health centers opened at Gaithersburg Elementary School during the 2005–2006 school year, at Summit Hall Elementary School in August 2008, and at New Hampshire Estates Elementary School in August 2009. Funding was approved in the DHHS Capital Improvements Program to plan and construct additional SBHCs at Rolling Terrace Elementary School in August 2011 and Highland Elementary School in August 2012. Planning and construction funds also were approved to construct a SBHC as part of the Viers Mill Elementary School addition project and the Weller Road Elementary School revitalization/expansion project. Both of these projects opened in August 2013. Funding is included in the DHHS CIP to construct a SBHC at South Lake Elementary School.

In spring 2006, the School-based Wellness Center Planning Group was convened. The planning group was charged with describing the services that would be offered at wellness centers at high schools and to identify criteria and a decision-making process for prioritizing schools sites for wellness centers. As a result of the work of the planning group, Northwood High School was the first school to receive a School-based Wellness Center (SBWC) in August 2007. School-based Wellness Centers opened in August 2013 at Gaithersburg and Watkins Mill high schools. Funding is included in the DHHS CIP to open a School-based Wellness Center in January 2016 at Wheaton High School and at Seneca Valley High School in August 2019. MCPS and DHHS staffs work collaboratively to develop the design for all the DHHS projects.

Kingsview Middle School in Germantown adjoins a county-operated community center. The community center is a 23,000 square foot building that contains a gymnasium, social hall, arts room, game room, and exercise room, as well as administrative offices, common areas, and conference spaces. The center is structurally integrated with the middle school building but has a separate and distinct main entry. An outdoor pool and bathhouse also are located on the site as a separate facility, consisting of the following: 50-meter lap pool, leisure pool, wading pool for toddlers, and common lounging areas. Other opportunities to collocate schools with compatible uses will be pursued in the future as land for new schools sites becomes more limited.

Community use of school facilities is another important way in which schools serve their communities. Outside of the instructional day, schools are used for a wide range of community activities. The Interagency Coordinating Board (ICB) for Community Use of Public Facilities (CUPF) manages school use, collects fees for most community uses of schools, and maintains an Enterprise Fund to pay for the cost of utilizing schools after school hours. Among the largest users of schools are childcare providers, county recreation groups, sports groups, and religious groups.

MCPS will participate in an interagency study that will inventory county land that is available for public facilities and identify opportunities for collocation of compatible types of facilities. This study, known as the "Future Public Facilities Infrastructure Study" comes at a time when land to site public facilities is becoming scarcer, and more efficient use of sites is necessary.

OBJECTIVE 6: Meet Special Education Program Space Needs

The Maryland State Department of Education established a target for local school systems to address the need for special education students to receive access to services in the general education environment. The FY 2016 proposed target requires 63.11 percent of students with disabilities to receive special education and related services in a general education setting. As a result of this mandate, the Department of Special Education Services (DSES), in collaboration with the Department of Facilities Management (DFM) and the Office of School Support and Improvement (OSSI), plan and coordinate the identification of program sites and locations to address the diverse needs of students with disabilities. This process is designed to ensure the delivery of special education services with an emphasis on providing services to the maximum extent appropriate in the school the student would attend if nondisabled.

MCPS chooses locations for special education programs by focusing on the delivery of services in the student's home school or in the school as close as possible to the student's home. The location of programs enables students with disabilities to receive special education services within the school, cluster, quad-cluster, or region of the county where the student resides.

The percentage of students who receive services in their home school, cluster, or quad-cluster has increased each year since 1998. The following model guides facility planning:

- Special education resource services are offered in all schools for Grades K–12. Sixty-eight elementary schools are designated as Home School Model Schools for the 2015–2016 school year. (See Appendix S for a description of the Home School Model program.)
- Learning and Academic Disabilities (LAD) Services and transition services are provided in all secondary schools.
- Special education services are provided at the cluster and quad-cluster level for elementary students who are recommended for LAD Services.
- Special education services are available in quad clusters or regionally for students who are recommended for the following services:
  - Augmentative and Alternative Communication Services
  - Autism Spectrum Disorders Services
  - Autism Resource Services
  - Aspergers Services
  - Bridge Services
  - Elementary Physical Disabilities Services
  - Elementary Learning Center
  - Emotional Disabilities Cluster Services
  - Gifted and Talented/Learning Disabled Program
  - Infants and Toddlers Program
  - Learning for Independence (LFI) Program
  - Preschool Education Program (PEP)
  - Prekindergarten Language Classes
  - School/Community-based (SCB) Program
  - Longview and Stephen Knolls
- Special education services are county-based for students in need of the following programs:
  - Carl Sandburg Learning Center
  - Deaf and Hard-of-Hearing Services
  - Preschool Vision Class
  - John L. Gildner Regional Institute for Children and Adolescents (RICA)
  - Rock Terrace School
  - Extensions
  - Secondary Physical Disabilities Services

Birth through 5 Years of Age Special Education Growth

The Montgomery County Infants and Toddlers Program provides services to children with developmental delays from birth to three years of age or until the start of the school year after turning four under the Extended Individualized Family Service Plan, in natural environments, such as home, child-care, or other community settings. Growth in the Infants and Toddlers Program has resulted in the location of five centers throughout the county.

MCPS provides a continuum of special education services for children ages three through five. Preschool Education Program (PEP) services range from consultative and itinerant services for children in community-based child care settings and pre-schools to itinerant instruction at home for medically fragile children. Classroom environments are provided for children who need a comprehensive approach to their learning needs.

Providing prekindergarten special education services in the least restrictive environment (LRE) is a challenge because of the limited number of general education prekindergarten classrooms and services available in MCPS. DSES and the Division of Early Childhood Programs and Services (DECPS) collaborate to collocate general and special education preschool classes to provide additional LRE opportunities to prekindergarten students. MCPS also is focused on increasing the number of locations where nondisabled community peers are invited to learn alongside students with disabilities in a prekindergarten classroom.

Chapter 4

Approved Actions and Planning Issues

Chapter 4 is organized alphabetically by high school cluster and consortia. Each section includes a map of the cluster service areas and tables containing enrollment, demographic, program capacity, and facilities information for individual schools. Capital projects approved for the FY 2016 Capital Budget and Amendments to the FY 2015–2020 Capital Improvements Program (CIP) are included. It is important to note that although cluster/consortia organization is used for the presentation of information, planning actions often cross cluster/consortia boundaries in order to meet program and facility needs for all students.

All schools are evaluated based on existing and planned program capacity. School system enrollment continues to grow. Over the next six years, enrollment is projected to increase by 11,526 students. Although temporary overutilization of facilities is accommodated with relocatable classrooms, long-term overutilization requires additional capacity to both elementary and secondary schools through classroom additions, revitalization/expansion projects, and new or reopened facilities. This year, MCPS houses about 9,300 students in 404 relocatable classrooms.

For each cluster and the Downcounty and Northeast consortia, information is presented within a common framework. Planning issues of a cluster wide nature are followed by a discussion of individual secondary and elementary schools with approved capital projects or non-capital actions. All clusters may not have cluster wide planning issues, and only schools with plans are discussed in each cluster section.

Following the narrative discussion of planning activities is a table labeled "Capital Projects" that summarizes all capital projects for that cluster or consortium. Five types of projects are identified under the "Type of Project" column. The types of projects are as follows:

- "Approved"—Project has an FY 2015 or FY 2016 appropriation approved in the FY 2015–2020 CIP.
- "Deferred"—Funds have been deferred for a future CIP.
- "Programmed"—Project has expenditures programmed in a future year of the CIP for planning and/or construction funds.
- "Proposed"—Project has facility planning funds approved for FY 2015 or FY 2016 for a feasibility study.

For each cluster and the two consortia, four summary tables and a bar graph are presented. The bar graph shows the effects of additions to capacity in the calculation of future utilization levels. The "Projected Enrollment and Available Capacity" table reflects the projected enrollment six years into the future for elementary and secondary schools and to the years 2024 and 2029 at the secondary level. Space availability is shown with approved CIP actions. This table also has a "comments" section that contains a brief explanation of program or facility changes that will impact capacity within

AAC—Augmentative and Alternative Communication

Add.—Addition

AUT—Autism Spectrum Disorders

BRIDGE—Bridge services

CSR—Class size reduction

DCC—Downcounty Consortium

DHOH—Deaf and Hard of Hearing

ED—Emotional Disability Program

ELC—Elementary Learning Center

ESOL—English for Speakers of Other Languages

GT/LD—Gifted and Talented/Learning Disabled

HS—Head Start

HSM–Home school model

LAD—Learning and Academic Disabilities

LANG—Speech/Language Disabilities

LFI—Learning for Independence

LTL—Linkages to Learning

METS—Multidisciplinary Educational Training and Support class (for non-English-speaking students with limited educational experience)

MSMC—Middle School Magnet Consortium

NEC—Northeast Consortium

PD—Physical Disabilities class

PEP—Preschool Education Program

pre-K—# of sessions of prekindergarten

pre-K Lang—Prekindergarten language class

Reg. Sec.—Regular secondary classroom

Reg. Elem.—Regular elementary classroom

Rev/Ex—Revitalization/Expansion

Rm CSR—# of classrooms for class-size reduction initiative

SBHC—School-based Health Center

SCB—School/Community-Based Programs for Students with Intellectual Disabilities

Sup. Rms.—Support rooms, such as art, music, and computer labs

TBD—To be determined

TS—# of Teaching Stations

VIS—Preschool or secondary Vision Impairment

Well Ctr—Wellness Center

any given year. To assist readers, a glossary of abbreviations and terms used in the tables and notes is included on the previous page. A second table, titled "Demographic Characteristics of Schools 2014–2015," shows the racial and ethnic group composition percentages, the student participation in the Free and Reduced-price Meals System (FARMS) Program, the percentage of English for Speakers of Other Languages (ESOL) and the Mobility Rate for schools. The "Capacity Table (School Year 2014–2015)" reflects detailed program capacity information for each school, along with special education program information. The final table, titled "Facilities Characteristics of Schools 2014–2015," shows facility information for each school.

Clusters for 2015–2016 School Year

BETHESDA-CHEVY CHASE CLUSTER

Bethesda-Chevy Chase HS (9–12)
- Westland MS (6–8)
  - Bethesda ES (K–5)
  - Chevy Chase ES (3–6)
  - North Chevy Chase ES (3–6)
  - Rock Creek Forest ES (K–5)
  - Rosemary Hills ES (pre-K–2)*
  - Somerset ES (K–5)
  - Westbrook ES (K–5)

WINSTON CHURCHILL CLUSTER

Winston Churchill HS (9–12)
- Cabin John MS (6–8) (shared with Wootton Cluster)*
  - Bells Mill ES (HS–5)
  - Seven Locks ES (K–5)
- Herbert Hoover MS (6–8)
  - Beverly Farms ES (K–5)
  - Potomac ES (K–5)
  - Wayside ES (K–5)

CLARKSBURG CLUSTER

Clarksburg HS (9–12)
- Neelsville MS (6–8) (shared with Watkins Mill Cluster)*
  - Capt. James E. Daly ES (pre-K–5)
  - Fox Chapel ES (pre-K–5)
- Rocky Hill MS (6–8) (shared with Damascus Cluster)*
  - Cedar Grove ES (K–5)*
  - Clarksburg ES (K–5)
  - William B. Gibbs, Jr. ES (pre-K–5)
  - Little Bennett ES (K–5)
  - Wilson Wims ES (K–4)*

DAMASCUS CLUSTER

Damascus HS (9–12)
- John T. Baker MS (6–8)
  - Clearspring ES (HS–5)
  - Damascus ES (K–5)
  - Laytonsville ES (K–5)*
  - Lois P. Rockwell ES (K–5)
  - Woodfield ES (K–5)
- Rocky Hill MS (6–8) (shared with Clarksburg Cluster)*
  - Cedar Grove ES (K–5)*
  - Wilson Wims ES (K–4)*

DOWNCOUNTY CONSORTIUM

Montgomery Blair HS (9–12)
Albert Einstein HS (9–12)
John F. Kennedy HS (9–12)
Northwood HS (9–12)
Wheaton HS (9–12)
- Argyle MS (6–8)
- A. Mario Loiederman MS (6–8)
- Parkland MS (6–8)
  - Bel Pre ES (pre-K–2)
  - Brookhaven ES (pre-K–5)
  - Georgian Forest ES (HS and pre-K–5)
  - Harmony Hills ES (HS and pre-K–5)
  - Sargent Shriver ES (pre-K–5)
  - Strathmore ES (3–5)
  - Viers Mill ES (HS and pre-K–5)
  - Weller Road ES (HS and pre-K–5)
  - Wheaton Woods ES (HS and pre-K–5)
- Eastern MS (6–8)
  - Montgomery Knolls ES (HS and pre-K–2)
  - New Hampshire Estates ES (HS and pre-K–2)
  - Oak View ES (3–5)
  - Pine Crest ES (3–5)
- Col. E. Brooke Lee MS (6–8)
  - Arcola ES (HS–5)
  - Glenallan ES (HS–5)
  - Kemp Mill ES (pre-K–5)
- Newport Mill MS (6–8)
  - Highland ES (HS and pre-K–5)*
  - Oakland Terrace ES (pre-K–5)
  - Rock View ES (pre-K–5)
- Silver Spring International MS (6–8)
  - Forest Knolls ES (HS and pre-K–5)
  - Highland View ES (K–5)
  - Rolling Terrace ES (HS and pre-K–5)
  - Sligo Creek ES (K–5)
- Sligo MS (6–8)
  - Glen Haven ES (pre-K–5)
  - Highland ES (HS and pre-K–5) *
  - Flora M. Singer ES (pre-K–5)
  - Woodlin ES (K–5)
- Takoma Park MS (6–8)
  - East Silver Spring ES (HS and pre-K–5)
  - Piney Branch ES (3–5)
  - Takoma Park ES (pre-K–2)

GAITHERSBURG CLUSTER

Gaithersburg HS (9–12)
- Forest Oak MS (6–8)
  - Goshen ES (K–5)
  - Rosemont ES (pre-K–5)
  - Summit Hall ES (HS and pre-K–5)
  - Washington Grove ES (HS and pre-K–5)
- Gaithersburg MS (6–8)
  - Gaithersburg ES (pre-K–5)
  - Laytonsville ES (K–5)*
  - Strawberry Knoll ES (HS and pre-K–5)

WALTER JOHNSON CLUSTER

Walter Johnson HS (9–12)
- North Bethesda MS (6–8)
  - Ashburton ES (K–5)
  - Kensington Parkwood ES (K–5)
  - Wyngate ES (K–5)
- Tilden MS (6–8)
  - Farmland ES (K–5)
  - Garrett Park ES (K–5)
  - Luxmanor ES (K–5)

COL. ZADOK MAGRUDER CLUSTER

Col. Zadok Magruder HS (9–12)
- Redland MS (6–8)
  - Cashell ES (pre-K–5)
  - Judith A. Resnik ES (pre-K–5)
  - Sequoyah ES (K–5)
- Shady Grove MS (6–8)
  - Candlewood ES (K–5)
  - Flower Hill ES (pre-K–5)
  - Mill Creek Towne ES (pre-K–5)

RICHARD MONTGOMERY CLUSTER

Richard Montgomery HS (9–12)
- Julius West MS (6–8)
  - Beall ES (HS and pre-K–5)
  - College Gardens ES (HS–5)
  - Ritchie Park ES (K–5)
  - Twinbrook ES (HS and pre-K–5)

NORTHEAST CONSORTIUM

James H. Blake HS (9–12)
Paint Branch HS (9–12)

Clusters for 2015–2016 School Year

Springbrook HS (9–12)
- Benjamin Banneker MS (6–8)
  - Burtonsville ES (K–5)
  - Fairland ES (HS and pre-K–5)*
  - Greencastle ES (pre-K–5)
- Briggs Chaney MS (6–8)
  - Cloverly ES (K–5)*
  - Fairland ES (HS and pre-K–5)*
  - Galway ES (pre-K–5)
  - William T. Page ES (pre-K–5)
- William H. Farquhar MS (6–8) (shared with Sherwood Cluster)*
  - Cloverly ES (K–5)*
  - Sherwood (K–5)*
  - Stonegate ES (K–5)*
- Francis Scott Key MS (6–8)
  - Burnt Mills ES (pre-K–5)
  - Cannon Road ES (K–5)
  - Cresthaven ES (3–5)
  - Dr. Charles R. Drew ES (pre-K–5)
  - Roscoe R. Nix ES (pre-K–2)
- White Oak MS (6–8)
  - Jackson Road ES (pre-K–5)
  - JoAnn Leleck ES at Broad Acres(HS and pre-K–5)
  - Stonegate ES (K–5)*
  - Westover ES (K–5)

NORTHWEST CLUSTER

Northwest HS (9–12)
- Kingsview MS (6–8)
  - Great Seneca Creek ES (K–5)*
  - Ronald McNair ES (pre-K–5)
  - Spark M. Matsunaga ES (K–5)
- Lakelands Park MS (6–8) (shared with Quince Orchard Cluster)*
  - Darnestown ES (K–5)
  - Diamond ES (K–5)*
- Roberto Clemente MS (6–8) (shared with Seneca Valley Cluster)*
  - Clopper Mill ES (HS and pre-K–5)
  - Germantown ES (K–5)
  - Great Seneca Creek ES (K–5)*

POOLESVILLE CLUSTER

Poolesville HS (9–12)
- John Poole MS (6–8)
  - Monocacy ES (K–5)
  - Poolesville ES (K–5)

QUINCE ORCHARD CLUSTER

Quince Orchard HS (9–12)
- Lakelands Park MS (6–8) (shared with Northwest Cluster)*
  - Brown Station ES (HS and pre-K–5)
  - Rachel Carson ES (pre-K–5)
- Ridgeview MS (6–8)
  - Diamond ES (K–5)*
  - Fields Road ES (pre-K–5)
  - Jones Lane ES (K–5)
  - Thurgood Marshall ES (K–5)

ROCKVILLE CLUSTER

Rockville HS (9–12)
- Earle B. Wood MS (6–8)
  - Lucy V. Barnsley ES (pre-K–5)
  - Flower Valley ES (K–5)
  - Maryvale ES (HS and pre-K–5)
  - Meadow Hall ES (K–5)
  - Rock Creek Valley ES (K–5)

SENECA VALLEY CLUSTER

Seneca Valley HS (9–12)
- Roberto W. Clemente MS (6–8) (shared with Northwest Cluster)*
  - S. Christa McAuliffe ES (HS–5)
  - Dr. Sally K. Ride (HS and pre-K–5)*
- Dr. Martin Luther King, Jr. MS (6–8)
  - Lake Seneca ES (pre-K–5)
  - Dr. Sally K. Ride ES (HS and pre-K–5)*
  - Waters Landing ES (K–5)

SHERWOOD CLUSTER

Sherwood HS (9–12)
- Rosa M. Parks MS (6–8)
  - Belmont ES (K–5)
  - Greenwood ES (K–5)
  - Olney ES (K–5)
- William H. Farquhar MS (6–8) (shared with Northeast Consortium)*
  - Brooke Grove ES (pre-K–5)
  - Sherwood ES (K–5)

WATKINS MILL CLUSTER

Watkins Mill HS (9–12)
- Montgomery Village MS (6–8)
  - Stedwick ES (pre-K–5)*
  - Watkins Mill ES (HS and pre-K–5)
  - Whetstone ES (pre-K–5)
- Neelsville MS (6–8) (shared with Clarksburg Cluster)*
  - South Lake ES (HS and pre-K–5)
  - Stedwick ES (pre-K–5)*

WALT WHITMAN CLUSTER

Walt Whitman HS (9–12)
- Thomas W. Pyle MS (6–8)
  - Bannockburn ES (K–5)
  - Bradley Hills ES (K–5)
  - Burning Tree ES (K–5)
  - Carderock Springs ES (K–5)
  - Wood Acres ES (K–5)


THOMAS S. WOOTTON CLUSTER

Thomas S. Wootton HS (9–12)
- Cabin John MS (6–8) (shared with Churchill Cluster)*
  - Cold Spring ES (K–5)
  - Stone Mill ES (K–5)
- Robert Frost MS (6–8)
  - DuFief ES (K–5)
  - Fallsmead ES (K–5)
  - Lakewood ES (K–5)
  - Travilah ES (K–5)

OTHER EDUCATIONAL FACILITIES

Additionally, Montgomery County Public Schools operates the following facilities:
- Thomas Edison High School of Technology
- Blair G. Ewing Center
- Stephen Knolls School
- Longview School
- RICA—Regional Institute for Children and Adolescents
- Rock Terrace School
- Carl Sandburg Learning Center

*Denotes schools with split articulation, i.e., some students feed into one school, while other students feed into another school in the same or different cluster.

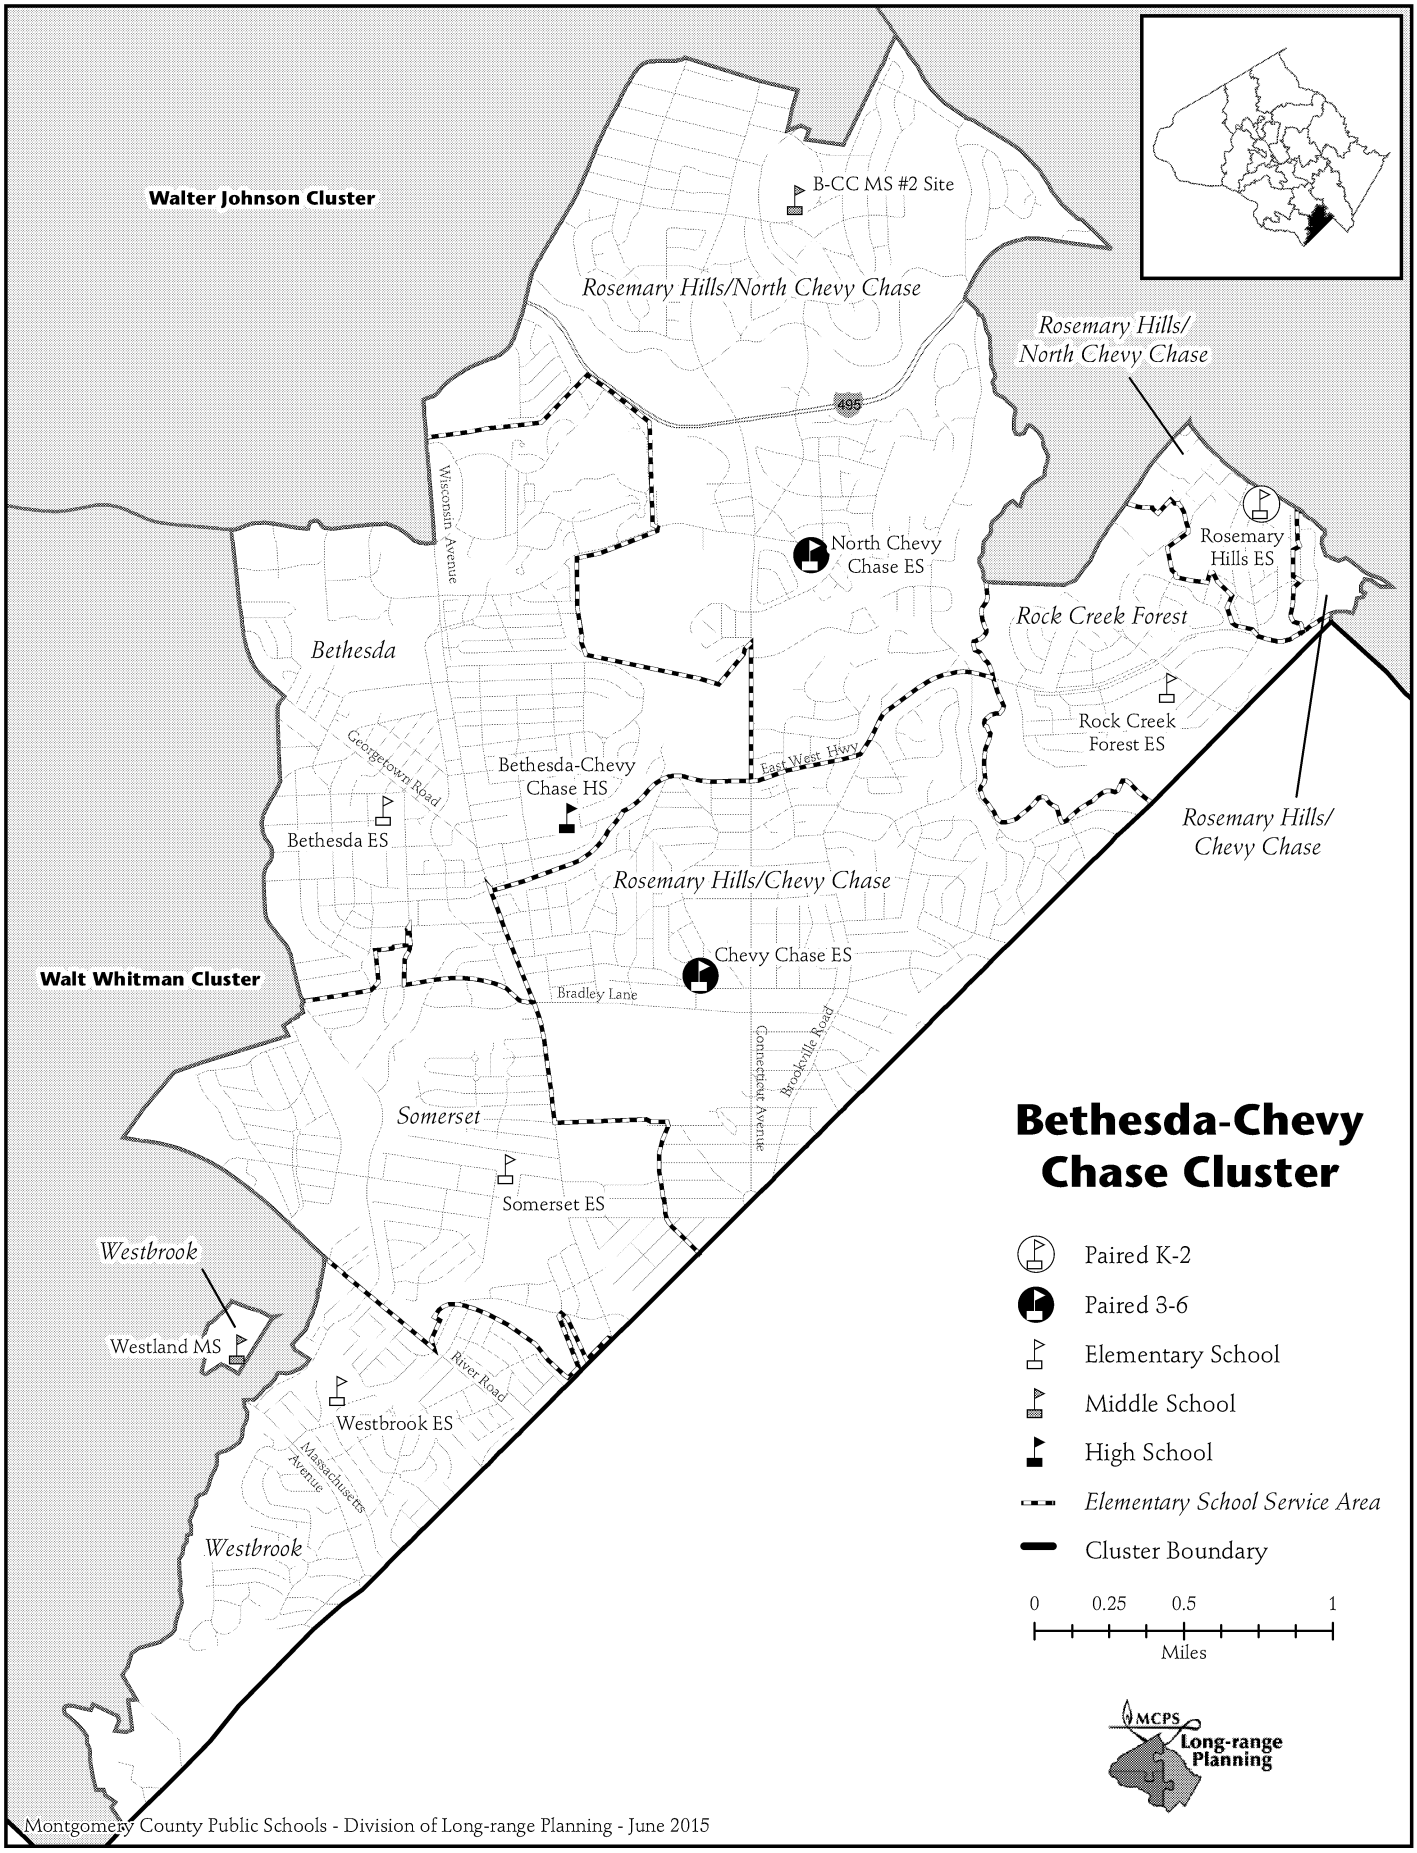
Walter Johnson Cluster
B-CC MS #2 Site
Rosemary Hills/North Chevy Chase
Rosemary Hills/
North Chevy Chase
495
Wisconsin Avenue
North Chevy
Chase ES
Rosemary
Hills ES
Rock Creek Forest
Bethesda
Rock Creek
Forest ES
Georgetown Road
East West Hwy
Bethesda-Chevy
Chase HS
Bethesda ES
Rosemary Hills/
Chevy Chase
Rosemary Hills/Chevy Chase
Chevy Chase ES
Walt Whitman Cluster
Bradley Lane
Connecticut Avenue
Brookville Road
Somerset
Somerset ES
Westbrook
Westland MS
River Road
Westbrook ES
Massachusetts
Avenue
Westbrook
Bethesda-Chevy
Chase Cluster
Paired K-2
Paired 3-6
Elementary School
Middle School
High School
Elementary School Service Area
Cluster Boundary
0
0.25
0.5
1
Miles
MCPS
Long-range
Planning
Montgomery County Public Schools - Division of Long-range Planning - June 2015

CLUSTER PLANNING ISSUES


The Bethesda-Chevy Chase Cluster includes the recently adopted Chevy Chase Lake Sector Plan that provides for up to 1,400 new, mostly multi-family residential units. Although the majority of the residential units can go forward at any time, build-out of all the residential units requires funding for the Purple Line to be secured. As with many sector plans in the county, build-out requires the redevelopment of many existing land uses in the area. The pace of construction will be market driven.

Student enrollment at all the schools in the Bethesda-Chevy Chase Cluster has increased dramatically over the past few years. To address the overutilization at the elementary schools, capital projects were approved as part of the Amended FY 2011–2016 CIP and FY 2013–2018 CIP, and several planning activities occurred over the past several years to develop long-range plans for elementary schools in this cluster. The approved capital projects for elementary schools include the following:

- An addition that opened at Somerset Elementary School during the 2010–2011 school year;
- An addition that opened at Westbrook Elementary School in August 2013;
- An addition at Bethesda Elementary School scheduled to open in August 2015;
- An addition at North Chevy Chase Elementary School scheduled to open in August 2015;
- A revitalization/expansion project at Rock Creek Forest Elementary School (with increased capacity) that opened in January 2015; and
- An addition at Rosemary Hills Elementary School that opened in spring 2015.

A summary of other planning actions and activities for other Bethesda-Chevy Chase Cluster elementary schools include the following:

- In March 2010, the Board of Education adopted a boundary change between Bethesda and Bradley Hills elementary schools to address the overutilization at Bethesda Elementary School. In August 2013, the western portion of the Bethesda Elementary School service area (that articulates to the Walt Whitman Cluster secondary schools) was reassigned to Bradley Hills Elementary School. A classroom addition opened in August 2013 at Bradley Hills Elementary School that provided sufficient capacity to accommodate the additional students.
- In November 2011, the Board of Education adopted the following boundary changes that were implemented in August 2013:
  - The East Bethesda community was reassigned from Rosemary Hills Elementary School to Bethesda Elementary School for Grades K–2, with continuation through Grade 5.
  - The Paddington Square Apartments community and the Naval Support Activity Bethesda were reassigned from Bethesda Elementary School to North Chevy Chase Elementary School for Grades 3–6 (and when reorganization occurs in August 2017, for Grades 3–5). Both of these areas remained assigned to Rosemary Hills Elementary School for Grades K–2.
  - The portion of the Summit Hills Apartments community with addresses 1703 and 1705 East West Highway was reassigned from North Chevy Chase Elementary School to Chevy Chase Elementary School for Grades 3–6 (and when reorganization occurs in August 2017, for Grades 3–5).
  - In March 2014, the Naval Support Activity Bethesda was reassigned from Rosemary Hills and North Chevy Chase elementary schools to Bethesda Elementary School for Grades K–5.
- A new middle school is planned in the Bethesda-Chevy Chase Cluster to address Grades 6–8 enrollment growth in the cluster and to allow the Grade 6 students currently enrolled at Chevy Chase and North Chevy Chase elementary schools to be reassigned to the middle school level. In addition, the reorganization of these two elementary schools, from Grades 3–6 to Grades 3–5, will help relieve some of the projected overutilization at these schools when the new middle school opens. A feasibility study for the new middle school, to be located at the Rock Creek Hills Local Park site, was conducted in summer 2011. An FY 2016 appropriation was approved to construct Bethesda-Chevy Chase Middle School #2.
- To address enrollment growth at the high school, a classroom addition is planned for Bethesda-Chevy Chase High School. An FY 2015 appropriation for construction funds was approved to begin the architectural design for the classroom addition.

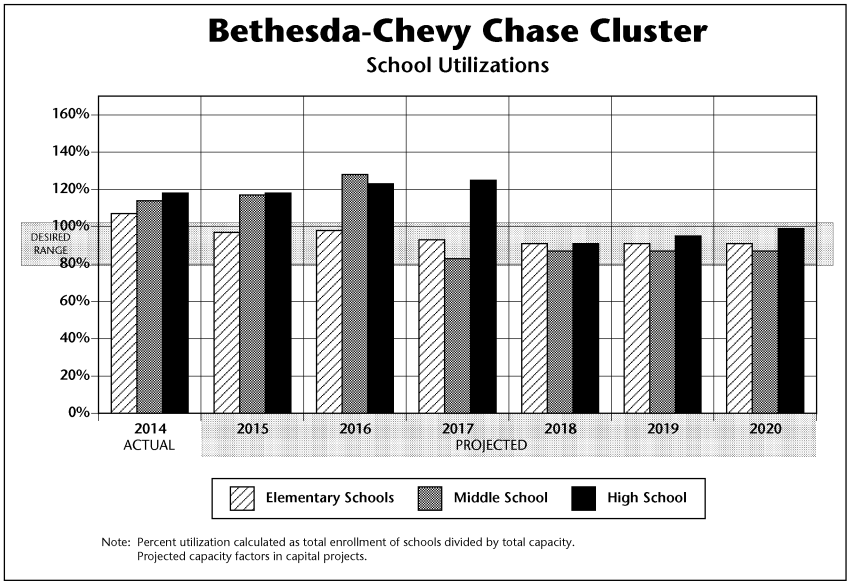

SCHOOLS

Bethesda Chevy Chase High School

Capital Project: Enrollment increases at the cluster elementary schools and at Westland Middle School have reached the high school. Bethesda-Chevy Chase High School is projected to exceed capacity by 700 students by the end of the six-year CIP planning period. Although the Board of Education requested a completion date for this project of August 2017, the County Council maintained the FY 2015–2020 completion date of August 2018. FY 2017 expenditures are approved to begin the construction of the classroom addition at Bethesda-Chevy Chase High School. In order for this project to be completed on schedule, county and state funding must be provided at levels approved in this CIP.

Bethesda Chevy Chase Middle School #2 (B-CC MS #2)

Capital Project: Enrollment increases at Westland Middle School, and the plan to reassign Grade 6 students from Chevy Chase and North Chevy Chase elementary schools to the middle school level, will result in a total cluster middle school enrollment of over 1,700 students by the end of the six-year planning period. Because the projected enrollment would far exceed the current capacity of Westland Middle School, Bethesda-Chevy Chase Middle School #2 is needed to accommodate the projected enrollment. An FY 2016 appropriation is approved to construct the new school. The boundary study process is scheduled to begin in January 2016 with Board of Education action in November 2016. The scheduled completion date for the new school is August 2017. In order for this project to be completed on schedule, county and state funding must be provided at levels approved in this CIP.

Westland Middle School

Planning Issue: Although a six-classroom addition opened in the 2009–2010 school year to accommodate the overutilization at Westland Middle School, student enrollment continues to increase beyond the capacity of the school. The opening of Bethesda-Chevy Chase Middle School #2 will address the overutilization of Westland Middle School. Relocatable classrooms will be utilized until the new school opens.

Bethesda Elementary School

Non-capital Solution: In March 2010, the Board of Education approved the reassignment of the western portion of the Bethesda Elementary School service area (the area that articulates to Whitman Cluster secondary schools) to Bradley Hills Elementary School, beginning in August 2013.

Capital Project: Enrollment projections that incorporate approved boundary changes indicate that enrollment at Bethesda Elementary School will exceed capacity by 92 seats or more throughout the six-year CIP planning period. An FY 2014 appropriation was approved to construct a classroom addition. The scheduled completion date for the addition is August 2015.

Chevy Chase Elementary School

Non-capital Solution: In November 2010, the Board of Education approved a plan to construct a new middle school in the Bethesda-Chevy Chase Cluster and reassign Grade 6 students from Chevy Chase and North Chevy Chase elementary schools to the middle school level when Bethesda-Chevy Chase Middle School #2 opens in August 2017.

North Chevy Chase Elementary School

Non-capital Solution: In November 2010, the Board of Education approved a plan to construct a new middle school in the Bethesda-Chevy Chase Cluster and reassign Grade 6 students from Chevy Chase and North Chevy Chase elementary schools to the middle school level when Bethesda-Chevy Chase Middle School #2 opens in August 2017.

Capital Project: Projections that incorporate approved boundary changes indicate enrollment at North Chevy Chase Elementary School will exceed capacity by 92 seats or more throughout the six-year CIP period. The reassignment of Grade 6 students out of North Chevy Chase Elementary School will relieve some, but not all, of the projected space deficit. An FY 2014 appropriation was approved to construct a classroom addition. The scheduled completion date for the addition is August 2015.

Rock Creek Forest Elementary School

Capital Project: A revitalization/expansion project was completed in January 2015.

Rosemary Hills Elementary School

Non-capital Solution: In November 2011, the Board of Education adopted boundary changes for Bethesda, Chevy Chase, North Chevy Chase, and Rosemary Hills elementary schools.

Capital Project: Enrollment projections that incorporate the approved boundary changes indicate enrollment at Rosemary Hills Elementary School will exceed capacity by 92 seats or more throughout the six-year CIP period. An FY 2014 appropriation was approved to construct a classroom addition. The scheduled completion date for the addition is August 2015.

Capital Project: A revitalization/expansion project is scheduled for this school. Although the Board of Education requested a completion date for this project of January 2022, the County Council maintained the FY 2015–2020 completion date of January 2023.

FY 2017 expenditures are programmed for facility planning for a feasibility study to determine the scope and cost of the project. In order for this project to be completed on this schedule, county and state funding must be provided at the levels approved in this CIP.

CAPITAL PROJECTS

School	Project	Project Status*	Date of Completion
Bethesda-Chevy Chase HS	Classroom addition	Programmed	Aug. 2018
Bethesda-Chevy Chase MS #2	New school	Approved	Aug. 2017
Bethesda ES	Classroom addition	Approved	Aug. 2015
North Chevy Chase ES	Classroom addition	Approved	Aug. 2015
Rock Creek Forest ES	Revitalization/ expansion	Approved	Jan. 2015
Rosemary Hills ES	Classroom addition	Approved	Aug. 2015
	Revitalization/ expansion	Programmed	Jan. 2023

"Approved"— Project has an FY 2015 or FY 2016 appropriation approved in the FY 2015–2020 CIP.

"Deferred"—Funds have been deferred for a future CIP.

"Programmed"—Project has expenditures programmed in a future year of the CIP for planning and/or construction funds.

"Proposed"—Project has facility planning funds approved for FY 2015 or approved for FY 2016 for a feasibility study.

Projected Enrollment and Space Availability

Effects of the Amended FY2015–2020 CIP and Non–CIP Actions on Space Available

Schools			Actual 14–15	Projections 15–16	16–17	17–18	18–19	19–20	20–21	2024	2029
Bethesda–Chevy Chase HS		Program Capacity	1683	1683	1683	1683	2398	2398	2398	2398	2398
		Enrollment	**1992**	**1989**	**2067**	**2097**	**2178**	**2287**	**2367**	**2500**	**2400**
		Available Space	*(309)*	*(306)*	*(384)*	*(414)*	*220*	*112*	*32*	*(102)*	*(2)*
		Comments	Planning for Addition				Addition Complete				
Bethesda-Chevy Chase MS #2		Program Capacity				922	922	922	922	922	922
		Enrollment				**0**	**0**	**0**	**0**	**0**	**0**
		Available Space				*922*	*922*	*922*	*922*	*922*	*922*
		Comments	Planning for new school			Opens Aug. 2017					
Westland MS		Program Capacity	1097	1097	1097	1097	1097	1097	1097	1097	1097
		Enrollment	**1254**	**1288**	**1403**	**1676**	**1758**	**1749**	**1765**	**1900**	**1800**
		Available Space	*(158)*	*(192)*	*(306)*	*(580)*	*(662)*	*(652)*	*(668)*	*(803)*	*(703)*
		Comments				See text					
Bethesda ES		Program Capacity	384	568	568	568	568	568	568		
Grades (K–5)		**Enrollment**	**517**	**530**	**544**	**542**	**527**	**533**	**556**		
		Available Space	*(133)*	*38*	*24*	*26*	*41*	*35*	*12*		
		Comments		Addition Complete							
Chevy Chase ES		Program Capacity	473	473	473	473	473	473	473		
Grades (3–6)		**Enrollment**	**541**	**557**	**542**	**422**	**406**	**405**	**406**		
Paired With		Available Space	*(68)*	*(84)*	*(69)*	*51*	*67*	*68*	*67*		
Rosemary Hills ES		Comments				See text					
North Chevy Chase ES		Program Capacity	266	358	358	358	358	358	358		
Grades (3–6)		**Enrollment**	**355**	**363**	**372**	**289**	**288**	**293**	**300**		
Paired With		Available Space	*(89)*	*(5)*	*(14)*	*69*	*70*	*65*	*58*		
Rosemary Hills ES		Comments		Addition Complete		See text					
Rock Creek Forest ES	CSR	Program Capacity	770	754	754	754	754	754	754		
		Enrollment	**628**	**665**	**685**	**684**	**663**	**656**	**661**		
		Available Space	*142*	*89*	*69*	*70*	*91*	*98*	*93*		
		Comments	Rev/Ex Complete	+ 2 AUT +1 PEP + PreK							
Rosemary Hills ES		Program Capacity	478	644	644	644	644	644	644		
Grades (pre-K–2)		**Enrollment**	**633**	**600**	**615**	**623**	**626**	**625**	**624**		
Paired With		Available Space	*(155)*	*44*	*29*	*21*	*18*	*19*	*20*		
Chevy Chase ES		Comments		Addition Complete -1 AUT	Facility Planning for Rev/Ex		Planning for Revitalization/ Expansion				
North Chevy Chase ES											
Somerset ES		Program Capacity	515	515	515	515	515	515	515		
		Enrollment	**567**	**557**	**542**	**551**	**545**	**540**	**511**		
		Available Space	*(52)*	*(42)*	*(27)*	*(36)*	*(30)*	*(25)*	*4*		
		Comments									
Westbrook ES		Program Capacity	554	549	549	549	549	549	549		
		Enrollment	**452**	**471**	**473**	**467**	**463**	**475**	**468**		
		Available Space	*102*	*78*	*76*	*82*	*86*	*74*	*81*		
		Comments		+1 PEP							
Cluster Information		HS Utilization	118%	118%	123%	125%	91%	95%	99%	104%	100%
		HS Enrollment	1992	1989	2067	2097	2178	2287	2367	2500	2400
		MS Utilization	114%	117%	128%	83%	87%	87%	87%	94%	89%
		MS Enrollment	1254	1288	1403	1676	1758	1749	1765	1900	1800
		ES Utilization	107%	97%	98%	93%	91%	91%	91%	93%	93%
		ES Enrollment	3693	3743	3773	3578	3518	3527	3526	3600	3600

Demographic Characteristics of Schools

Schools	2014–2015 Total Enrollment	Two or more races %	Black or Afr. Amr. %	Asian%	Hispanic %	White %	2014–2015 FARMS%*	2014–2015 ESOL%**	2013–2014 Mobility Rate%***
Bethesda-Chevy Chase HS	1992	5.3%	14.2%	5.6%	16.8%	57.9%	11.6%	≤ 5.0%	8.2%
Westland MS	1254	≤ 5.0%	10.6%	5.8%	15.8%	62.4%	12.5%	6.5%	7.2%
Bethesda ES	518	7.3%	8.5%	14.5%	9.1%	60.6%	6.6%	12.7%	15.0%
Chevy Chase ES	541	7.0%	11.8%	≤ 5.0%	9.2%	66.7%	13.9%	5.9%	5.6%
North Chevy Chase ES	355	6.2%	14.4%	5.4%	15.8%	58.0%	14.1%	5.4%	5.4%
Rock Creek Forest ES	628	5.7%	15.8%	5.3%	32.0%	40.9%	24.4%	17.0%	8.3%
Rosemary Hills ES	633	5.8%	22.1%	≤ 5.0%	15.0%	52.1%	27.6%	18.2%	9.1%
Somerset ES	567	7.8%	5.3%	9.0%	14.5%	63.1%	6.9%	13.6%	12.1%
Westbrook ES	452	7.7%	≤ 5.0%	≤ 5.0%	10.0%	76.3%	≤ 5.0%	≤ 5.0%	5.1%
Elementary Cluster Total	**3694**	**6.8%**	**11.9%**	**6.8%**	**15.6%**	**58.8%**	**14.6%**	**12.0%**	**8.8%**
Elementary County Total	75,144	≤ 5.0%	21.2%	13.9%	30.4%	29.3%	40.2%	23.3%	13.3%

**Percent of students approved for Free and Reduced-priced Meals Program (FARMS) during the 2014–2015 school year.*

***Percent of English for Speakers of Other Languages (ESOL) during the 2014–2015 school year. High School students are served in regional ESOL centers.*

****Mobility Rate is the number of entries plus withdrawals during the 2013–2014 school year compared to total enrollment.*

Notes: Native Hawaiian/Pacific Islander and American Indian/Alaskan Native categories total less than 1% and were therefore excluded from the table.

Due to federal and state guidelines, demographic characteristics of schools of less than or equal to 5.0% are reported as ≤ 5.0%.


Program Capacity Table

(School Year 2014–2015)

Schools	Grades Served	Capacity (HS @90% MS@85%)	Total Rooms	Support Rooms	Regular Secondary @25	Regular Elementary @23	CSR Grades 1–2 @18	Pre–K @20	Pre–K @40	HS @20	CSR KIND @18	KIND @22	ESOL @15	METS @15	Special Education Services: School Based: HSM @13	Cluster Based: ELEM LAD @13	Quad Cluster Based: ELC @10	LANG @12	LFI @10	SCB @6	County & Regional Based: AAC@7	AUT @6	BRIDGE @10	DHOH @7	ED @10	EXTENSIONS @6	GT/LD @13	PD @7	PEP@6	PEP @12	PEP @18	VISION (Elementary) @7	OTHER
Bethesda-Chevy Chase HS	9-12	1683	76		73								2	1																		
Westland MS	6-8	1097	52		51								1																			
Bethesda ES	K-5	384	21	3		13						3				1				1												
Chevy Chase ES	3-6	473	24	3		20									1																	
North Chevy Chase ES	3-6	266	15	3		11									1																	
Rock Creek Forest ES	K-5	770	40	4		20	10		1		5																					
Rosemary Hills ES	PreK-2	478	27	4		11			1			7			1							3										
Somerset ES	K-5	515	27	4		18						4			1																	
Westbrook ES	K-5	554	30	4		19						3			1										2					1		

Facility Characteristics of Schools 2014–2015

Schools	Year Facility Opened	Year Reopened/ Revitalized	Total Square Footage	Site Size Acres	Adjacent Park	Reloc-atable Classrooms	Linkages to Learning Program	Home School Model
Bethesda-Chevy Chase HS	1934	2001	308,215	16.4		8		
Westland MS	1951	1997	146,006	25.1		6		
Bethesda ES	1952	1999	75,257	8.42		5		Yes
Chevy Chase ES	1936	2000	70,976	3.8		1		Yes
North Chevy Chase ES	1953	1995	65,982	7.9		5		Yes
Rock Creek Forest ES	1950	2015	98,140	8				Yes
Rosemary Hills ES	1956	1988	86,548	6.1		7		Yes
Somerset ES	1949	2005	80,122	3.7				Yes
Westbrook ES	1939	1990	91,359	12.5	Yes			Yes

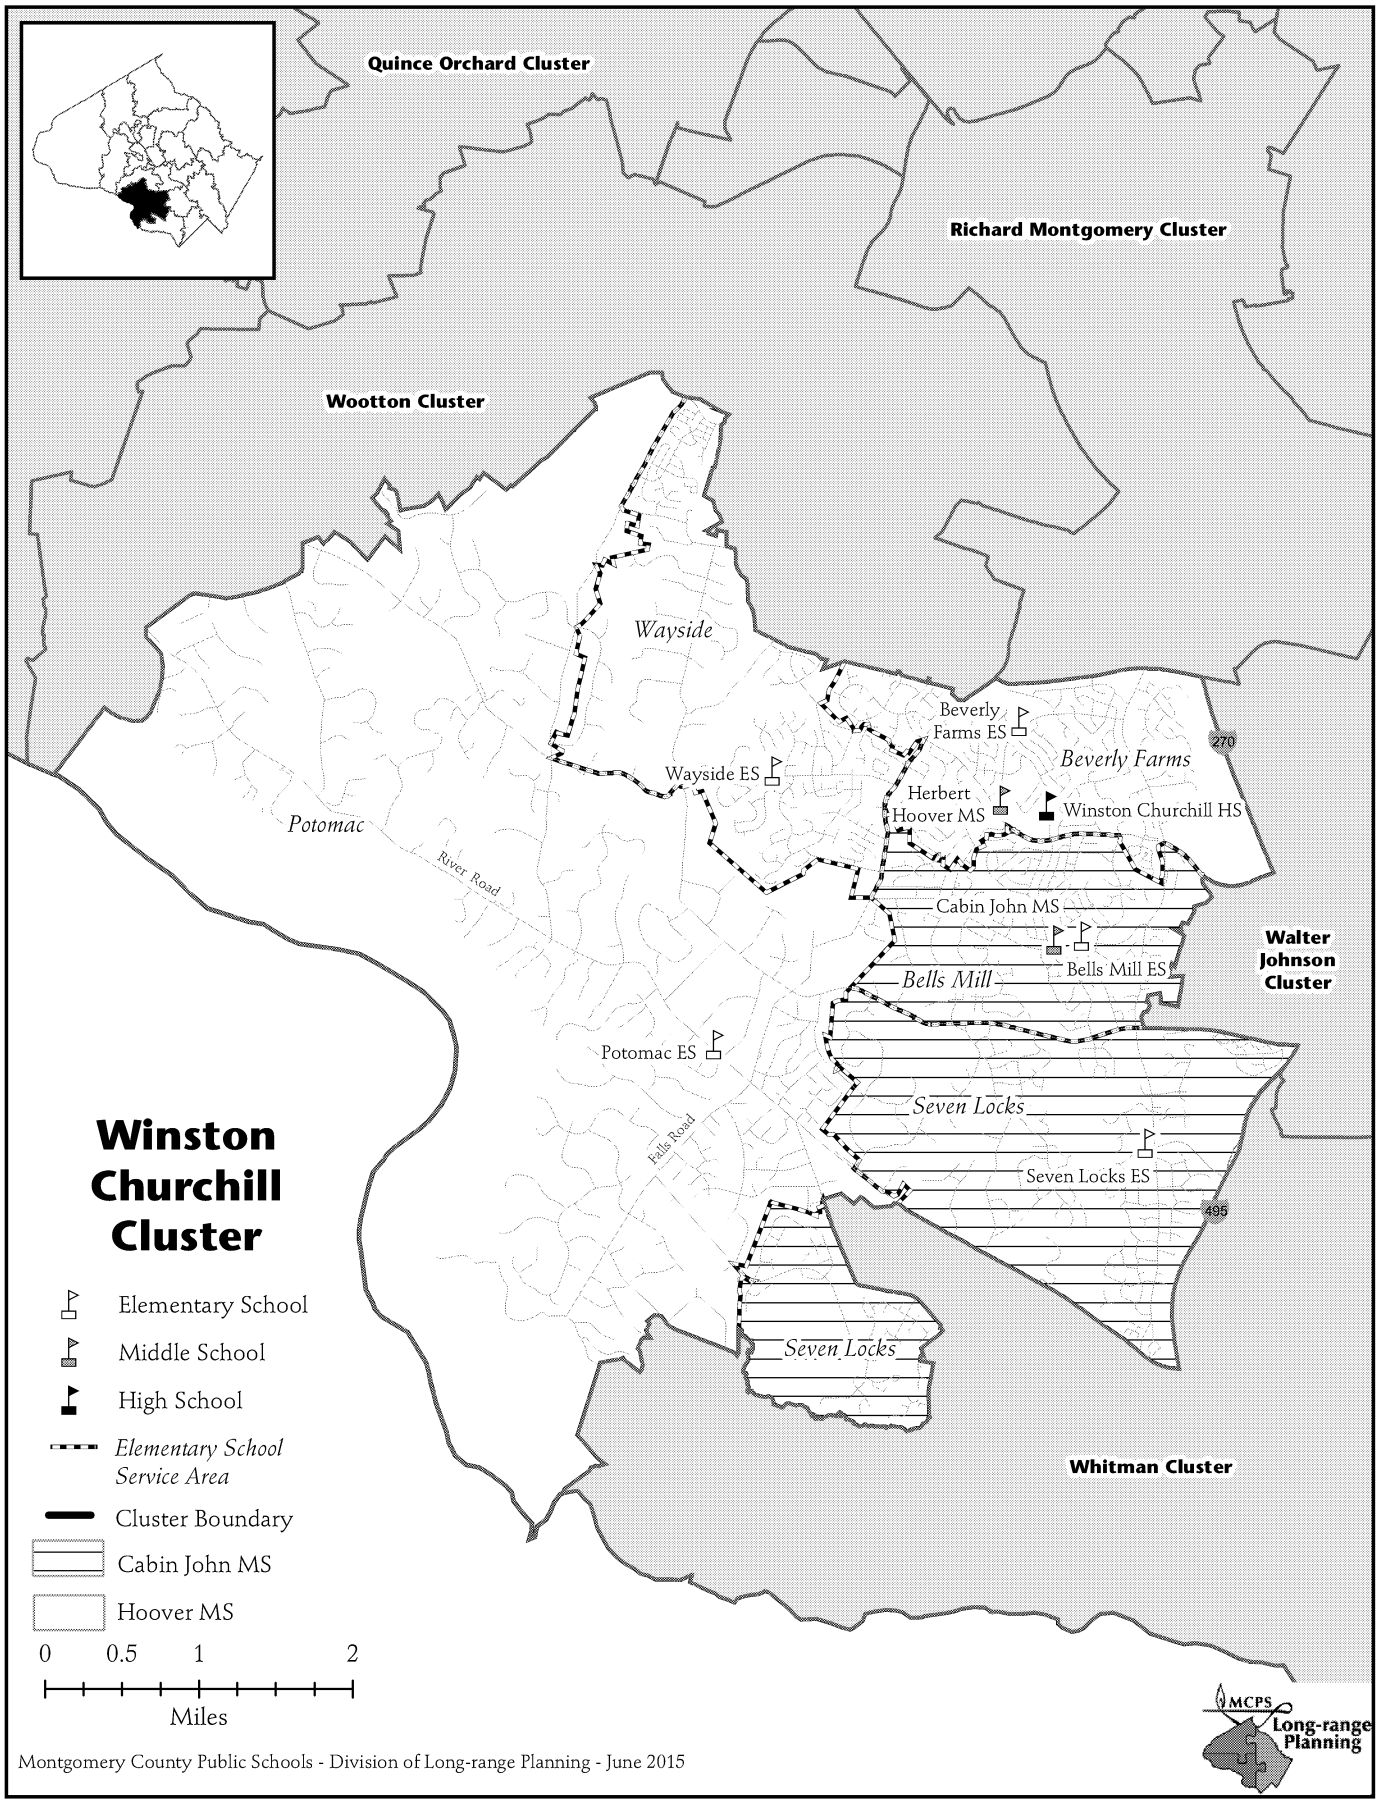
Quince Orchard Cluster
Richard Montgomery Cluster
Wootton Cluster
Wayside
Beverly Farms ES
Beverly Farms
270
Wayside ES
Herbert Hoover MS
Winston Churchill HS
Potomac
River Road
Cabin John MS
Walter Johnson Cluster
Bells Mill ES
Bells Mill
Potomac ES
Seven Locks
Falls Road
Seven Locks ES
495
Seven Locks
Whitman Cluster
Winston Churchill Cluster
Elementary School
Middle School
High School
Elementary School Service Area
Cluster Boundary
Cabin John MS
Hoover MS
0 0.5 1 2
Miles
MCPS
Long-range Planning
Montgomery County Public Schools - Division of Long-range Planning - June 2015

SCHOOLS

Potomac Elementary School

Capital Project: A revitalization/expansion project is scheduled for this school. Although the Board of Education requested a completion date of January 2019, the County Council maintained the approved FY 2015–2020 CIP completion date of January 2020. During the feasibility study, an option was explored to relocate the school from the current River Road location to the Brickyard Road school site. After careful consideration of both site options, the school will remain at the River Road location. An FY 2016 appropriation for planning funds is approved to begin the architectural design for the project. In order for this project to be completed on this schedule, county and state funding must be provided at the levels approved in this CIP.

Wayside Elementary School

Capital Project: A revitalization/expansion project is scheduled for this school. Although the approved FY 2015–2020 CIP had a completion of August 2018 for the revitalization/expansion project, the County Council approved the Board of Education's request to complete the project in August 2017. An FY 2016 appropriation is approved to construct this project.

CAPITAL PROJECTS


School	Project	Project Status*	Date of Completion
Potomac ES	Revitalization/ expansion	Approved	Jan. 2020
Wayside ES	Revitalization/ expansion	Approved	Aug. 2017

"Approved"— Project has an FY 2015 or FY 2016 appropriation approved in the FY 2015–2020 CIP.

"Deferred"—Funds have been deferred for a future CIP.

"Programmed"—Project has expenditures programmed in a future year of the CIP for planning and/or construction funds.

"Proposed"—Project has facility planning funds approved for FY 2015 or approved for FY 2016 for a feasibility study.

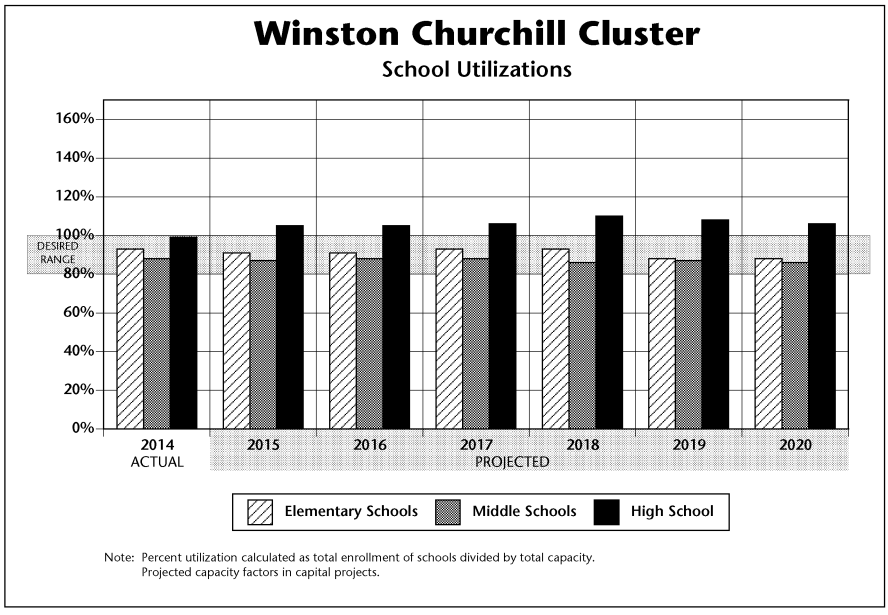

Projected Enrollment and Space Availability

Effects of the Amended FY2015–2020 CIP and Non–CIP Actions on Space Available

Schools			Actual 14–15	Projections 15–16	16–17	17–18	18–19	19–20	20–21	2024	2029
Winston Churchill HS		Program Capacity	2013	2013	2013	2013	2013	2013	2013	2013	2013
		Enrollment	**1996**	**2104**	**2106**	**2134**	**2206**	**2171**	**2142**	**2200**	**2100**
		Available Space	*17*	*(91)*	*(93)*	*(121)*	*(193)*	*(158)*	*(129)*	*(187)*	*(87)*
		Comments									
Cabin John MS		Program Capacity	1129	1113	1113	1113	1113	1113	1113	1113	1113
		Enrollment	**943**	**954**	**965**	**996**	**1002**	**1032**	**1029**	**1100**	**1000**
		Available Space	*186*	*159*	*148*	*117*	*111*	*81*	*84*	*13*	*113*
		Comments		+1 AUT							
Herbert Hoover MS		Program Capacity	1139	1139	1139	1139	1139	1139	1139	1139	1139
		Enrollment	**1058**	**1007**	**1018**	**992**	**938**	**917**	**907**	**950**	**900**
		Available Space	*81*	*132*	*121*	*147*	*201*	*222*	*232*	*189*	*239*
		Comments									
Bells Mill ES		Program Capacity	626	609	609	609	609	609	609		
		Enrollment	**611**	**609**	**636**	**636**	**647**	**641**	**634**		
		Available Space	*15*	*0*	*(27)*	*(27)*	*(38)*	*(32)*	*(25)*		
		Comments		+1 AUT							
Beverly Farms ES		Program Capacity	690	690	690	690	690	690	690		
		Enrollment	**621**	**600**	**573**	**571**	**557**	**564**	**560**		
		Available Space	*69*	*90*	*117*	*119*	*133*	*126*	*130*		
		Comments									
Potomac ES		Program Capacity	424	424	424	424	424	548	548		
		Enrollment	**474**	**445**	**435**	**440**	**441**	**437**	**437**		
		Available Space	*(50)*	*(21)*	*(11)*	*(16)*	*(17)*	*111*	*111*		
		Comments		Planning for Revitalization/ Expansion			@ Radnor	Rev/Ex Complete Jan. 2020			
Seven Locks ES		Program Capacity	425	425	425	425	425	425	425		
		Enrollment	**398**	**395**	**405**	**422**	**423**	**419**	**427**		
		Available Space	*27*	*30*	*20*	*3*	*2*	*6*	*(2)*		
		Comments									
Wayside ES		Program Capacity	671	671	671	641	641	641	641		
		Enrollment	**533**	**509**	**509**	**517**	**519**	**504**	**513**		
		Available Space	*138*	*162*	*162*	*124*	*122*	*137*	*128*		
		Comments		Move to Grosvenor Jan. 2016	@ Grosvenor	Rev/Ex Complete Aug. 2017					
Cluster Information		HS Utilization	99%	105%	105%	106%	110%	108%	106%	109%	104%
		HS Enrollment	1996	2104	2106	2134	2206	2171	2142	2200	2100
		MS Utilization	88%	87%	88%	88%	86%	87%	86%	91%	84%
		MS Enrollment	2001	1961	1983	1988	1940	1949	1936	2050	1900
		ES Utilization	93%	91%	91%	93%	93%	88%	88%	89%	89%
		ES Enrollment	2637	2558	2558	2586	2587	2565	2571	2600	2600

Demographic Characteristics of Schools

Schools	2014–2015 Total Enrollment	Two or more races %	Black or Afr. Amer. %	Asian%	Hispanic %	White %	2014–2015 FARMS%*	ESOL%**	2013–2014 Mobility Rate%***
Winston Churchill HS	1996	≤ 5.0%	7.9%	23.2%	8.9%	55.7%	≤ 5.0%	≤ 5.0%	≤ 5.0%
Cabin John MS	943	≤ 5.0%	10.7%	27.1%	9.1%	48.7%	8.7%	≤ 5.0%	≤ 5.0%
Herbert Hoover MS	1058	6.7%	7.0%	29.8%	5.6%	50.9%	≤ 5.0%	≤ 5.0%	5.3%
Bells Mill ES	611	6.1%	11.3%	25.4%	8.2%	48.9%	9.5%	7.7%	5.9%
Beverly Farms ES	621	6.6%	7.1%	28.8%	8.5%	48.8%	5.6%	6.6%	6.6%
Potomac ES	474	≤ 5.0%	≤ 5.0%	32.7%	≤ 5.0%	54.0%	≤ 5.0%	6.5%	≤ 5.0%
Seven Locks ES	398	8.3%	8.3%	17.8%	10.3%	54.5%	5.5%	11.6%	≤ 5.0%
Wayside ES	533	5.8%	6.4%	36.4%	5.6%	45.6%	≤ 5.0%	11.4%	5.9%
Elementary Cluster Total	**2637**	**6.3%**	**7.6%**	**28.6%**	**7.2%**	**50.0%**	**5.4%**	**8.6%**	**5.7%**
Elementary County Total	75,144	≤ 5.0%	21.2%	13.9%	30.4%	29.3%	40.2%	23.3%	13.3%

**Percent of students approved for Free and Reduced-priced Meals Program (FARMS) during the 2014–2015 school year.*

***Percent of English for Speakers of Other Languages (ESOL) during the 2014–2015 school year. High School students are served in regional ESOL centers.*

****Mobility Rate is the number of entries plus withdrawals during the 2013–2014 school year compared to total enrollment.*
Notes: Native Hawaiian/Pacific Islander and American Indian/Alaskan Native categories total less than 1% and were therefore excluded from the table.

Due to federal and state guidelines, demographic characteristics of schools of less than or equal to 5.0% are reported as ≤ 5.0%.


Program Capacity Table

(School Year 2014–2015)

Schools	Grades Served	Capacity (HS @90% MS@85%)	Total Rooms	Support Rooms	Regular Secondary @25	Regular Elementary @23	CSR Grades 1–2 @18	Pre–K @20	Pre–K @40	HS @20	CSR KIND @18	KIND @22	ESOL @15	METS @15	Special Education Services: School Based HSM @13	School Based ELEM LAD @13	Cluster Based ELC @10	Quad Cluster Based LANG @12	Quad Cluster Based LFI @10	Quad Cluster Based SCB @6	County & Regional Based AAC@7	County & Regional Based AUT @6	County & Regional Based BRIDGE @10	County & Regional Based DHOH @7	County & Regional Based ED @10	County & Regional Based EXTENSIONS @6	County & Regional Based GT/LD @13	County & Regional Based PD @7	County & Regional Based PEP@6	County & Regional Based PEP @12	County & Regional Based PEP @18	County & Regional Based VISION (Elementary) @7	County & Regional Based OTHER
Winston Churchill HS	9-12	2013	94		87								1									2	5										
Cabin John MS	6-8	1129	57		51														2	1		2											
Herbert Hoover MS	6-8	1139	56		52																		4										
Bells Mill ES	HS-5	626	32	3		22				1		4										2											
Beverly Farms ES	K-5	690	35	4		26						3				2																	
Potomac ES	K-5	424	22	3		15						3			1																		
Seven Locks ES	K-5	425	23	4		16						2			1																		
Wayside ES	K-5	671	36	4		25						3								2									1	1			

Facility Characteristics of Schools 2014–2015

Schools	Year Facility Opened	Year Reopened/ Revitalized	Total Square Footage	Site Size Acres	Adjacent Park	Reloc-atable Classrooms	Linkages to Learning Program	Home School Model
Winston Churchill HS	1964	2001	322,078	30.3				
Cabin John MS	1967	2011	159,514	18.2				
Herbert Hoover MS	1966	2013	165,367	19.1				
Bells Mill ES	1968	2009	77,244	9.6				
Beverly Farms ES	1965	2013	98,916	5	Yes			
Potomac ES	1949	1976	57,713	9.6		5		Yes
Seven Locks ES	1964	2012	66,915	9.9				Yes
Wayside ES	1969		77,507	9.3				

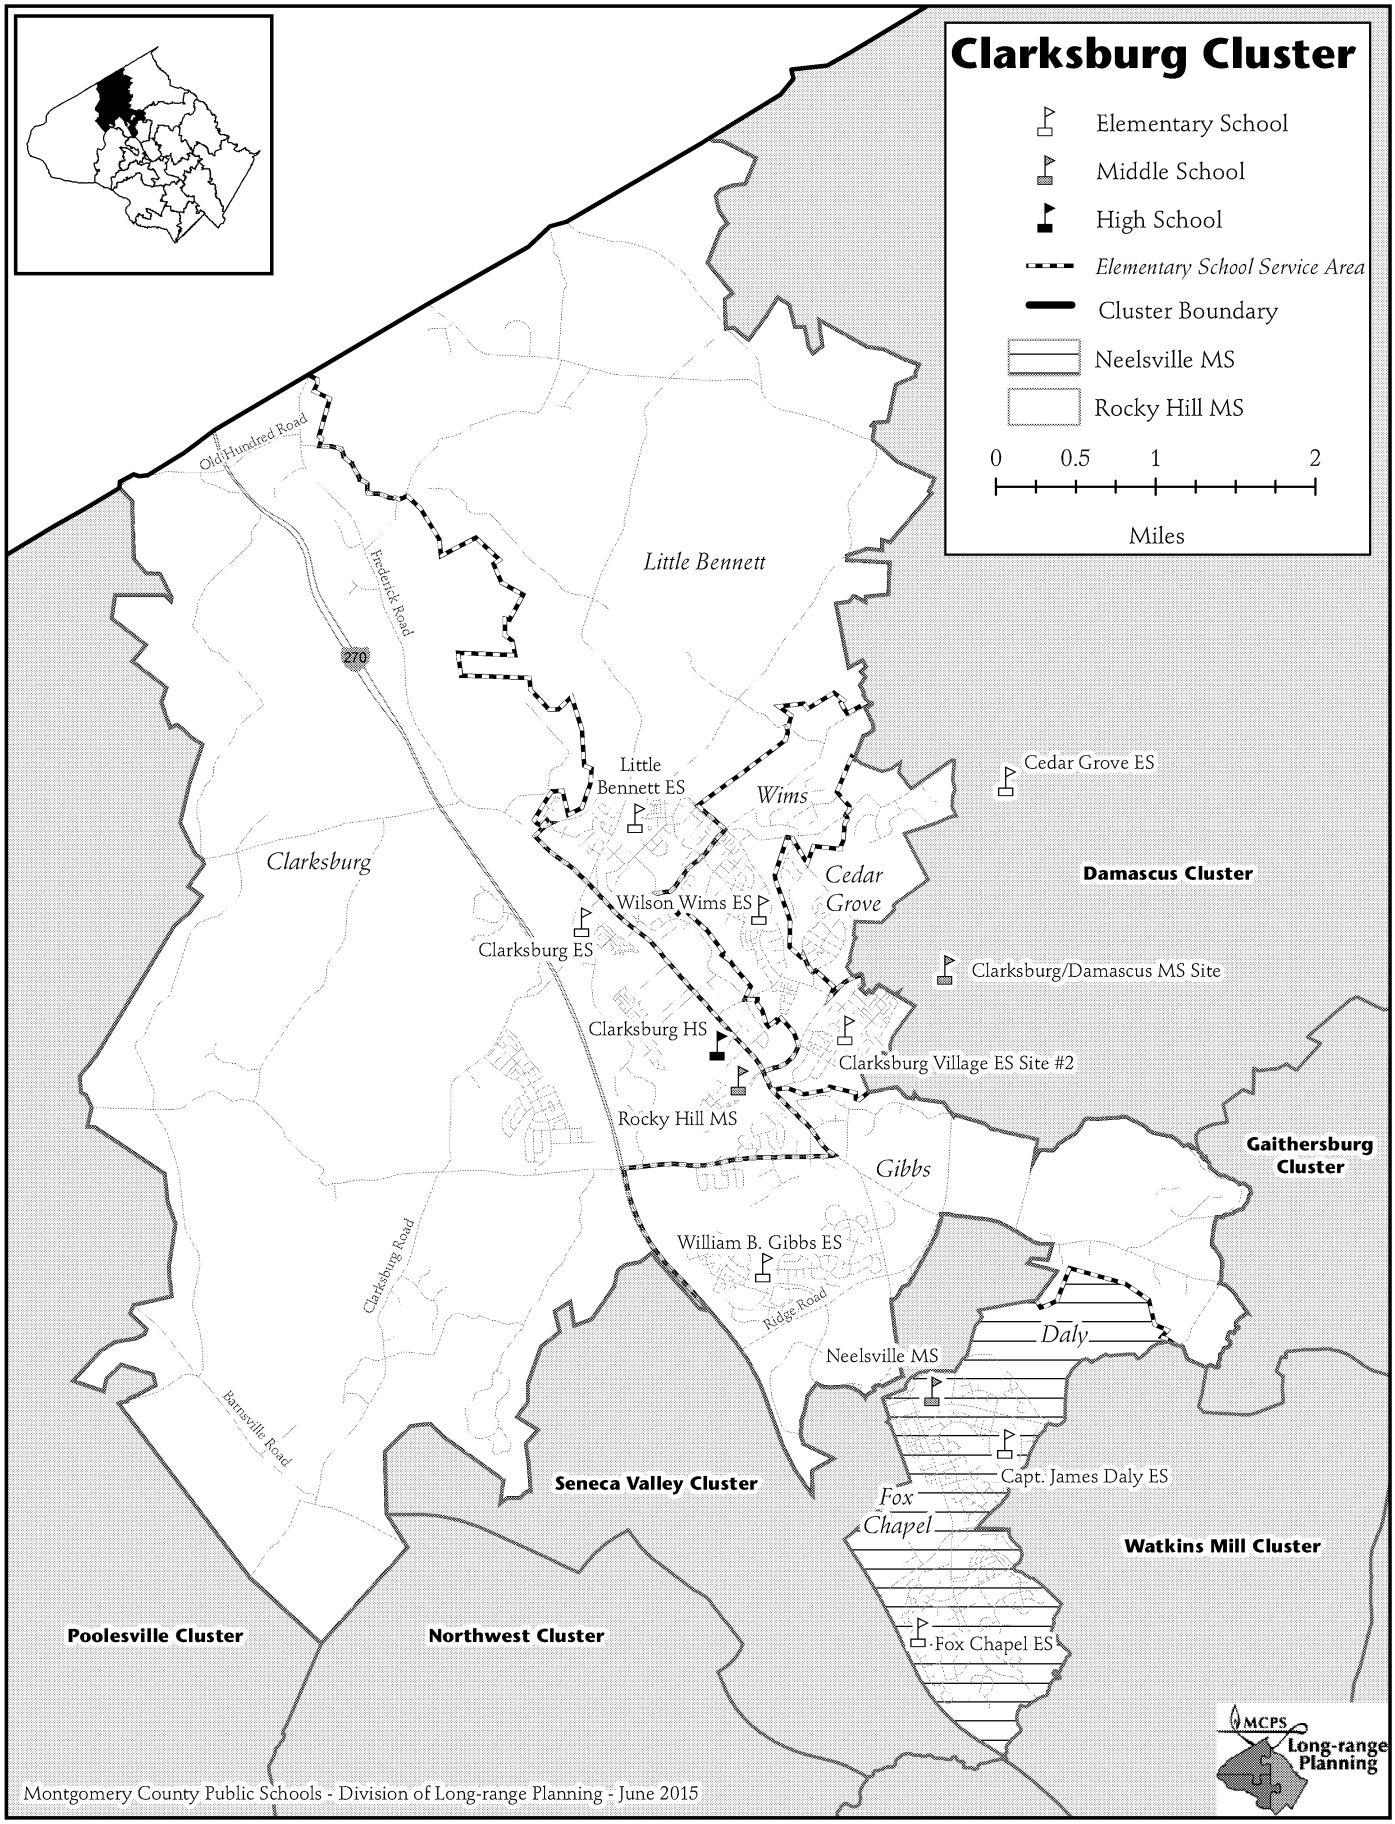
Clarksburg Cluster
Elementary School
Middle School
High School
Elementary School Service Area
Cluster Boundary
Neelsville MS
Rocky Hill MS
0 0.5 1 2
Miles
Old Hundred Road
Frederick Road
270
Little Bennett
Little Bennett ES
Wims
Cedar Grove ES
Damascus Cluster
Clarksburg
Cedar Grove
Wilson Wims ES
Clarksburg ES
Clarksburg/Damascus MS Site
Clarksburg HS
Clarksburg Village ES Site #2
Rocky Hill MS
Gaithersburg Cluster
Gibbs
William B. Gibbs ES
Clarksburg Road
Ridge Road
Daly
Neelsville MS
Capt. James Daly ES
Barnesville Road
Seneca Valley Cluster
Fox Chapel
Watkins Mill Cluster
Fox Chapel ES
Poolesville Cluster
Northwest Cluster
MCPS
Long-range Planning
Montgomery County Public Schools - Division of Long-range Planning - June 2015

CLUSTER PLANNING ISSUES

Planning Issue: The Clarksburg Master Plan allows for the development of up to 15,000 residential units. The plan includes five future elementary school sites and one future middle school site. A large number of housing units have been constructed. A new cluster of schools was formed in the 2006–2007 school year when Clarksburg High School opened to accommodate the enrollment growth from the new development. Little Bennett Elementary School opened in August 2006, William B. Gibbs, Jr. Elementary School opened in August 2009, and Wilson Wims Elementary School opened in August 2014. To address the enrollment growth in the cluster, a high school addition is scheduled to open in August 2015, and a new middle school is scheduled to open in August 2016. With continued growth in elementary school enrollment, another new elementary school will be needed in the near future.

SCHOOLS

Clarksburg High School

Planning Issue: Although a classroom addition is scheduled to open in August 2015 to accommodate the overutilization at Clarksburg High School, student enrollment will continue to exceed capacity by nearly 500 students by the end of the six-year planning period. Enrollment also is projected to exceed capacity at Northwest High School by nearly 300 students. The Seneca Valley High School service area is adjacent to the Clarksburg and Northwest high school service areas. A revitalization/expansion project of Seneca Valley High School, approved for completion in August 2019, will be designed and constructed with a capacity for 2400 students. The enrollment at Seneca Valley High School is projected to be 1395 students by the end of the six-year planning period. With a capacity of 2400 seats, there will be approximately 1000 seats available to accommodate students from Clarksburg and Northwest high schools when the project is complete.

Capital Project: Projections indicate that enrollment at Clarksburg High School will exceed capacity throughout the six-year period. An FY 2014 appropriation was approved for construction funds to construct the classroom addition project. The scheduled completion date for the addition is August 2015.

Clarksburg/Damascus Middle School


Capital Project: Projections indicate that enrollment at Rocky Hill Middle School will exceed capacity throughout the six-year CIP period. A new school is needed to address middle school space deficits in the cluster. The scheduled completion date for the new school is August 2016. An FY 2015 appropriation was approved to construct the new school.

Planning Study: A boundary study was approved to determine the service area for Clarksburg/Damascus Middle School. Representatives from Montgomery Village, Neelsville, and Rocky Hill middle schools participated in the boundary advisory study in spring 2015 with Board of Education action in November 2015.

Neelsville Middle School

Capital Project: Projections indicate enrollment at Neelsville Middle School will exceed capacity by 150 seats or more by the end of the six-year period. An FY 2015 appropriation was approved for facility planning to determine the feasibility, scope, and cost for a classroom addition. The need for the

Clarksburg Cluster Articulation*




* "Cluster" is defined as the collection of elementary schools that articulate to the same high school.

* South Lake Elementary School and a portion of Stedwick Elementary School also articulate to Neelsville Middle School but thereafter to Watkins Mill High School.

** Portions of Cedar Grove and Wilson Wims Elementary Schools also articulates to Damascus High School.

Clarksburg Cluster

School Utilizations

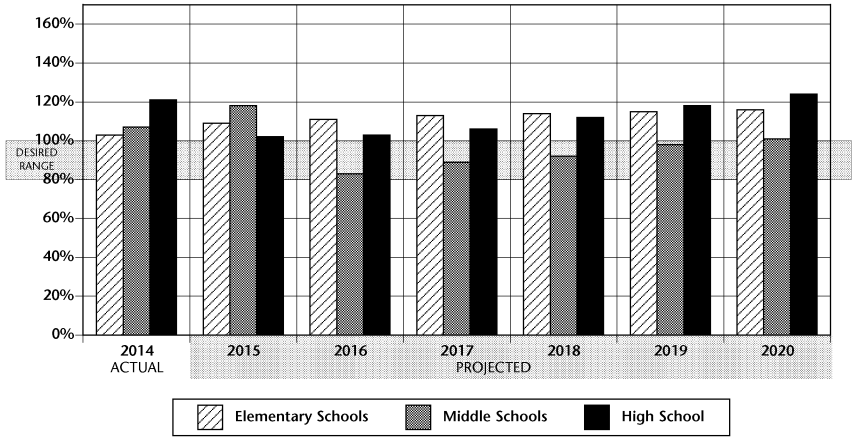

Note: Percent utilization calculated as total enrollment of schools divided by total capacity. Projected capacity factors in capital projects.

addition will determined after the outcome of the boundary study for the Clarksburg/Damascus Middle School. If enrollment continues to exceed capacity by 150 seats or more after the boundaries are set for the new school, a date for the addition will be considered in a future CIP. Relocatable classrooms will be utilized until additional capacity can be added.

Planning Study: A boundary study is approved to determine the service area for Clarksburg/Damascus Middle School. Representatives from Montgomery Village, Neelsville, and Rocky Hill middle schools will participate in the boundary advisory study. The boundary advisory study will take place in spring 2015 with Board of Education action in November 2015.

Rocky Hill Middle School

Capital Project: Projections indicate that enrollment at Rocky Hill Middle School will exceed capacity throughout the six-year CIP period. The scheduled completion date for the new school is August 2016. An FY 2015 appropriation was approved to construct the new school. Relocatable classrooms are being utilized until the additional capacity is added.

Planning Study: A boundary study is approved to determine the service area for Clarksburg/Damascus Middle School. Representatives from Montgomery Village, Neelsville, and Rocky Hill middle schools will participate in the boundary advisory study. The boundary advisory study will take place in spring 2015 with Board of Education action in November 2015.

Cedar Grove Elementary School

Utilization: Enrollment is projected to exceed capacity by more than 92 seats throughout the six-year CIP period. Although the opening of Wilson Wims Elementary School provided some relief, current projections indicate the need for another elementary school in the Clarksburg Cluster. Relocatable classrooms will be utilized until a new school opens in the Clarksburg cluster.

Capital Project: A site has been approved for a new elementary school in the Clarksburg Cluster. An FY 2015 appropriation was approved for facility planning for a feasibility study to determine the scope and cost for a new elementary school. An opening date for this school will be determined in a future CIP.

Clarksburg Elementary School

Utilization: Enrollment at Clarksburg Elementary School is projected to exceed capacity by more than 92 seats throughout the six-year CIP period. Relocatable classrooms will be utilized until a new school opens in the Clarksburg Cluster.

Capital Project: A site has been approved for a new elementary school in the Clarksburg Cluster. An FY 2015 appropriation was approved for facility planning for a feasibility study to determine the scope and cost for a new elementary school. An opening date for this school will be determined in a future CIP.

Clarksburg Cluster Elementary School (Clarksburg Village Site #2)

Capital Project: Clarksburg Village Site #2 was approved as the site for this new elementary school. Prior to identifying a site for this school, the school was referred to as Clarksburg Elementary School #8. With an approved site, the school is now identified as Clarksburg Cluster Elementary School (Clarksburg Village Site #2) until a permanent name is chosen by the Board of Education. An FY 2015 appropriation was approved for facility planning for a feasibility study to determine the scope and cost for another new elementary school. An opening date for this school will be determined in a future CIP.

Capt. James E. Daly Elementary School

Capital Project: Because projections indicated enrollment at Capt. James E. Daly Elementary School would exceed capacity by 92 seats or more by the end of the six-year period, an FY 2012 appropriation was approved for facility planning to determine the feasibility, scope, and cost for a classroom addition. Due to fiscal constraints in the county and because the current enrollment did not exceed capacity by more than 150 seats by the end of the six-year planning period when the FY 2015–2020 CIP was prepared in the fall 2013, no funds were programmed in the current CIP for a classroom addition. A date for the addition will be considered in a future CIP. Relocatable classrooms will be utilized until additional capacity can be added.

Wilson Wims Elementary School

Utilization: Enrollment at Wilson Wims Elementary School is projected to exceed capacity by 92 seats or more throughout the six-year period. Relocatable classrooms will be utilized until a new school opens in the Clarksburg Cluster.

Capital Project: A site was approved for a new elementary school in the Clarksburg Cluster. An FY 2015 appropriation was approved for facility planning for a feasibility study to determine the scope and cost for a new elementary school. An opening date for this school will be determined in a future CIP.

CAPITAL PROJECTS

School	Project	Project Status*	Date of Completion
Clarksburg HS	Classroom addition	Approved	Aug. 2015
Clarksburg/ Damascus MS	New school	Approved	Aug. 2016
Neelsville MS	Classroom addition	Proposed	TBD
Clarksburg ES (Clarksburg Village Site #2)	New school	Proposed	TBD
Capt. James E. Daly ES	Classroom addition	Proposed	TBD

"Approved"— Project has an FY 2015 or FY 2016 appropriation approved in the FY 2015–2020 CIP.

"Deferred"—Funds have been deferred for a future CIP.

"Programmed"—Project has expenditures programmed in a future year of the CIP for planning and/or construction funds.

"Proposed"—Project has facility planning funds approved for FY 2015 or approved for FY 2016 for a feasibility study.

Projected Enrollment and Space Availability

Effects of the Amended FY2015–2020 CIP and Non–CIP Actions on Space Available

Schools			Actual 14–15	Projections 15–16	16–17	17–18	18–19	19–20	20–21	2024	2029
Clarksburg HS		Program Capacity	1638	1980	1980	1980	1980	1980	1980	1980	1980
		Enrollment	**1974**	**2010**	**2033**	**2103**	**2222**	**2332**	**2458**	**2600**	**2900**
		Available Space	*(336)*	*(30)*	*(53)*	*(123)*	*(242)*	*(352)*	*(478)*	*(620)*	*(920)*
		Comments	See text	Addition Complete							
Clarksburg/Damascus MS		Program Capacity			965	965	965	965	965	965	965
		Enrollment			**0**	**0**	**0**	**0**	**0**	**0**	**0**
		Available Space			*965*	*965*	*965*	*965*	*965*	*965*	*965*
		Comments	Boundary Study		Opens Aug. 2016						
Neelsville MS		Program Capacity	922	922	922	922	922	922	922	922	922
		Enrollment	**914**	**953**	**977**	**997**	**1060**	**1132**	**1128**	**1200**	**1100**
		Available Space	8	(31)	(55)	(75)	(138)	(210)	(206)	(278)	(178)
		Comments	Boundary Study Fac. Plng for Addition								
Rocky Hill MS		Program Capacity	995	995	995	995	995	995	995	995	995
		Enrollment	**1133**	**1312**	**1408**	**1563**	**1599**	**1698**	**1778**	**1900**	**2100**
		Available Space	*(138)*	*(318)*	*(414)*	*(568)*	*(604)*	*(704)*	*(784)*	*(905)*	*(1105)*
		Comments	Boundary Study								
Cedar Grove ES		Program Capacity	405	405	405	405	405	405	405		
		Enrollment	**641**	**649**	**674**	**686**	**697**	**690**	**690**		
		Available Space	*(236)*	*(244)*	*(269)*	*(281)*	*(292)*	*(285)*	*(285)*		
		Comments	See text								
Clarksburg ES		Program Capacity	312	312	312	312	312	312	312		
		Enrollment	**305**	**329**	**363**	**397**	**440**	**468**	**506**		
		Available Space	7	(17)	(51)	(85)	(128)	(156)	(194)		
		Comments	See text								
Clarksburg Cluster ES (Clarksburg Village #2)		Program Capacity									
		Enrollment									
		Available Space									
		Comments	Facility Planning for new school								
Capt. James E. Daly ES	CSR	Program Capacity	518	518	518	518	518	518	518		
		Enrollment	**593**	**591**	**617**	**611**	**596**	**604**	**600**		
		Available Space	*(75)*	*(73)*	*(99)*	*(93)*	*(78)*	*(86)*	*(82)*		
		Comments									
Fox Chapel ES	CSR	Program Capacity	683	683	683	683	683	683	683		
		Enrollment	**601**	**604**	**615**	**614**	**600**	**591**	**606**		
		Available Space	*82*	*79*	*68*	*69*	*83*	*92*	*77*		
		Comments									
William B. Gibbs, Jr. ES		Program Capacity	740	740	740	740	740	740	740		
		Enrollment	**778**	**757**	**761**	**751**	**747**	**750**	**733**		
		Available Space	*(38)*	*(17)*	*(21)*	*(11)*	*(7)*	*(10)*	*7*		
		Comments									
Little Bennett ES		Program Capacity	*676*	*676*	*676*	*676*	*676*	*676*	*676*		
		Enrollment	**691**	**628**	**608**	**620**	**614**	**619**	**615**		
		Available Space	*(15)*	*48*	*68*	*56*	*62*	*57*	*61*		
		Comments									
Wilson Wims ES		Program Capacity	759	754	754	754	754	754	754		
		Enrollment	**660**	**880**	**919**	**954**	**977**	**971**	**972**		
		Available Space	*99*	*(126)*	*(165)*	*(200)*	*(223)*	*(217)*	*(218)*		
		Comments	Opens See text	+1 PEP							
Cluster Information		HS Utilization	121%	102%	103%	106%	112%	118%	124%	131%	146%
		HS Enrollment	1974	2010	2033	2103	2222	2332	2458	2600	2900
		MS Utilization	107%	118%	83%	89%	92%	98%	101%	108%	111%
		MS Enrollment	2047	2265	2385	2560	2659	2830	2906	3100	3200
		ES Utilization	103%	109%	111%	113%	114%	115%	116%	120%	127%
		ES Enrollment	4269	4438	4557	4633	4671	4693	4722	4900	5200

Demographic Characteristics of Schools

Schools	2014–2015 Total Enrollment	Two or more races %	Black or Afr. Amer. %	Asian%	Hispanic %	White %	2014–2015 FARMS%*	ESOL%**	2013–2014 Mobility Rate%***
Clarksburg HS	1974	≤ 5.0%	27.9%	17.7%	25.6%	24.3%	30.0%	≤ 5.0%	10.8%
Neelsville MS	914	≤ 5.0%	34.6%	7.9%	44.6%	8.5%	64.0%	16.7%	16.7%
Rocky Hill MS	1133	5.4%	22.1%	26.3%	16.2%	29.9%	20.3%	≤ 5.0%	9.0%
Cedar Grove ES	641	5.6%	10.6%	36.3%	10.8%	36.0%	12.5%	9.4%	13.1%
Clarksburg ES	307	7.2%	14.7%	36.2%	13.7%	27.7%	15.0%	15.3%	9.4%
Captain James Daly ES	593	≤ 5.0%	33.7%	5.6%	46.0%	10.6%	70.0%	37.9%	17.4%
Fox Chapel ES	601	≤ 5.0%	27.3%	19.3%	40.1%	9.3%	51.1%	29.0%	12.5%
William B. Gibbs Jr. ES	778	6.7%	25.2%	29.0%	16.8%	22.2%	30.8%	13.1%	10.4%
Little Bennett ES	691	8.1%	16.2%	30.2%	11.1%	34.0%	16.1%	9.3%	6.6%
Wilson Wims ES	662	7.3%	14.8%	40.3%	11.5%	25.8%	11.0%	9.4%	%
Elementary Cluster Total	**4273**	**6.1%**	**20.7%**	**28.0%**	**21.3%**	**23.7%**	**31.8%**	**18.3%**	**11.3%**
Elementary County Total	**75,144**	**≤ 5.0%**	**21.2%**	**13.9%**	**30.4%**	**29.3%**	**40.2%**	**23.3%**	**13.3%**

**Percent of students approved for Free and Reduced-priced Meals Program (FARMS) during the 2014–2015 school year.*

***Percent of English for Speakers of Other Languages (ESOL) during the 2014–2015 school year. High School students are served in regional ESOL centers.*

****Mobility Rate is the number of entries plus withdrawals during the 2013–2014 school year compared to total enrollment.*
Notes: Native Hawaiian/Pacific Islander and American Indian/Alaskan Native categories total less than 1% and were therefore excluded from the table.

Due to federal and state guidelines, demographic characteristics of schools of less than or equal to 5.0% are reported as ≤ 5.0%.


Program Capacity Table

(School Year 2014–2015)

Schools	Grades Served	Capacity (HS @90% MS@85%)	Total Rooms	Support Rooms	Regular Secondary @25	Regular Elementary @23	CSR Grades 1–2 @18	Pre–K @20	Pre–K @40	HS @20	CSR KIND @18	KIND @22	ESOL @15	METS @15	Special Education Services: School Based: HSM @13	ELEM LAD @13	Quad Cluster Based: ELC @10	LANG @12	LFI @10	SCB @6	County & Regional Based: AAC@7	AUT @6	BRIDGE @10	DHOH @7	ED @10	EXTENSIONS @6	GT/LD @13	PD @7	PEP@6	PEP @12	PEP @18	VISION (Elementary) @7	OTHER
Clarksburg HS	9-12	1638	75		71								1												3								
Neelsville MS	6-8	922	45		41								3	1																			
Rocky Hill MS	6-8	995	48		46																				2								
Cedar Grove ES	K-5	405	25	5		13						4										3											
Clarksburg ES	K-5	312	19	4		9						3				3																	
Captain James Daly ES	PreK-5	518	32	5		5	12		1		6					3																	
Fox Chapel ES	PreK-5	683	36	4		17	9		1		5																						
William B. Gibbs Jr. ES	K-5	740	37	4		23			1			5			1														1	2			
Little Bennett ES	K-5	676	34	4		25						4			1																		
Wilson Wims ES	K-5	759	37	3		27						6																1					

Facility Characteristics of Schools 2014–2015

Schools	Year Facility Opened	Year Reopened/ Revitalized	Total Square Footage	Site Size Acres	Adjacent Park	Reloc-atable Classrooms	Linkages to Learning Program	Home School Model
Clarksburg HS	1995	2006	344,574	62.73		11		
Neelsville MS	1981		131,432	29.2				
Rocky Hill MS	2004		148,065	23.3		11		
Cedar Grove ES	1960	1987	57,037	10.1		7		
Clarksburg ES	1952	1993	54,983	9.97		4		
Captain James Daly ES	1989		78,210	10	Yes	4		
Fox Chapel ES	1974		85,182	10.34	Yes		Yes	Yes
William B. Gibbs Jr. ES	2009		88,042	10.75				Yes
Little Bennett ES	2006		82,511	4.81	Yes	4		Yes
Wilson Wims ES	2014		91,931	9.29	Yes			

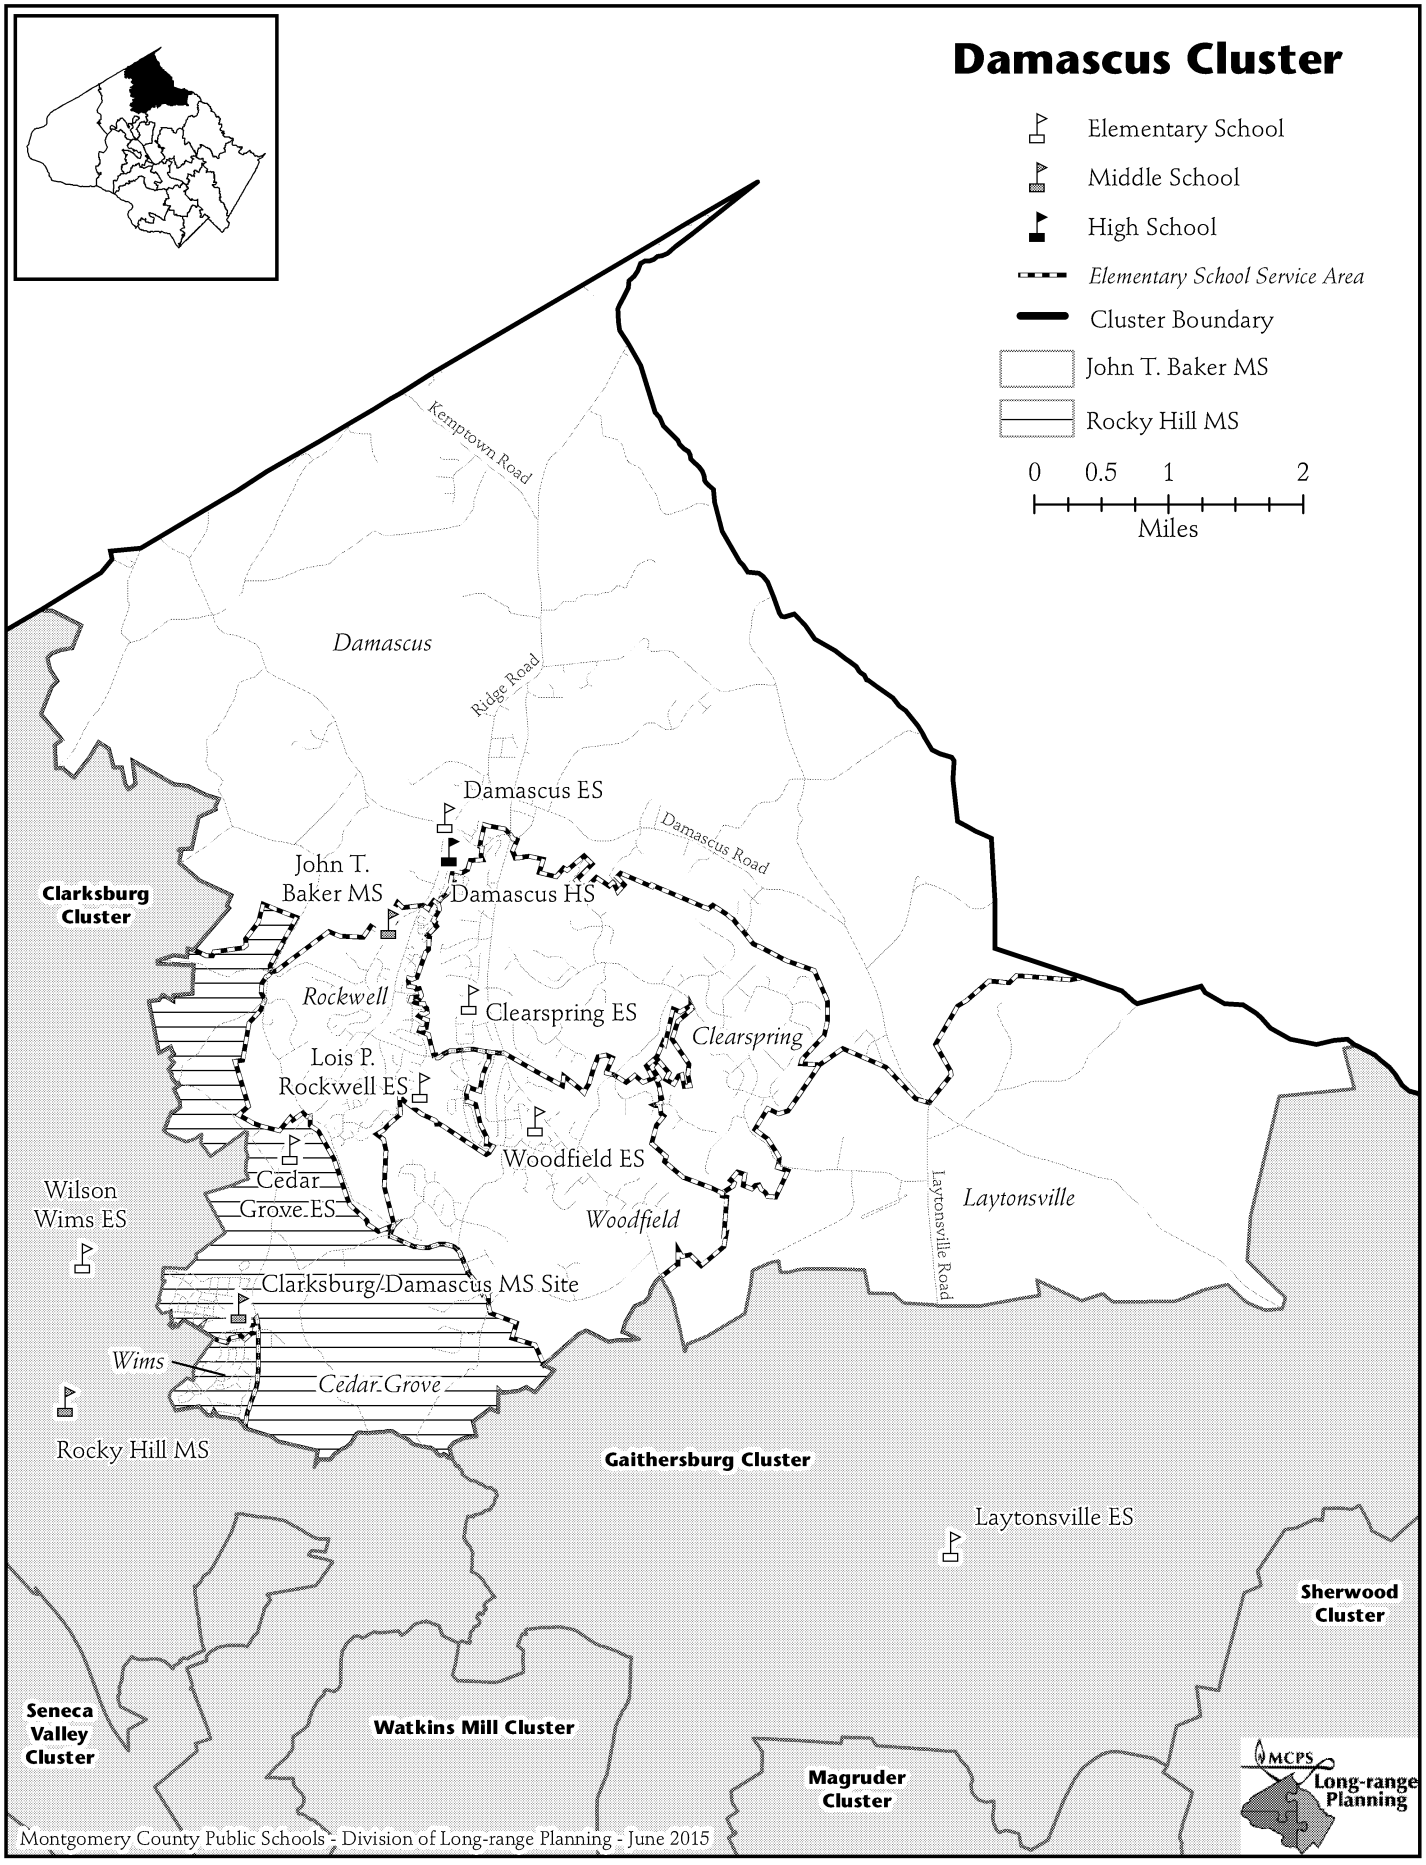
Damascus Cluster
Elementary School
Middle School
High School
Elementary School Service Area
Cluster Boundary
John T. Baker MS
Rocky Hill MS
0 0.5 1 2
Miles
Kemptown Road
Damascus
Ridge Road
Damascus ES
Damascus Road
John T. Baker MS
Damascus HS
Clarksburg Cluster
Rockwell
Clearspring ES
Clearspring
Lois P. Rockwell ES
Woodfield ES
Cedar Grove ES
Wilson Wims ES
Woodfield
Laytonsville
Laytonsville Road
Clarksburg/Damascus MS Site
Wims
Cedar Grove
Rocky Hill MS
Gaithersburg Cluster
Laytonsville ES
Sherwood Cluster
Seneca Valley Cluster
Watkins Mill Cluster
Magruder Cluster
MCPS
Long-range Planning
Montgomery County Public Schools - Division of Long-range Planning - June 2015

SCHOOLS

Clarksburg/Damascus Middle School

Capital Project: Projections indicate that enrollment at Rocky Hill Middle School will exceed capacity throughout the six-year CIP period. A new school is needed to address middle school space deficits in the cluster. The scheduled completion date for the new school is August 2016. An FY 2015 appropriation was approved to construct the new school.

Planning Study: A boundary study was approved to determine the service area for Clarksburg/Damascus Middle School. Representatives from Montgomery Village, Neelsville, and Rocky Hill middle schools participated in the boundary advisory study in spring 2015 with Board of Education action in November 2015.

Cedar Grove Elementary School

Utilization: Enrollment is projected to exceed capacity by more than 92 seats throughout the six-year CIP period. Although the opening of Wilson Wims Elementary School provided some relief, current projections indicate the need for another elementary school in the Clarksburg Cluster. Relocatable classrooms will be utilized until a new school opens in the Clarksburg cluster.

Capital Project: A site was approved for a new elementary school in the Clarksburg Cluster. An FY 2015 appropriation was approved for facility planning for a feasibility study to determine the scope and cost for a new elementary school. An opening date for this school will be determined in a future CIP.

Damascus Elementary School

Capital Project: A revitalization/expansion project is scheduled for this school. Although the Board of Education requested a completion date of January 2022, the County Council maintained the approved FY 2015–2020 CIP completion date of January 2023. FY 2017 expenditures are programmed for facility planning for a feasibility study to determine the scope and cost of the project. In order for this project to be completed on this schedule, county and state funding must be provided at the levels approved in this CIP.

CAPITAL PROJECTS

School	Project	Project Status*	Date of Completion
Clarksburg/ Damascus MS	New school	Approved	Aug. 2016
Damascus ES	Revitalization/ expansion	Programmed	Jan. 2023

"Approved"— Project has an FY 2015 or FY 2016 appropriation approved in the FY 2015–2020 CIP.

"Deferred"—Funds have been deferred for a future CIP.

"Programmed"—Project has expenditures programmed in a future year of the CIP for planning and/or construction funds.

"Proposed"—Project has facility planning funds approved for FY 2015 or approved for FY 2016 for a feasibility study.

Damascus Cluster Articulation*

Damascus High School

John T. Baker MS	Rocky Hill MS
Clearspring ES	Cedar Grove ES**
Damascus ES	Wilson Wims ES**
Laytonsville ES***	
Lois P. Rockwell ES	
Woodfield ES	

* "Cluster" is defined as the collection of elementary schools that articulate to the same high school.


* Clarksburg Elementary School and Little Bennett Elementary School also articulate to Rocky Hill Middle School but thereafter to Clarksburg High School.

** Portions of Cedar Grove and Wilson Wims Elementary Schools articulate to Clarksburg High School.

***Most of Laytonsville Elementary School articulates to Gaithersburg Middle School and Gaithersburg High School.

Damascus Cluster

School Utilizations

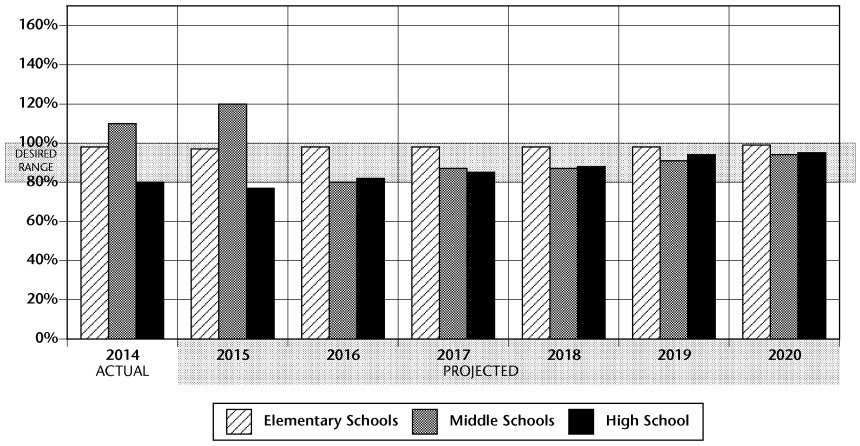

Note: Percent utilization calculated as total enrollment of schools divided by total capacity. Projected capacity factors in capital projects.

Projected Enrollment and Space Availability

Effects of the Amended FY2015–2020 CIP and Non–CIP Actions on Space Available

Schools			Actual 14–15	Projections 15–16	16–17	17–18	18–19	19–20	20–21	2024	2029
Damascus HS		Program Capacity	1551	1551	1551	1551	1551	1551	1551	1551	1551
		Enrollment	**1246**	**1197**	**1269**	**1324**	**1371**	**1453**	**1467**	**1550**	**1450**
		Available Space	*305*	*354*	*282*	*227*	*180*	*98*	*84*	*1*	*101*
		Comments									
John T. Baker MS		Program Capacity	741	741	741	741	741	741	741	741	741
		Enrollment	**772**	**776**	**766**	**776**	**759**	**758**	**754**	**800**	**750**
		Available Space	*(31)*	*(35)*	*(25)*	*(35)*	*(18)*	*(17)*	*(13)*	*(59)*	*(9)*
		Comments									
Clarksburg/Damascus MS		Program Capacity			965	965	965	965	965	965	965
		Enrollment			**0**	**0**	**0**	**0**	**0**	**0**	**0**
		Available Space			*965*	*965*	*965*	*965*	*965*	*965*	*965*
		Comments	Planning for new school		Opens Aug. 2016						
Rocky Hill MS		Program Capacity	995	995	995	995	995	995	995	995	995
		Enrollment	**1133**	**1312**	**1408**	**1563**	**1599**	**1698**	**1778**	**1900**	**2100**
		Available Space	*(138)*	*(318)*	*(414)*	*(568)*	*(604)*	*(704)*	*(784)*	*(905)*	*(1105)*
		Comments	Boundary Study								
Cedar Grove ES		Program Capacity	405	405	405	405	405	405	405		
		Enrollment	**641**	**649**	**674**	**686**	**697**	**690**	**690**		
		Available Space	*(236)*	*(244)*	*(269)*	*(281)*	*(292)*	*(285)*	*(285)*		
		Comments									
Clearspring ES		Program Capacity	642	639	639	639	639	639	639		
		Enrollment	**624**	**621**	**626**	**610**	**602**	**611**	**601**		
		Available Space	*18*	*18*	*13*	*29*	*37*	*28*	*38*		
		Comments		+1 preK							
Damascus ES		Program Capacity	328	328	328	328	328	328	328		
		Enrollment	**297**	**299**	**301**	**284**	**292**	**288**	**300**		
		Available Space	*31*	*29*	*27*	*44*	*36*	*40*	*28*		
		Comments			Facility Planning for Rev/Ex		Planning for Revitalization/ Expansion				
Lois P. Rockwell ES		Program Capacity	523	523	523	523	523	523	523		
		Enrollment	**456**	**444**	**449**	**450**	**445**	**446**	**444**		
		Available Space	*67*	*79*	*74*	*73*	*78*	*77*	*79*		
		Comments									
Woodfield ES		Program Capacity	471	471	471	471	471	471	471		
		Enrollment	**302**	**284**	**280**	**279**	**284**	**288**	**306**		
		Available Space	*169*	*187*	*191*	*192*	*187*	*183*	*165*		
		Comments									
Cluster Information		HS Utilization	80%	77%	82%	85%	88%	94%	95%	100%	93%
		HS Enrollment	1246	1197	1269	1324	1371	1453	1467	1550	1450
		MS Utilization	110%	120%	80%	87%	87%	91%	94%	100%	106%
		MS Enrollment	1905	2088	2174	2339	2358	2456	2532	2700	2850
		ES Utilization	98%	97%	98%	98%	98%	98%	99%	101%	101%
		ES Enrollment	2320	2297	2330	2309	2320	2323	2341	2400	2400

Demographic Characteristics of Schools

Schools	2014–2015 Total Enrollment	Two or more races %	Black or Afr. Amer. %	Asian%	Hispanic %	White %	2014–2015 FARMS%*	ESOL%**	2013–2014 Mobility Rate%***
Damascus HS	1246	≤ 5.0%	10.8%	5.7%	16.5%	62.1%	16.7%	≤ 5.0%	≤ 5.0%
John T Baker MS	772	5.1%	8.2%	6.3%	18.1%	61.8%	16.5%	≤ 5.0%	7.4%
Rocky Hill MS	1133	5.4%	22.1%	26.3%	16.2%	29.9%	20.3%	≤ 5.0%	9.0%
Cedar Grove ES	641	5.6%	10.6%	36.3%	10.8%	36.0%	12.5%	9.4%	13.1%
Clearspring ES	624	8.2%	13.5%	14.6%	20.5%	43.3%	24.5%	9.0%	6.3%
Damascus ES	297	≤ 5.0%	6.7%	≤ 5.0%	22.6%	62.0%	25.3%	11.4%	10.5%
Lois P. Rockwell ES	456	6.1%	11.8%	9.9%	21.5%	50.4%	22.6%	12.3%	9.5%
Woodfield ES	302	7.0%	13.2%	≤ 5.0%	18.5%	56.0%	19.2%	5.3%	≤ 5.0%
Elementary Cluster Total	**2320**	**6.3%**	**11.5%**	**17.0%**	**18.0%**	**46.7%**	**19.3%**	**9.1%**	**9.2%**
Elementary County Total	75,144	≤ 5.0%	21.2%	13.9%	30.4%	29.3%	40.2%	23.3%	13.3%

**Percent of students approved for Free and Reduced-priced Meals Program (FARMS) during the 2014–2015 school year.*

***Percent of English for Speakers of Other Languages (ESOL) during the 2014–2015 school year. High School students are served in regional ESOL centers.*

****Mobility Rate is the number of entries plus withdrawals during the 2013–2014 school year compared to total enrollment.*
Notes: Native Hawaiian/Pacific Islander and American Indian/Alaskan Native categories total less than 1% and were therefore excluded from the table.

Due to federal and state guidelines, demographic characteristics of schools of less than or equal to 5.0% are reported as ≤ 5.0%.


Program Capacity Table


(School Year 2014–2015)

Schools	Grades Served	Capacity (HS @90% MS@85%)	Total Rooms	Support Rooms	Regular Secondary @25	Regular Elementary @23	CSR Grades 1–2 @18	Pre–K @20	Pre–K @40	HS @20	CSR KIND @18	KIND @22	ESOL @15	METS @15	Special Education Services: School Based: HSM @13	ELEM LAD @13	Cluster Based: ELC @10	Quad Cluster Based: LANG @12	LFI @10	SCB @6	County & Regional Based: AAC@7	AUT @6	BRIDGE @10	DHOH @7	ED @10	EXTENSIONS @6	GT/LD @13	PD @7	PEP@6	PEP @12	PEP @18	VISION (Elementary) @7	OTHER
Damascus HS	9-12	1551	74		67														3	3													1
John T Baker MS	6-8	741	37		34														1	2													
Rocky Hill MS	6-8	995	48		46																				2								
Cedar Grove ES	K-5	405	25	5		13						4										3											
Clearspring ES	HS-5	642	34	3		22				1		3					5																
Damascus ES	K-5	328	21	4		11						2			1					3													
Lois P. Rockwell ES	K-5	523	29	4		17						3																	1	3		1
Woodfield ES	K-5	471	24	3		17						2																		2		

Facility Characteristics of Schools 2014–2015

Schools	Year Facility Opened	Year Reopened/ Revitalized	Total Square Footage	Site Size Acres	Adjacent Park	Reloc-atable Classrooms	Linkages to Learning Program	Home School Model
Damascus HS	1950	1978	235,986	32.7				
John T Baker MS	1971		120,532	22	Yes			
Rocky Hill MS	2004		148,065	23.3		11		
Cedar Grove ES	1960	1987	57,037	10.1		7		
Clearspring ES	1988		77,535	10	Yes			
Damascus ES	1934	1980	53,239	9.4				Yes
Lois P. Rockwell ES	1992		75,520	10.6				
Woodfield ES	1962	1985	53,212	10				

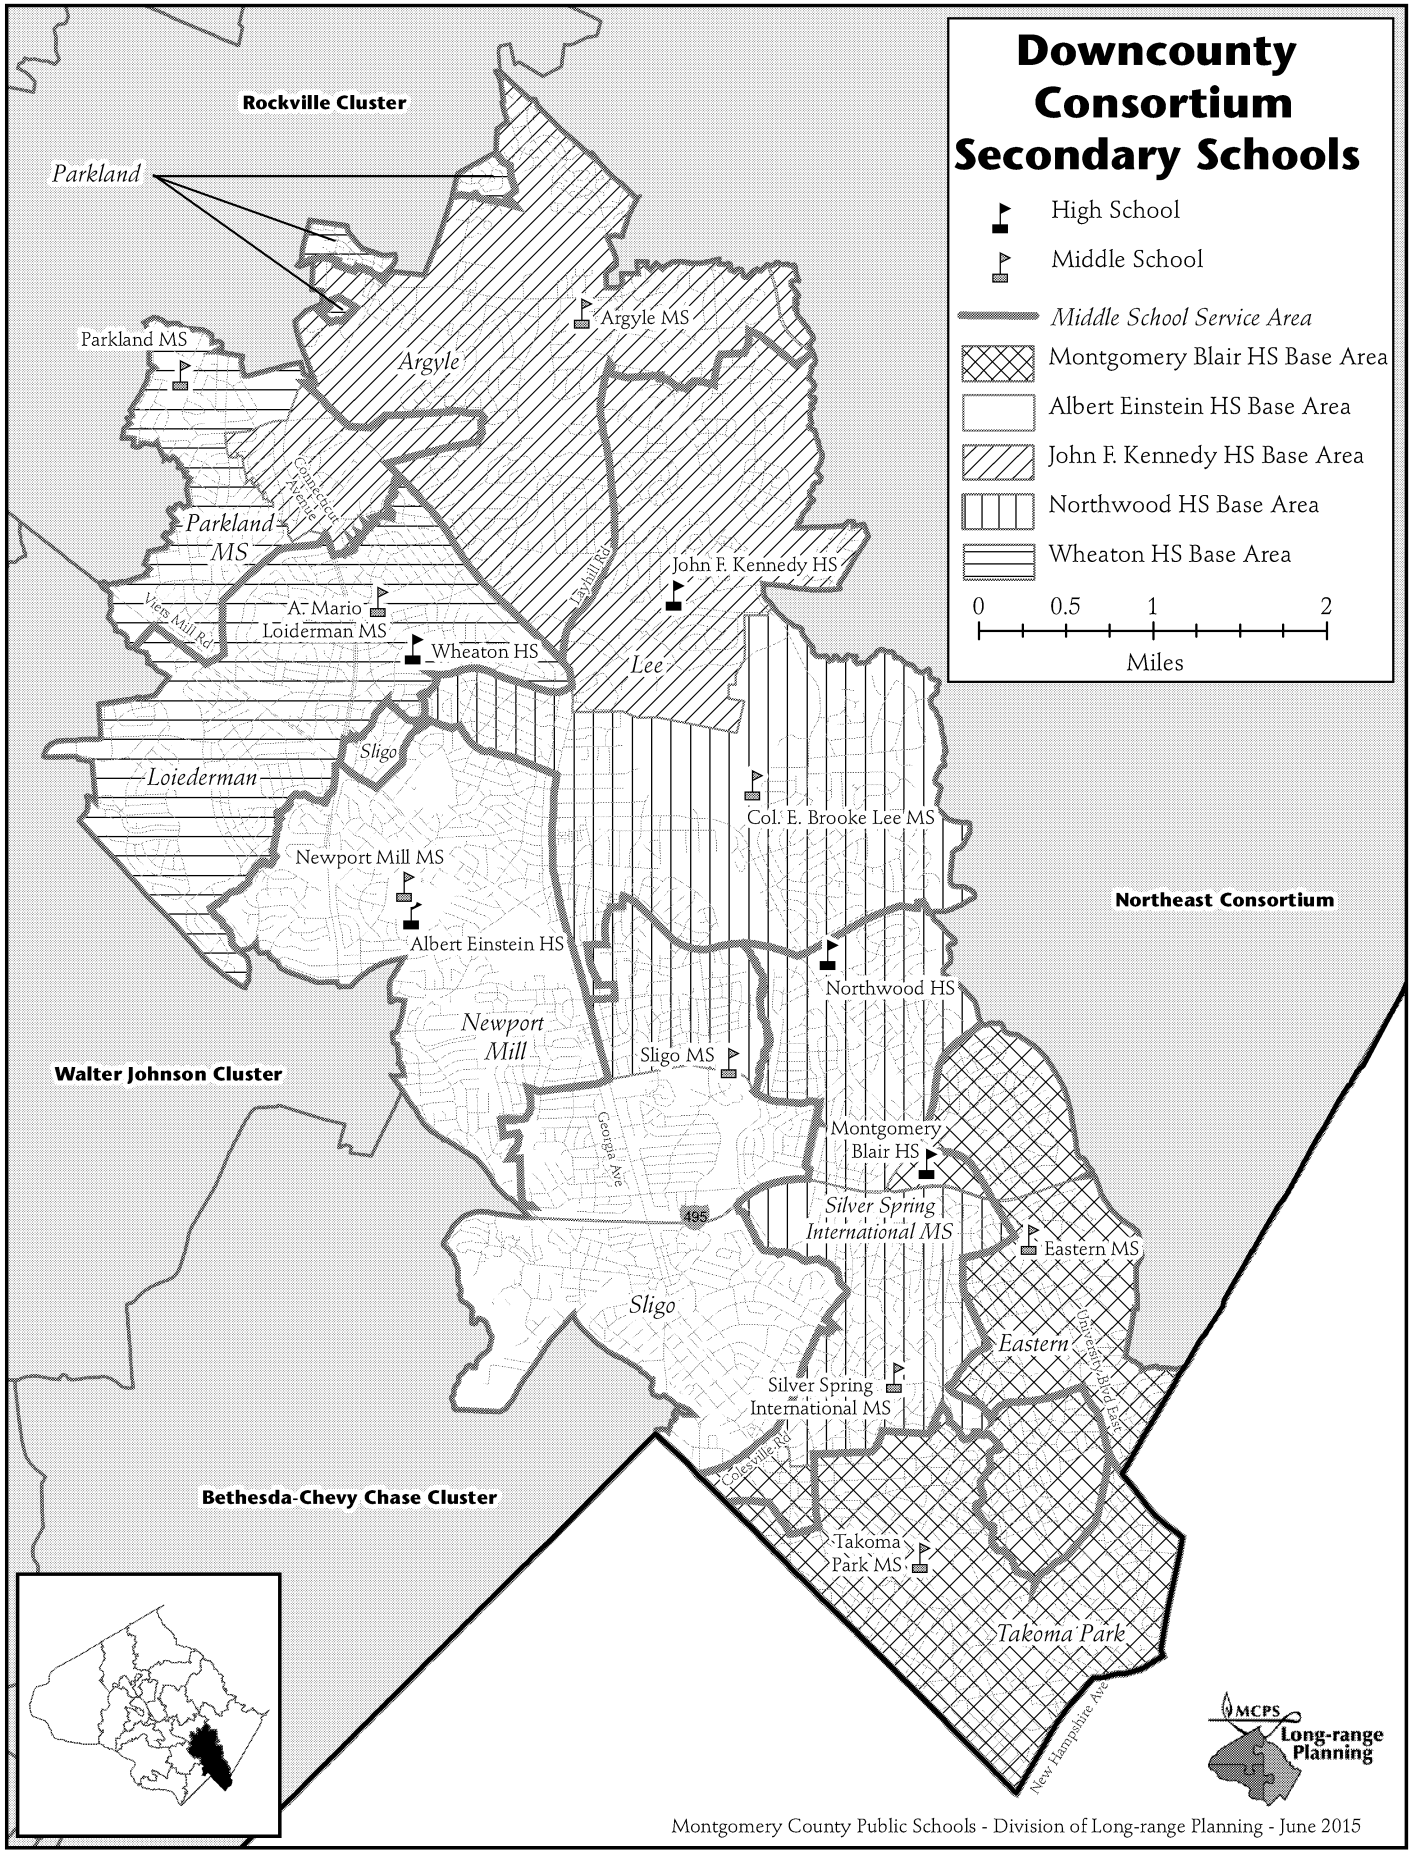
Downcounty Consortium Secondary Schools
High School
Middle School
Middle School Service Area
Montgomery Blair HS Base Area
Albert Einstein HS Base Area
John F. Kennedy HS Base Area
Northwood HS Base Area
Wheaton HS Base Area
0 0.5 1 2
Miles
Rockville Cluster
Parkland
Parkland MS
Argyle
Argyle MS
Connecticut Avenue
Parkland MS
Viers Mill Rd
A. Mario Loiderman MS
Wheaton HS
Layhill Rd
John F. Kennedy HS
Lee
Sligo
Loiederman
Col. E. Brooke Lee MS
Newport Mill MS
Albert Einstein HS
Northeast Consortium
Northwood HS
Newport Mill
Sligo MS
Walter Johnson Cluster
Georgia Ave
Montgomery Blair HS
Silver Spring International MS
495
Eastern MS
Sligo
Eastern
University Blvd East
Silver Spring International MS
Colesville Rd
Bethesda-Chevy Chase Cluster
Takoma Park MS
Takoma Park
New Hampshire Ave
MCPS
Long-range Planning
Montgomery County Public Schools - Division of Long-range Planning - June 2015

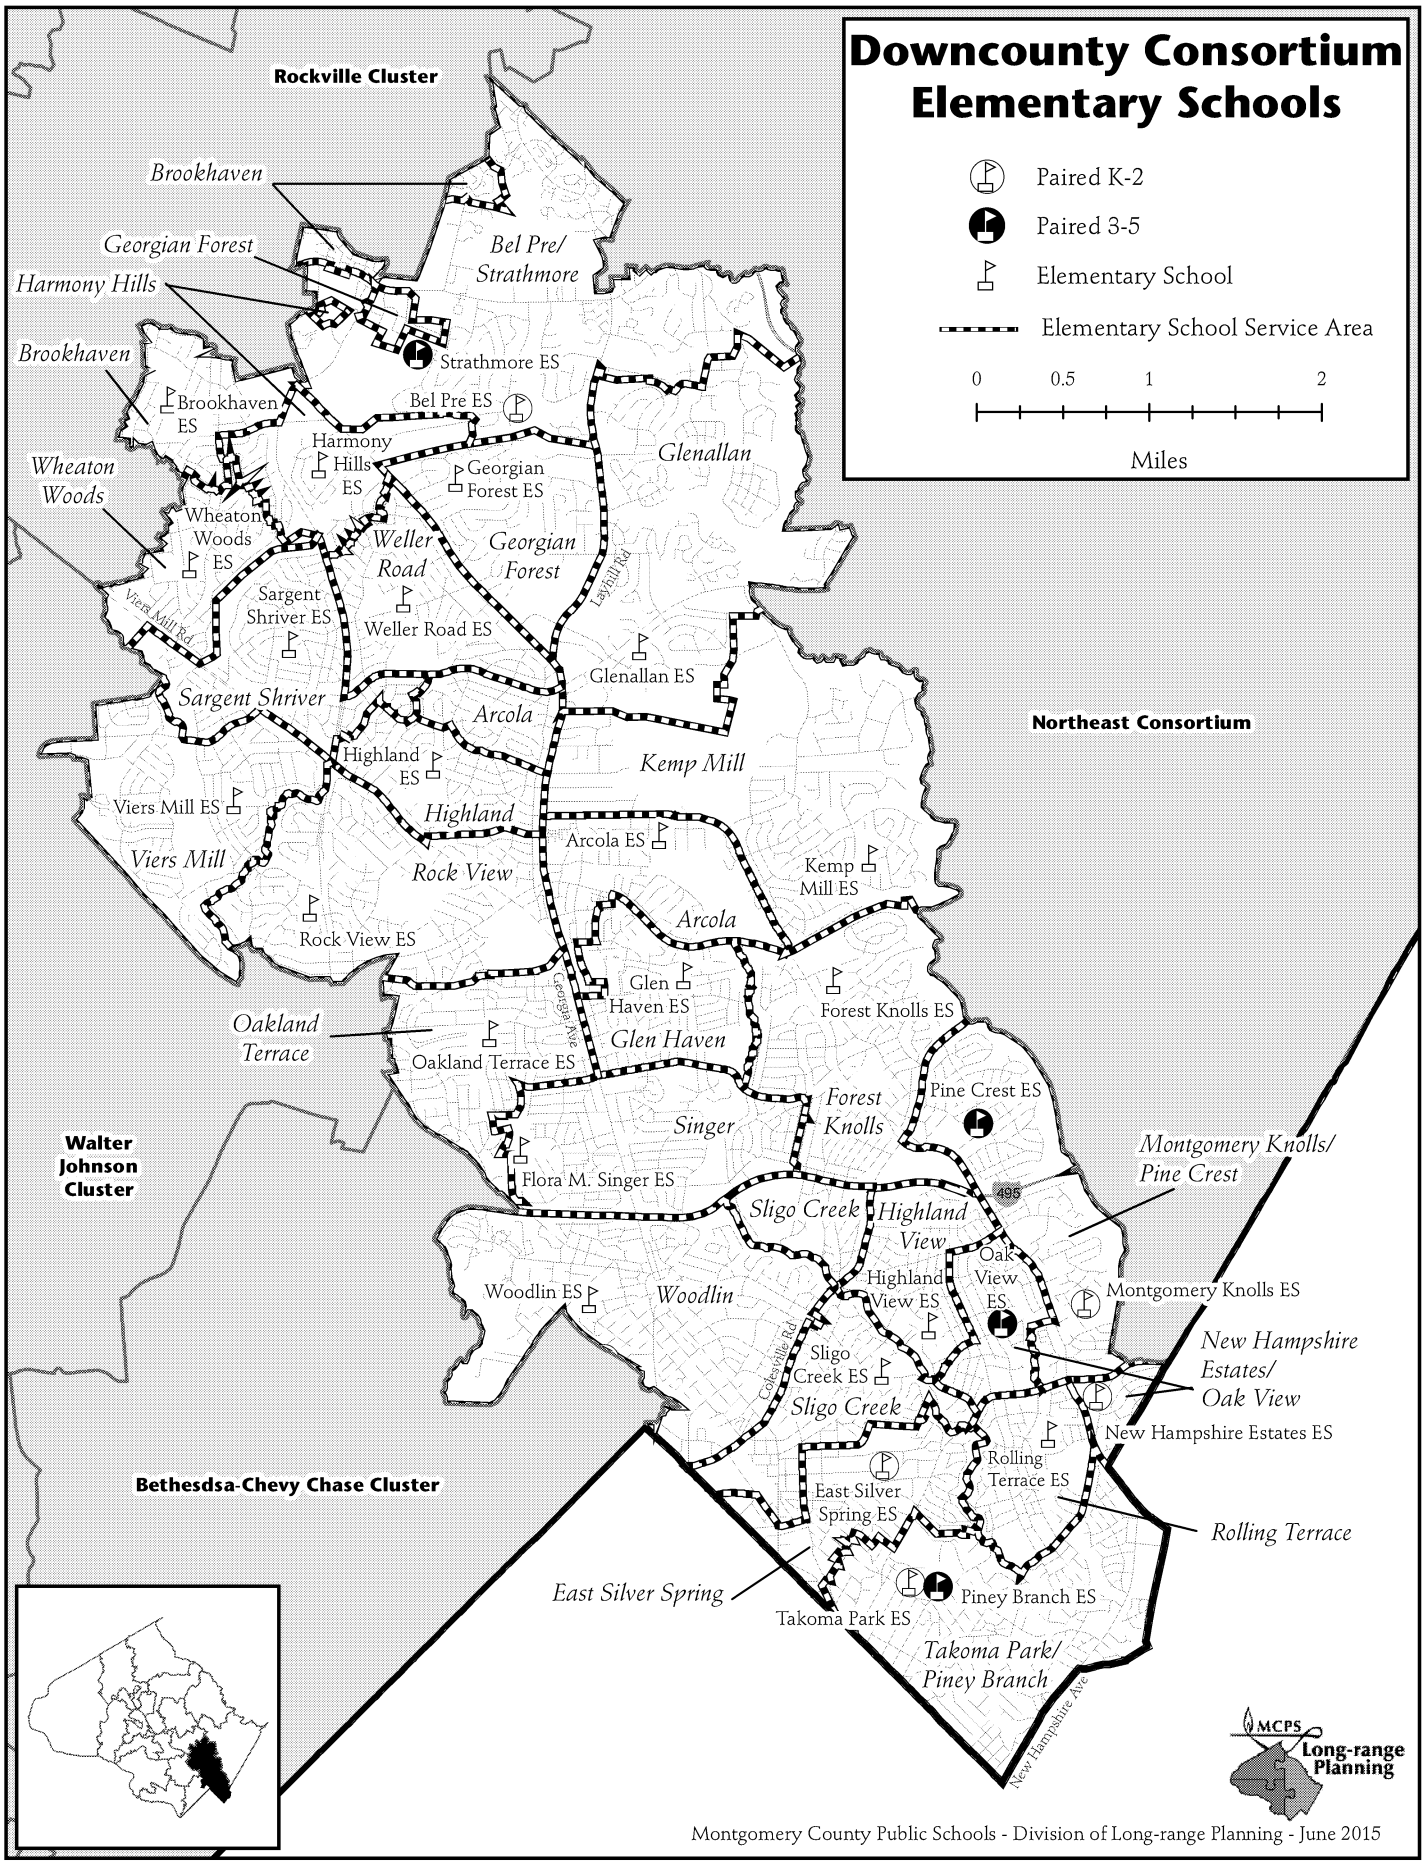
Downcounty Consortium Elementary Schools
Paired K-2
Paired 3-5
Elementary School
Elementary School Service Area
0
0.5
1
2
Miles
Rockville Cluster
Brookhaven
Georgian Forest
Harmony Hills
Brookhaven
Wheaton Woods
Bel Pre/ Strathmore
Strathmore ES
Brookhaven ES
Bel Pre ES
Harmony Hills ES
Georgian Forest ES
Glenallan
Wheaton Woods ES
Weller Road
Georgian Forest
Layhill Rd
Viers Mill Rd
Sargent Shriver ES
Weller Road ES
Glenallan ES
Sargent Shriver
Arcola
Northeast Consortium
Highland ES
Kemp Mill
Viers Mill ES
Highland
Arcola ES
Viers Mill
Rock View
Kemp Mill ES
Arcola
Rock View ES
Glen Haven ES
Forest Knolls ES
Georgia Ave
Oakland Terrace
Glen Haven
Oakland Terrace ES
Forest Knolls
Pine Crest ES
Singer
Walter Johnson Cluster
Flora M. Singer ES
Montgomery Knolls/ Pine Crest
Sligo Creek
Highland View
495
Oak View ES
Highland View ES
Woodlin ES
Woodlin
Montgomery Knolls ES
Colesville Rd
Sligo Creek ES
New Hampshire Estates/ Oak View
Sligo Creek
New Hampshire Estates ES
Rolling Terrace ES
East Silver Spring ES
Bethesdsa-Chevy Chase Cluster
Rolling Terrace
East Silver Spring
Piney Branch ES
Takoma Park ES
Takoma Park/ Piney Branch
New Hampshire Ave
MCPS
Long-range Planning
Montgomery County Public Schools - Division of Long-range Planning - June 2015

CONSORTIUM PLANNING ISSUES

The Downcounty Consortium provides a program delivery model for five high schools in the Silver Spring and Wheaton areas. Students living in this area of the county are able to choose from five high schools they wish to attend, based on different academy programs offered at the high schools. The Downcounty Consortium choice programs are offered at Montgomery Blair, Albert Einstein, John F. Kennedy, Northwood, and Wheaton high schools. Choice patterns are monitored for the impact on projected enrollment and facility utilization.

A high school base area map and middle school articulation diagram are included for the five consortium high schools. Students residing in a base area are guaranteed to attend the high school located serving that base area, if it is their first choice.

The Middle Schools Magnet Consortium (MSMC) includes three middle schools—Argyle, A. Mario Loiederman, and Parkland middle schools. The programs at these schools are open to all middle school students in the county.


Planning Issue: The Downcounty Consortium includes three recent land use plans that will add a large number of multi-family housing units in the future. The 2012 adopted Wheaton Sector Plan provides for up to 7,060 mostly multi-family residential units. The majority of these housing units require the redevelopment of the Westfield Wheaton Mall. The 2013 adopted Glenmont Sector Plan provides for up to 5,800 mostly multi-family residential units. This plan requires the redevelopment of existing land uses, including the Glenmont Shopping Center, to achieve build-out density. The 2013 adopted Long Branch Sector Plan provides for up to 3,200 mostly multi-family residential units. This plan requires the redevelopment of existing land uses and funding for the Purple Line to achieve build-out density. It is anticipated that the three sector plans will take 20 to 30 years to build-out, and the pace of construction will be market driven. A future elementary school site is included in the Glenmont Sector Plan.

Planning Issue: There has been significant enrollment growth in the Downcounty Consortium since 2007. This growth began at the elementary schools where many schools no longer have the space to accommodate the projected enrollment and has now approached the secondary school levels. To address the overutilization of elementary schools in the midsection of the Downcounty Consortium, a comprehensive capacity study was conducted during the 2012–2013 school year. The following schools were included in the scope of the study: Arcola, Brookhaven, Forest Knolls, Georgian Forest, Glen Haven, Glenallan, Harmony Hills, Highland, Kemp Mill, Sargent Shriver, Weller Road, and Wheaton Woods elementary schools. Based on the findings of this study, five classroom addition projects are approved in the CIP. The addition projects are located at Brookhaven, Glen Haven, Highland, Kemp Mill and Sargent Shriver elementary schools. These additions, along with space that is available at Georgian Forest and Weller Road elementary schools, will address the overutilization issues at Arcola, Highland, Kemp Mill, and Sargent Shriver elementary schools. Boundary studies will be conducted prior to the opening of the five new additions. Although Forest Knolls Elementary School was included in the midsection comprehensive study, a solution for this school will be developed as part of a second comprehensive capacity study in the lower portion of the Downcounty Consortium described below.

A second comprehensive capacity study was approved for the lower portion of the Downcounty Consortium to address enrollment growth in this area. The comprehensive capacity study for this area was conducted during the 2014–2015 school year. This capacity study included the following schools: East Silver Spring, Forest Knolls, Highland View, Montgomery Knolls, New Hampshire Estates, Oak View, Pine Crest, Piney Branch, Rolling Terrace, Sligo Creek, Takoma Park, and Woodlin elementary schools. A plan to address the overutilization of schools in this area will be considered as part of the FY 2017–2022 CIP.

At the middle school level, facility planning funds were approved for feasibility studies to determine the scope, cost, and feasibility of classroom additions at the following schools: Col. E. Brooke Lee, A. Mario Loiederman, Parkland, Silver Spring International, and Takoma Park middle schools. Completion dates for these additions will be considered in a future CIP after the feasibility studies are conducted.

At the high school level, enrollment is projected to exceed capacity by the end of the six-year planning period at all five high schools. A comprehensive capacity study is approved for the Downcounty Consortium high schools to study the

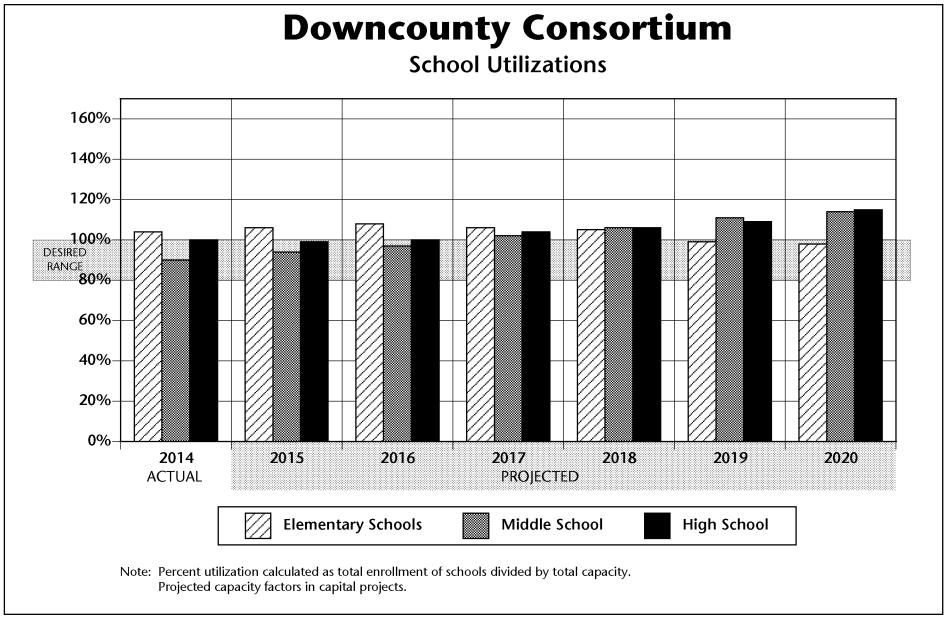

possibility of adding capacity to the Downcounty Consortium through classroom additions at Montgomery Blair, Albert Einstein, John F. Kennedy, and/or Northwood high schools. As part of the revitalization/expansion project at Wheaton High School, the building shell of the master-planned addition is being constructed as part of the ongoing project. Constructing the building shell during ongoing construction will enable classrooms to be built-out in the future when enrollment pressures require additional capacity.

SCHOOLS

Montgomery Blair High School

Planning Study: A comprehensive capacity study is approved for the Downcounty Consortium high schools to study the possibility of adding capacity through classroom additions at Montgomery Blair, Albert Einstein, John F. Kennedy, and/or Northwood high schools. As part of the revitalization/expansion project at Wheaton High School, the building shell of the master-planned addition is being constructed as part of the ongoing project. Constructing the building shell during ongoing construction will enable classrooms to be built-out in the future when high schools in the Downcounty Consortium require additional capacity. An FY 2016 appropriation for facility planning is approved for the capacity study. A plan to address the overutilization of the high schools will be considered as part of the FY 2017–2022 CIP.

Albert Einstein High School

Planning Study: A comprehensive capacity study is approved for the Downcounty Consortium high schools to study the possibility of adding capacity through classroom additions at Montgomery Blair, Albert Einstein, John F. Kennedy, and/or Northwood high schools. As part of the revitalization/expansion project at Wheaton High School, the building shell of the master-planned addition is being constructed as part of the ongoing project. Constructing the building shell during ongoing construction will enable classrooms to be built-out in the future when high schools in the Downcounty Consortium require additional capacity. An FY 2016 appropriation for facility planning is approved for the capacity study. A plan to address the overutilization of the high schools will be considered as part of the FY 2017–2022 CIP.


John F. Kennedy High School

Planning Study: A comprehensive capacity study is approved for the Downcounty Consortium high schools to study the possibility of adding capacity through classroom additions at Montgomery Blair, Albert Einstein, John F. Kennedy, and/or Northwood high schools. As part of the revitalization/expansion project at Wheaton High School, the building shell of the master-planned addition is being constructed as part of the ongoing project. Constructing the building shell during ongoing construction will enable classrooms to be built-out in the future when high schools in the Downcounty Consortium require additional capacity. An FY 2016 appropriation for facility planning is approved for the capacity study. A plan to address the overutilization of the high schools will be considered as part of the FY 2017–2022 CIP.

Capital Project: An FY 2016 appropriation is approved in the Department of Health and Human Services (DHHS) Capital Budget for a feasibility study of a School-based Wellness Center at John F. Kennedy High School. This study will be completed as part of the comprehensive capacity study. A completion date for this project will be determined in a future DHHS CIP request.

Northwood High School

Planning Study: A comprehensive capacity study is approved for the Downcounty Consortium high schools to study the possibility of adding capacity through classroom additions at Montgomery Blair, Albert Einstein, John F. Kennedy, and/

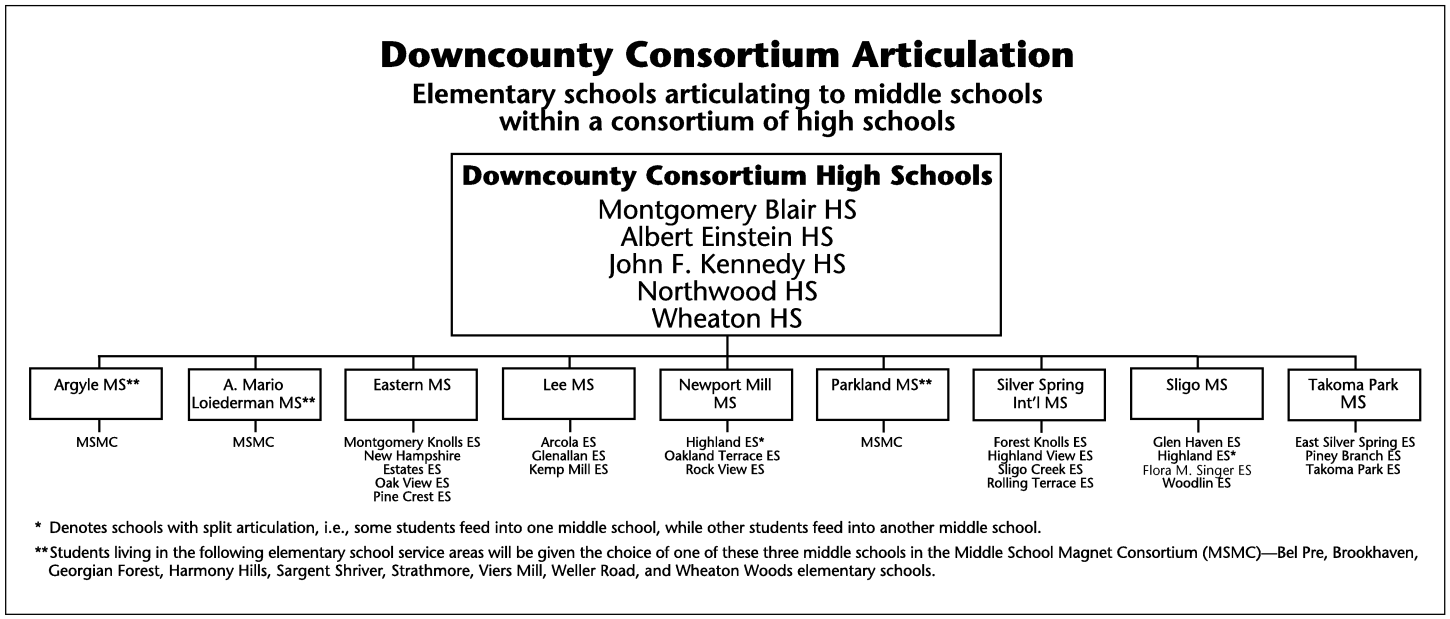

* Denotes schools with split articulation, i.e., some students feed into one middle school, while other students feed into another middle school.

**Students living in the following elementary school service areas will be given the choice of one of these three middle schools in the Middle School Magnet Consortium (MSMC)—Bel Pre, Brookhaven, Georgian Forest, Harmony Hills, Sargent Shriver, Strathmore, Viers Mill, Weller Road, and Wheaton Woods elementary schools.

or Northwood high schools. As part of the revitalization/expansion project at Wheaton High School, the building shell of the master-planned addition is being constructed as part of the ongoing project. Constructing the building shell during ongoing construction will enable classrooms to be built-out in the future when high schools in the Downcounty Consortium require additional capacity. An FY 2016 appropriation for facility planning is approved for the capacity study. A plan to address the overutilization of the high schools will be considered as part of the FY 2017–2022 CIP.

Wheaton High School

Planning Study: Wheaton High School and Thomas Edison High School of Technology (TEHST) are located on the same site and share one facility. These schools are scheduled for revitalization/expansion projects. Two major planning studies were conducted to prepare for the revitalization/expansion projects of these schools. During the fall and winter 2010–2011, a Roundtable Discussion, with broad stakeholder involvement, met to explore various approaches for the future relationship between the two schools. Following the Roundtable review, the Board of Education took action on March 28, 2011, to keep the two schools separate with distinct identities and directed staff to conduct a feasibility study to review two options—a one-building option and a two-building option. At the conclusion of the feasibility study, on September 13, 2011, the Board of Education adopted a two-building option for the revitalization/expansion projects of Wheaton High School and Thomas Edison High School of Technology.

Capital Project: An FY 2014 appropriation for construction funds was approved to construct the replacement facility for Wheaton High School. An FY 2016 appropriation is approved to construct Thomas Edison High School of Technology. The completion dates for these schools are scheduled for January 2016 for the Wheaton High School facility, August 2017 for the Thomas Edison High School of Technology facility, and August 2018 for restoration of the site. In order for these projects to be completed on schedule, county and state funding must be provided at levels approved in this CIP.

Capital Project: An FY 2014 appropriation for construction funds is approved in the Department of Health and Human Services (DHHS) Capital Budget for a School-based Wellness Center at Wheaton High School. The construction of the Wellness Center will coincide with the replacement facility.

Planning Study: A comprehensive capacity study is approved for the Downcounty Consortium high schools to study the possibility of adding capacity through classroom additions at Montgomery Blair, Albert Einstein, John F. Kennedy, and/or Northwood high schools. As part of the revitalization/expansion project at Wheaton High School, the building shell of the master-planned addition is being constructed as part of the ongoing project. Constructing the building shell during ongoing construction will enable classrooms to be built-out in the future when high schools in the Downcounty Consortium require additional capacity. An FY 2016 appropriation for facility planning is approved for the capacity study. A plan to address the overutilization of the high schools will be considered as part of the FY 2017–2022 CIP.

Eastern Middle School

Capital Project: A revitalization/expansion project is scheduled for this school. Although the Board of Education requested a completion of August 2021, the County Council maintained the approved FY 2015–2020 CIP completion date of August 2022. FY 2017 expenditures are programmed for facility planning for a feasibility study to determine the scope and cost of the project. In order for this project to be completed on this schedule, county and state funding must be provided at the levels approved in this CIP.

Col. E. Brooke Lee Middle School

Capital Project: Projections indicate enrollment at Col. E. Brooke Lee Middle School will exceed capacity by 150 seats or more by the end of the six-year period. An FY 2015 appropriation was approved for facility planning to determine the feasibility, scope, and cost for a classroom addition. A date for the addition will be considered in a future CIP. Relocatable classrooms will be utilized until additional capacity can be added.

A. Mario Loiederman Middle School

Capital Project: Projections indicate enrollment at A. Mario Loiederman Middle School will exceed capacity by 150 seats or more by the end of the six-year period. An FY 2014 appropriation was approved for facility planning to determine the feasibility, scope, and cost for a classroom addition. A date for the addition will be considered in a future CIP. Relocatable classrooms will be utilized until additional capacity can be added.

Newport Mill Middle School

Non-capital Solution: On November 17, 2011, the Board of Education adopted boundary changes for Oakland Terrace Elementary School, Newport Mill, and Sligo middle schools, and created the service area for Flora M. Singer Elementary School. The boundary changes for the middle school are being phased in, beginning in the 2014–2015 school year.

Parkland Middle School

Capital Project: Projections indicate enrollment at Parkland Middle School will exceed capacity by 150 seats or more by the end of the six-year period. An FY 2015 appropriation was approved for facility planning to determine the feasibility, scope, and cost for a classroom addition. A date for the addition will be considered in a future CIP. Relocatable classrooms will be utilized until additional capacity can be added.

Silver Spring International Middle School

Capital Project: Projections indicate enrollment at Silver Spring International Middle School will exceed capacity by 150 seats or more by the end of the six-year period. An FY 2015 appropriation was approved for facility planning to determine the feasibility, scope, and cost to provide additional space in the existing facility. A date for the project will be considered in a future CIP. Relocatable classrooms will be utilized until additional capacity can be added.

Sligo Middle School

Non-capital Solution: On November 17, 2011, the Board of Education adopted boundary changes for Oakland Terrace Elementary School, Newport Mill, and Sligo middle schools, and created the service area for Flora M. Singer Elementary School. The boundary changes for the middle school are being phased in, beginning in the 2014–2015 school year.

Takoma Park Middle School

Capital Project: Projections indicate enrollment at Takoma Park Middle School will exceed capacity by 150 seats or more by the end of the six-year period. An FY 2015 appropriation was approved for facility planning to determine the feasibility, scope, and cost for a classroom addition. A date for the addition will be considered in a future CIP. Relocatable classrooms will be utilized until additional capacity can be added.

Arcola Elementary School

Capital Project: An FY 2014 appropriation was approved for the construction of a classroom addition. The scheduled completion date for the addition is August 2015. Even with the addition, the enrollment at Arcola Elementary School will exceed the new capacity. Relocatable classrooms will continue to be utilized until approved additions at other elementary schools in the area are completed. Boundary changes, where needed, will be made when the additional capacity opens.

Capital Project: A comprehensive capacity study to address overutilization at several elementary schools in the midsection of the Downcounty Consortium was conducted during the 2012–2013 school year. The following schools were included in the scope of the study: Arcola, Brookhaven, Forest Knolls, Georgian Forest, Glen Haven, Glenallan, Harmony Hills, Highland, Kemp Mill, Sargent Shriver, Weller Road, and Wheaton Woods elementary schools. Based on the outcome of the study, an FY 2016 appropriation for planning funds are approved to begin the architectural design for five classroom addition projects at Brookhaven, Glen Haven, Highland, Kemp Mill, and Sargent Shriver elementary schools. These projects will address overutilization at Arcola, Harmony Hills, Highland, Kemp Mill, and Sargent Shriver elementary schools. Although the Board of Education requested a completion date of August 2018 for these projects, the County Council maintained the approved FY 2015–2020 CIP completion date of August 2019. In order for these projects to be completed on schedule, county and state funding must be provided at the levels approved in this CIP.

Brookhaven Elementary School

Capital Project: A comprehensive capacity study to address overutilization at several elementary schools in the midsection of the Downcounty Consortium was conducted during the 2012–2013 school year. The following schools were included in the scope of the study: Arcola, Brookhaven, Forest Knolls, Georgian Forest, Glen Haven, Glenallan, Harmony Hills, Highland, Kemp Mill, Sargent Shriver, Weller Road, and Wheaton Woods elementary schools. Based on the outcome of the study, an FY 2016 appropriation for planning funds are approved to begin the architectural design for five classroom addition projects at Brookhaven, Glen Haven, Highland, Kemp Mill, and Sargent Shriver elementary schools. These projects will address overutilization at Arcola, Harmony Hills, Highland, Kemp Mill, and Sargent Shriver elementary schools. Although the Board of Education requested a completion date of August 2018 for these projects, the County Council maintained the approved FY 2015–2020 CIP completion date of August 2019. In order for these projects to be completed on schedule, county and state funding must be provided at the levels approved in this CIP.

East Silver Spring Elementary School

Planning Study: A comprehensive capacity study to address overutilization at several elementary schools in the lower section of the Downcounty Consortium was conducted during the 2014–2015 school year. This capacity study included the following schools: East Silver Spring, Forest Knolls, Highland View, Montgomery Knolls, New Hampshire Estates, Oak View, Takoma Park, Pine Crest, Piney Branch, Rolling Terrace, Sligo Creek, and Woodlin elementary schools.

Forest Knolls Elementary School

Planning Study: Enrollment projections indicate enrollment at Forest Knolls Elementary School will exceed capacity by 92 seats or more throughout the six-year CIP period. A comprehensive capacity study to address overutilization at several elementary schools in the midsection Downcounty Consortium was conducted during the 2012–2013 school year that included Forest Knolls Elementary School. However, due to growth in enrollment in these schools and Forest Knolls Elementary School's proximity to the lower section of the Downcounty Consortium, Forest Knolls Elementary School was included in a second comprehensive capacity study in the lower section of the Downcounty Consortium. The comprehensive capacity study for the lower area was conducted during the 2014–2015 school year. This capacity study included the following schools: East Silver Spring, Forest Knolls, Highland View, Montgomery Knolls, New Hampshire Estates, Oak View, Takoma Park, Pine Crest, Piney Branch, Rolling Terrace, Sligo Creek, and Woodlin elementary schools. A plan to address the overutilization of schools in this area will be considered as part of the FY 2017–2022 CIP.

Glen Haven Elementary School

Capital Project: A comprehensive capacity study to address overutilization at several elementary schools in the midsection of the Downcounty Consortium was conducted during the 2012–2013 school year. The following schools were included in the scope of the study: Arcola, Brookhaven, Forest Knolls, Georgian Forest, Glen Haven, Glenallan, Harmony Hills, Highland, Kemp Mill, Sargent Shriver, Weller Road, and Wheaton Woods elementary schools. Based on the outcome of the study, an FY 2016 appropriation for planning funds are approved to begin the architectural design for five classroom addition projects at Brookhaven, Glen Haven, Highland, Kemp Mill, and Sargent Shriver elementary schools. These projects will address overutilization at Arcola, Harmony Hills, Highland, Kemp Mill, and Sargent Shriver elementary schools. Although the Board of Education requested a completion date of August 2018 for these projects, the County Council maintained the approved FY 2015–2020 CIP completion date of August 2019. In order for these projects to be completed on schedule, county and state funding must be provided at the levels approved in this CIP.

Harmony Hills Elementary School

Capital Project: A comprehensive capacity study to address overutilization at several elementary schools in the midsection of the Downcounty Consortium was conducted during the 2012–2013 school year. The following schools were included in the scope of the study: Arcola, Brookhaven, Forest Knolls, Georgian Forest, Glen Haven, Glenallan, Harmony Hills, Highland, Kemp Mill, Sargent Shriver, Weller Road, and Wheaton Woods elementary schools. Based on the outcome of the study, an FY 2016 appropriation for planning funds are approved to begin the architectural design for five classroom addition projects at Brookhaven, Glen Haven, Highland, Kemp Mill, and Sargent Shriver elementary schools. These projects will address overutilization at Arcola, Harmony Hills, Highland, Kemp Mill, and Sargent Shriver elementary schools. Although Board of Education requested a completion date of August 2018 for these projects, the County Council maintained the approved FY 2015–2020 CIP completion date of August 2019. In order for these projects to be completed on schedule, county and state funding must be provided at the levels approved in this CIP.

Highland Elementary School

Capital Project: A comprehensive capacity study to address overutilization at several elementary schools in the midsection of the Downcounty Consortium was conducted during the 2012–2013 school year. The following schools were included in the scope of the study: Arcola, Brookhaven, Forest Knolls, Georgian Forest, Glen Haven, Glenallan, Harmony Hills, Highland, Kemp Mill, Sargent Shriver, Weller Road, and Wheaton Woods elementary schools. Based on the outcome of the study, an FY 2016 appropriation for planning funds are approved to begin the architectural design for five classroom addition projects at Brookhaven, Glen Haven, Highland, Kemp Mill, and Sargent Shriver elementary schools. These projects will address overutilization at Arcola, Harmony Hills, Highland, Kemp Mill, and Sargent Shriver elementary schools. Although the Board of Education requested a completion date of August 2018 for these projects, the County Council maintained the approved FY 2015–2020 CIP completion date of August 2019. In order for these projects to be completed on schedule, county and state funding must be provided at the levels approved in this CIP.

Highland View Elementary School

Capital Project: Projections indicate enrollment at Highland View Elementary School will exceed capacity by 92 seats or more by the end of the six-year period. FY 2015 expenditures for planning funds were programmed to begin the architectural design of a classroom addition project. However, due to enrollment growth in nearby schools in the lower portion of the Downcounty Consortium, planning for the addition is deferred until a comprehensive plan can be developed from the comprehensive capacity study for the lower portion of the Downcounty Consortium. The comprehensive capacity study for the lower area was conducted during the 2014–2015 school year. This capacity study included the following schools: East Silver Spring, Forest Knolls, Highland View, Montgomery Knolls, New Hampshire Estates, Oak View, Takoma Park, Pine Crest, Piney Branch, Rolling Terrace, Sligo Creek, and Woodlin elementary schools. A plan to address the overutilization of schools in this area will be considered as part of the FY 2017–2022 CIP.

Kemp Mill Elementary School

Capital Project: A comprehensive capacity study to address overutilization at several elementary schools in the midsection of the Downcounty Consortium was conducted during the 2012–2013 school year. The following schools were included in the scope of the study: Arcola, Brookhaven, Forest Knolls, Georgian Forest, Glen Haven, Glenallan, Harmony Hills, Highland, Kemp Mill, Sargent Shriver, Weller Road, and Wheaton Woods elementary schools. Based on the outcome of the study, an FY 2016 appropriation for planning funds are approved to begin the architectural design for five classroom addition projects at Brookhaven, Glen Haven, Highland, Kemp Mill, and Sargent Shriver elementary schools. These projects will address overutilization at Arcola, Harmony Hills, Highland, Kemp Mill, and Sargent Shriver elementary schools. Although the Board of Education requested a completion date of August 2018 for these projects, the County Council maintained the approved FY 2015–2020 CIP completion date of August 2019. In order for these projects to be completed on schedule, county and state funding must be provided at the levels approved in this CIP.

Montgomery Knolls Elementary School

Planning Study: A comprehensive capacity study to address overutilization at several elementary schools in the lower section of the Downcounty Consortium was conducted during the 2014–2015 school year. This capacity study included the following schools: East Silver Spring, Forest Knolls, Highland View, Montgomery Knolls, New Hampshire Estates, Oak View, Takoma Park, Pine Crest, Piney Branch, Rolling Terrace, Sligo Creek, and Woodlin elementary schools.

New Hampshire Estates Elementary School

Planning Study: A comprehensive capacity study to address overutilization at several elementary schools in the lower section of the Downcounty Consortium was conducted during the 2014–2015 school year. This capacity study included the following schools: East Silver Spring, Forest Knolls, Highland View, Montgomery Knolls, New Hampshire Estates, Oak View, Takoma Park, Pine Crest, Piney Branch, Rolling Terrace, Sligo Creek, and Woodlin elementary schools.

Oak View Elementary School

Planning Study: A comprehensive capacity study to address overutilization at several elementary schools in the lower section of the Downcounty Consortium was conducted during the 2014–2015 school year. This capacity study included the following schools: East Silver Spring, Forest Knolls, Highland View, Montgomery Knolls, New Hampshire Estates, Oak View, Takoma Park, Pine Crest, Piney Branch, Rolling Terrace, Sligo Creek, and Woodlin elementary schools.

Pine Crest Elementary School

Planning Study: A comprehensive capacity study to address overutilization at several elementary schools in the lower section of the Downcounty Consortium was conducted during the 2014–2015 school year. This capacity study included the following schools: East Silver Spring, Forest Knolls, Highland View, Montgomery Knolls, New Hampshire Estates, Oak View, Takoma Park, Pine Crest, Piney Branch, Rolling Terrace, Sligo Creek, and Woodlin elementary schools.

Piney Branch Elementary School

Planning Study: A comprehensive capacity study to address overutilization at several elementary schools in the lower section of the Downcounty Consortium was conducted during the 2014–2015 school year. This capacity study included the following schools: East Silver Spring, Forest Knolls, Highland View, Montgomery Knolls, New Hampshire Estates, Oak View, Takoma Park, Pine Crest, Piney Branch, Rolling Terrace, Sligo Creek, and Woodlin elementary schools.

Rolling Terrace Elementary School

Planning Study: Projections indicate enrollment at Rolling Terrace Elementary School will exceed capacity by 92 seats or more by the end of the six-year CIP period. A comprehensive capacity study to address overutilization at several elementary schools in the lower section of the Downcounty Consortium was conducted during the 2014–2015 school year. This capacity study included the following schools: East Silver Spring, Forest Knolls, Highland View, Montgomery Knolls, New Hampshire Estates, Oak View, Takoma Park, Pine Crest, Piney Branch, Rolling Terrace, Sligo Creek, and Woodlin elementary schools. A plan to address the overutilization of schools in this area will be considered as part of the FY 2017–2022 CIP.

Sargent Shriver Elementary School

Capital Project: A comprehensive capacity study to address overutilization at several elementary schools in the midsection of the Downcounty Consortium was conducted during the 2012–2013 school year. The following schools were included in the scope of the study: Arcola, Brookhaven, Forest Knolls, Georgian Forest, Glen Haven, Glenallan, Harmony Hills, Highland, Kemp Mill, Sargent Shriver, Weller Road, and Wheaton Woods elementary schools. Based on the outcome of the study, an FY 2016 appropriation for planning funds are approved to begin the architectural design for five classroom addition projects at Brookhaven, Glen Haven, Highland, Kemp Mill, and Sargent Shriver elementary schools. These projects will address overutilization at Arcola, Harmony Hills, Highland, Kemp Mill, and Sargent Shriver elementary schools. Although the Board of Education requested a completion date of August 2018 for these projects, the County Council maintained the approved FY 2015–2020 CIP completion date of August 2019. In order for these projects to be completed on schedule, county and state funding must be provided at the levels approved in this CIP.

Sligo Creek Elementary School

Planning Study: A comprehensive capacity study to address overutilization at several elementary schools in the lower section of the Downcounty Consortium was conducted during the 2014–2015 school year. This capacity study included the following schools: East Silver Spring, Forest Knolls, Highland View, Montgomery Knolls, New Hampshire Estates, Oak View, Takoma Park, Pine Crest, Piney Branch, Rolling Terrace, Sligo Creek, and Woodlin elementary schools.

Takoma Park Elementary School

Planning Study: A comprehensive capacity study to address overutilization at several elementary schools in the lower section of the Downcounty Consortium was conducted during the 2014–2015 school year. This capacity study included the following schools: East Silver Spring, Forest Knolls, Highland View, Montgomery Knolls, New Hampshire Estates, Oak View, Takoma Park, Pine Crest, Piney Branch, Rolling Terrace, Sligo Creek, and Woodlin elementary schools.

Wheaton Woods Elementary School

Capital Project: A revitalization/expansion project is scheduled for this school. Capital Project: A revitalization/expansion project is scheduled for this school. Although the approved

FY 2015–2020 CIP had a completion of August 2018 for the revitalization/expansion project, the County Council approved the Board of Education's request to complete the project in August 2017. An FY 2016 appropriation is approved to construct this project. Funding was approved in the Department of Health and Human Services Capital Budget to construct a child care classroom and Linkages to Learning suite as part of the project.

Woodlin Elementary School

Capital Project: Enrollment projections indicate enrollment at Woodlin Elementary School will exceed capacity by 92 seats or more by the end of the six-year CIP period. An FY 2013 appropriation was approved for facility planning to determine the feasibility, scope, and cost for a classroom addition at Woodlin Elementary School. However, due to enrollment growth in nearby schools in the lower portion of the Downcounty Consortium, planning for the addition is deferred until a comprehensive plan can be developed from the comprehensive capacity study for the lower portion of the Downcounty Consortium. The comprehensive capacity study for the lower area was conducted during the 2014–2015 school year. This capacity study included the following schools: East Silver Spring, Forest Knolls, Highland View, Montgomery Knolls, New Hampshire Estates, Oak View, Takoma Park, Pine Crest, Piney Branch, Rolling Terrace, Sligo Creek, and Woodlin elementary schools. A plan to address the overutilization of schools in this area will be considered as part of the FY 2017–2022 CIP.

CAPITAL PROJECTS

School	Project	Project Status*	Date of Completion
John F. Kennedy HS	School-based Wellness Center	Proposed	TBD
Wheaton HS	Revitalization/ expansion	Approved	Jan. 2016 Aug. 2018, site
	Wellness Center	Approved	Jan. 2016
Eastern MS	Revitalization/ expansion	Programmed	Aug. 2022
Col. E. Brooke Lee MS	Classroom addition	Proposed	TBD
A. Mario Loiederman MS	Classroom addition	Proposed	TBD
Parkland MS	Classroom addition	Proposed	TBD
Silver Spring International MS	Classroom addition	Proposed	TBD
Takoma Park MS	Classroom addition	Proposed	TBD
Arcola ES	Classroom addition	Approved	Aug. 2015
Brookhaven ES	Classroom addition	Approved	Aug. 2019
Glen Haven ES	Classroom addition	Approved	Aug. 2019
Highland ES	Classroom addition	Approved	Aug. 2019
Highland View ES	Classroom addition	Deferred	TBD
Kemp Mill ES	Classroom addition	Approved	Aug. 2019
Sargent Shriver ES	Classroom addition	Approved	Aug. 2019
Wheaton Woods ES	Revitalization/ expansion	Approved	Aug. 2017
Woodlin ES	Classroom addition	Deferred	TBD

"Approved"— Project has an FY 2015 or FY 2016 appropriation approved in the FY 2015–2020 CIP.

"Deferred"—Funds have been deferred for a future CIP.

"Programmed"—Project has expenditures programmed in a future year of the CIP for planning and/or construction funds.

"Proposed"—Project has facility planning funds approved for FY 2015 or approved for FY 2016 for a feasibility study.

Projected Enrollment and Space Availability

Effects of the Amended FY2015–2020 CIP and Non–CIP Actions on Space Available

Schools			Actual 14–15	Projections 15–16	16–17	17–18	18–19	19–20	20–21	2024	2029
Montgomery Blair HS		Program Capacity	2920	2920	2920	2920	2920	2920	2920	2920	2920
		Enrollment	**2900**	**2957**	**2915**	**2994**	**3034**	**3110**	**3212**	**3400**	**3300**
		Available Space	*20*	*(36)*	*6*	*(74)*	*(114)*	*(190)*	*(292)*	*(480)*	*(380)*
		Comments		See text							
Albert Einstein HS		Program Capacity	1621	1604	1604	1604	1604	1604	1604	1604	1604
		Enrollment	**1699**	**1665**	**1698**	**1753**	**1782**	**1828**	**1978**	**2100**	**2000**
		Available Space	*(78)*	*(61)*	*(94)*	*(149)*	*(178)*	*(224)*	*(374)*	*(496)*	*(396)*
		Comments		See text +1 EXT							
John F. Kennedy HS		Program Capacity	1847	1833	1833	1833	1833	1833	1833	1833	1833
		Enrollment	**1570**	**1563**	**1672**	**1788**	**1855**	**1925**	**1975**	**2100**	**2000**
		Available Space	*277*	*270*	*161*	*45*	*(22)*	*(92)*	*(142)*	*(267)*	*(167)*
		Comments		See text +1 LFI Fac. Plng Well Ctr.							
Northwood HS		Program Capacity	1519	1519	1519	1519	1519	1519	1519	1519	1519
		Enrollment	**1586**	**1631**	**1630**	**1666**	**1785**	**1794**	**1963**	**2100**	**2000**
		Available Space	*(67)*	*(112)*	*(111)*	*(147)*	*(266)*	*(275)*	*(444)*	*(581)*	*(481)*
		Comments		See text							
Wheaton HS		Program Capacity	1356	1596	1596	1596	1596	1596	1596	1596	1596
		Enrollment	**1467**	**1578**	**1567**	**1621**	**1608**	**1659**	**1737**	**1900**	**1800**
		Available Space	*(111)*	*18*	*29*	*(25)*	*(12)*	*(63)*	*(141)*	*(304)*	*(204)*
		Comments		Rev/Ex Complete See text							
Argyle MS		Program Capacity	897	897	897	897	897	897	897	897	897
		Enrollment	**920**	**932**	**930**	**920**	**939**	**941**	**958**	**1000**	**950**
		Available Space	*(23)*	*(35)*	*(33)*	*(23)*	*(42)*	*(44)*	*(61)*	*(103)*	*(53)*
		Comments									
Eastern MS		Program Capacity	1024	1024	1024	1024	1024	1024	1024	1024	1024
		Enrollment	**868**	**904**	**971**	**1014**	**1054**	**1067**	**1095**	**1200**	**1100**
		Available Space	*156*	*120*	*53*	*10*	*(30)*	*(43)*	*(71)*	*(176)*	*(76)*
		Comments			Facility Planning for Rev/Ex	Planning for Revitalization/ Expansion			Move to Woodward Aug. 2020		
Col. E. Brooke Lee MS		Program Capacity	743	727	727	727	727	727	727	727	727
		Enrollment	**719**	**749**	**796**	**819**	**891**	**943**	**1046**	**1200**	**1100**
		Available Space	*24*	*(22)*	*(69)*	*(92)*	*(164)*	*(216)*	*(319)*	*(473)*	*(373)*
		Comments	Facility Planning for Addition	+1 EXT			Facility Planning for Rev/Ex		Planning for Rev/Ex		
A. Mario Loiederman MS		Program Capacity	897	897	897	897	897	897	897	897	897
		Enrollment	**909**	**942**	**949**	**996**	**1065**	**1096**	**1094**	**1200**	**1100**
		Available Space	*(12)*	*(45)*	*(52)*	*(99)*	*(168)*	*(199)*	*(197)*	*(303)*	*(203)*
		Comments	Facility Planning for Addition								
Newport Mill MS		Program Capacity	825	825	825	825	825	825	825	825	825
		Enrollment	**599**	**605**	**607**	**649**	**660**	**683**	**672**	**800**	**750**
		Available Space	*226*	*220*	*218*	*176*	*164*	*142*	*152*	*25*	*75*
		Comments									
Parkland MS		Program Capacity	948	948	948	948	948	948	948	948	948
		Enrollment	**941**	**961**	**961**	**1005**	**1086**	**1126**	**1128**	**1200**	**1100**
		Available Space	*7*	*(13)*	*(13)*	*(57)*	*(138)*	*(178)*	*(180)*	*(252)*	*(152)*
		Comments	Facility Planning for Addition								
Silver Spring International MS		Program Capacity	1118	1118	1118	1118	1118	1118	1118	1118	1118
		Enrollment	**979**	**1010**	**1064**	**1141**	**1207**	**1282**	**1311**	**1400**	**1300**
		Available Space	*139*	*108*	*54*	*(23)*	*(89)*	*(164)*	*(193)*	*(282)*	*(182)*
		Comments	Facility Planning for Addition								
Sligo MS		Program Capacity	915	915	915	915	915	915	915	915	915
		Enrollment	**523**	**632**	**741**	**821**	**814**	**901**	**919**	**950**	**900**
		Available Space	*392*	*283*	*174*	*94*	*101*	*14*	*(4)*	*(35)*	*15*
		Comments									
Takoma Park MS		Program Capacity	939	939	939	939	939	939	939	939	939
		Enrollment	**996**	**1021**	**1036**	**1053**	**1103**	**1166**	**1202**	**1300**	**1200**
		Available Space	*(57)*	*(82)*	*(97)*	*(114)*	*(164)*	*(227)*	*(263)*	*(361)*	*(261)*
		Comments	Facility Planning for Addition								

Schools			Actual 14–15	Projections 15–16	16–17	17–18	18–19	19–20	20–21	2024	2029
Arcola ES	CSR	Program Capacity	496	659	659	659	659	659	659		
		Enrollment	**719**	**737**	**780**	**781**	**784**	**766**	**750**		
		Available Space	*(223)*	*(78)*	*(121)*	*(122)*	*(125)*	*(107)*	*(91)*		
		Comments		Addition Complete							
Bel Pre ES	CSR	Program Capacity	638	640	640	640	640	640	640		
Grades (pre-K-2)		**Enrollment**	**541**	**575**	**560**	**546**	**539**	**538**	**537**		
Paired With		Available Space	*97*	*65*	*80*	*94*	*101*	*102*	*103*		
Strathmore ES		Comments	Rev/Ex Complete	+1 preK							
Brookhaven ES	CSR	Program Capacity	486	486	486	486	486	706	706		
		Enrollment	**458**	**454**	**467**	**456**	**452**	**448**	**454**		
		Available Space	*28*	*32*	*19*	*30*	*34*	*258*	*252*		
		Comments		Planning for Addition				Addition Complete See text			
East Silver Spring ES	CSR	Program Capacity	582	582	582	582	582	582	582		
		Enrollment	**525**	**558**	**572**	**578**	**576**	**567**	**556**		
		Available Space	*57*	*24*	*10*	*4*	*6*	*15*	*26*		
		Comments	See text								
Forest Knolls ES	CSR	Program Capacity	560	560	560	560	560	560	560		
		Enrollment	**737**	**785**	**790**	**783**	**794**	**784**	**750**		
		Available Space	*(177)*	*(225)*	*(230)*	*(223)*	*(234)*	*(224)*	*(190)*		
		Comments	See text								
Georgian Forest ES	CSR	Program Capacity	649	649	649	649	649	649	649		
		Enrollment	**571**	**577**	**587**	**578**	**566**	**555**	**551**		
		Available Space	*78*	*72*	*62*	*71*	*83*	*94*	*98*		
		Comments									
Glen Haven ES	CSR	Program Capacity	576	576	576	576	576	705	705		
		Enrollment	**547**	**590**	**625**	**637**	**656**	**634**	**632**		
		Available Space	*29*	*(14)*	*(49)*	*(61)*	*(80)*	*71*	*73*		
		Comments		Planning for Addition				Addition Complete See text			
Glenallan ES	CSR	Program Capacity	762	762	762	762	762	762	762		
		Enrollment	**650**	**686**	**703**	**727**	**733**	**741**	**716**		
		Available Space	*112*	*76*	*59*	*35*	*29*	*21*	*46*		
		Comments									
Harmony Hills ES	CSR	Program Capacity	709	709	709	709	709	709	709		
		Enrollment	**736**	**767**	**797**	**800**	**781**	**786**	**775**		
		Available Space	*(27)*	*(58)*	*(88)*	*(91)*	*(72)*	*(77)*	*(66)*		
		Comments									
Highland ES	CSR	Program Capacity	522	522	522	522	522	714	714		
		Enrollment	**541**	**569**	**585**	**594**	**593**	**588**	**586**		
		Available Space	*(19)*	*(47)*	*(63)*	*(72)*	*(71)*	*126*	*128*		
		Comments		Planning for Addition				Addition Complete See text			
Highland View ES	CSR	Program Capacity	298	298	298	298	298	298	298		
		Enrollment	**426**	**422**	**425**	**426**	**423**	**410**	**408**		
		Available Space	*(128)*	*(124)*	*(127)*	*(128)*	*(125)*	*(112)*	*(110)*		
		Comments	See text								
Kemp Mill ES	CSR	Program Capacity	453	453	453	453	453	696	696		
		Enrollment	**531**	**550**	**569**	**593**	**583**	**579**	**566**		
		Available Space	*(78)*	*(97)*	*(116)*	*(140)*	*(130)*	*117*	*130*		
		Comments		Planning for Addition				Addition Complete See text			
Montgomery Knolls ES	CSR	Program Capacity	540	540	540	540	540	540	540		
Grades (K–2)		**Enrollment**	**510**	**528**	**506**	**489**	**480**	**479**	**479**		
Paired With		Available Space	*30*	*12*	*34*	*51*	*60*	*61*	*61*		
Pine Crest ES		Comments	See text								
New Hampshire Estates ES	CSR	Program Capacity	480	480	480	480	480	480	480		
Grades (pre-K–2)		**Enrollment**	**516**	**524**	**533**	**517**	**504**	**503**	**502**		
Paired With		Available Space	*(36)*	*(44)*	*(53)*	*(37)*	*(24)*	*(23)*	*(22)*		
Oak View ES		Comments	See text								
Oak View ES	CSR	Program Capacity	358	358	358	358	358	358	358		
Grades (3–5)		**Enrollment**	**379**	**410**	**443**	**467**	**465**	**462**	**446**		
Paired With		Available Space	*(21)*	*(52)*	*(85)*	*(109)*	*(107)*	*(104)*	*(88)*		
New Hampshire ES		Comments	See text								

Schools			Actual 14–15	Projections 15–16	16–17	17–18	18–19	19–20	20–21	2024	2029
Oakland Terrace ES	CSR	Program Capacity	513	513	513	513	513	513	513		
		Enrollment	**491**	**490**	**494**	**480**	**482**	**473**	**476**		
		Available Space	*22*	*23*	*19*	*33*	*31*	*40*	*37*		
		Comments									
Pine Crest ES	CSR	Program Capacity	381	381	381	381	381	381	381		
Grades (3–5)		**Enrollment**	**473**	**464**	**465**	**463**	**468**	**459**	**441**		
Paired With		Available Space	*(92)*	*(83)*	*(84)*	*(82)*	*(87)*	*(78)*	*(60)*		
Montgomery Knolls ES		Comments	See text								
Piney Branch ES	CSR	Program Capacity	611	611	611	611	611	611	611		
Grades (3–5)		**Enrollment**	**527**	**557**	**608**	**626**	**618**	**607**	**591**		
Paired With		Available Space	*84*	*54*	*3*	*(15)*	*(7)*	*4*	*20*		
Takoma Park ES		Comments	See text								
Rock View ES	CSR	Program Capacity	687	687	687	687	687	687	687		
		Enrollment	**657**	**646**	**658**	**654**	**664**	**666**	**660**		
		Available Space	*30*	*41*	*29*	*33*	*23*	*21*	*27*		
		Comments									
Rolling Terrace ES	CSR	Program Capacity	*724*	*747*	*747*	*747*	*747*	*747*	*747*		
		Enrollment	**905**	**925**	**942**	**929**	**919**	**895**	**888**		
		Available Space	*(181)*	*(178)*	*(195)*	*(182)*	*(172)*	*(148)*	*(141)*		
		Comments	See text								
Sargent Shriver ES	CSR	Program Capacity	673	673	673	673	673	814	814		
		Enrollment	**756**	**770**	**790**	**787**	**767**	**756**	**774**		
		Available Space	*(83)*	*(97)*	*(117)*	*(114)*	*(94)*	*58*	*40*		
		Comments		Planning for Addition				Addition Complete See text			
Flora M. Singer ES	CSR	Program Capacity	680	680	680	680	680	680	680		
		Enrollment	**677**	**724**	**734**	**733**	**736**	**721**	**705**		
		Available Space	*3*	*(44)*	*(54)*	*(53)*	*(56)*	*(41)*	*(25)*		
		Comments									
Sligo Creek ES		Program Capacity	664	664	664	664	664	664	664		
		Enrollment	**639**	**664**	**676**	**666**	**676**	**678**	**672**		
		Available Space	*25*	*0*	*(12)*	*(2)*	*(12)*	*(14)*	*(8)*		
		Comments	See text								
Strathmore ES	CSR	Program Capacity	439	439	439	439	439	439	439		
Grades (3–5)		**Enrollment**	**455**	**463**	**461**	**481**	**485**	**472**	**456**		
Paired With		Available Space	*(16)*	*(24)*	*(22)*	*(42)*	*(46)*	*(33)*	*(17)*		
Bel Pre ES		Comments									
Takoma Park ES	CSR	Program Capacity	636	636	636	636	636	636	636		
Grades (pre-K–2)		**Enrollment**	**654**	**653**	**628**	**611**	**599**	**603**	**602**		
Paired With		Available Space	*(18)*	*(17)*	*8*	*25*	*37*	*33*	*34*		
Piney Branch ES		Comments	See text								
Viers Mill ES	CSR	Program Capacity	760	743	743	743	743	743	743		
		Enrollment	**714**	**730**	**760**	**750**	**736**	**732**	**714**		
		Available Space	*46*	*13*	*(17)*	*(7)*	*7*	*11*	*29*		
		Comments		+1 PEP							
Weller Road ES	CSR	Program Capacity	*752*	*772*	*772*	*772*	*772*	*772*	*772*		
		Enrollment	**652**	**689**	**686**	**694**	**701**	**692**	**683**		
		Available Space	*100*	*83*	*86*	*78*	*71*	*80*	*89*		
		Comments	-1 PEP	+1 preK							
Wheaton Woods ES	CSR	Program Capacity	358	358	358	770	770	770	770		
		Enrollment	**537**	**546**	**552**	**560**	**560**	**554**	**556**		
		Available Space	*(179)*	*(188)*	*(194)*	*210*	*210*	*216*	*214*		
		Comments		Move to North Lake Jan. 2016	@ North Lake	Rev/Ex Complete Aug. 2017					
Woodlin ES		Program Capacity	462	462	462	462	462	462	462		
		Enrollment	**623**	**637**	**634**	**618**	**637**	**633**	**635**		
		Available Space	*(161)*	*(175)*	*(172)*	*(156)*	*(175)*	*(171)*	*(173)*		
		Comments	See text								
Cluster Information		HS Utilization	100%	99%	100%	104%	106%	109%	115%	122%	117%
		HS Enrollment	9222	9394	9482	9822	10064	10316	10865	11600	11100
		MS Utilization	90%	94%	97%	102%	106%	111%	114%	124%	115%
		MS Enrollment	7454	7756	8055	8418	8819	9205	9425	10250	9500
		ES Utilization	104%	106%	108%	106%	105%	99%	98%	100%	100%
		ES Enrollment	17147	17690	18030	18024	17977	17781	17561	18000	18000

Demographic Characteristics of Schools

Schools	2014–2015						2014–2015		2013–2014
	Total Enrollment	Two or more races %	Black or Afr. Amer. %	Asian%	Hispanic %	White %	FARMS%*	ESOL%**	Mobility Rate%***
Montgomery Blair HS	2900	≤ 5.0%	26.6%	15.6%	31.2%	22.4%	37.6%	11.8%	11.0%
Albert Einstein HS	1699	≤ 5.0%	21.6%	10.7%	45.1%	20.0%	44.8%	11.5%	13.1%
John F. Kennedy HS	1570	≤ 5.0%	34.0%	8.5%	50.6%	5.2%	53.5%	13.2%	13.3%
Northwood HS	1586	≤ 5.0%	24.4%	6.4%	52.1%	14.2%	47.5%	17.6%	15.1%
Wheaton HS	1467	≤ 5.0%	24.6%	10.0%	54.6%	8.5%	53.9%	17.0%	14.2%
Argyle MS	920	≤ 5.0%	33.5%	10.8%	44.9%	8.2%	60.8%	13.3%	14.3%
Eastern MS	868	≤ 5.0%	19.0%	15.0%	38.5%	23.0%	45.0%	15.6%	10.1%
Col. E. Brooke Lee MS	719	≤ 5.0%	24.8%	7.9%	56.7%	7.5%	64.8%	19.7%	16.8%
A. Mario Loiederman MS	909	≤ 5.0%	25.4%	6.7%	53.1%	12.0%	60.6%	18.3%	12.8%
Newport Mill MS	599	≤ 5.0%	17.0%	10.9%	50.4%	18.0%	53.8%	16.4%	15.3%
Parkland MS	941	≤ 5.0%	21.1%	19.3%	44.3%	11.7%	49.4%	9.5%	5.6%
Silver Spring International MS	979	5.1%	23.0%	5.4%	36.7%	29.8%	43.5%	13.8%	10.6%
Sligo MS	523	≤ 5.0%	24.5%	8.2%	41.7%	23.1%	45.9%	13.0%	14.2%
Takoma Park MS	996	6.0%	27.9%	21.5%	15.5%	28.7%	26.4%	6.8%	8.4%
Arcola ES	719	≤ 5.0%	18.4%	8.1%	68.8%	≤ 5.0%	74.7%	43.9%	18.8%
Bel Pre ES	543	≤ 5.0%	42.2%	6.3%	40.9%	6.3%	68.9%	45.9%	19.8%
Brookhaven ES	458	≤ 5.0%	35.6%	7.9%	44.3%	8.7%	66.8%	40.0%	16.7%
East Silver Spring ES	525	≤ 5.0%	54.9%	≤ 5.0%	21.7%	15.2%	58.7%	34.3%	16.8%
Forest Knolls ES	737	≤ 5.0%	15.2%	7.1%	42.1%	30.9%	39.6%	25.2%	7.4%
Georgian Forest ES	571	≤ 5.0%	30.3%	6.5%	52.7%	8.8%	78.6%	31.0%	24.5%
Glen Haven ES	547	≤ 5.0%	22.5%	8.4%	49.7%	15.2%	61.2%	36.4%	23.2%
Glenallan ES	650	≤ 5.0%	33.5%	9.5%	45.4%	8.3%	64.6%	25.8%	24.3%
Harmony Hills ES	736	≤ 5.0%	16.6%	6.0%	73.4%	≤ 5.0%	86.8%	52.6%	17.9%
Highland ES	542	≤ 5.0%	13.3%	≤ 5.0%	74.4%	≤ 5.0%	80.6%	54.2%	12.0%
Highland View ES	426	5.2%	24.2%	≤ 5.0%	30.8%	35.2%	46.5%	30.3%	12.1%
Kemp Mill ES	531	≤ 5.0%	17.7%	≤ 5.0%	71.8%	≤ 5.0%	77.8%	49.9%	22.0%
Montgomery Knolls ES	510	≤ 5.0%	25.5%	≤ 5.0%	48.6%	20.4%	63.9%	48.6%	11.6%
New Hampshire Estates ES	516	≤ 5.0%	17.6%	≤ 5.0%	77.5%	≤ 5.0%	90.5%	68.0%	17.2%
Oak View ES	379	≤ 5.0%	17.2%	7.4%	61.7%	12.4%	76.0%	38.5%	13.1%
Oakland Terrace ES	491	8.6%	15.5%	9.4%	28.1%	38.1%	31.4%	16.3%	10.4%
Pine Crest ES	473	≤ 5.0%	19.2%	8.2%	38.1%	30.2%	50.3%	21.4%	9.9%
Piney Branch ES	527	5.7%	37.0%	≤ 5.0%	16.1%	37.2%	34.9%	14.6%	6.5%
Rock View ES	657	6.2%	16.7%	10.4%	45.5%	20.7%	51.6%	26.0%	15.2%
Rolling Terrace ES	905	≤ 5.0%	15.1%	≤ 5.0%	64.4%	14.7%	70.1%	51.8%	14.4%
Sargent Shriver ES	756	≤ 5.0%	12.7%	7.5%	74.6%	≤ 5.0%	80.8%	49.1%	13.8%
Flora M. Singer ES	677	≤ 5.0%	14.0%	6.9%	38.8%	34.9%	42.2%	28.8%	10.4%
Sligo Creek ES	639	8.3%	22.2%	5.9%	10.2%	53.1%	13.3%	9.1%	7.6%
Strathmore ES	455	≤ 5.0%	42.0%	5.9%	41.3%	7.3%	62.4%	19.6%	16.8%
Takoma Park ES	654	5.8%	33.9%	≤ 5.0%	20.2%	37.0%	34.3%	31.7%	10.0%
Viers Mill ES	714	≤ 5.0%	11.6%	8.0%	60.8%	16.2%	65.1%	44.7%	13.4%
Weller Road ES	652	≤ 5.0%	10.7%	10.0%	73.6%	≤ 5.0%	76.5%	47.4%	19.2%
Wheaton Woods ES	537	≤ 5.0%	29.6%	7.8%	55.5%	6.0%	82.5%	48.4%	14.1%
Woodlin ES	623	9.6%	24.7%	5.9%	18.5%	40.8%	24.6%	14.3%	11.3%
Elementary Cluster Total	**17150**	**≤ 5.0%**	**23.0%**	**6.4%**	**48.8%**	**17.9%**	**62.5%**	**37.7%**	**14.8%**
Elementary County Total	75,144	≤ 5.0%	21.2%	13.9%	30.4%	29.3%	40.2%	23.3%	13.3%

**Percent of students approved for Free and Reduced-priced Meals Program (FARMS) during the 2014–2015 school year.*

***Percent of English for Speakers of Other Languages (ESOL) during the 2014–2015 school year. High School students are served in regional ESOL centers.*

****Mobility Rate is the number of entries plus withdrawals during the 2013–2014 school year compared to total enrollment.*
Notes: Native Hawaiian/Pacific Islander and American Indian/Alaskan Native categories total less than 1% and were therefore excluded from the table.

Due to federal and state guidelines, demographic characteristics of schools of less than or equal to 5.0% are reported as ≤ 5.0%.


Program Capacity Table

(School Year 2014–2015)

Schools	Grades Served	Capacity (HS @90% MS@85%)	Total Rooms	Support Rooms	Regular Secondary @25	Regular Elementary @23	CSR Grades 1–2 @18	Pre–K @20	Pre–K @40	HS @20	CSR KIND @18	KIND @22	ESOL @15	METS @15	Special Education Services: School Based: HSM @13	School Based: ELEM LAD @13	Cluster Based: ELC @10	Quad Cluster Based: LANG @12	Quad Cluster Based: LFI @10	Quad Cluster Based: SCB @6	County & Regional Based: AAC@7	AUT @6	BRIDGE @10	DHOH @7	ED @10	EXTENSIONS @6	GT/LD @13	PD @7	PEP@6	PEP @12	PEP @18	VISION (Elementary) @7	OTHER
Montgomery Blair HS	9-12	2920	133		125								6	2																		
Albert Einstein HS	9-12	1621	80		67								3	1					3	4						2						
John F. Kennedy HS	9-12	1847	86		79								3						2	2												
Northwood HS	9-12	1519	73		61								6	2										3		1						
Wheaton HS	9-12	1356	65		56								5						2	2												
Argyle MS	6-8	897	43		41								2																			
Eastern MS	6-8	1024	51		45								3	1										2								
Col. E. Brooke Lee MS	6-8	743	37		33								2												1	1						
A. Mario Loiederman MS	6-8	897	43		41								1	1																		
Newport Mill MS	6-8	825	41		37								1						3													
Parkland MS	6-8	948	45		44								1																			
Silver Spring International MS	6-8	1118	53		52								1																			
Sligo MS	6-8	915	49		42								1							2												4
Takoma Park MS	6-8	939	45		43								2																			
Arcola ES	HS-5	496	32	5		3	15				8				1																	
Bel Pre ES	PreK-2	638	37	3			22		2		9																					1
Brookhaven ES	PreK-5	486	29	4		6	8		1		4					2													1	3		
East Silver Spring ES	HS-5	582	34	4		9	9		1	1	5				1	2												1		1		
Forest Knolls ES	K-5	560	34	4		5	13		1		8				1												2					
Georgian Forest ES	HS-5	649	36	4		13	9		1	1	6													2								
Glen Haven ES	PreK-5	576	35	5		10	10		1		5									2								1		1		
Glenallan ES	HS-5	762	44	5		16	12			1	7					2												1				
Harmony Hills ES	HS-5	709	41	6		11	14		1	1	8																					
Highland ES	HS-5	522	33	7		7	11		1	1	5				1																	
Highland View ES	K-5	298	21	5		3	8				4				1																	
Kemp Mill ES	PreK-5	453	28	5		4	10		1	1	6				1																	
Montgomery Knolls ES	HS-2	540	35	6			15		1	1	8																			1	3		
New Hampshire Estates ES	HS-2	480	32	6			12	2		4	8																					
Oak View ES	3-5	358	19	3		15									1																	
Oakland Terrace ES	K-5	513	32	5		8	9	1			5				1	2															1	
Pine Crest ES	3-5	381	21	4		16									1																	
Piney Branch ES	3-5	611	31	4		26									1																	
Rock View ES	PreK-5	687	39	4		14	11		1		5						3														1	
Rolling Terrace ES	HS-5	724	40	4		15	11		1	1	6				1																	1
Sargent Shriver ES	PreK-5	673	37	4		12	12		1		7			1																		
Flora M. Singer ES	PreK-5	680	38	4		14	10		1		6						3															
Sligo Creek ES	K-5	664	35	4		23						5			1						2											
Strathmore ES	3-5	439	25	4		18									1					2												
Takoma Park ES	PreK-2	636	40	4			22	1	1		10																					2
Viers Mill ES	HS-5	760	42	4		14	11		1	1	7				1															3		
Weller Road ES	HS-5	752	43	7		16	11		1	1	6																			1		
Wheaton Woods ES	HS-5	358	26	7		2	9		1	1	5																					1
Woodlin ES	K-5	462	26	3		13						5			1				4													

Facility Characteristics of Schools 2014–2015

Schools	Year Facility Opened	Year Reopened/ Revitalized	Total Square Footage	Site Size Acres	Adjacent Park	Reloc-atable Classrooms	Linkages to Learning Program	Home School Model
Montgomery Blair HS	1998		386,567	30.2	Yes			
Albert Einstein HS	1962	1997	276,462	26.67	Yes			
John F. Kennedy HS	1964	1999	280,048	29.1				
Northwood HS	1956	2004	254,054	29.6				
Wheaton HS	1954	1983	333,268	28.2		2		
Argyle MS	1971	1993	120,205	19.9				
Eastern MS	1951	1976	152,030	14.5				
Col. E. Brooke Lee MS	1966		123,199	16.5	Yes			
A. Mario Loiederman MS	1956	2005	131,746	17.08				
Newport Mill MS	1958	2002	108,240	8.4	Yes			
Parkland MS	1963	2007	151,169	9.2	Yes			
Silver Spring International MS	1934	1999	152,731	10.64	Yes			
Sligo MS	1959	1991	149,527	21.7	Yes			
Takoma Park MS	1939	1999	137,348	18.8	Yes	1		
Arcola ES	1956	2007	95,421	5	Yes	6		Yes
Bel Pre ES	1968	2014	95,330	8.9	Yes			Yes
Brookhaven ES	1961	1995	81,320	8.57				
East Silver Spring ES	1929	1975	88,895	8.4				
Forest Knolls ES	1960	1993	89,564	7.8		4		Yes
Georgian Forest ES	1961	1995	88,111	11	Yes		Yes	Yes
Glen Haven ES	1950	2004	85,845	10	Yes			
Glenallan ES	1966	2013	98,700	12.1				
Harmony Hills ES	1957	1999	85,648	10.2	Yes	5	Yes	Yes
Highland ES	1950	1989	87,491	11	Yes			Yes
Highland View ES	1953	1994	59,213	6.6		6		Yes
Kemp Mill ES	1960	1996	68,222	10		3		Yes
Montgomery Knolls ES	1952	1989	97,213	10.3				
New Hampshire Estates ES	1954	1988	73,306	5.4				
Oak View ES	1949	1985	57,560	11.3		1		Yes
Oakland Terrace ES	1950	1993	79,145	9.5	Yes	2		Yes
Pine Crest ES	1941	1992	53,778	5.6	Yes	5		Yes
Piney Branch ES	1973		99,706	1.97	Yes			Yes
Rock View ES	1955	1999	91,977	7.4				Yes
Rolling Terrace ES	1988		92,241	4.3		8		Yes
Sargent Shriver ES	1954	2006	91,628	9.17		9		Yes
Flora M. Singer ES	2012		95,831	12.67	Yes			Yes
Sligo Creek ES	1934	1999	98,799	15.6	Yes			Yes
Strathmore ES	1970		59,497	10.8	Yes			Yes
Takoma Park ES	1979		85,553	4.7				
Viers Mill ES	1950	1991	120,572	10.52				Yes
Weller Road ES	1953	2013	121,346	11.1				
Wheaton Woods ES	1952	1976	66,763	8		9		
Woodlin ES	1944	1974	60,725	11		9		Yes

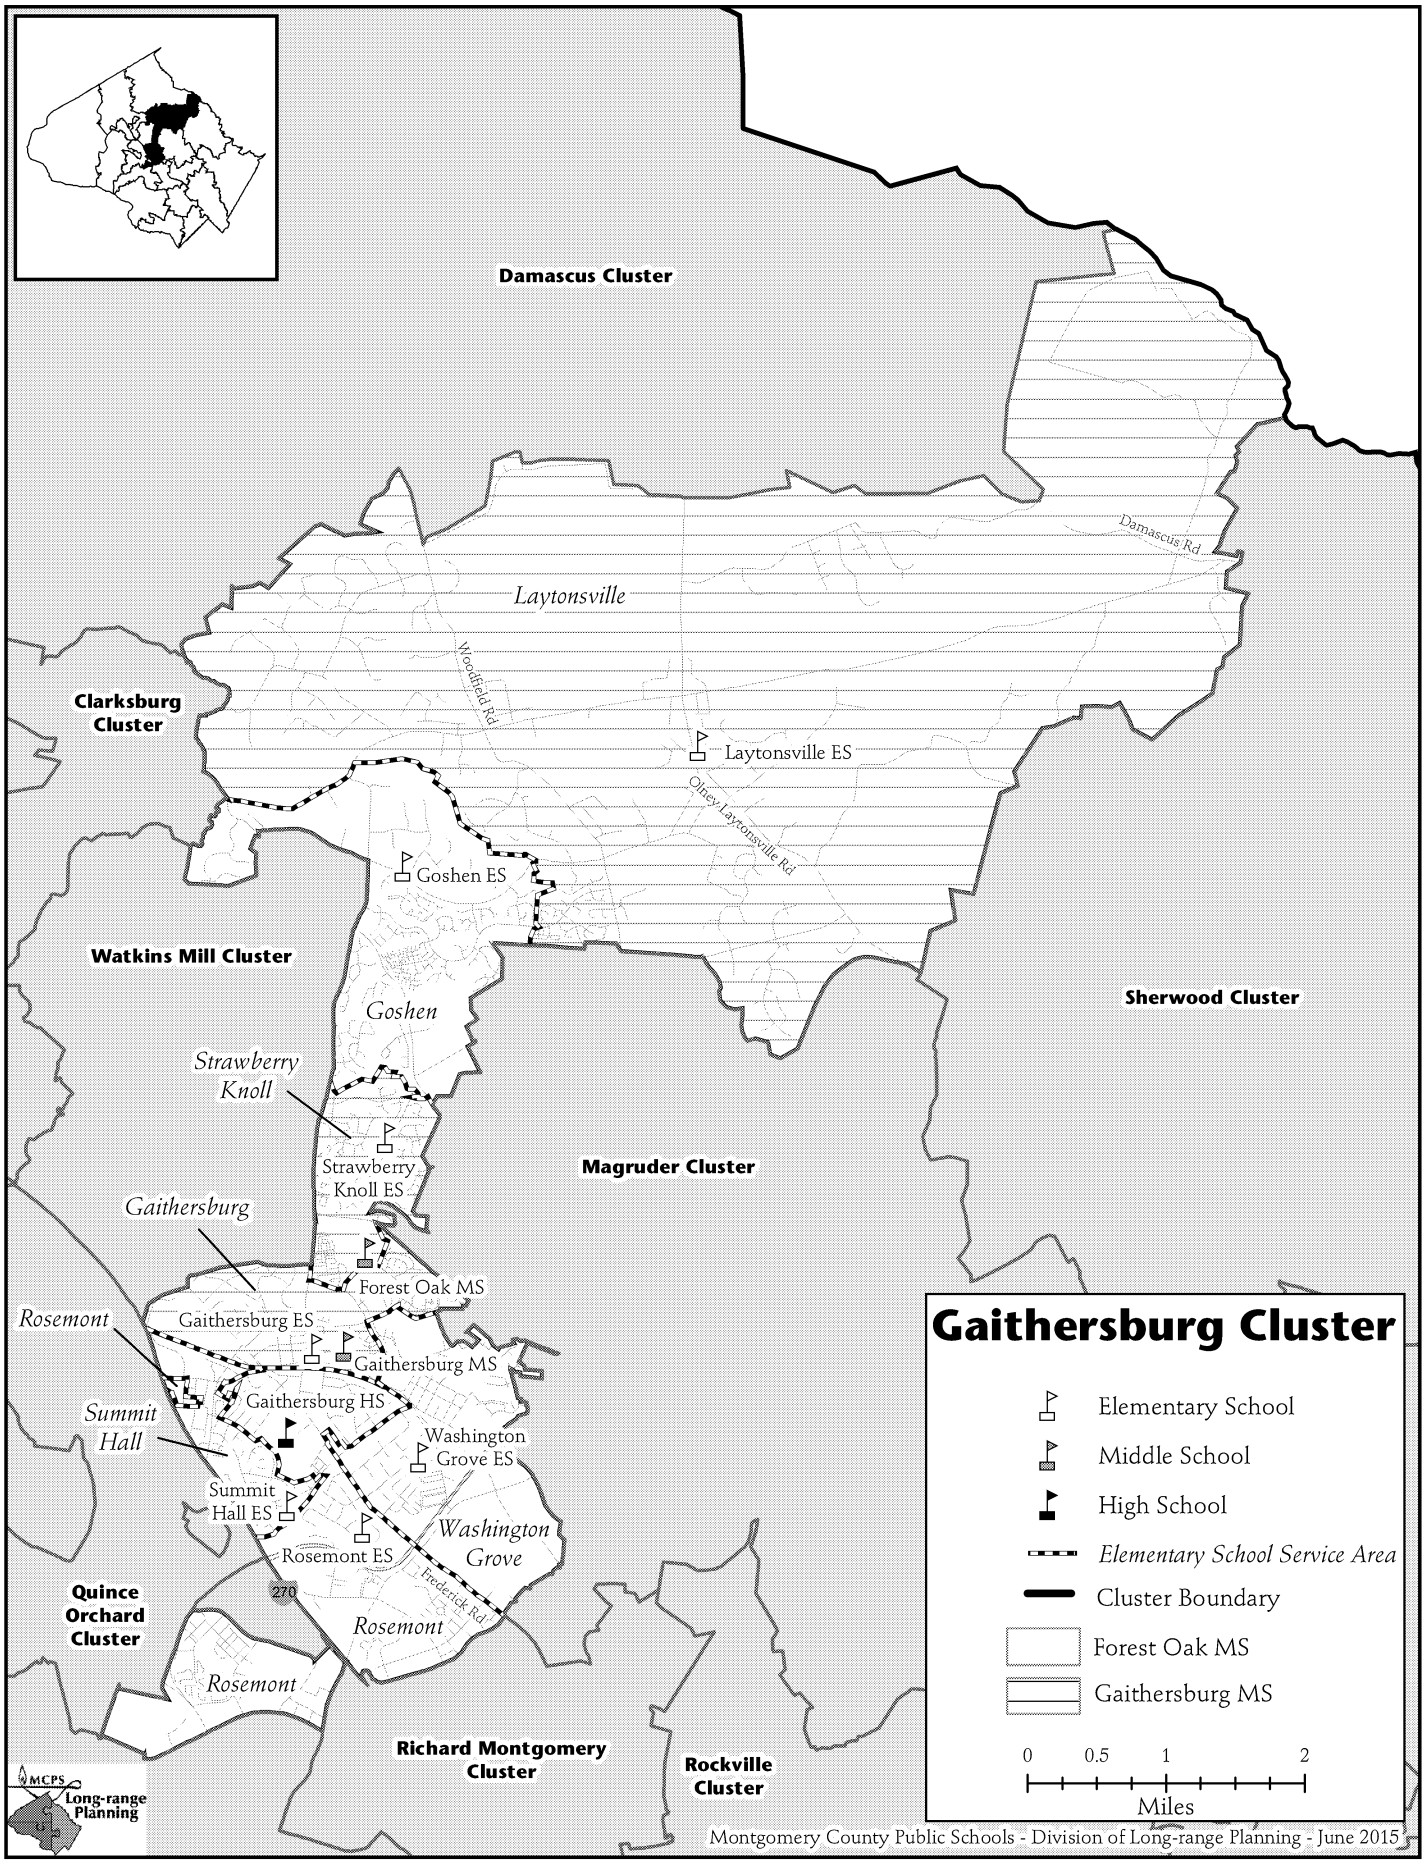
Damascus Cluster
Laytonsville
Damascus Rd
Woodfield Rd
Clarksburg Cluster
Laytonsville ES
Olney-Laytonsville Rd
Goshen ES
Watkins Mill Cluster
Goshen
Sherwood Cluster
Strawberry Knoll
Strawberry Knoll ES
Magruder Cluster
Gaithersburg
Forest Oak MS
Rosemont
Gaithersburg ES
Gaithersburg MS
Gaithersburg HS
Summit Hall
Washington Grove ES
Summit Hall ES
Rosemont ES
Washington Grove
Frederick Rd
270
Quince Orchard Cluster
Rosemont
Rosemont
Richard Montgomery Cluster
Rockville Cluster
MCPS
Long-range Planning
Gaithersburg Cluster
Elementary School
Middle School
High School
Elementary School Service Area
Cluster Boundary
Forest Oak MS
Gaithersburg MS
0 0.5 1 2
Miles
Montgomery County Public Schools - Division of Long-range Planning - June 2015

CLUSTER PLANNING ISSUES

Planning Issue: The 2006 adopted Shady Grove Sector Plan provides for up to 6,020 new residential units near the Shady Grove METRO station. Most of the planned units are within the Gaithersburg Cluster. A large portion of the plan requires the relocation of county and school system facilities located along Crabbs Branch Way, including the MCPS Central Food Production facility, the Shady Grove School Bus Depot, and the Shady Grove Division of Maintenance Depot. Infrastructure improvements also are required to achieve build-out of the plan. It is anticipated that it will take many years for build-out of the plan to occur. The pace of construction will be market driven. An elementary school site is included in the sector plan.

Since 2007, elementary school enrollment in the Gaithersburg Cluster has increased by 600 students. In addition, development of the Crown community, with 1,500 residential units in the Rosemont Elementary School service area, is moving ahead. A comprehensive capacity study was approved for the Gaithersburg Cluster to address enrollment growth in this area. The study was conducted during the 2014–2015 school year and included all the elementary schools in the cluster.

SCHOOLS

Gaithersburg Elementary School

Planning Study: A comprehensive capacity study was approved for the Gaithersburg Cluster to address enrollment growth in this area. The study was conducted during the 2014–2015 school year and included all the elementary schools in the cluster. A plan to address the overutilization of schools in this area will be considered as part of the FY 2017–2022 CIP.

Goshen Elementary School

Planning Study: A comprehensive capacity study was approved for the Gaithersburg Cluster to address enrollment growth in this area. The study was conducted during the 2014–2015 school year and included all the elementary schools in the cluster. A plan to address the overutilization of schools in this area will be considered as part of the FY 2017–2022 CIP.

Laytonsville Elementary School

Planning Study: A comprehensive capacity study was approved for the Gaithersburg Cluster to address enrollment growth in this area. The study was conducted during the 2014–2015 school year and included all the elementary schools in the cluster. A plan to address the overutilization of schools in this area will be considered as part of the FY 2017–2022 CIP.

Rosemont Elementary School


Planning Study: Projections indicate enrollment at Rosemont Elementary School will exceed capacity by 92 seats or more by the end of the six-year planning period. Planning Study: A comprehensive capacity study was approved for the Gaithersburg Cluster to address enrollment growth in this area. The study was conducted during the 2014–2015 school year and included all the elementary schools in the cluster. A plan to address the overutilization of schools in this area will be considered as part of the FY 2017–2022 CIP.

Strawberry Knoll Elementary School

Planning Study: Projections indicate enrollment at Strawberry Knoll Elementary School will exceed capacity by 92 seats or more by the end of the six-year period. An FY 2012 appropriation was approved for facility planning to determine the feasibility, scope, and cost for a classroom addition project. However, due to enrollment growth in the cluster, planning for the addition is deferred until a comprehensive plan can be developed from the comprehensive capacity study for the Gaithersburg Cluster to address enrollment growth in this area. The study was conducted during the 2014–2015 school year and included all the elementary schools in the cluster. A plan to address the overutilization of schools in this area will be considered as part of the FY 2017–2022 CIP.

Summit Hall Elementary School

Planning Study: Projections indicate enrollment at Summit Hall Elementary School will exceed capacity by 92 seats or more by the end of the six-year period. An FY 2012 appropriation was approved for facility planning to determine the feasibility, scope, and cost for a classroom addition project. However, due to enrollment growth in the cluster, planning for the addition is deferred until a comprehensive plan can be developed from the comprehensive capacity study for the Gaithersburg Cluster to address enrollment growth in this area.

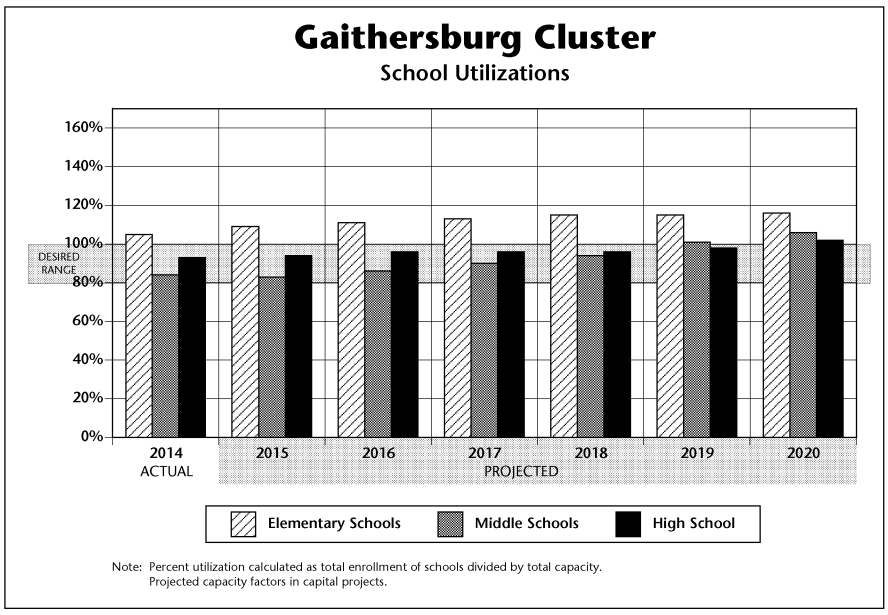

The study was conducted during the 2014–2015 school year and included all the elementary schools in the cluster. A plan to address the overutilization of schools in this area will be considered as part of the FY 2017–2022 CIP.

Capital Project: A revitalization/expansion project is scheduled for this school. Although the Board of Education requested a completion date of January 2022, the County Council maintained the approved FY 2015–2020 CIP completion date of January 2023. FY 2017 expenditures are programmed for facility planning for a feasibility study to determine the scope and cost of the project. In order for this project to be completed on this schedule, county and state funding must be provided at the levels approved in this CIP.

Washington Grove Elementary School

Planning Study: A comprehensive capacity study was approved for the Gaithersburg Cluster to address enrollment growth in this area. The study was conducted during the 2014–2015 school year and included all the elementary schools in the cluster. A plan to address the overutilization of schools in this area will be considered as part of the FY 2017–2022 CIP.

CAPITAL PROJECTS

School	Project	Project Status*	Date of Completion
Strawberry Knoll ES	Classroom addition	Deferred	TBD
Summit Hall ES	Revitalization/ expansion	Programmed	Jan. 2023, Addition Deferred TBD

"Approved"— Project has an FY 2015 or FY 2016 appropriation approved in the FY 2015–2020 CIP.

"Deferred"—Funds have been deferred for a future CIP.

"Programmed"—Project has expenditures programmed in a future year of the CIP for planning and/or construction funds.

"Proposed"—Project has facility planning funds approved for FY 2015 or approved for FY 2016 for a feasibility study.

Projected Enrollment and Space Availability

Effects of the Amended FY2015–2020 CIP and Non–CIP Actions on Space Available

Schools			Actual 14–15	Projections 15–16	16–17	17–18	18–19	19–20	20–21	2024	2029
Gaithersburg HS		Program Capacity	2407	2407	2407	2407	2407	2407	2407	2407	2407
		Enrollment	**2245**	**2264**	**2300**	**2321**	**2318**	**2352**	**2451**	**2600**	**2500**
		Available Space	*162*	*143*	*107*	*86*	*89*	*55*	*(44)*	*(193)*	*(93)*
		Comments									
Forest Oak MS		Program Capacity	949	949	949	949	949	949	949	949	949
		Enrollment	**834**	**797**	**790**	**835**	**876**	**972**	**1019**	**1100**	**1000**
		Available Space	*115*	*152*	*159*	*114*	*73*	*(23)*	*(70)*	*(151)*	*(51)*
		Comments									
Gaithersburg MS		Program Capacity	933	933	933	933	933	933	933	933	933
		Enrollment	**749**	**760**	**830**	**853**	**894**	**934**	**975**	**1050**	**950**
		Available Space	*184*	*173*	*103*	*80*	*39*	*(1)*	*(42)*	*(117)*	*(17)*
		Comments									
Gaithersburg ES	CSR	Program Capacity	771	771	771	771	771	771	771		
		Enrollment	**795**	**871**	**915**	**925**	**918**	**907**	**868**		
		Available Space	*(24)*	*(100)*	*(144)*	*(154)*	*(147)*	*(136)*	*(97)*		
		Comments	See text								
Goshen ES	CSR	Program Capacity	533	533	533	533	533	533	533		
		Enrollment	**577**	**602**	**600**	**608**	**607**	**594**	**592**		
		Available Space	*(44)*	*(69)*	*(67)*	*(75)*	*(74)*	*(61)*	*(59)*		
		Comments	See text								
Laytonsville ES		Program Capacity	448	448	448	448	448	448	448		
		Enrollment	**428**	**416**	**408**	**404**	**396**	**389**	**383**		
		Available Space	*20*	*32*	*40*	*44*	*52*	*59*	*65*		
		Comments	See text								
Rosemont ES	CSR	Program Capacity	590	613	613	613	613	613	613		
		Enrollment	**569**	**634**	**682**	**730**	**787**	**821**	**855**		
		Available Space	*21*	*(21)*	*(69)*	*(117)*	*(174)*	*(208)*	*(242)*		
		Comments	See text	-1 Supp. Room							
Strawberry Knoll ES	CSR	Program Capacity	453	476	476	476	476	476	476		
		Enrollment	**599**	**633**	**640**	**627**	**630**	**625**	**626**		
		Available Space	*(146)*	*(157)*	*(164)*	*(151)*	*(154)*	*(149)*	*(150)*		
		Comments	See text	-1 Supp. Room							
Summit Hall ES	CSR	Program Capacity	443	466	466	466	466	466	466		
		Enrollment	**634**	**669**	**663**	**666**	**669**	**653**	**650**		
		Available Space	*(191)*	*(203)*	*(197)*	*(200)*	*(203)*	*(187)*	*(184)*		
		Comments	See text	-1 Supp. Room	Facility Planning for Rev/Ex		Planning for Revitalization/ Expansion				
Washington Grove ES	CSR	Program Capacity	603	623	623	623	623	623	623		
		Enrollment	**414**	**447**	**439**	**463**	**497**	**529**	**575**		
		Available Space	*189*	*176*	*184*	*160*	*126*	*94*	*48*		
		Comments	See text	+1 preK							
Cluster Information		HS Utilization	93%	94%	96%	96%	96%	98%	102%	108%	104%
		HS Enrollment	2245	2264	2300	2321	2318	2352	2451	2600	2500
		MS Utilization	84%	83%	86%	90%	94%	101%	106%	114%	104%
		MS Enrollment	1583	1557	1620	1688	1770	1906	1994	2150	1950
		ES Utilization	105%	109%	111%	113%	115%	115%	116%	120%	120%
		ES Enrollment	4016	4272	4347	4423	4504	4518	4549	4700	4700

Demographic Characteristics of Schools

Schools	2014–2015 Total Enrollment	Two or more races %	Black or Afr. Amer. %	Asian%	Hispanic %	White %	2014–2015 FARMS%*	ESOL%**	2013–2014 Mobility Rate%***
Gaithersburg HS	2245	≤ 5.0%	25.1%	8.6%	44.5%	17.9%	43.2%	16.1%	16.1%
Forest Oak MS	834	≤ 5.0%	27.2%	7.3%	47.7%	13.3%	57.8%	17.9%	16.6%
Gaithersburg MS	749	≤ 5.0%	23.1%	9.3%	41.1%	21.2%	47.4%	12.8%	16.7%
Gaithersburg ES	795	≤ 5.0%	14.3%	≤ 5.0%	73.8%	6.0%	81.8%	48.7%	20.6%
Goshen ES	577	6.2%	24.6%	10.4%	34.5%	23.9%	42.8%	20.6%	11.5%
Laytonsville ES	428	6.1%	15.7%	7.9%	16.4%	53.7%	17.1%	5.6%	10.7%
Rosemont ES	569	≤ 5.0%	23.9%	9.1%	47.8%	13.9%	61.3%	42.4%	23.2%
Strawberry Knoll ES	599	5.8%	26.0%	14.7%	39.1%	13.5%	46.6%	21.7%	16.6%
Summit Hall ES	634	≤ 5.0%	21.1%	≤ 5.0%	68.1%	≤ 5.0%	80.6%	50.2%	19.4%
Washington Grove ES	414	≤ 5.0%	22.0%	9.9%	57.7%	8.5%	73.9%	51.9%	28.5%
Elementary Cluster Total	**4016**	**≤ 5.0%**	**20.9%**	**8.3%**	**50.6%**	**15.9%**	**61.4%**	**36.5%**	**18.5%**
Elementary County Total	**75,144**	**≤ 5.0%**	**21.2%**	**13.9%**	**30.4%**	**29.3%**	**40.2%**	**23.3%**	**13.3%**

**Percent of students approved for Free and Reduced-priced Meals Program (FARMS) during the 2014–2015 school year.*

***Percent of English for Speakers of Other Languages (ESOL) during the 2014–2015 school year. High School students are served in regional ESOL centers.*

****Mobility Rate is the number of entries plus withdrawals during the 2013–2014 school year compared to total enrollment.*
Notes: Native Hawaiian/Pacific Islander and American Indian/Alaskan Native categories total less than 1% and were therefore excluded from the table.

Due to federal and state guidelines, demographic characteristics of schools of less than or equal to 5.0% are reported as ≤ 5.0%.


Program Capacity Table

(School Year 2014–2015)

Schools	Grades Served	Capacity (HS @90% MS@85%)	Total Rooms	Support Rooms	Regular Secondary @25	Regular Elementary @23	CSR Grades 1–2 @18	Pre–K @20	Pre–K @40	HS @20	CSR KIND @18	KIND @22	ESOL @15	METS @15	Special Education Services: School Based: HSM @13	School Based: ELEM LAD @13	Quad Cluster Based: ELC @10	Quad Cluster Based: LANG @12	Quad Cluster Based: LFI @10	Quad Cluster Based: SCB @6	County & Regional Based: AAC@7	County & Regional Based: AUT @6	County & Regional Based: BRIDGE @10	County & Regional Based: DHOH @7	County & Regional Based: ED @10	County & Regional Based: EXTENSIONS @6	County & Regional Based: GT/LD @13	County & Regional Based: PD @7	County & Regional Based: PEP@6	County & Regional Based: PEP @12	County & Regional Based: PEP @18	County & Regional Based: VISION (Elementary) @7	County & Regional Based: OTHER
Gaithersburg HS	9-12	2407	122		93								7	4					3	4			7										4
Forest Oak MS	6-8	949	47		43								2							2													
Gaithersburg MS	6-8	933	49		41								1									3	4										
Gaithersburg ES	PreK-5	771	44	4		14	12		1		9				1							3											
Goshen ES	K-5	533	34	6		8	12				6				1			1															
Laytonsville ES	K-5	448	27	4		15						3			1					4													
Rosemont ES	PreK-5	590	36	4		9	11		1		6				1							4											
Strawberry Knoll ES	HS-5	453	32	5		2	11	1		1	5				1							2							1	1	2		
Summit Hall ES	HS-5	443	28	5		2	12		1	1	6				1																		
Washington Grove ES	HS-5	603	34	4		12	7	1	1	1	3				1														1	1	2		

Facility Characteristics of Schools 2014–2015

Schools	Year Facility Opened	Year Reopened/ Revitalized	Total Square Footage	Site Size Acres	Adjacent Park	Reloc-atable Classrooms	Linkages to Learning Program	Home School Model
Gaithersburg HS	1951	2013	427,048	41.07	Yes			
Forest Oak MS	1999		132,259	41.2				
Gaithersburg MS	1960	1988	157,694	22.82				
Gaithersburg ES	1947		94,468	9.22		7		Yes
Goshen ES	1988		76,740	10.5		5		Yes
Laytonsville ES	1951	1989	64,160	10.4		1		Yes
Rosemont ES	1965	1995	88,764	8.9		2		Yes
Strawberry Knoll ES	1988		78,723	10.8	Yes	6		Yes
Summit Hall ES	1971		68,059	10.2	Yes	10		Yes
Washington Grove ES	1956	1984	86,266	10.7				Yes

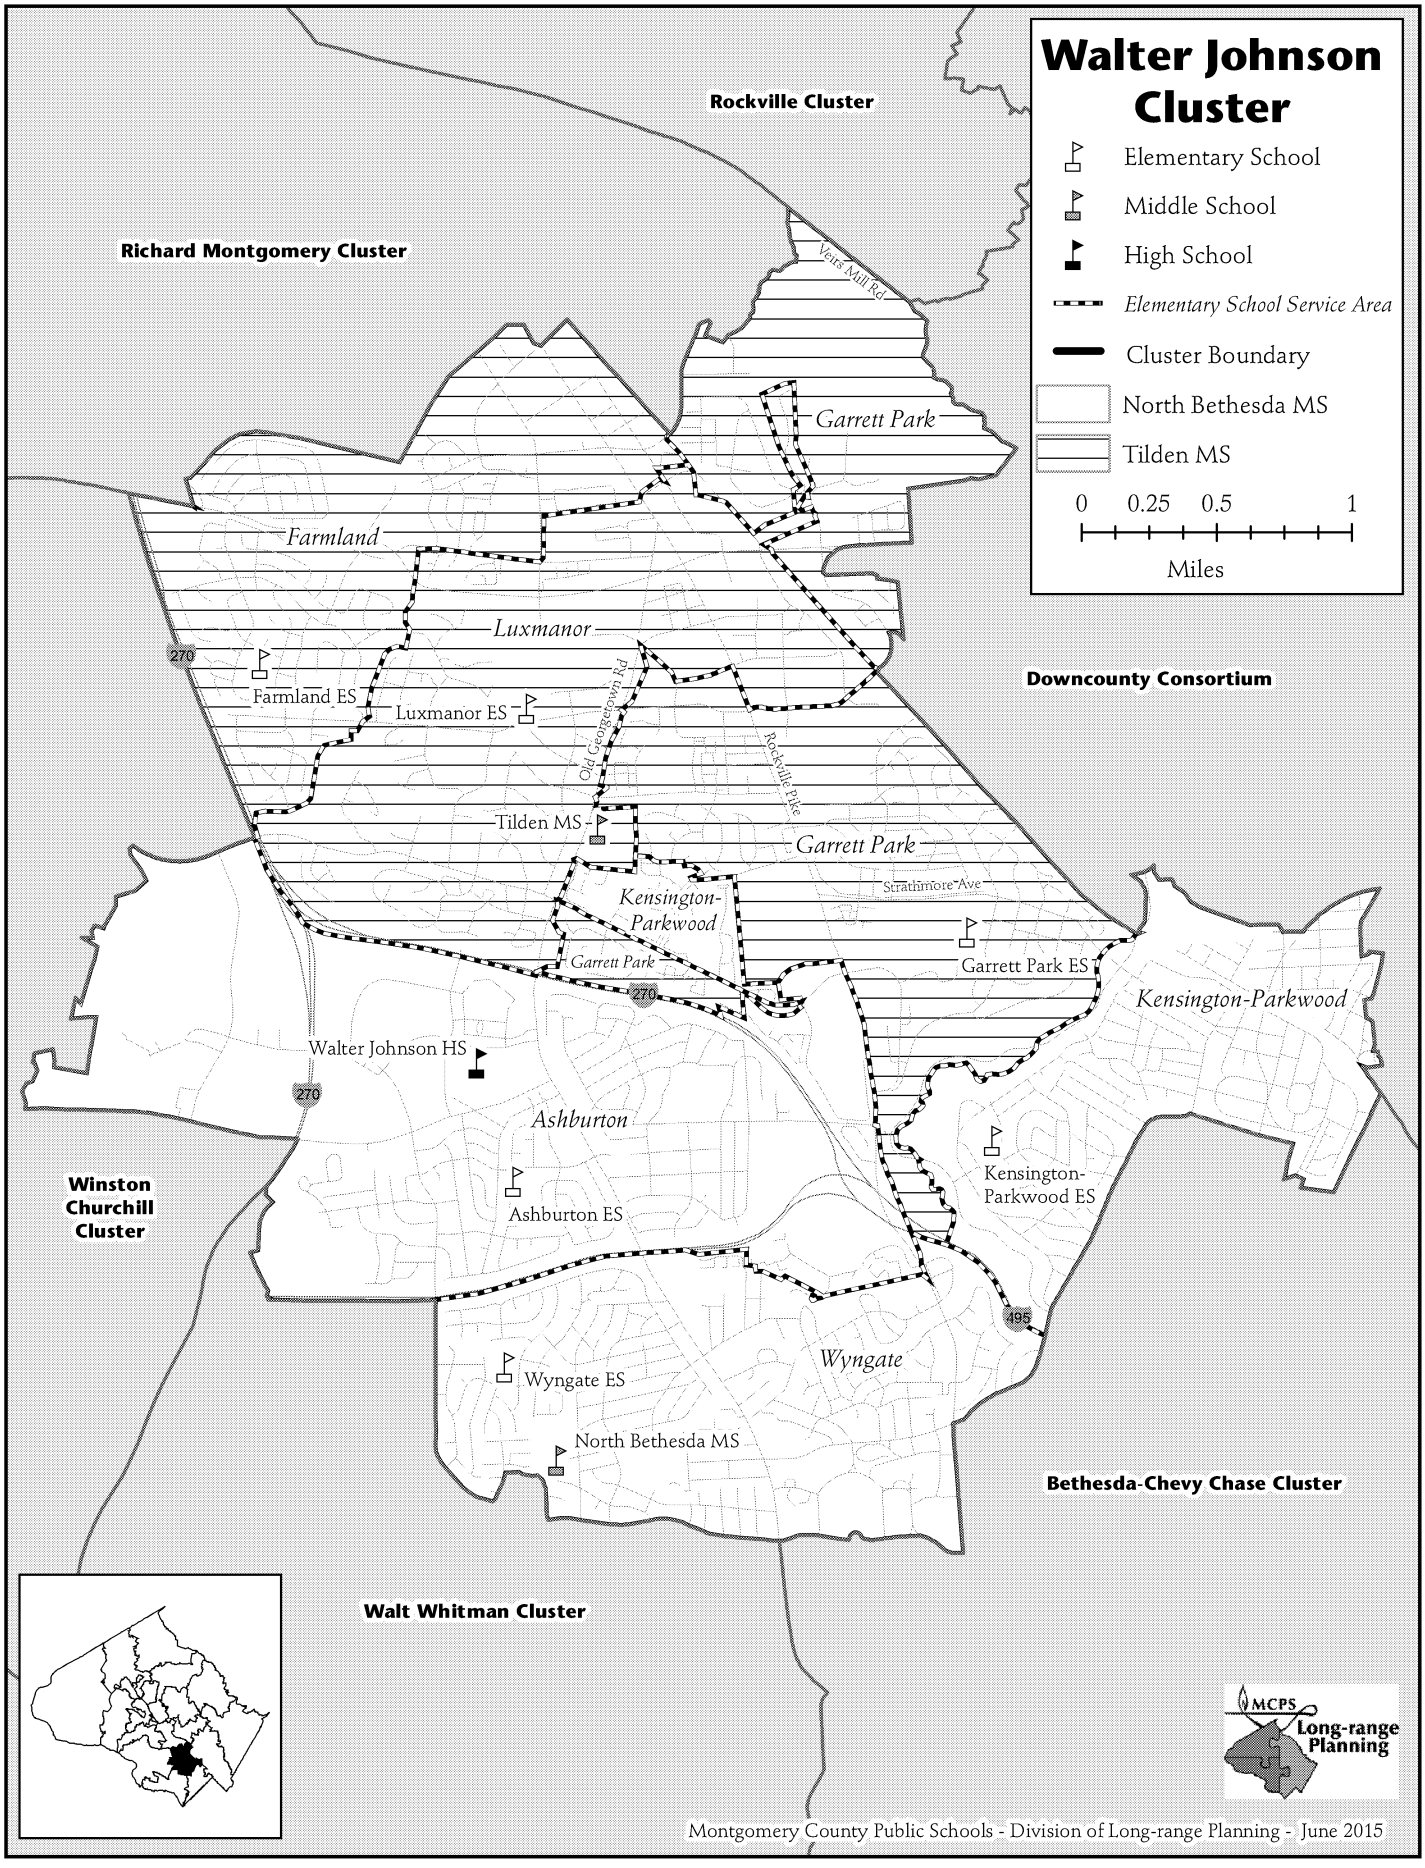
Walter Johnson Cluster
Elementary School
Middle School
High School
Elementary School Service Area
Cluster Boundary
North Bethesda MS
Tilden MS
0 0.25 0.5 1
Miles
Rockville Cluster
Richard Montgomery Cluster
Veirs Mill Rd
Garrett Park
Farmland
Luxmanor
270
Farmland ES
Luxmanor ES
Old Georgetown Rd
Rockville Pike
Downcounty Consortium
Tilden MS
Garrett Park
Strathmore Ave
Kensington-Parkwood
Garrett Park
Garrett Park ES
Kensington-Parkwood
270
Walter Johnson HS
270
Ashburton
Kensington-Parkwood ES
Winston Churchill Cluster
Ashburton ES
495
Wyngate
Wyngate ES
North Bethesda MS
Bethesda-Chevy Chase Cluster
Walt Whitman Cluster
MCPS
Long-range Planning
Montgomery County Public Schools - Division of Long-range Planning - June 2015

CLUSTER PLANNING ISSUES

Planning Issue: The 2010 adopted White Flint Sector Plan provides for up to 9,800 mostly multi-family housing units in the White Flint METRO station area. The sector plan is completely within the Walter Johnson Cluster. The plan requires the redevelopment of existing land uses and is phased with major roadway improvements. It is anticipated that it will take 20 to 30 years for build-out of the plan to occur, and the timing of construction will be market driven. Development of some projects has recently begun. A future elementary school site is included in the sector plan.

SCHOOLS

Walter Johnson High School

Capital Project: Projections indicate enrollment at Walter Johnson High School will exceed capacity by 200 seats or more by the end of the six-year CIP period. An FY 2015 appropriation is approved for facility planning to determine the feasibility, scope, and cost for a classroom addition. A date for the addition will be considered in a future CIP. Relocatable classrooms will be utilized until additional capacity can be added.

North Bethesda Middle School

Capital Project: Projections indicate enrollment at North Bethesda Middle School will exceed capacity by 150 seats or more by the end of the six-year CIP planning period. A classroom addition project is approved for this school. Although the Board of Education requested a completion date of August 2017, the County Council maintained the approved FY 2015–2020 CIP completion date of August 2018. FY 2017 expenditures are programmed to begin the construction of the classroom addition project. Relocatable classrooms will be utilized until additional capacity can be added. In order for this project to be completed on schedule, county and state funding must be provided at the levels approved in this CIP.

Tilden Middle School


Planning Study: On November 17, 2015, the Board of Education approved a Roundtable Discussion Group to explore the possible collocation of Rock Terrace School with Tilden Middle School on the Tilden Lane site. With an upcoming revitalization/expansion project, Tilden Middle School was identified because of its central location in the Walter Johnson Cluster its large site size and accessibility to accommodate the two schools, and the long history of the Walter Johnson cluster serving special education students.

Board of Education policy IOB, Education of Students with Disabilities, states that MCPS is committed to providing students with disabilities the opportunity to interact with nondisabled peers to the maximum extent possible. The Maryland State Department of Education (MSDE) has stated that state funding would be very difficult to acquire for stand-alone special education centers because students in these centers are not provided opportunities to receive instruction in the general education setting to the maximum extent appropriate. The collocation of special education centers with general education schools, such as the Longview School at Matsunaga Elementary School, allows the school system to address the facility needs of the stand-alone special education centers while meeting the goal to provide special education students with opportunities to receive instruction in the general education environment to the maximum extent appropriate.

Rock Terrace School, which serves students ages 12–21 throughout the county, and focuses on school-to-work programs, was assessed for revitalization/expansion using the Facilities Assessment with Criteria and Testing (FACT) methodology in the 2010–2011 school year. Of the secondary schools assessed that year, Rock Terrace School received the highest score and was in the greatest need of revitalization/expansion. (See Appendices E and F for additional information.)

The Roundtable Discussion Group included parents and staff from Rock Terrace School and Tilden Middle School as well as a representative from the MCCPTA Special Education Committee and the Walter Johnson Cluster. Staff from the Department of Special Education Services, the Division of Long-range Planning, and Division of Construction also participated in the process. To support the activities, an architect was hired to develop concept plans for the possible collocation of the two schools. The activities of the Roundtable included the following:

- Identify opportunities for special education students to receive instruction in the general education environment to the maximum extent appropriate
- Discuss the facility and site implications

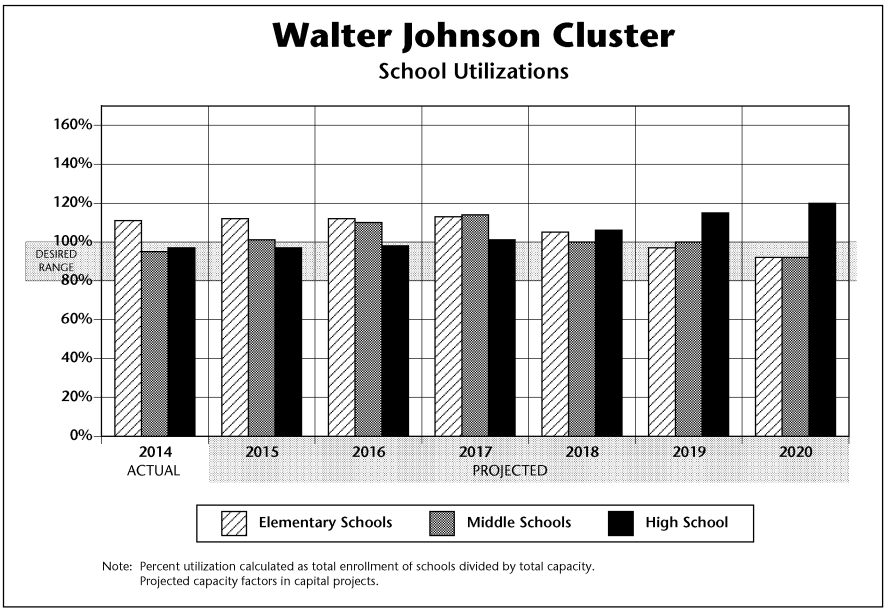

- Conduct site visits and engage in discussions with parents and staff at other collocated or soon to be collocated schools in the county and state.
- The Roundtable Discussion Group met from December 2014 through February 2015 and submitted a report to the interim superintendent of schools in March 2015. Following input from the Roundtable Discussion Group and the community at large, the interim superintendent of schools recommended and the Board of Education approved the collocation of Rock Terrace School and Tilden Middle School on May 12, 2015.

Capital Project: A revitalization/expansion project is scheduled for this school. Although the Board of Education requested a completion date of August 2019, the County Council maintained the FY 2015–2020 approved completion date of August 2020.

Tilden Middle School is currently located in the Woodward facility on Old Georgetown Road. Rather than revitalize/expand the Woodward facility for Rock Terrace School and Tilden Middle School, the current Tilden Holding Facility, located on Tilden Lane, will be revitalized/expanded to house both Rock Terrace School and Tilden Middle School. The Woodward facility will then become a secondary school holding facility for school revitalization/expansion projects scheduled after Tilden Middle School. Although an FY 2014 appropriation was approved for facility planning funds for a feasibility study to determine the scope for facility planning and cost for the revitalization/expansion project of Tilden Middle School, the feasibility study for Rock Terrace School and Tilden Middle School will begin in summer 2015. An FY 2016 appropriation for planning funds is approved to begin the architectural design for the project. In order for this project to be completed on this schedule, county and state funding must be provided at the levels approved in this CIP.

Ashburton Elementary School

Capital Project: Projections indicate enrollment at Ashburton Elementary School will exceed capacity by 92 seats or more by the end of the six-year CIP period. A classroom addition project is approved for this school. Although the Board of Education requested a completion date of August 2019, the County Council maintained the approved FY 2015–2020 CIP completion date of August 2020. FY 2017 expenditures are programmed for planning funds to begin the architectural design for a classroom addition. The scope of the addition has been increased to accommodate the projected enrollment. Relocatable classrooms will be utilized until additional capacity can be added. In order for this project to be completed on schedule, county and state funding must be provided at the levels approved in this CIP.

Kensington-Parkwood Elementary School

Capital Project: Projections indicate enrollment at Kensington-Parkwood Elementary School will exceed capacity by 92 seats or more by the end of the six-year CIP period. A classroom addition project is approved for this school. Although the Board of Education requested a completion date of August 2017, the County Council maintained the approved FY 2015–2020 CIP completion date of August 2018. FY 2017 expenditures are programmed to construct the classroom addition. Relocatable classrooms will be utilized until additional capacity can be added. In order for this project to be completed on schedule, county and state funding must be provided at the levels approved in this CIP.

Luxmanor Elementary School

Capital Project: A revitalization/expansion project is scheduled for this school. Although the Board of Education requested a completion date of January 2019, the County Council maintained the approved FY 2015–2020 CIP completion date of January 2020. An FY 2016 appropriation for planning funds is approved to begin the architectural design for the project. In order for this project to be completed on this schedule, county and state funding must be provided at the levels approved in this CIP.

CAPITAL PROJECTS

School	Project	Project Status*	Date of Completion
Walter Johnson HS	Classroom addition	Proposed	TBD
North Bethesda MS	Classroom Addition	Programmed	Aug. 2018
Tilden MS	Revitalization/ expansion, with collocation of Rock Terrace School	Approved	Aug. 2020
Ashburton ES	Classroom Addition	Programmed	Aug. 2020
Kensington-Parkwood ES	Classroom addition	Programmed	Aug. 2018
Luxmanor ES	Revitalization/ expansion	Approved	Jan. 2020

"Approved"— Project has an FY 2015 or FY 2016 appropriation approved in the FY 2015–2020 CIP.

"Deferred"—Funds have been deferred for a future CIP.

"Programmed"—Project has expenditures programmed in a future year of the CIP for planning and/or construction funds.

"Proposed"—Project has facility planning funds approved for FY 2015 or approved for FY 2016 for a feasibility study.

Projected Enrollment and Space Availability

Effects of the Amended FY2015–2020 CIP and Non–CIP Actions on Space Available

Schools		Actual 14–15	Projections 15–16	16–17	17–18	18–19	19–20	20–21	2024	2029
Walter Johnson HS	Program Capacity	2335	2335	2335	2335	2335	2335	2335	2335	2335
	Enrollment	**2264**	**2260**	**2287**	**2361**	**2472**	**2676**	**2798**	**2800**	**2800**
	Available Space	*71*	*75*	*48*	*(26)*	*(137)*	*(341)*	*(463)*	*(465)*	*(465)*
	Comments	Facility Planning for Addition								
North Bethesda MS	Program Capacity	874	874	874	874	1208	1208	1208	1208	1208
	Enrollment	**951**	**1031**	**1113**	**1172**	**1184**	**1195**	**1162**	**1300**	**1200**
	Available Space	*(77)*	*(157)*	*(239)*	*(298)*	*24*	*13*	*46*	*(92)*	*8*
	Comments	Planning for Addition				Addition Complete				
Tilden MS	Program Capacity	972	972	972	972	972	972	1200	1200	1200
	Enrollment	**798**	**827**	**922**	**937**	**990**	**995**	**1050**	**1200**	**1100**
	Available Space	*174*	*145*	*50*	*35*	*(18)*	*(23)*	*150*	*0*	*100*
	Comments	Fac. Plng. for Rev/Ex See text	Planning for Revitalization/ Expansion			Rev/Ex in Progress See text		Rev/Ex Complete Aug. 2020		
Ashburton ES	Program Capacity	629	652	652	652	652	652	881		
	Enrollment	**892**	**915**	**886**	**881**	**877**	**840**	**835**		
	Available Space	*(263)*	*(263)*	*(234)*	*(229)*	*(225)*	*(188)*	*46*		
	Comments		-1 Supp. Room	Planning for Addition				Addition Complete		
Farmland ES	Program Capacity	728	728	728	728	728	728	728		
	Enrollment	**655**	**684**	**696**	**724**	**709**	**703**	**700**		
	Available Space	*73*	*44*	*32*	*4*	*19*	*25*	*28*		
	Comments									
Garrett Park ES	Program Capacity	753	753	753	753	753	753	753		
	Enrollment	**749**	**784**	**776**	**791**	**794**	**783**	**769**		
	Available Space	*4*	*(31)*	*(23)*	*(38)*	*(41)*	*(30)*	*(16)*		
	Comments									
Kensington–Parkwood ES	Program Capacity	472	472	472	472	746	746	746		
	Enrollment	**654**	**642**	**656**	**646**	**642**	**635**	**645**		
	Available Space	*(182)*	*(170)*	*(184)*	*(174)*	*104*	*111*	*101*		
	Comments	Planning for Addition				Addition Complete				
Luxmanor ES	Program Capacity	428	428	428	428	428	745	745		
	Enrollment	**466**	**471**	**485**	**501**	**519**	**557**	**578**		
	Available Space	*(38)*	*(43)*	*(57)*	*(73)*	*(91)*	*188*	*167*		
	Comments		Planning for Revitalization/ Expansion			@ Grosvenor	Rev/Ex Complete Jan. 2020			
Wyngate ES	Program Capacity	*777*	*777*	*777*	*777*	*777*	*777*	*777*		
	Enrollment	**770**	**763**	**753**	**744**	**753**	**744**	**750**		
	Available Space	*7*	*14*	*24*	*33*	*24*	*33*	*27*		
	Comments									
Cluster Information	HS Utilization	97%	97%	98%	101%	106%	115%	120%	120%	120%
	HS Enrollment	2264	2260	2287	2361	2472	2676	2798	2800	2800
	MS Utilization	95%	101%	110%	114%	100%	100%	92%	104%	96%
	MS Enrollment	1749	1858	2035	2109	2174	2190	2212	2500	2300
	ES Utilization	111%	112%	112%	113%	105%	97%	92%	95%	95%
	ES Enrollment	4186	4259	4252	4287	4294	4262	4277	4400	4400

Demographic Characteristics of Schools

Schools	2014–2015 Total Enrollment	Two or more races %	Black or Afr. Amer. %	Asian%	Hispanic %	White %	2014–2015 FARMS%*	ESOL%**	2013–2014 Mobility Rate%***
Walter Johnson HS	2264	5.6%	9.5%	12.3%	16.3%	56.0%	6.8%	≤ 5.0%	6.3%
North Bethesda MS	951	6.2%	6.7%	10.3%	12.7%	63.5%	6.0%	≤ 5.0%	5.7%
Tilden MS	798	5.5%	8.6%	14.9%	19.3%	51.4%	12.3%	10.4%	9.6%
Ashburton ES	892	9.1%	13.8%	15.6%	13.8%	47.5%	12.7%	11.0%	11.9%
Farmland ES	655	≤ 5.0%	6.0%	32.5%	9.6%	47.3%	8.9%	24.6%	17.5%
Garrett Park ES	749	8.0%	11.1%	14.4%	22.4%	43.4%	17.2%	20.2%	13.2%
Kensington-Parkwood ES	654	7.3%	6.7%	6.4%	9.8%	69.4%	6.4%	5.8%	≤ 5.0%
Luxmanor ES	466	5.4%	10.1%	25.8%	18.2%	40.6%	15.5%	22.3%	17.6%
Wyngate ES	770	8.3%	≤ 5.0%	8.8%	11.6%	67.1%	≤ 5.0%	8.8%	≤ 5.0%
Elementary Cluster Total	**4186**	**7.3%**	**8.7%**	**16.5%**	**14.1%**	**53.0%**	**10.7%**	**15.2%**	**11.1%**
Elementary County Total	**75,144**	**≤ 5.0%**	**21.2%**	**13.9%**	**30.4%**	**29.3%**	**40.2%**	**23.3%**	**13.3%**

**Percent of students approved for Free and Reduced-priced Meals Program (FARMS) during the 2014–2015 school year.*

***Percent of English for Speakers of Other Languages (ESOL) during the 2014–2015 school year. High School students are served in regional ESOL centers.*

****Mobility Rate is the number of entries plus withdrawals during the 2013–2014 school year compared to total enrollment.*

Notes: Native Hawaiian/Pacific Islander and American Indian/Alaskan Native categories total less than 1% and were therefore excluded from the table.

Due to federal and state guidelines, demographic characteristics of schools of less than or equal to 5.0% are reported as ≤ 5.0%.


Program Capacity Table

(School Year 2014–2015)

Schools	Grades Served	Capacity (HS @90% MS@85%)	Total Rooms	Support Rooms	Regular Secondary @25	Regular Elementary @23	CSR Grades 1–2 @18	Pre–K @20	Pre–K @40	HS @20	CSR KIND @18	KIND @22	ESOL @15	METS @15	Special Education Services: School Based: HSM @13	Cluster Based: ELEM LAD @13	Quad Cluster Based: ELC @10	LANG @12	LFI @10	SCB @6	County & Regional Based: AAC@7	AUT @6	BRIDGE @10	DHOH @7	ED @10	EXTENSIONS @6	GT/LD @13	PD @7	PEP@6	PEP @12	PEP @18	VISION (Elementary) @7	OTHER
Walter Johnson HS	9-12	2335	107		101								2						2			1					1						
North Bethesda MS	6-8	874	42		40								1														1						
Tilden MS	6-8	972	52		43								2						2			3											2
Ashburton ES	K-5	629	34	4		18						5				3														1	3		
Farmland ES	K-5	728	37	4		26						5							2														
Garrett Park ES	K-5	753	37	4		27						6																					
Kensington-Parkwood ES	K-5	472	27	5		15						4				3																	
Luxmanor ES	K-5	428	24	4		14						4								1										1			
Wyngate ES	K-5	777	38	4		29						5																					

Facility Characteristics of Schools 2014–2015

Schools	Year Facility Opened	Year Reopened/ Revitalized	Total Square Footage	Site Size Acres	Adjacent Park	Reloc-atable Classrooms	Linkages to Learning Program	Home School Model
Walter Johnson HS	1956	2009	365,138	30.9				
North Bethesda MS	1955	1999	130,461	19.99		2		
Tilden MS	1967	1991	135,150	29.8				
Ashburton ES	1957	1993	81,438	8.3		8		
Farmland ES	1963	2011	89,988	4.8	Yes			
Garrett Park ES	1948	2012	96,348	4.4	Yes			
Kensington-Parkwood ES	1952	2006	77,136	9.9		7		
Luxmanor ES	1966		61,694	6.5	Yes	3		
Wyngate ES	1952	1997	89,104	9.5				

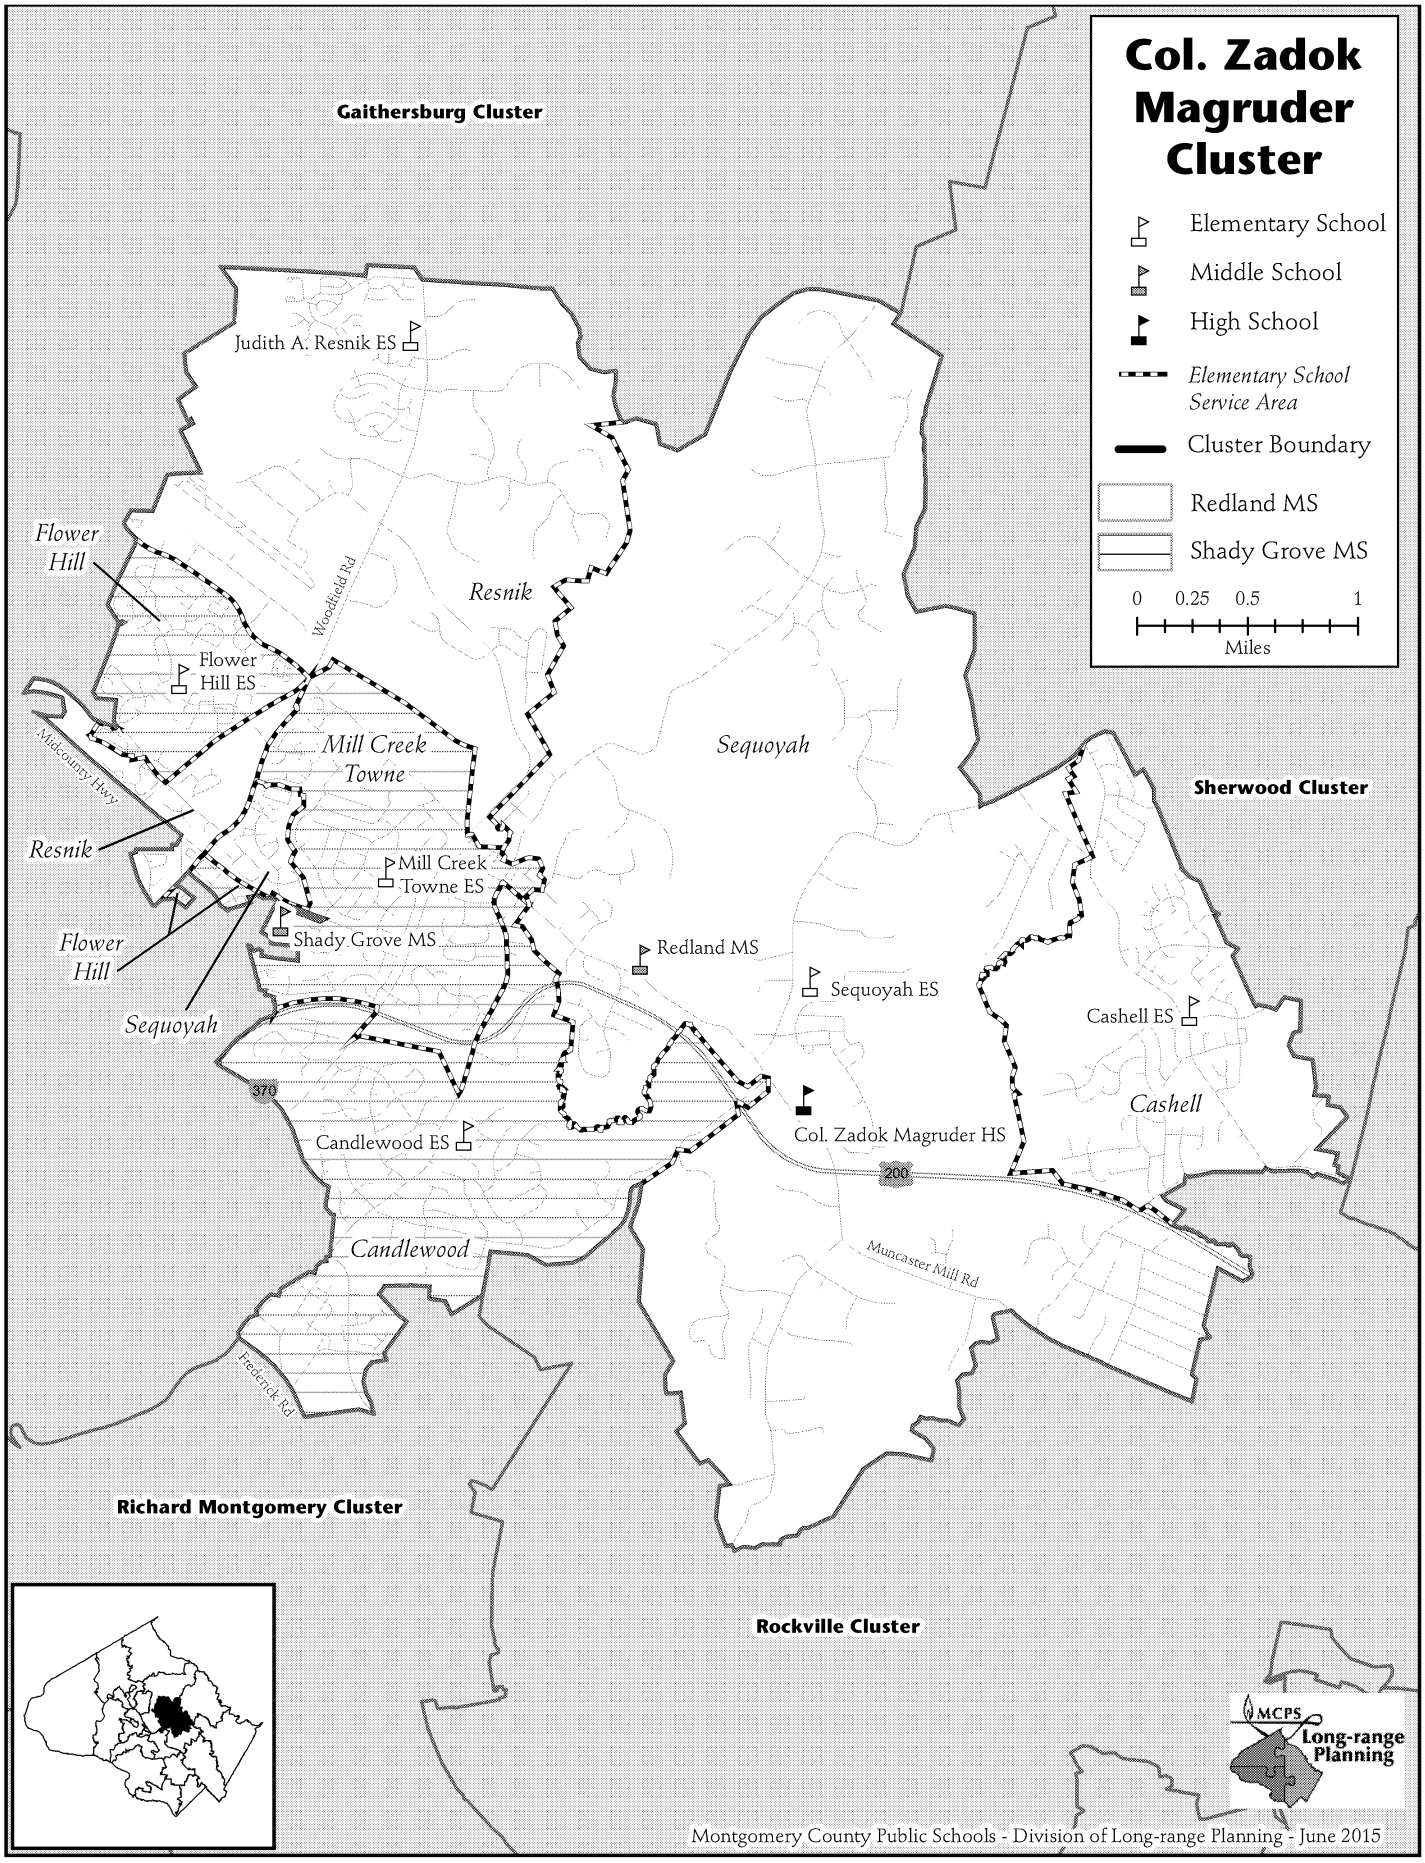
Col. Zadok Magruder Cluster
Elementary School
Middle School
High School
Elementary School Service Area
Cluster Boundary
Redland MS
Shady Grove MS
0 0.25 0.5 1
Miles
Gaithersburg Cluster
Judith A. Resnik ES
Flower Hill
Woodfield Rd
Resnik
Flower Hill ES
Mill Creek Towne
Sequoyah
Sherwood Cluster
Midcounty Hwy
Resnik
Mill Creek Towne ES
Shady Grove MS
Redland MS
Sequoyah ES
Cashell ES
Flower Hill
Sequoyah
370
Candlewood ES
Col. Zadok Magruder HS
Cashell
200
Candlewood
Muncaster Mill Rd
Frederick Rd
Richard Montgomery Cluster
Rockville Cluster
MCPS
Long-range Planning
Montgomery County Public Schools - Division of Long-range Planning - June 2015

SCHOOLS

Candlewood Elementary School

Capital Project: A revitalization/expansion project was completed in January 2015.

Judith A. Resnik Elementary School

Capital Project: Projections indicate enrollment at Judith A. Resnik Elementary School will exceed capacity by 92 seats or more by the end of the six-year CIP period. A classroom addition project is approved for this school. Although the Board of Education requested a completion date of August 2019, the County Council maintained the approved FY 2015–2020 CIP completion date of August 2020. FY 2017 expenditures are programmed to begin the architectural design for the classroom addition. Relocatable classrooms will be utilized until additional capacity can be provided. In order for this project to be completed on schedule, county and state funding must be provided at the levels approved in this CIP.

CAPITAL PROJECTS


School	Project	Project Status*	Date of Completion
Candlewood ES	Revitalization/ expansion	Approved	Jan. 2015
Judith A. Resnik ES	Classroom addition	Programmed	Aug. 2020

"Approved"— Project has an FY 2015 or FY 2016 appropriation approved in the FY 2015–2020 CIP.

"Deferred"—Funds have been deferred for a future CIP.

"Programmed"—Project has expenditures programmed in a future year of the CIP for planning and/or construction funds.

"Proposed"—Project has facility planning funds approved for FY 2015 or approved for FY 2016 for a feasibility study.

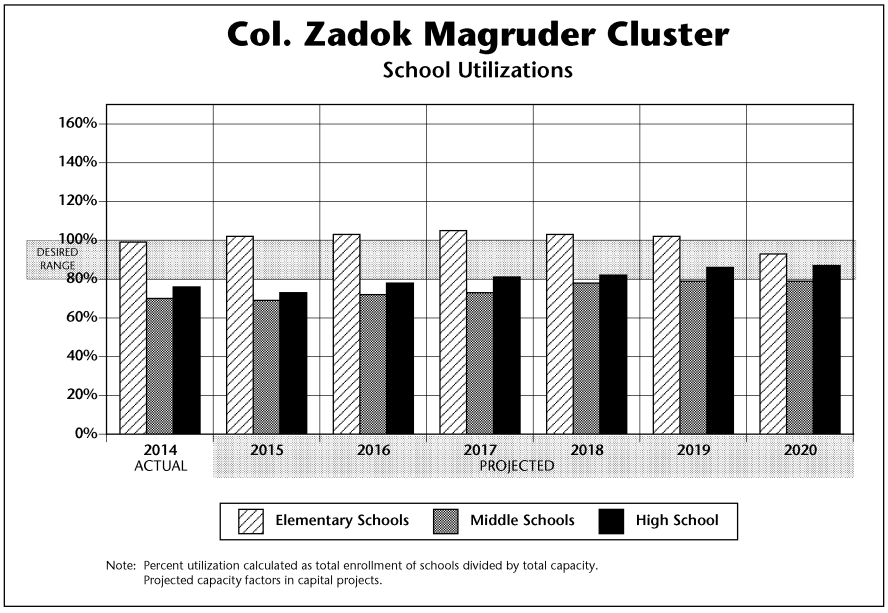

Projected Enrollment and Space Availability

Effects of the Amended FY2015–2020 CIP and Non–CIP Actions on Space Available

Schools			Actual 14–15	Projections 15–16	16–17	17–18	18–19	19–20	20–21	2024	2029
Col. Zadok Magruder HS		Program Capacity	1995	1968	1941	1941	1941	1941	1941	1941	1941
		Enrollment	**1520**	**1442**	**1521**	**1564**	**1599**	**1666**	**1686**	**1800**	**1700**
		Available Space	*475*	*526*	*420*	*377*	*342*	*275*	*255*	*141*	*241*
		Comments		+2 ED	+2 ED						
Redland MS		Program Capacity	*757*	*757*	*757*	*757*	*757*	*757*	*757*	*757*	*757*
		Enrollment	**540**	**552**	**572**	**588**	**653**	**693**	**697**	**750**	**700**
		Available Space	*216*	*204*	*184*	*168*	*104*	*64*	*60*	*7*	*57*
		Comments									
Shady Grove MS		Program Capacity	867	867	867	867	867	867	867	867	867
		Enrollment	**592**	**576**	**600**	**601**	**610**	**594**	**581**	**650**	**600**
		Available Space	*275*	*291*	*267*	*266*	*257*	*273*	*286*	*217*	*267*
		Comments									
Candlewood ES		Program Capacity	550	510	493	476	476	476	476		
		Enrollment	**329**	**334**	**355**	**364**	**369**	**374**	**390**		
		Available Space	*221*	*176*	*138*	*112*	*107*	*102*	*86*		
		Comments	Rev/Ex Complete	+1 EXT + Student Services	+1 EXT	+1 EXT					
Cashell ES		Program Capacity	341	341	341	341	341	341	341		
		Enrollment	**337**	**361**	**377**	**385**	**379**	**369**	**367**		
		Available Space	*4*	*(20)*	*(36)*	*(44)*	*(38)*	*(28)*	*(26)*		
		Comments									
Flower Hill ES	CSR	Program Capacity	483	483	483	483	483	483	483		
		Enrollment	**505**	**501**	**465**	**459**	**449**	**442**	**438**		
		Available Space	*(22)*	*(18)*	*18*	*24*	*34*	*41*	*45*		
		Comments									
Mill Creek Towne ES	CSR	Program Capacity	326	326	326	326	326	326	326		
		Enrollment	**412**	**416**	**398**	**395**	**391**	**386**	**386**		
		Available Space	*(86)*	*(90)*	*(72)*	*(69)*	*(65)*	*(60)*	*(60)*		
		Comments									
Judith A. Resnik ES	CSR	Program Capacity	493	493	493	493	493	493	751		
		Enrollment	**615**	**627**	**635**	**626**	**609**	**585**	**599**		
		Available Space	*(122)*	*(134)*	*(142)*	*(133)*	*(116)*	*(92)*	*152*		
		Comments			Planning for Addition				Addition Complete		
Sequoyah ES	CSR	Program Capacity	470	470	470	470	470	470	470		
		Enrollment	**433**	**439**	**464**	**482**	**480**	**485**	**481**		
		Available Space	*37*	*31*	*6*	*(12)*	*(10)*	*(15)*	*(11)*		
		Comments									
Cluster Information		HS Utilization	76%	73%	78%	81%	82%	86%	87%	93%	88%
		HS Enrollment	1520	1442	1521	1564	1599	1666	1686	1800	1700
		MS Utilization	70%	69%	72%	73%	78%	79%	79%	86%	80%
		MS Enrollment	1132	1128	1172	1189	1263	1287	1278	1400	1300
		ES Utilization	99%	102%	103%	105%	103%	102%	93%	95%	95%
		ES Enrollment	2631	2678	2694	2711	2677	2641	2661	2700	2700

Demographic Characteristics of Schools

Schools	2014–2015 Total Enrollment	Two or more races %	Black or Afr. Amer. %	Asian%	Hispanic %	White %	2014–2015 FARMS%*	ESOL%**	2013–2014 Mobility Rate%***
Col. Zadok Magruder HS	1520	≤ 5.0%	18.1%	14.5%	34.5%	28.9%	33.5%	6.1%	9.8%
Redland MS	540	≤ 5.0%	20.0%	11.5%	33.1%	30.9%	38.1%	9.4%	8.3%
Shady Grove MS	592	6.4%	20.6%	14.4%	33.1%	25.5%	41.0%	9.1%	11.2%
Candlewood ES	329	≤ 5.0%	12.5%	19.5%	20.4%	42.9%	21.9%	16.1%	11.9%
Cashell ES	337	6.8%	12.8%	9.8%	23.7%	46.6%	21.7%	11.0%	≤ 5.0%
Flower Hill ES	505	≤ 5.0%	30.5%	12.9%	45.1%	7.3%	63.0%	32.7%	18.4%
Mill Creek Towne ES	412	6.1%	14.1%	10.9%	42.0%	26.5%	48.5%	28.9%	16.7%
Judith A. Resnik ES	615	≤ 5.0%	31.7%	12.7%	38.0%	14.3%	55.9%	28.6%	14.0%
Sequoyah ES	433	≤ 5.0%	17.1%	10.9%	47.8%	20.6%	55.9%	33.0%	16.5%
Elementary Cluster Total	**2631**	**≤ 5.0%**	**21.5%**	**12.6%**	**37.6%**	**23.6%**	**47.4%**	**26.3%**	**14.3%**
Elementary County Total	75,144	≤ 5.0%	21.2%	13.9%	30.4%	29.3%	40.2%	23.3%	13.3%

**Percent of students approved for Free and Reduced-priced Meals Program (FARMS) during the 2014–2015 school year.*

***Percent of English for Speakers of Other Languages (ESOL) during the 2014–2015 school year. High School students are served in regional ESOL centers.*

****Mobility Rate is the number of entries plus withdrawals during the 2013–2014 school year compared to total enrollment.*
Notes: Native Hawaiian/Pacific Islander and American Indian/Alaskan Native categories total less than 1% and were therefore excluded from the table.

Due to federal and state guidelines, demographic characteristics of schools of less than or equal to 5.0% are reported as ≤ 5.0%.


Program Capacity Table

(School Year 2014–2015)

Schools	Grades Served	Capacity (HS @90% MS@85%)	Total Rooms	Support Rooms	Regular Secondary @25	Regular Elementary @23	CSR Grades 1–2 @18	Pre–K @20	Pre–K @40	HS @20	CSR KIND @18	KIND @22	ESOL @15	METS @15	Special Education Services: School Based: HSM @13	School Based: ELEM LAD @13	Cluster Based: ELC @10	Quad Cluster Based: LANG @12	Quad Cluster Based: LFI @10	Quad Cluster Based: SCB @6	County & Regional Based: AAC@7	AUT @6	BRIDGE @10	DHOH @7	ED @10	EXTENSIONS @6	GT/LD @13	PD @7	PEP@6	PEP @12	PEP @18	VISION (Elementary) @7	OTHER
Col. Zadok Magruder HS	9-12	1995	91		87								2									2											
Redland MS	6-8	757	36		35								1																				
Shady Grove MS	6-8	867	45		40																				2								3
Candlewood ES	K-5	550	28	4		22						2																					
Cashell ES	PreK-5	341	21	3		11		1				2								2									2				
Flower Hill ES	PreK-5	483	29	5		9	8		1		4													2									
Mill Creek Towne ES	HS-5	326	25	5		2	8	1			3						5	1															
Judith A. Resnik ES	PreK-5	493	31	5		5	13		1		5																	2					
Sequoyah ES	K-5	470	30	5		7	10				5					3																	

Facility Characteristics of Schools 2014–2015

Schools	Year Facility Opened	Year Reopened/ Revitalized	Total Square Footage	Site Size Acres	Adjacent Park	Reloc-atable Classrooms	Linkages to Learning Program	Home School Model
Col. Zadok Magruder HS	1970		295,478	30				
Redland MS	1971		112,297	20.64	Yes			
Shady Grove MS	1995	1999	129,206	20				
Candlewood ES	1968	2015	82,222	11.8				
Cashell ES	1969	2009	71,171	10.24				
Flower Hill ES	1985		58,770	10	Yes	4		
Mill Creek Towne ES	1966	2000	67,465	8.4		3		
Judith A. Resnik ES	1991		78,547	12.8		6		
Sequoyah ES	1990		72,582	10	Yes			

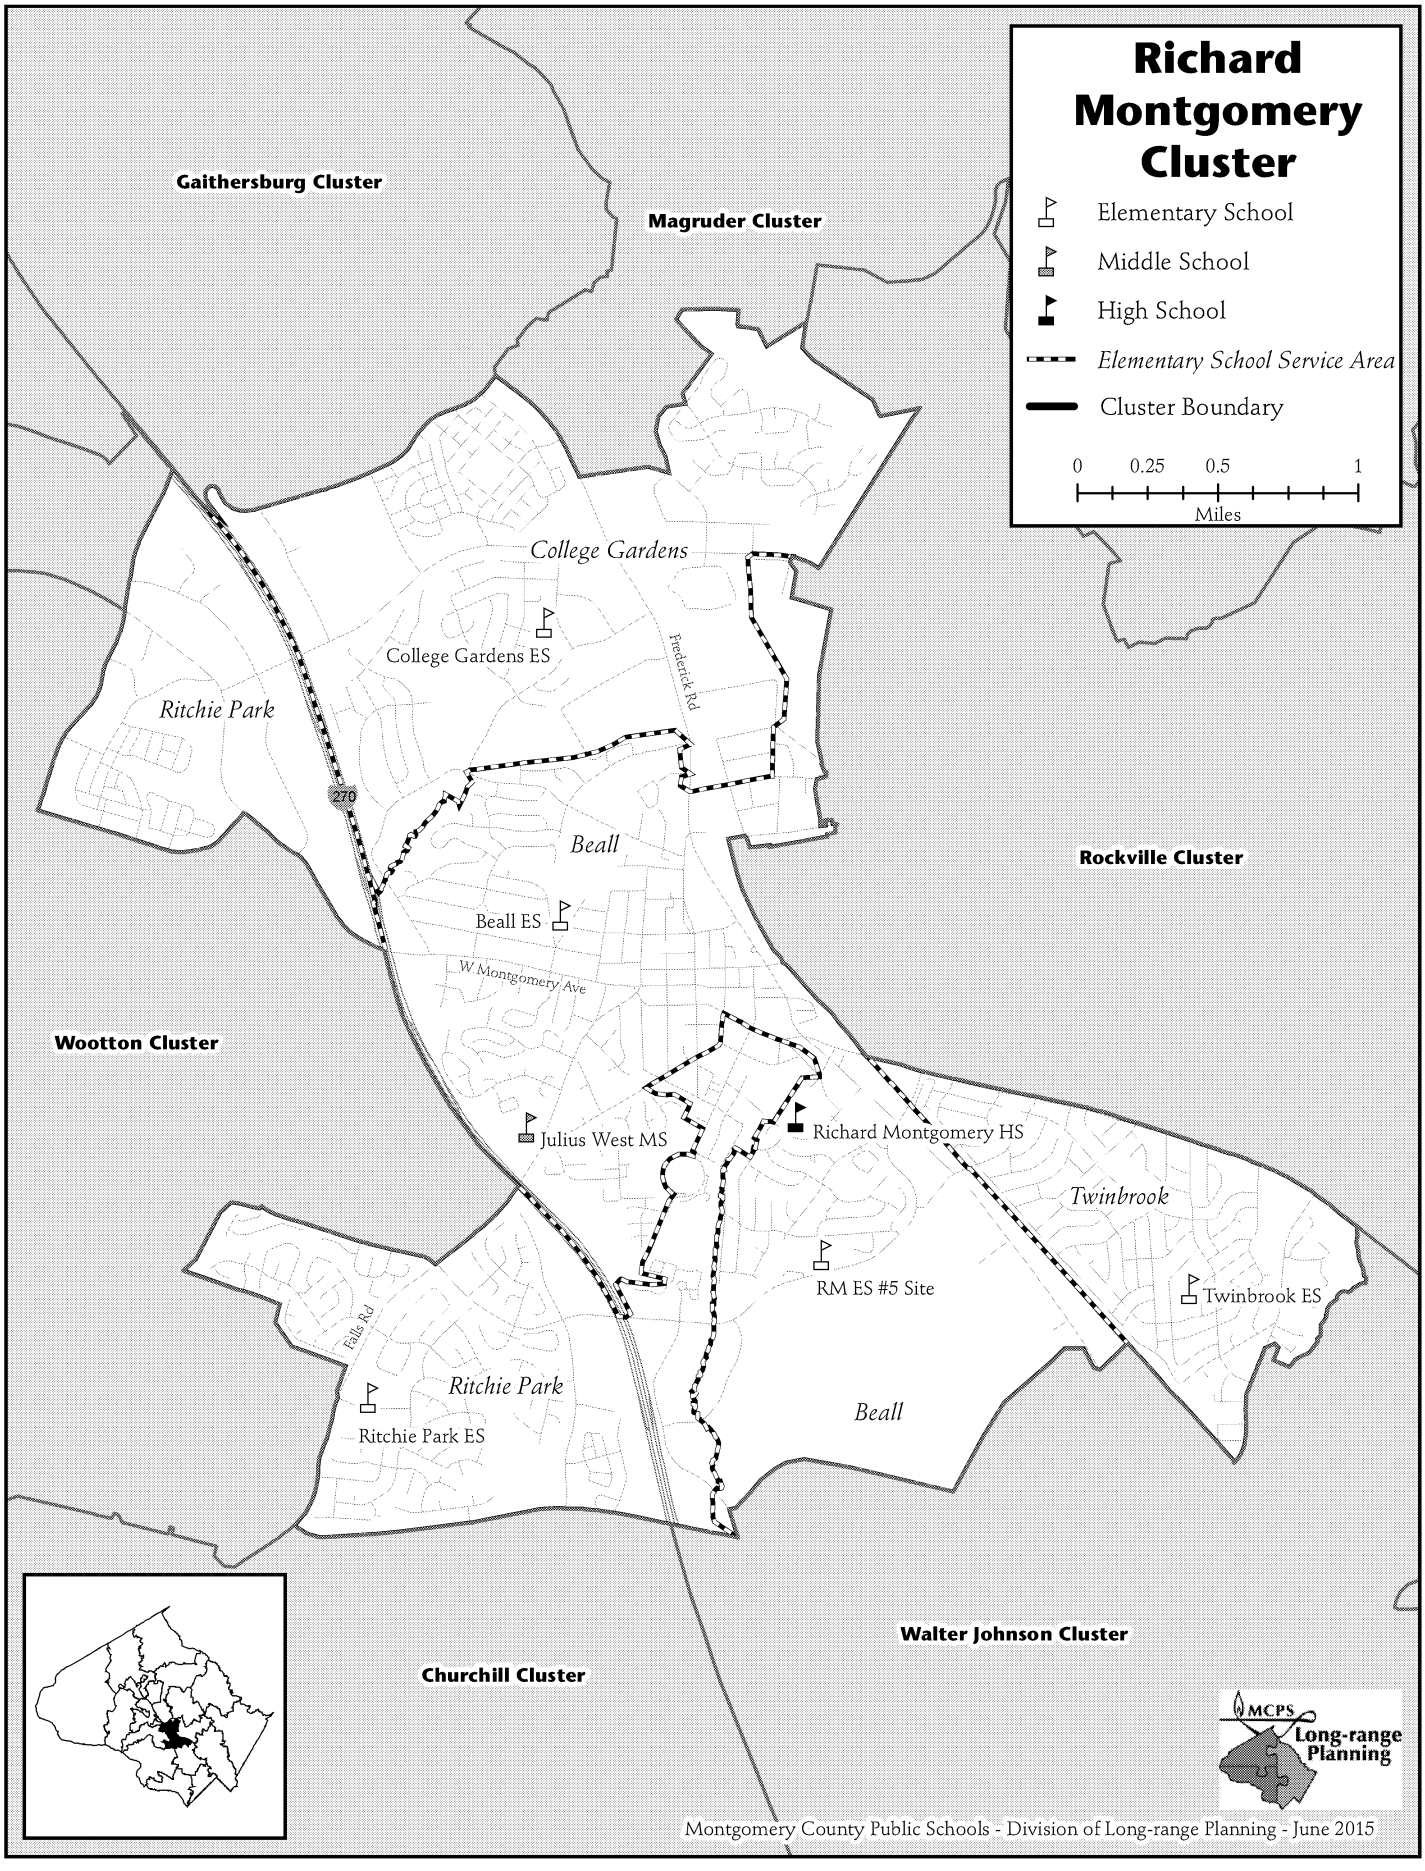
Richard Montgomery Cluster
Elementary School
Middle School
High School
Elementary School Service Area
Cluster Boundary
0 0.25 0.5 1
Miles
Gaithersburg Cluster
Magruder Cluster
College Gardens
College Gardens ES
Frederick Rd
Ritchie Park
270
Beall
Rockville Cluster
Beall ES
W Montgomery Ave
Wootton Cluster
Julius West MS
Richard Montgomery HS
Twinbrook
RM ES #5 Site
Twinbrook ES
Falls Rd
Ritchie Park
Ritchie Park ES
Beall
Walter Johnson Cluster
Churchill Cluster
MCPS
Long-range Planning
Montgomery County Public Schools - Division of Long-range Planning - June 2015

CLUSTER PLANNING ISSUE

Planning Issue: The City of Rockville is developing the Rockville Pike Plan with adoption anticipated in 2015. Preliminary planning suggests between 4,000 and 6,000, mostly multi-family residential units, may be provided in the Rockville Pike corridor. This development would occur on either side of Rockville Pike, from the intersection at Veirs Mill Road at the north to Rollins Avenue in the south. Most of this area is in the Richard Montgomery Cluster. The plan will require the redevelopment of existing land uses and require significant roadway improvements. It is anticipated that the plan would take 20 to 30 years to build-out and the pace of construction will be market driven.

Student enrollment at elementary schools in the Richard Montgomery Cluster has increased significantly over the past few years. The magnitude of enrollment growth in the cluster requires the opening of a new elementary school. A new elementary school is scheduled to open at the site of the former Hungerford Park Elementary School, located at 332 W. Edmonston Avenue in the City of Rockville. Julius West Middle School enrollment is projected to exceed capacity by almost 300 students by the end of the six-year CIP planning period. An addition project is scheduled for this school.

SCHOOLS

Richard Montgomery High School

Capital Project: Projections indicate enrollment at Richard Montgomery High School will exceed capacity by 200 seats or more by the end of the six-year CIP period. An FY 2016 appropriation is approved for facility planning to determine the feasibility, scope, and cost for a classroom addition. A date for the addition will be considered in a future CIP. Relocatable classrooms will be utilized until additional capacity can be added.

Julius West Middle School

Capital Project: Projections indicate enrollment at Julius West Middle School will exceed capacity by 150 seats or more by the end of the six-year CIP planning period. An FY 2015 appropriation was approved to begin the construction of the addition. The scheduled completion date for the addition is August 2016. Relocatable classrooms will be utilized until additional capacity can be provided.

Beall Elementary School


Capital Project: Projections indicate enrollment at Beall Elementary School will exceed capacity by 92 seats or more throughout the six-year CIP planning period. Relocatable classrooms will be utilized until Richard Montgomery Cluster Elementary School #5 (Hungerford Park site) opens. Although the Board of Education requested a completion date of August 2017, the County Council maintained the approved FY 2015–2020 CIP completion date of August 2018. FY 2017 expenditures are programmed in the Rehabilitation and Renovation of Closed Schools (RROCS) Project to construct the new elementary school. In order for this project to be completed on schedule, county and state funding must be provided at the levels approved in this CIP.

College Gardens Elementary School

Capital Project: Projections indicate enrollment at College Gardens Elementary School will exceed capacity by 92 seats or more throughout the six-year CIP planning period. Relocatable classrooms will be utilized until Richard Montgomery Cluster Elementary School #5 (Hungerford Park site) opens. Although the Board of Education requested a completion date of August 2017, the County Council maintained the approved FY 2015–2020 CIP completion date of August 2018. FY 2017 expenditures are programmed in the Rehabilitation and Renovation of Closed Schools (RROCS) Project to construct the new elementary school. In order for this project to be completed on schedule, county and state funding must be provided at the levels approved in this CIP.

Ritchie Park Elementary School

Capital Project: Projections indicate enrollment at Ritchie Park Elementary School will exceed capacity by 92 seats or more throughout the six-year CIP planning period. Relocatable classrooms will be utilized until Richard Montgomery Cluster Elementary School #5 (Hungerford Park site) opens. Although the Board of Education requested a completion date of August 2017, the County Council maintained the approved FY 2015–2020 CIP completion date of August 2018. FY 2017 expenditures are programmed in the Rehabilitation and Renovation of Closed Schools (RROCS) Project to construct the new elementary school. In order for this project to

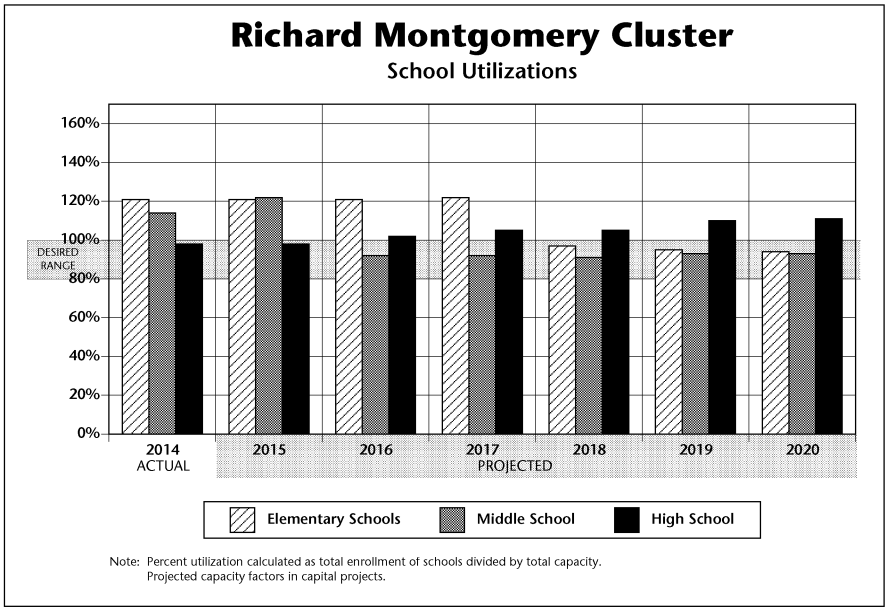

be completed on schedule, county and state funding must be provided at the levels approved in this CIP.

Richard Montgomery Cluster Elementary School #5 (Hungerford Park site)

Capital Project: Enrollment projections indicate the need for a new school in the cluster. Relocatable classrooms will be utilized at existing elementary schools until Richard Montgomery Cluster Elementary School #5 (Hungerford Park site) opens. Although the Board of Education requested a completion date of August 2017, the County Council maintained the approved FY 2015–2020 CIP completion date of August 2018. FY 2017 expenditures are programmed in the Rehabilitation and Renovation of Closed Schools (RROCS) Project to construct the new elementary school. In order for this project to be completed on schedule, county and state funding must be provided at the levels approved in this CIP.

Twinbrook Elementary School

Capital Project: A revitalization/expansion project is scheduled for this school. Although the Board of Education requested a completion date of January 2022, the County Council maintained the approved FY 2015–2020 CIP completion date of January 2023. FY 2017 expenditures are programmed for facility planning for a feasibility study to determine the scope and cost of the project. In order for this project to be completed on this schedule, county and state funding must be provided at the levels approved in this CIP.

CAPITAL PROJECTS

School	Project	Project Status*	Date of Completion
Richard Montgomery HS	Classroom addition	Proposed	TBD
Julius West MS	Classroom addition	Approved	Aug. 2016
Richard Montgomery Cluster ES #5	New school	Programmed	Aug. 2018
Twinbrook ES	Revitalization/ expansion	Programmed	Jan. 2023

"Approved"— Project has an FY 2015 or FY 2016 appropriation approved in the FY 2015–2020 CIP.

"Deferred"—Funds have been deferred for a future CIP.

"Programmed"—Project has expenditures programmed in a future year of the CIP for planning and/or construction funds.

"Proposed"—Project has facility planning funds approved for FY 2015 or approved for FY 2016 for a feasibility study.

Projected Enrollment and Space Availability

Effects of the Amended FY2015–2020 CIP and Non–CIP Actions on Space Available

Schools			Actual 14–15	Projections 15–16	16–17	17–18	18–19	19–20	20–21	2024	2029
Richard Montgomery HS		Program Capacity	2236	2236	2236	2236	2236	2236	2236	2236	2236
		Enrollment	**2199**	**2192**	**2280**	**2348**	**2355**	**2460**	**2479**	**2500**	**2500**
		Available Space	*38*	*44*	*(44)*	*(112)*	*(118)*	*(224)*	*(242)*	*(264)*	*(264)*
		Comments		Facility Planning for Addition							
Julius West MS		Program Capacity	1054	1054	1445	1445	1445	1445	1445	1445	1445
		Enrollment	**1201**	**1281**	**1329**	**1330**	**1315**	**1341**	**1351**	**1400**	**1400**
		Available Space	*(147)*	*(227)*	*116*	*115*	*130*	*104*	*94*	*45*	*45*
		Comments			Addition Complete						
Beall ES		Program Capacity	638	638	638	638	638	638	638		
		Enrollment	**801**	**814**	**793**	**794**	**798**	**790**	**783**		
		Available Space	*(163)*	*(176)*	*(155)*	*(156)*	*(160)*	*(152)*	*(145)*		
		Comments									
College Gardens ES		Program Capacity	694	694	694	694	694	694	694		
		Enrollment	**873**	**886**	**882**	**868**	**859**	**838**	**834**		
		Available Space	*(179)*	*(192)*	*(188)*	*(174)*	*(165)*	*(144)*	*(140)*		
		Comments									
Richard Montgomery Cluster ES #5 (Hungerford Park)		Program Capacity					602	602	602		
		Enrollment					**0**	**0**	**0**		
		Available Space					*602*	*602*	*602*		
		Comments	Planning for new school				Opens Aug. 2018				
Ritchie Park ES		Program Capacity	387	387	387	387	387	387	387		
		Enrollment	**551**	**545**	**541**	**551**	**564**	**554**	**551**		
		Available Space	*(164)*	*(158)*	*(154)*	*(164)*	*(177)*	*(167)*	*(164)*		
		Comments									
Twinbrook ES	CSR	Program Capacity	563	563	563	563	563	563	563		
		Enrollment	**531**	**525**	**551**	**560**	**565**	**548**	**556**		
		Available Space	*32*	*38*	*12*	*3*	*(2)*	*15*	*7*		
		Comments			Facility Planning for Rev/Ex		Planning for Revitalization/ Expansion				
Cluster Information		HS Utilization	98%	98%	102%	105%	105%	110%	111%	112%	112%
		HS Enrollment	2199	2192	2280	2348	2355	2460	2479	2500	2500
		MS Utilization	114%	122%	92%	92%	91%	93%	93%	97%	97%
		MS Enrollment	1201	1281	1329	1330	1315	1341	1351	1400	1400
		ES Utilization	121%	121%	121%	122%	97%	95%	94%	97%	97%
		ES Enrollment	2756	2770	2767	2773	2786	2730	2724	2800	2800

Demographic Characteristics of Schools

Schools	2014–2015 Total Enrollment	Two or more races %	Black or Afr. Amer. %	Asian%	Hispanic %	White %	2014–2015 FARMS%*	ESOL%**	2013–2014 Mobility Rate%***
Richard Montgomery HS	2199	≤ 5.0%	16.3%	25.1%	23.5%	30.0%	20.2%	6.5%	11.2%
Julius West MS	1201	5.9%	15.2%	20.6%	26.5%	31.7%	29.6%	11.2%	12.4%
Beall ES	801	7.5%	13.9%	21.7%	22.2%	34.6%	26.2%	15.1%	12.3%
College Gardens ES	873	6.4%	16.6%	22.9%	14.3%	39.5%	15.1%	13.1%	16.3%
Ritchie Park ES	551	5.3%	9.8%	21.6%	18.0%	44.8%	19.2%	11.4%	10.0%
Twinbrook ES	531	≤ 5.0%	10.9%	15.6%	57.6%	11.9%	66.7%	46.1%	18.1%
Elementary Cluster Total	**2756**	**6.0%**	**13.4%**	**20.9%**	**25.7%**	**33.8%**	**29.2%**	**19.8%**	**14.3%**
Elementary County Total	**75,144**	**≤ 5.0%**	**21.2%**	**13.9%**	**30.4%**	**29.3%**	**40.2%**	**23.3%**	**13.3%**

**Percent of students approved for Free and Reduced-priced Meals Program (FARMS) during the 2014–2015 school year.*

***Percent of English for Speakers of Other Languages (ESOL) during the 2014–2015 school year. High School students are served in regional ESOL centers.*

****Mobility Rate is the number of entries plus withdrawals during the 2013–2014 school year compared to total enrollment.*

Notes: Native Hawaiian/Pacific Islander and American Indian/Alaskan Native categories total less than 1% and were therefore excluded from the table.

Due to federal and state guidelines, demographic characteristics of schools of less than or equal to 5.0% are reported as ≤ 5.0%.


Program Capacity Table


(School Year 2014–2015)

Schools	Grades Served	Capacity (HS @90% MS@85%)	Total Rooms	Support Rooms	Regular Secondary @25	Regular Elementary @23	CSR Grades 1–2 @18	Pre–K @20	Pre–K @40	HS @20	CSR KIND @18	KIND @22	ESOL @15	METS @15	Special Education Services: School Based: HSM @13	School Based: ELEM LAD @13	Quad Cluster Based: ELC @10	Quad Cluster Based: LANG @12	Quad Cluster Based: LFI @10	Quad Cluster Based: SCB @6	County & Regional Based: AAC@7	County & Regional Based: AUT @6	County & Regional Based: BRIDGE @10	County & Regional Based: DHOH @7	County & Regional Based: ED @10	County & Regional Based: EXTENSIONS @6	County & Regional Based: GT/LD @13	County & Regional Based: PD @7	County & Regional Based: PEP@6	County & Regional Based: PEP @12	County & Regional Based: PEP @18	County & Regional Based: VISION (Elementary) @7	County & Regional Based: OTHER
Richard Montgomery HS	9-12	2237	102		97								2												3							
Julius West MS	6-8	1054	52		47								2	1											2							
Beall ES	HS-5	638	33	4		19			1	1		5						2			1											
College Gardens ES	HS-5	694	36	4		24				1		5										2										
Ritchie Park ES	K-5	387	21	4		13						4																				
Twinbrook ES	HS-5	563	34	6		9	11		1	1	4					2																

Facility Characteristics of Schools 2014–2015

Schools	Year Facility Opened	Year Reopened/ Revitalized	Total Square Footage	Site Size Acres	Adjacent Park	Reloc-atable Classrooms	Linkages to Learning Program	Home School Model
Richard Montgomery HS	1942	2007	311,500	29.05				
Julius West MS	1961	1995	147,223	21.3		6		
Beall ES	1954	1991	79,477	8.4	Yes	8		
College Gardens ES	1967	2008	96,986	7.9	Yes	6		
Ritchie Park ES	1966	1997	58,500	9.2		6		
Twinbrook ES	1952	1986	79,818	10.5		4		

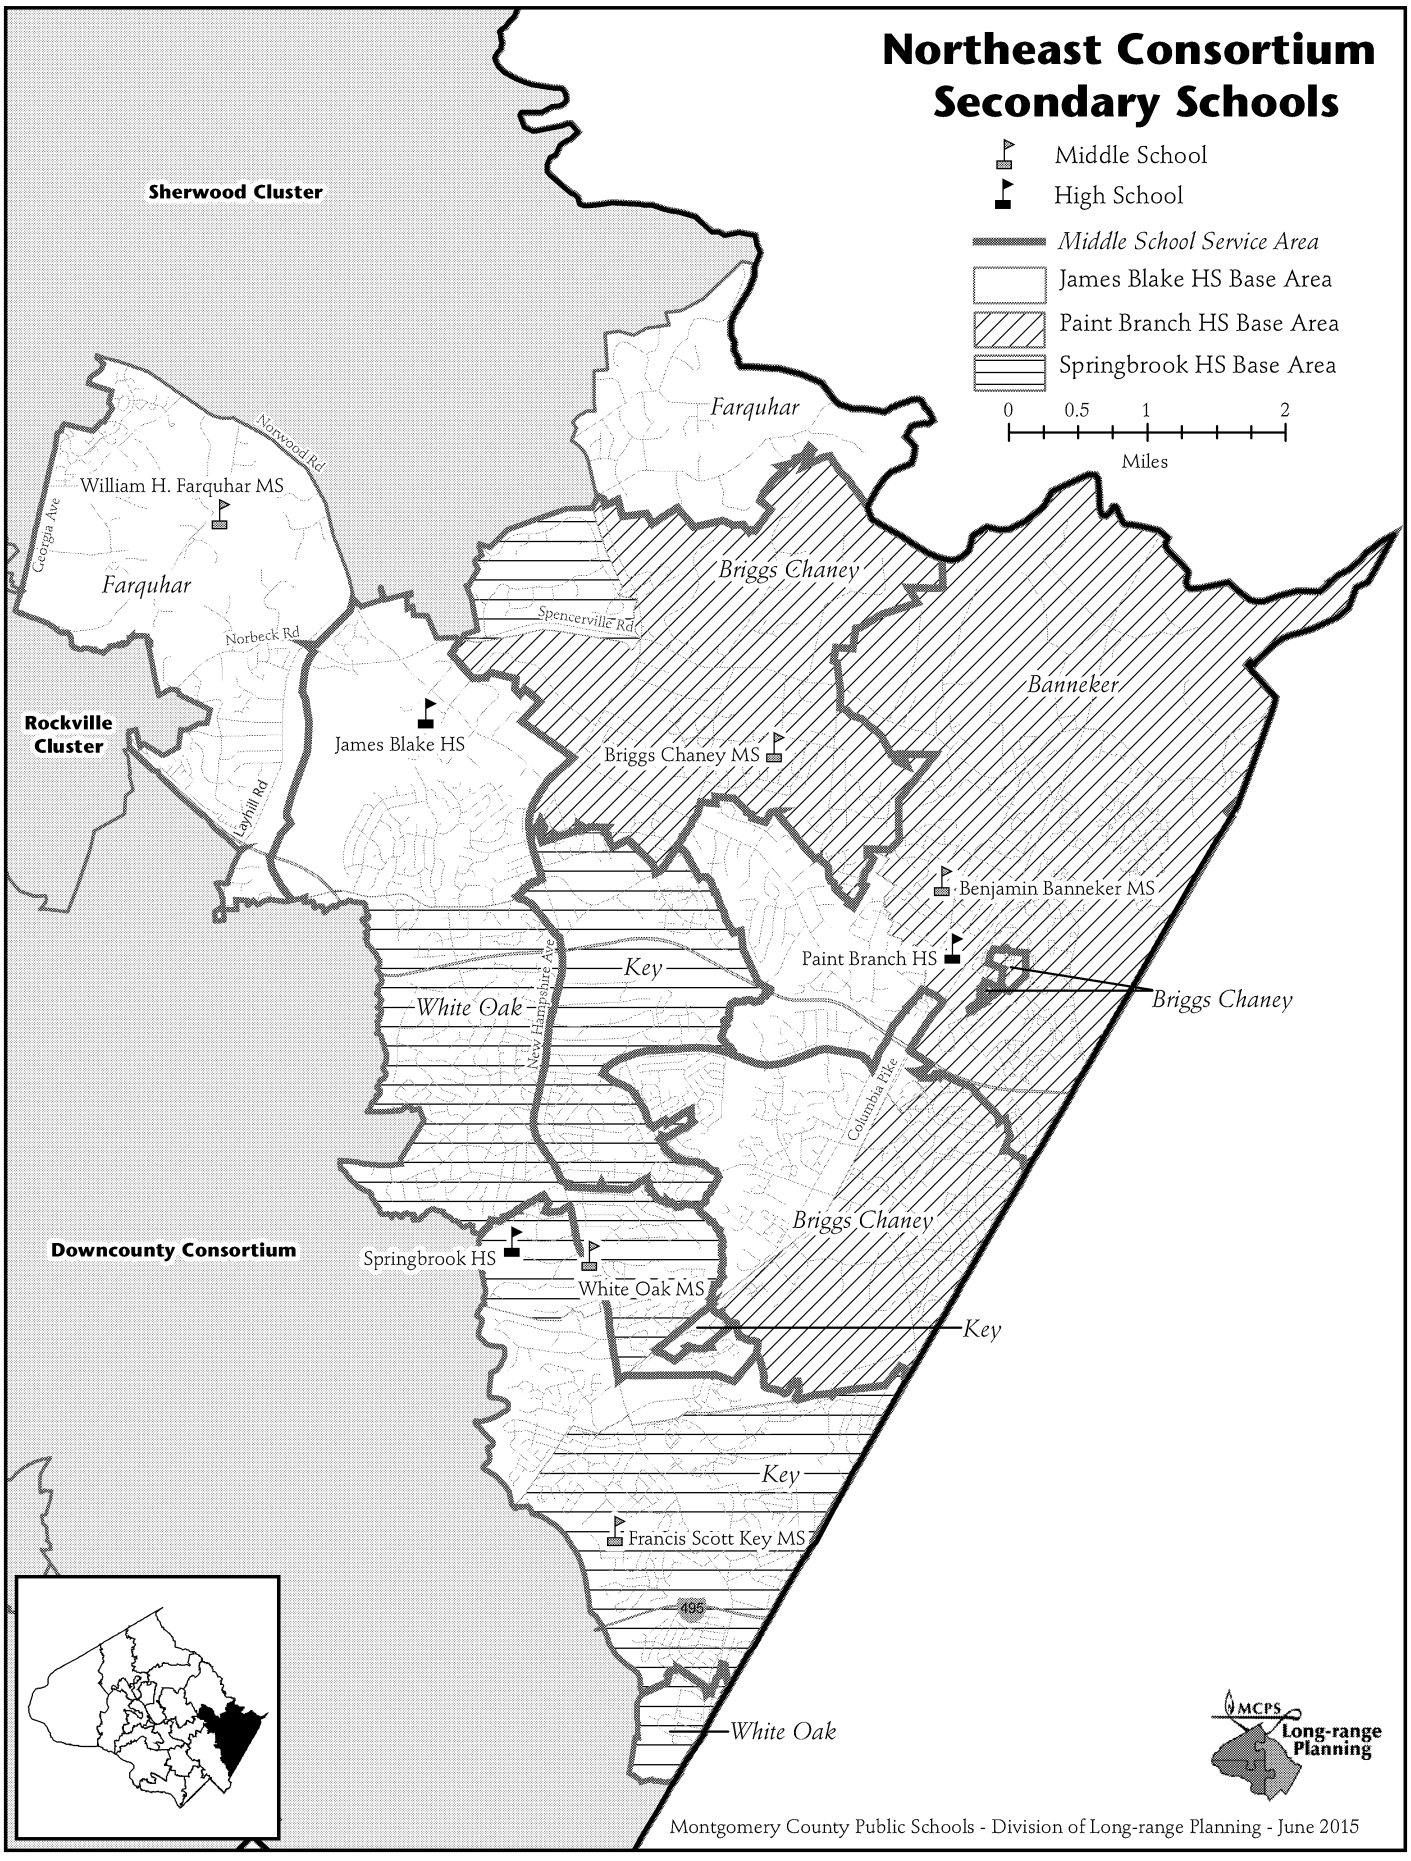
Northeast Consortium
Secondary Schools
Middle School
High School
Middle School Service Area
James Blake HS Base Area
Paint Branch HS Base Area
Springbrook HS Base Area
0 0.5 1 2
Miles
Sherwood Cluster
Rockville Cluster
Downcounty Consortium
Norwood Rd
Georgia Ave
William H. Farquhar MS
Farquhar
Norbeck Rd
Layhill Rd
James Blake HS
Spencerville Rd
Briggs Chaney
Briggs Chaney MS
Banneker
Benjamin Banneker MS
Paint Branch HS
Briggs Chaney
New Hampshire Ave
Key
White Oak
Columbia Pike
Springbrook HS
White Oak MS
Francis Scott Key MS
495
MCPS
Long-range Planning
Montgomery County Public Schools - Division of Long-range Planning - June 2015

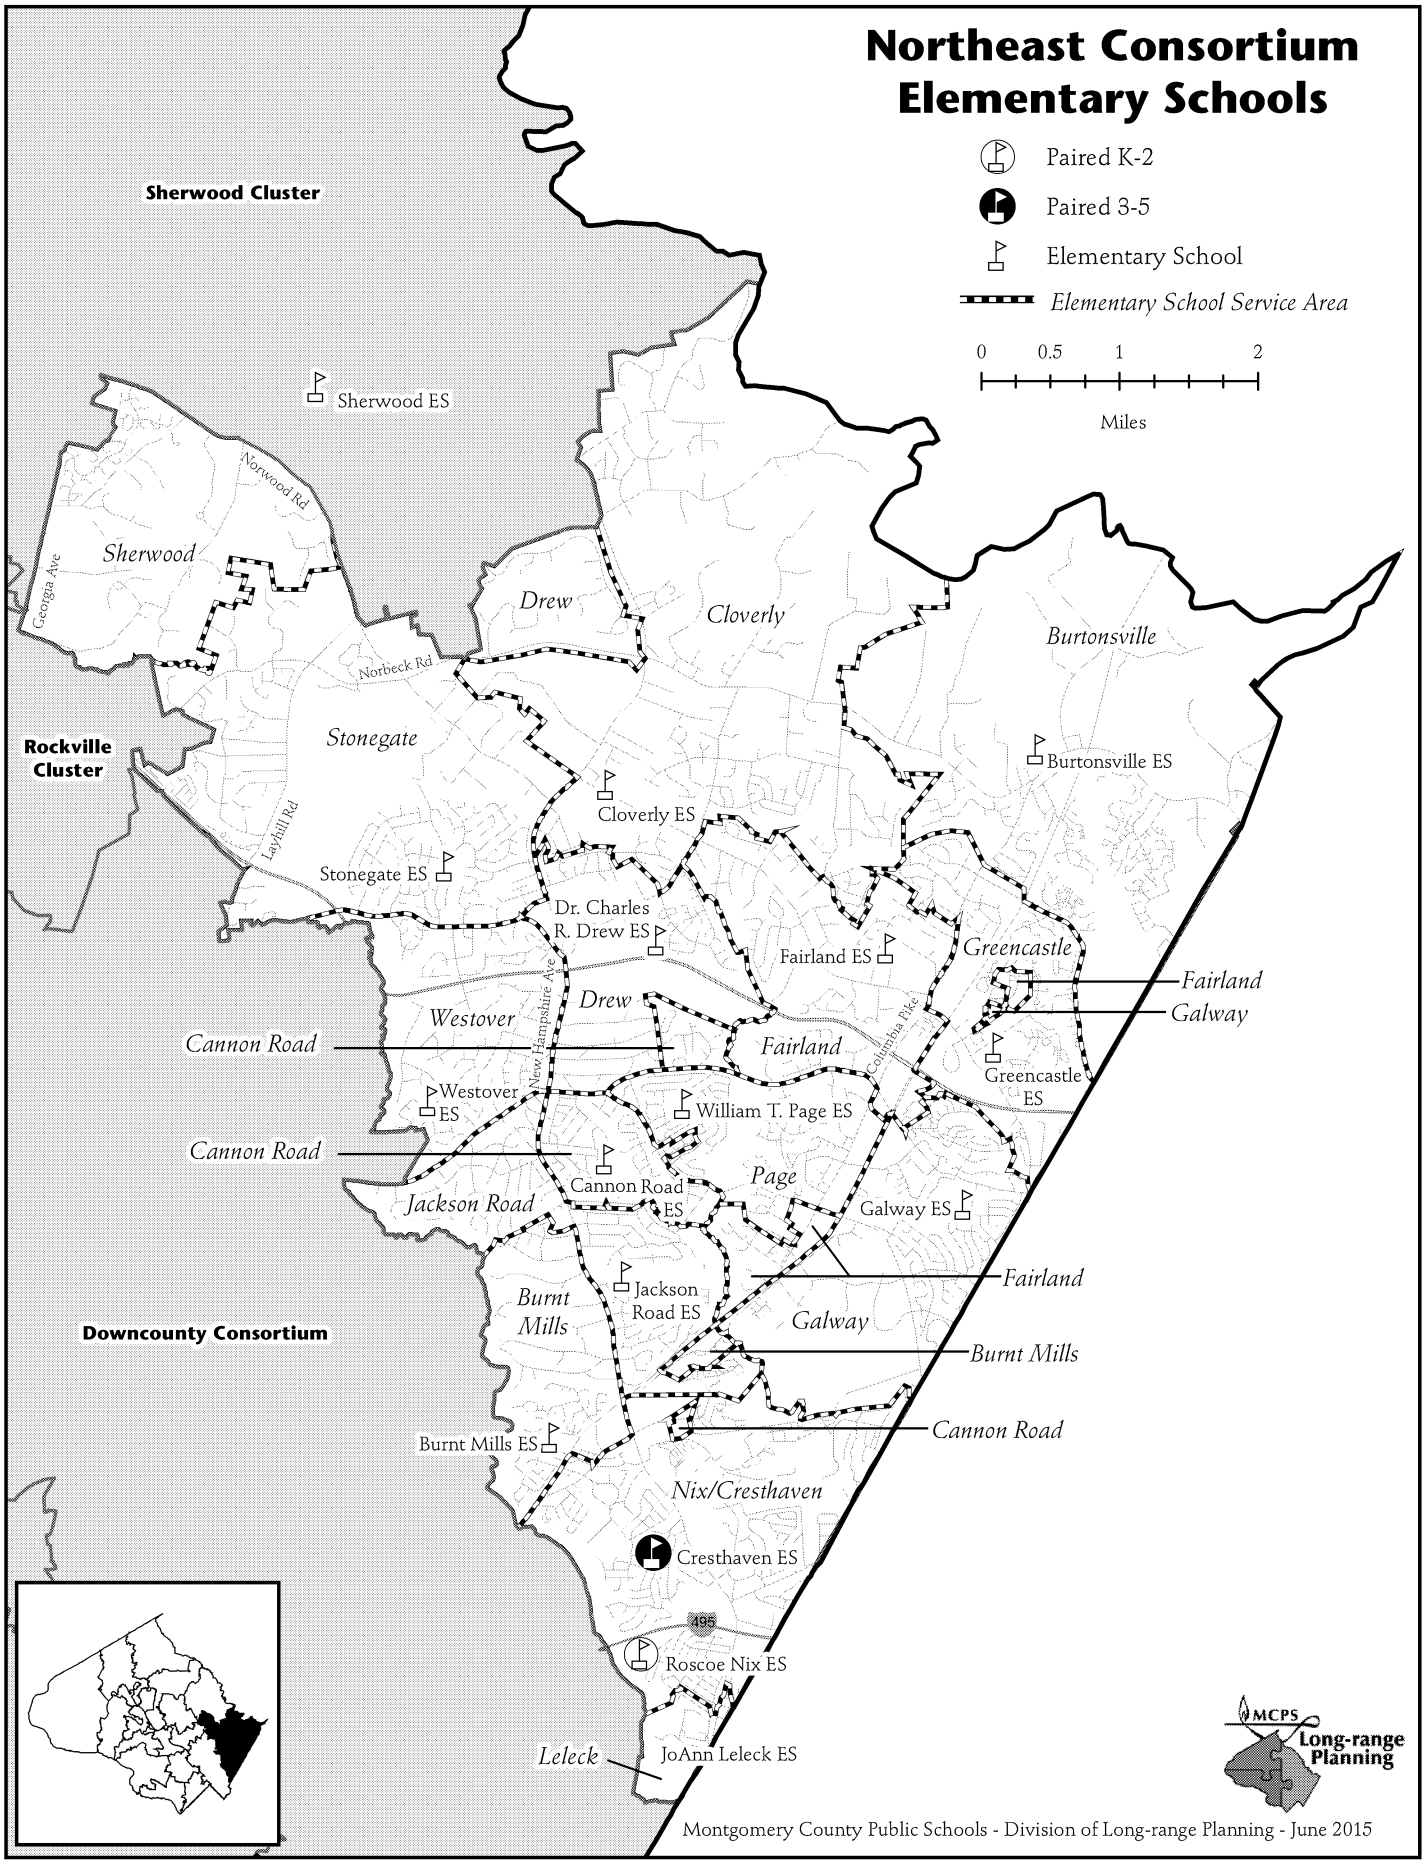
Northeast Consortium
Elementary Schools
Paired K-2
Paired 3-5
Elementary School
Elementary School Service Area
0 0.5 1 2
Miles
Sherwood Cluster
Rockville Cluster
Downcounty Consortium
Sherwood ES
Norwood Rd
Georgia Ave
Sherwood
Drew
Cloverly
Burtonsville
Norbeck Rd
Stonegate
Burtonsville ES
Cloverly ES
Layhill Rd
Stonegate ES
Dr. Charles R. Drew ES
Fairland ES
Greencastle
Fairland
Galway
Drew
Westover
New Hampshire Ave
Columbia Pike
Cannon Road
Fairland
Greencastle ES
Westover ES
William T. Page ES
Cannon Road
Page
Cannon Road ES
Jackson Road
Galway ES
Fairland
Burnt Mills
Jackson Road ES
Galway
Burnt Mills
Cannon Road
Burnt Mills ES
Nix/Cresthaven
Cresthaven ES
495
Roscoe Nix ES
Leleck
JoAnn Leleck ES
MCPS
Long-range Planning
Montgomery County Public Schools - Division of Long-range Planning - June 2015

CONSORTIUM PLANNING ISSUES

The Northeast Consortium provides a program delivery model for the three high schools in the northeast area of the county. Students living in this area of the county are able to choose which of three high schools they wish to attend, based on different signature programs offered at the high schools. The Northeast Consortium choice programs are offered at James Hubert Blake, Paint Branch, and Springbrook high schools. Choice patterns will be monitored for their impact on projected enrollment and facility utilization.

A high school base area map and middle school articulation diagram are included for the three consortium high schools. Students residing in a base area are guaranteed to attend the high school serving that base area, if it is their first choice.

Planning Issue: The 2014 adopted White Oak Science Gateway Master Plan provides for up to 8,570 mostly multi-family residential units. The plan will require the redevelopment of many existing land uses. It is anticipated that it will take 20 to 30 years for build-out of the plan to occur and the pace of construction will be market driven. A future elementary school site is included in the plan.

SCHOOLS

William H. Farquhar Middle School

Capital Project: A revitalization/expansion project is scheduled for this school with a completion date of August 2016. An FY 2015 appropriation was approved to construct the project on an adjacent property.

JoAnn Leleck Elementary School at Broad Acres

Capital Project: Previous projections indicated enrollment at JoAnn Leleck Elementary School at Broad Acres would exceed capacity by 92 seats or more by the end of the six-year CIP period. Therefore an FY 2014 appropriation was approved for facility planning to determine the feasibility, scope, and cost for a classroom addition. With the revised capacity calculation for class-size reduction schools, the enrollment projections will not exceed 92 seats or more by the end of the current six-year period. A date for the addition will be considered in a future CIP if the enrollment of the school exceeds the capacity by more than 92 seats. Relocatable classrooms will be utilized until additional capacity can be added.

Burnt Mills Elementary School


Capital Project: Projections indicate enrollment at Burnt Mills Elementary School will exceed capacity by 92 seats or more by the end of the six-year CIP period. An FY 2012 appropriation was approved for facility planning to determine the feasibility, scope, and cost for a classroom addition. The school is on the revitalization/expansion project schedule, but outside of the six-year CIP planning period. However, due to fiscal constraints in the county and because enrollment did not exceed capacity by more than 150 seats by the end of the six-year CIP planning period when the FY 2015–2020 CIP was prepared in fall 2013, no funds were included in the CIP for a classroom addition. Because the school has a revitalization/expansion project planned, the additional capacity needed to address the space deficit will be added during that project. Relocatable classrooms will be utilized until additional capacity can be added as part of the project.

Burtonsville Elementary School

Capital Project: Projections indicate enrollment at Burtonsville Elementary School will exceed capacity by 92 seats or more by the end of the six-year CIP period. A classroom addition project is approved for this school. Although the Board of Education requested a completion date of August 2019, the County Council maintained the approved FY 2015–2020 CIP completion date of August 2020. FY 2017 expenditures are programmed for planning funds to begin the architectural design for the classroom addition. Relocatable classrooms will be utilized until additional capacity can be added. In order for this project to be completed on schedule, county and state funding must be provided at the levels approved in this CIP.

Northeast Consortium Articulation

Elementary schools articulating to middle schools within a consortium of high schools

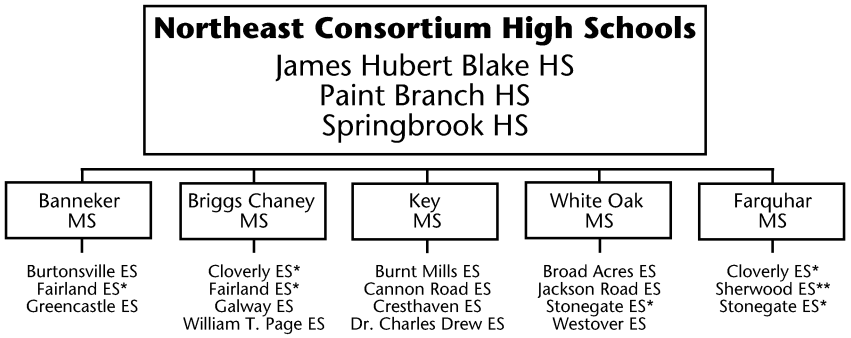

* Denotes schools with split articulation, i.e., some students feed into one middle school, while other students feed into another middle school.

** Students from Sherwood ES articulate to the Northeast Consortium high schools and Sherwood High School.

Greencastle Elementary School

Capital Project: Previous projections indicated enrollment at Greencastle Elementary School would exceed capacity by 92 seats or more by the end of the six-year CIP period. An FY 2013 appropriation was approved for facility planning to determine the feasibility, scope, and cost for a classroom addition. However, due to fiscal constraints in the county and because enrollment did not exceed capacity by more than 150 seats by the end of the six-year CIP planning period when the FY 2015–2020 CIP was prepared in fall 2013, no funds were included in the CIP for a classroom addition. A date for the addition will be considered in a future CIP. Relocatable classrooms will be utilized until additional capacity can be added.

Stonegate Elementary School

Capital Project: A revitalization/expansion project is scheduled for this school. Although the Board of Education requested a completion date of August 2020, the County Council maintained the approved FY 2015–2020 CIP completion date of August 2021. An FY 2015 appropriation was approved for facility planning for a feasibility study to determine the scope and cost of the project. In order for this project to be completed on this schedule, county and state funding must be provided at the levels approved in this CIP.

CAPITAL PROJECTS


School	Project	Project Status*	Date of Completion
Farquhar MS	Revitalization/ expansion	Approved	Aug. 2016
JoAnn Leleck ES at Broad Acres	Classroom addition	Proposed	TBD
Burtonsville ES	Classroom addition	Programmed	Aug. 2020
Greencastle ES	Classroom addition	Proposed	TBD
Stonegate ES	Revitalization/ expansion	Approved	Aug. 2021

"Approved"— Project has an FY 2015 or FY 2016 appropriation approved in the FY 2015–2020 CIP.

"Deferred"—Funds have been deferred for a future CIP.

"Programmed"—Project has expenditures programmed in a future year of the CIP for planning and/or construction funds.

"Proposed"—Project has facility planning funds approved for FY 2015 or approved for FY 2016 for a feasibility study.

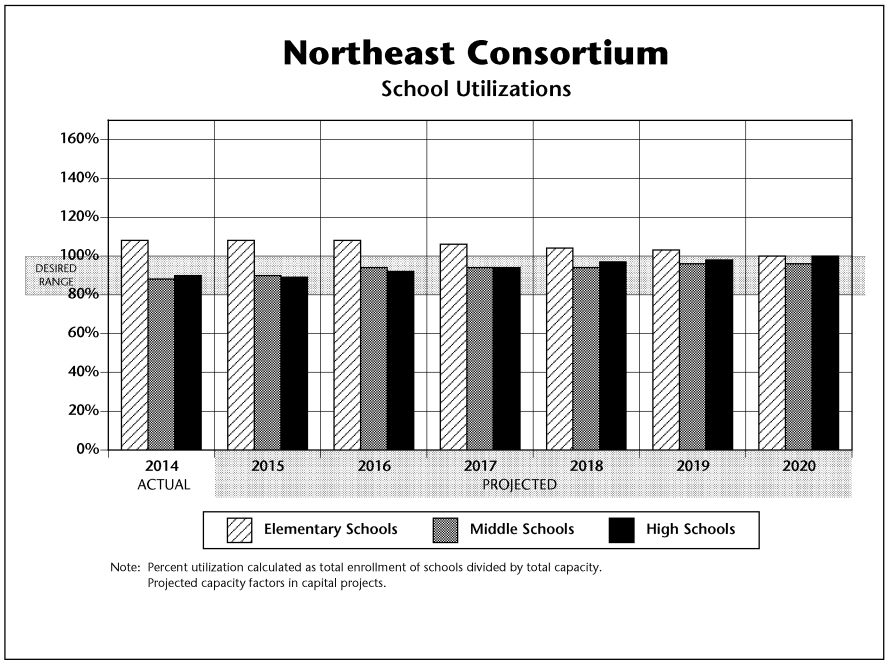

Projected Enrollment and Space Availability

Effects of the Amended FY2015–2020 CIP and Non–CIP Actions on Space Available

Schools			Actual 14–15	Projections 15–16	16–17	17–18	18–19	19–20	20–21	2024	2029
James Hubert Blake HS		Program Capacity	1743	1743	1743	1743	1743	1743	1743	1743	1743
		Enrollment	**1607**	**1578**	**1580**	**1653**	**1717**	**1744**	**1781**	**1900**	**1800**
		Available Space	*136*	*165*	*163*	*90*	*26*	*(1)*	*(38)*	*(157)*	*(57)*
		Comments									
Paint Branch HS		Program Capacity	2034	2034	2034	2034	2034	2034	2034	2034	2034
		Enrollment	**1996**	**1992**	**2056**	**2095**	**2140**	**2152**	**2158**	**2300**	**2200**
		Available Space	*38*	*42*	*(22)*	*(61)*	*(106)*	*(118)*	*(124)*	*(266)*	*(166)*
		Comments									
Springbrook HS		Program Capacity	2145	2162	2162	2162	2162	2162	2162	2162	2162
		Enrollment	**1750**	**1740**	**1810**	**1852**	**1883**	**1927**	**1976**	**2100**	**2000**
		Available Space	*395*	*422*	*352*	*310*	*279*	*235*	*186*	*62*	*162*
		Comments		-1 SCB							
Benjamin Banneker MS		Program Capacity	803	803	803	803	803	803	803	803	803
		Enrollment	**884**	**877**	**866**	**884**	**868**	**898**	**859**	**950**	**900**
		Available Space	*(81)*	*(74)*	*(63)*	*(81)*	*(65)*	*(95)*	*(56)*	*(147)*	*(97)*
		Comments									
Briggs Chaney MS		Program Capacity	969	969	969	969	969	969	969	969	969
		Enrollment	**891**	**903**	**906**	**853**	**854**	**904**	**902**	**1000**	**900**
		Available Space	*78*	*66*	*63*	*116*	*115*	*65*	*67*	*(31)*	*69*
		Comments									
William H. Farquhar MS		Program Capacity	906	906	752	752	752	752	752	752	752
		Enrollment	**586**	**589**	**615**	**593**	**592**	**577**	**580**	**650**	**600**
		Available Space	*320*	*317*	*137*	*159*	*160*	*175*	*172*	*102*	*152*
		Comments	Revitalization/ Expansion in progress		Rev/Ex Complete Aug. 2016						
Francis Scott Key MS		Program Capacity	961	961	961	961	961	961	961	961	961
		Enrollment	**942**	**976**	**957**	**959**	**970**	**1012**	**1013**	**1100**	**1000**
		Available Space	*18*	*(16)*	*4*	*2*	*(10)*	*(52)*	*(52)*	*(139)*	*(39)*
		Comments									
White Oak MS		Program Capacity	962	962	962	962	962	962	962	962	962
		Enrollment	**750**	**784**	**834**	**892**	**893**	**899**	**912**	**950**	**850**
		Available Space	*212*	*178*	*128*	*70*	*69*	*63*	*50*	*12*	*112*
		Comments									

Schools			Actual 14–15	Projections 15–16	16–17	17–18	18–19	19–20	20–21	2024	2029
Burnt Mills ES	CSR	Program Capacity	402	425	425	425	425	425	425		
		Enrollment	**538**	**554**	**580**	**553**	**549**	**538**	**521**		
		Available Space	*(136)*	*(129)*	*(155)*	*(128)*	*(124)*	*(113)*	*(96)*		
		Comments	See text	-1 Supp. Room							
Burtonsville ES	CSR	Program Capacity	485	485	485	485	485	485	735		
		Enrollment	**660**	**648**	**653**	**648**	**651**	**653**	**675**		
		Available Space	*(175)*	*(163)*	*(168)*	*(163)*	*(166)*	*(168)*	*60*		
		Comments			Planning for Addition				Addition Complete		
Cannon Road ES	CSR	Program Capacity	521	521	521	521	521	521	521		
		Enrollment	**432**	**438**	**434**	**436**	**434**	**428**	**426**		
		Available Space	*89*	*83*	*87*	*85*	*87*	*93*	*95*		
		Comments									
Cloverly ES		Program Capacity	454	454	454	454	454	454	454		
		Enrollment	**462**	**453**	**448**	**447**	**445**	**428**	**426**		
		Available Space	*(8)*	*1*	*6*	*7*	*9*	*26*	*28*		
		Comments									
Cresthaven ES Grades (3-5) Paired With Roscoe R. Nix ES	CSR	Program Capacity	467	467	467	467	467	467	467		
		Enrollment	**503**	**504**	**534**	**496**	**489**	**484**	**486**		
		Available Space	*(36)*	*(37)*	*(67)*	*(29)*	*(22)*	*(17)*	*(19)*		
		Comments									
Dr. Charles R. Drew ES	CSR	Program Capacity	456	456	456	456	456	456	456		
		Enrollment	**444**	**447**	**444**	**456**	**450**	**444**	**448**		
		Available Space	*12*	*9*	*12*	*0*	*6*	*12*	*8*		
		Comments									
Fairland ES	CSR	Program Capacity	648	648	648	648	648	648	648		
		Enrollment	**623**	**633**	**623**	**622**	**610**	**583**	**577**		
		Available Space	*25*	*15*	*25*	*26*	*38*	*65*	*71*		
		Comments									
Galway ES	CSR	Program Capacity	790	790	790	790	790	790	790		
		Enrollment	**808**	**797**	**788**	**790**	**777**	**737**	**740**		
		Available Space	*(18)*	*(7)*	*2*	*0*	*13*	*53*	*50*		
		Comments									
Greencastle ES	CSR	Program Capacity	582	582	582	582	582	582	582		
		Enrollment	**817**	**816**	**816**	**798**	**782**	**756**	**756**		
		Available Space	*(235)*	*(234)*	*(234)*	*(216)*	*(200)*	*(174)*	*(174)*		
		Comments									
Jackson Road ES	CSR	Program Capacity	709	709	709	709	709	709	709		
		Enrollment	**727**	**717**	**733**	**724**	**731**	**717**	**696**		
		Available Space	*(18)*	*(8)*	*(24)*	*(15)*	*(22)*	*(8)*	*13*		
		Comments									

Schools			Actual 14–15	Projections 15–16	16–17	17–18	18–19	19–20	20–21	2024	2029
JoAnn Leleck ES at Broad Acres	CSR	Program Capacity	672	715	715	715	715	715	715		
		Enrollment	**756**	**815**	**792**	**773**	**762**	**763**	**745**		
		Available Space	*(84)*	*(100)*	*(77)*	*(58)*	*(47)*	*(48)*	*(30)*		
		Comments		+1 preK -1 Supp. Room							
Roscoe R. Nix ES Grades (preK-2) Paired with Cresthaven ES	CSR	Program Capacity	521	521	521	521	521	521	521		
		Enrollment	**518**	**505**	**507**	**509**	**511**	**510**	**509**		
		Available Space	*3*	*16*	*14*	*12*	*10*	*11*	*12*		
		Comments									
William T. Page ES	CSR	Program Capacity	379	379	379	379	379	379	379		
		Enrollment	**410**	**412**	**389**	**373**	**372**	**372**	**364**		
		Available Space	*(31)*	*(33)*	*(10)*	*6*	*7*	*7*	*15*		
		Comments									
Sherwood ES		Program Capacity	569	569	569	569	569	569	569		
		Enrollment	**499**	**510**	**507**	**499**	**419**	**484**	**482**		
		Available Space	*70*	*59*	*62*	*70*	*150*	*85*	*87*		
		Comments									
Stonegate ES		Program Capacity	395	395	395	395	395	395	395		
		Enrollment	**492**	**475**	**474**	**465**	**465**	**460**	**442**		
		Available Space	*(97)*	*(80)*	*(79)*	*(70)*	*(70)*	*(65)*	*(47)*		
		Comments	Facility Planning for Rev/Ex			Planning for Revitalization/ Expansion		Move to Fairland Jan. 2020	@ Fairland		
Westover ES		Program Capacity	293	293	293	293	293	293	293		
		Enrollment	**304**	**326**	**332**	**340**	**337**	**346**	**345**		
		Available Space	*(11)*	*(33)*	*(39)*	*(47)*	*(44)*	*(53)*	*(52)*		
		Comments									
Cluster Information		HS Utilization	90%	89%	92%	94%	97%	98%	100%	106%	101%
		HS Enrollment	5353	5310	5446	5600	5740	5823	5915	5900	5900
		MS Utilization	88%	90%	94%	94%	94%	96%	96%	105%	96%
		MS Enrollment	4053	4129	4178	4181	4177	4290	4266	4450	4450
		ES Utilization	108%	108%	108%	106%	104%	103%	100%	98%	98%
		ES Enrollment	8993	9050	9054	8929	8784	8703	8638	8500	8500

Demographic Characteristics of Schools

Schools	2014–2015 Total Enrollment	Two or more races %	Black or Afr. Amer. %	Asian%	Hispanic %	White %	2014–2015 FARMS%*	2014–2015 ESOL%**	2013–2014 Mobility Rate%***
James Blake HS	1607	≤ 5.0%	43.4%	8.9%	21.7%	21.8%	32.9%	≤ 5.0%	9.7%
Paint Branch HS	1996	≤ 5.0%	54.6%	14.7%	16.8%	9.9%	35.6%	≤ 5.0%	11.6%
Springbrook HS	1750	≤ 5.0%	41.9%	11.1%	35.8%	8.2%	44.7%	10.2%	12.4%
Benjamin Banneker MS	884	5.2%	61.9%	10.4%	16.2%	6.2%	51.6%	≤ 5.0%	10.4%
Briggs Chaney MS	891	≤ 5.0%	53.2%	13.4%	19.9%	8.6%	45.9%	9.0%	15.0%
William H. Farquhar MS	586	6.1%	15.7%	14.2%	13.8%	50.2%	11.8%	≤ 5.0%	5.7%
Francis Scott Key MS	942	≤ 5.0%	42.5%	10.3%	40.0%	≤ 5.0%	62.6%	13.3%	13.0%
White Oak MS	750	≤ 5.0%	30.7%	11.2%	44.0%	10.9%	56.8%	16.8%	13.4%
Burnt Mills ES	538	≤ 5.0%	65.8%	≤ 5.0%	21.4%	5.8%	67.1%	24.9%	20.5%
Burtonsville ES	660	≤ 5.0%	62.0%	15.9%	12.9%	5.5%	52.3%	13.5%	11.6%
Cannon Road ES	432	≤ 5.0%	41.0%	9.5%	40.7%	6.5%	65.7%	14.1%	15.3%
Cloverly ES	462	8.7%	21.4%	18.6%	17.7%	33.3%	16.5%	11.7%	5.9%
Cresthaven ES	503	≤ 5.0%	36.8%	12.7%	44.7%	≤ 5.0%	72.0%	23.1%	16.2%
Dr. Charles R. Drew ES	444	6.5%	43.5%	18.7%	21.4%	9.7%	50.9%	17.8%	13.7%
Fairland ES	623	≤ 5.0%	60.0%	7.7%	20.5%	9.3%	55.1%	18.3%	21.2%
Galway ES	808	≤ 5.0%	58.9%	10.5%	22.6%	≤ 5.0%	58.3%	26.9%	16.7%
Greencastle ES	817	≤ 5.0%	67.0%	7.3%	20.2%	≤ 5.0%	63.6%	15.1%	23.9%
Jackson Road ES	727	≤ 5.0%	51.7%	9.2%	32.6%	≤ 5.0%	74.1%	30.3%	19.8%
JoAnn Leleck ES	758	≤ 5.0%	13.3%	5.3%	80.6%	≤ 5.0%	94.7%	67.2%	20.5%
Roscoe R. Nix ES	518	≤ 5.0%	39.0%	9.3%	44.0%	5.4%	74.3%	43.1%	21.8%
William T. Page ES	410	≤ 5.0%	52.2%	17.3%	20.5%	7.6%	54.1%	23.9%	11.7%
Sherwood ES	499	≤ 5.0%	20.2%	11.6%	11.8%	51.9%	16.6%	7.2%	8.2%
Stonegate ES	492	7.9%	33.5%	14.2%	18.1%	25.8%	21.3%	8.1%	12.2%
Westover ES	304	≤ 5.0%	33.2%	15.8%	22.4%	23.4%	23.4%	14.8%	7.6%
Elementary Cluster Total	**8995**	**≤ 5.0%**	**45.3%**	**11.1%**	**29.2%**	**10.7%**	**57.0%**	**24.1%**	**16.2%**
Elementary County Total	75,144	≤ 5.0%	21.2%	13.9%	30.4%	29.3%	40.2%	23.3%	13.3%

**Percent of students approved for Free and Reduced-priced Meals Program (FARMS) during the 2014–2015 school year.*

***Percent of English for Speakers of Other Languages (ESOL) during the 2014–2015 school year. High School students are served in regional ESOL centers.*

****Mobility Rate is the number of entries plus withdrawals during the 2013–2014 school year compared to total enrollment.*
Notes: Native Hawaiian/Pacific Islander and American Indian/Alaskan Native categories total less than 1% and were therefore excluded from the table.

Due to federal and state guidelines, demographic characteristics of schools of less than or equal to 5.0% are reported as ≤ 5.0%.


Program Capacity Table

(School Year 2014–2015)

Schools	Grades Served	Capacity (HS @90% MS@85%)	Total Rooms	Support Rooms	Regular Secondary @25	Regular Elementary @23	CSR Grades 1–2 @18	Pre–K @20	Pre–K @40	HS @20	CSR KIND @18	KIND @22	ESOL @15	METS @15	Special Education Services																		
															School Based	Cluster Based	Quad Cluster Based				County & Regional Based												
															HSM @13	ELEM LAD @13	ELC @10	LANG @12	LFI @10	SCB @6	AAC@7	AUT @6	BRIDGE @10	DHOH @7	ED @10	EXTENSIONS @6	GT/LD @13	PD @7	PEP@6	PEP @12	PEP @18	VISION (Elementary) @7	OTHER
James Blake HS	9-12	1743	79		77															2												
Paint Branch HS	9-12	2034	94		88														3						3							
Springbrook HS	9-12	2145	101		92								3						2	3												1
Benjamin Banneker MS	6-8	803	40		36								1						3													
Briggs Chaney MS	6-8	969	46		45								1																			
William H. Farquhar MS	6-8	906	44		42														1	1												
Francis Scott Key MS	6-8	961	46		44								2																			
White Oak MS	6-8	962	49		43								2	1						2												1
Burnt Mills ES	PreK-5	402	24	4		5	9		1		4				1																	
Burtonsville ES	K-5	485	29	4		7	12				6																					
Cannon Road ES	K-5	521	32	4		11	8				4					2		1			2											
Cloverly ES	K-5	454	27	4		14						3										3								1	2		
Cresthaven ES	3-5	467	27	4		18									1		4															
Dr. Charles R. Drew ES	PreK-5	456	29	4		8	6	1	1		3					2				4												
Fairland ES	HS-5	648	38	4		12	11	1		1	6														2				1			
Galway ES	PreK-5	790	45	6		18	11		1		6						3															
Greencastle ES	PreK-5	582	35	5		5	14		1		7				1																2	
Jackson Road ES	PreK-5	709	40	5		15	11		1		4																		1	1	2		
JoAnn Leleck ES	HS-5	672	40	7		11	12	1	1	1	6			1																		
Roscoe R. Nix ES	PreK-2	521	34	4			16		1		9				1							3											
William T. Page ES	PreK-5	379	24	4		4	9		1		4				1																		1
Sherwood ES	K-5	569	31	3		20						3			1					1		1							1	1			
Stonegate ES	K-5	395	23	4		13						3							3													
Westover ES	K-5	293	19	3		9						2						2				3											

Facility Characteristics of Schools 2014–2015

Schools	Year Facility Opened	Year Reopened/ Revitalized	Total Square Footage	Site Size Acres	Adjacent Park	Reloc-atable Classrooms	Linkages to Learning Program	Home School Model
James Blake HS	1998		297,125	91.09				
Paint Branch HS	1969	2012	347,169	45.98				
Springbrook HS	1960	1994	305,006	25.13	Yes			
Benjamin Banneker MS	1974		117,035	20			Yes	
Briggs Chaney MS	1991		115,000	29.4				
William H. Farquhar MS	1968		116,300	20				
Francis Scott Key MS	1966	2009	147,424	20.6			Yes	
White Oak MS	1962	1993	140,990	17.3				
Burnt Mills ES	1964	1990	57,318	15.1		4		Yes
Burtonsville ES	1952	1993	71,349	11.9		6		
Cannon Road ES	1967	2012	83,377	4.4	Yes			
Cloverly ES	1961	1989	61,991	10	Yes	2		
Cresthaven ES	1962	2010	76,862	9.8				Yes
Dr. Charles R. Drew ES	1991		73,975	12				
Fairland ES	1992		92,227	11.8				
Galway ES	1967	2009	103,170	9	Yes	2		Yes
Greencastle ES	1988		78,275	18.9		6		Yes
Jackson Road ES	1959	1995	91,465	8.8				
JoAnn Leleck ES	1952	1974	88,922	6.2	Yes	6		Yes
Roscoe R. Nix ES	2006		88,351	8.97	Yes			Yes
William T. Page ES	1965	2003	58,726	9.8		2		Yes
Sherwood ES	1977		81,727	10.85		1		Yes
Stonegate ES	1971		52,468	10.3		4		
Westover ES	1964	1998	54,645	7.6		2		

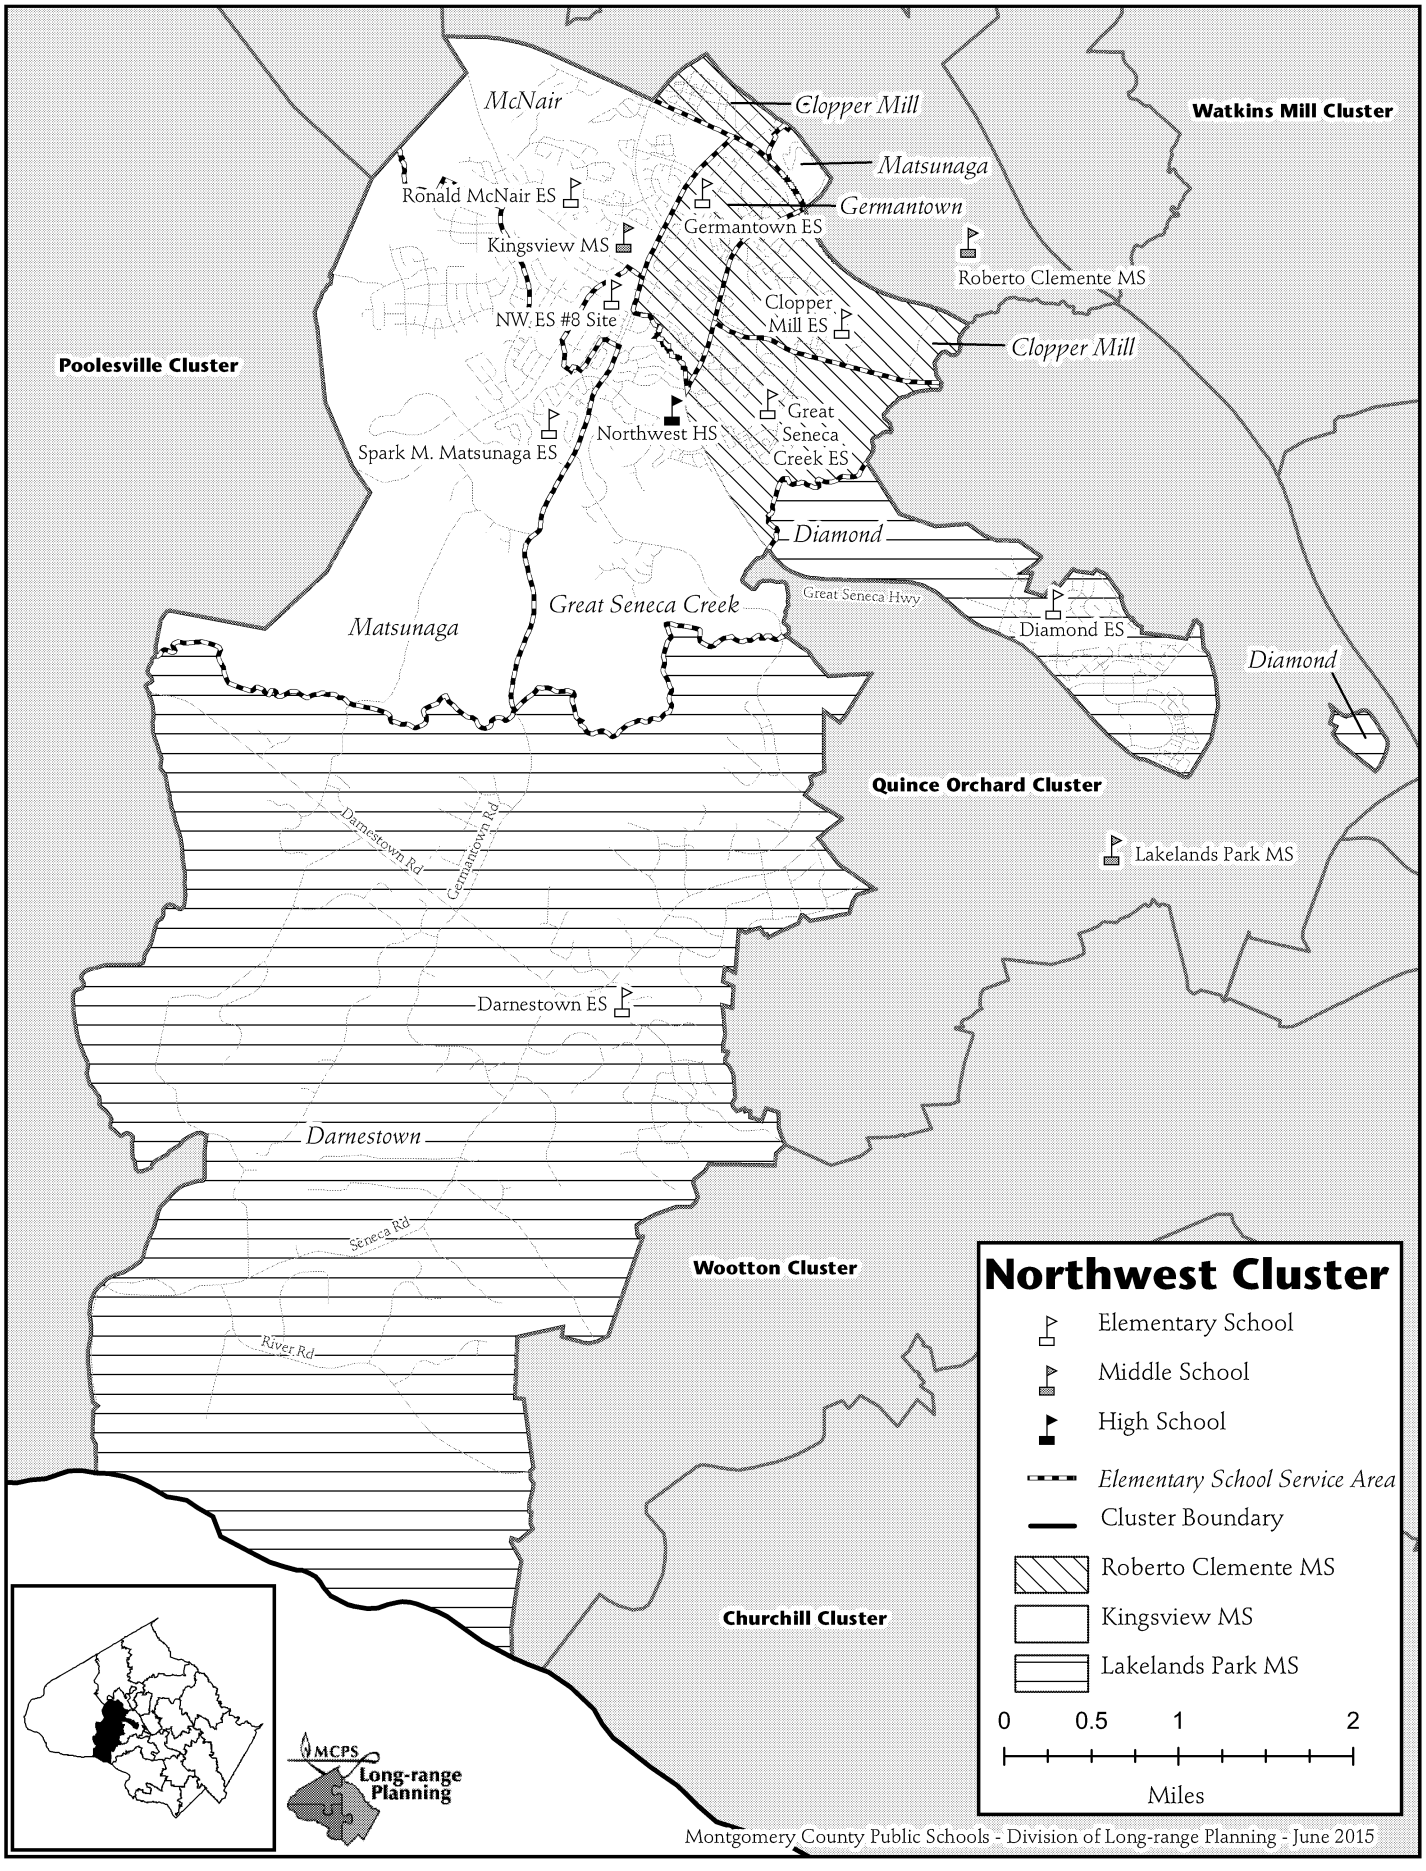
McNair
Clopper Mill
Watkins Mill Cluster
Matsunaga
Ronald McNair ES
Germantown
Germantown ES
Kingsview MS
Roberto Clemente MS
NW ES #8 Site
Clopper Mill ES
Clopper Mill
Poolesville Cluster
Great Seneca Creek ES
Spark M. Matsunaga ES
Northwest HS
Diamond
Great Seneca Hwy
Great Seneca Creek
Matsunaga
Diamond ES
Diamond
Quince Orchard Cluster
Darnestown Rd
Germantown Rd
Lakelands Park MS
Darnestown ES
Darnestown
Seneca Rd
Wootton Cluster
River Rd
Churchill Cluster
Northwest Cluster
Elementary School
Middle School
High School
Elementary School Service Area
Cluster Boundary
Roberto Clemente MS
Kingsview MS
Lakelands Park MS
0 0.5 1 2
Miles
MCPS
Long-range Planning
Montgomery County Public Schools - Division of Long-range Planning - June 2015

SCHOOLS

Northwest High School

Planning Issue: Projections indicate enrollment at Northwest High School will exceed capacity by nearly 300 students by the end of the six year CIP planning period. Enrollment also is projected to exceed capacity at Clarksburg High School by nearly 500 students. The Seneca Valley High School service area is adjacent to the Clarksburg and Northwest high school service areas. A revitalization/expansion project of Seneca Valley High School, approved for completion in August 2019, will be designed and constructed with a capacity for 2400 students. The enrollment at Seneca Valley High School is projected to be 1395 students by the end of the six-year planning period. With a capacity of 2400 seats, there will be approximately 1000 seats available to accommodate students from Clarksburg and Northwest high schools when the project is complete.

Clopper Mill Elementary School

Capital Project: Projections indicate enrollment at Clopper Mill Elementary School will exceed capacity throughout the six-year CIP period. Relocatable classrooms will be utilized until Northwest #8 opens. Although the Board of Education requested a completion date of August 2017, the County Council maintained the approved FY 2015–2020 CIP completion date of August 2018. FY 2017 expenditures are programmed to construct the new Northwest Elementary School #8. In order for this project to be completed on schedule, county and state funding must be provided at the levels approved in this CIP.


Diamond Elementary School

Capital Project: Projections indicate enrollment at Diamond Elementary School will exceed capacity by 92 seats or more by the end of the six-year CIP period. A classroom addition project is approved for this school. Although the Board of Education requested a completion date of August 2017, the County Council maintained the approved FY 2015–2020 CIP completion date of August 2018. FY 2017 expenditures are programmed to construct the classroom addition. Relocatable classrooms will be utilized until additional capacity can be added. In order for this project to be completed on schedule, county and state funding must be provided at the levels approved in this CIP.

Spark M. Matsunaga Elementary School

Capital Project: Projections indicate enrollment at Spark M. Matsunaga Elementary School will exceed capacity by 92 seats or more by the end of the six-year CIP period. Relocatable classrooms will be utilized until Northwest #8 opens. Although the Board of Education requested a completion date of August 2017, the County Council maintained the approved FY 2015–2020 CIP completion date of August 2018. FY 2017 expenditures are programmed to construct the new Northwest Elementary School #8. In order for this project to be completed on schedule, county and state funding must be provided at the levels approved in this CIP.

Northwest Cluster Articulation*



* "Cluster" is defined as the collection of elementary schools that articulate to the same high school.

* S. Christa McAuliffe and Sally K. Ride elementary schools (south of Middlebrook Road) also articulate to Roberto Clemente Middle School, but thereafter articulate to Seneca Valley High School.


* Brown Station and Rachel Carson elementary schools also articulate to Lakelands Park Middle School but thereafter articulate to Quince Orchard High School.

** Diamond Elementary School (south of Great Seneca Highway) also articulates to Ridgeview Middle School and to Quince Orchard High School.

** A portion of Great Seneca Creek Elementary School articulates to Roberto Clemente Middle School and another portion to Kingsview Middle School.

Northwest Cluster

School Utilizations

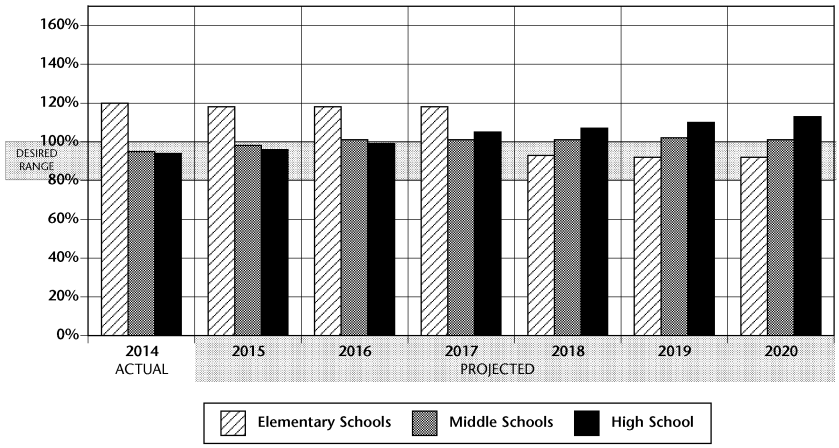

Note: Percent utilization calculated as total enrollment of schools divided by total capacity. Projected capacity factors in capital projects.

Ronald McNair Elementary School

Capital Project: Projections indicate enrollment at Ronald McNair Elementary School will exceed capacity by 92 seats or more by the end of the six-year CIP period. Relocatable classrooms will be utilized until Northwest #8 opens. Although the Board of Education requested a completion date of August 2017, the County Council maintained the approved FY 2015–2020 CIP completion date of August 2018. FY 2017 expenditures are programmed to construct the new Northwest Elementary School #8. In order for this project to be completed on schedule, county and state funding must be provided at the levels approved in this CIP.

Northwest Elementary School #8

Capital Project: Projections indicate enrollment at several elementary schools in the Northwest Cluster will exceed capacity throughout the six-year planning period. Relocatable classrooms will be utilized at these schools until Northwest #8 opens Although the Board of Education requested a completion date of August 2017, the County Council maintained the approved FY 2015–2020 CIP completion date of August 2018. FY 2017 expenditures are programmed to construct the new Northwest Elementary School #8. The boundary study process is scheduled to occur in spring 2017 with Board of Education action in November 2017. In order for this project to be completed on schedule, county and state funding must be provided at the levels approved in this CIP.

CAPITAL PROJECTS

School	Project	Project Status*	Date of Completion
Diamond ES	Classroom addition	Programmed	Aug. 2018
Northwest ES #8	New school	Programmed	Aug. 2018

"Approved"— Project has an FY 2015 or FY 2016 appropriation approved in the FY 2015–2020 CIP.

"Deferred"—Funds have been deferred for a future CIP.

"Programmed"—Project has expenditures programmed in a future year of the CIP for planning and/or construction funds.

"Proposed"—Project has facility planning funds approved for FY 2015 or approved for FY 2016 for a feasibility study.

Projected Enrollment and Space Availability

Effects of the Amended FY2015–2020 CIP and Non–CIP Actions on Space Available

Schools			Actual 14–15	Projections 15–16	16–17	17–18	18–19	19–20	20–21	2024	2029
Northwest HS		Program Capacity	2241	2241	2241	2241	2241	2241	2241	2241	2241
		Enrollment	***2116***	***2162***	***2218***	***2352***	***2402***	***2471***	***2540***	**2700**	**2600**
		Available Space	*125*	*79*	*23*	*(111)*	*(161)*	*(230)*	*(299)*	*(459)*	*(359)*
		Comments	See text								
Roberto Clemente MS		Program Capacity	1231	1231	1231	1231	1231	1231	1231	1231	1231
		Enrollment	**1208**	**1268**	**1297**	**1279**	**1279**	**1291**	**1286**	**1300**	**1300**
		Available Space	*23*	*(37)*	*(66)*	*(48)*	*(48)*	*(60)*	*(55)*	*(69)*	*(69)*
		Comments									
Kingsview MS		Program Capacity	1041	1041	1041	1041	1041	1041	1041	1041	1041
		Enrollment	**1002**	**1022**	**1067**	**1075**	**1057**	**1039**	**974**	**1000**	**950**
		Available Space	*39*	*19*	*(26)*	*(34)*	*(16)*	*2*	*67*	*41*	*91*
		Comments									
Lakelands Park MS		Program Capacity	1122	1122	1122	1122	1122	1122	1122	1122	1122
		Enrollment	**1011**	**1048**	**1063**	**1062**	**1106**	**1135**	**1184**	**1300**	**1200**
		Available Space	*111*	*74*	*59*	*60*	*16*	*(13)*	*(62)*	*(178)*	*(78)*
		Comments									
Clopper Mill ES	CSR	Program Capacity	417	457	457	457	457	457	457		
		Enrollment	**457**	**496**	**513**	**525**	**532**	**542**	**546**		
		Available Space	*(40)*	*(39)*	*(56)*	*(68)*	*(75)*	*(85)*	*(89)*		
		Comments		+1 preK -1 Supp. Room							
Darnestown ES		Program Capacity	471	471	471	471	471	471	471		
		Enrollment	**310**	**284**	**300**	**312**	**327**	**339**	**350**		
		Available Space	*161*	*187*	*171*	*159*	*144*	*132*	*121*		
		Comments									
Diamond ES		Program Capacity	463	463	463	463	670	670	670		
		Enrollment	**648**	**654**	**644**	**653**	**639**	**613**	**615**		
		Available Space	*(185)*	*(191)*	*(181)*	*(190)*	*31*	*57*	*55*		
		Comments	Planning for Addition				Addition Complete				
Germantown ES		Program Capacity	333	328	328	328	328	328	328		
		Enrollment	**316**	**346**	**350**	**348**	**360**	**360**	**343**		
		Available Space	*17*	*(18)*	*(22)*	*(20)*	*(32)*	*(32)*	*(15)*		
		Comments		+1 PEP							
Great Seneca Creek ES	CSR	Program Capacity	566	566	566	566	566	566	566		
		Enrollment	**732**	**711**	**685**	**677**	**667**	**668**	**675**		
		Available Space	*(166)*	*(145)*	*(119)*	*(111)*	*(101)*	*(102)*	*(109)*		
		Comments									
Spark M. Matsunaga ES		Program Capacity	652	652	652	652	652	652	652		
		Enrollment	**926**	**877**	**864**	**836**	**822**	**822**	**843**		
		Available Space	*(274)*	*(225)*	*(212)*	*(184)*	*(170)*	*(170)*	*(191)*		
		Comments									
Ronald McNair ES		Program Capacity	623	623	623	623	623	623	623		
		Enrollment	**851**	**839**	**840**	**832**	**823**	**792**	**794**		
		Available Space	*(228)*	*(216)*	*(217)*	*(209)*	*(200)*	*(169)*	*(171)*		
		Comments									
Northwest ES #8		Program Capacity					740	740	740		
		Enrollment					***0***	***0***	***0***		
		Available Space					*740*	*740*	*740*		
		Comments	Planning for new school				Opens Aug. 2018				
Cluster Information		HS Utilization	94%	96%	99%	105%	107%	110%	113%	120%	116%
		HS Enrollment	2116	2162	2218	2352	2402	2471	2540	2700	2600
		MS Utilization	95%	98%	101%	101%	101%	102%	101%	106%	102%
		MS Enrollment	3221	3338	3427	3416	3442	3465	3444	3600	3450
		ES Utilization	120%	118%	118%	118%	93%	92%	92%	95%	95%
		ES Enrollment	4240	4207	4196	4183	4170	4136	4166	4300	4300

Demographic Characteristics of Schools

Schools	2014–2015 Total Enrollment	Two or more races %	Black or Afr. Amer. %	Asian%	Hispanic %	White %	2014–2015 FARMS%*	2014–2015 ESOL%**	2013–2014 Mobility Rate%***
Northwest HS	2116	5.6%	27.6%	17.8%	20.5%	28.4%	27.6%	≤ 5.0%	8.6%
Roberto Clemente MS	1208	5.3%	25.4%	26.4%	25.6%	17.1%	33.2%	≤ 5.0%	11.0%
Kingsview MS	1002	5.2%	20.8%	26.8%	13.0%	34.2%	17.0%	≤ 5.0%	≤ 5.0%
Lakelands Park MS	1011	≤ 5.0%	12.5%	14.4%	18.9%	49.8%	22.0%	5.4%	8.9%
Clopper Mill ES	458	≤ 5.0%	38.2%	5.5%	45.0%	7.2%	69.7%	25.8%	24.0%
Darnestown ES	310	5.2%	≤ 5.0%	11.3%	8.1%	70.6%	≤ 5.0%	≤ 5.0%	≤ 5.0%
Diamond ES	648	≤ 5.0%	10.0%	41.5%	11.9%	31.9%	9.0%	17.3%	16.7%
Germantown ES	316	≤ 5.0%	30.1%	20.9%	24.1%	20.9%	31.3%	12.7%	15.6%
Great Seneca Creek ES	732	6.3%	30.3%	13.7%	25.1%	24.5%	38.1%	11.9%	15.3%
Spark M. Matsunaga ES	926	≤ 5.0%	18.5%	36.9%	13.6%	26.0%	18.3%	10.5%	8.3%
Ronald McNair ES	851	5.3%	22.7%	30.8%	15.9%	25.1%	26.3%	17.7%	9.7%
Elementary Cluster Total	**4241**	**≤ 5.0%**	**22.1%**	**25.9%**	**19.5%**	**27.3%**	**27.4%**	**14.4%**	**13.0%**
Elementary County Total	**75,144**	**≤ 5.0%**	**21.2%**	**13.9%**	**30.4%**	**29.3%**	**40.2%**	**23.3%**	**13.3%**

**Percent of students approved for Free and Reduced-priced Meals Program (FARMS) during the 2014–2015 school year.*

***Percent of English for Speakers of Other Languages (ESOL) during the 2014–2015 school year. High School students are served in regional ESOL centers.*

****Mobility Rate is the number of entries plus withdrawals during the 2013–2014 school year compared to total enrollment.*
Notes: Native Hawaiian/Pacific Islander and American Indian/Alaskan Native categories total less than 1% and were therefore excluded from the table.

Due to federal and state guidelines, demographic characteristics of schools of less than or equal to 5.0% are reported as ≤ 5.0%.


Program Capacity Table

(School Year 2014–2015)

Schools	Grades Served	Capacity (HS @90% MS@85%)	Total Rooms	Support Rooms	Regular Secondary @25	Regular Elementary @23	CSR Grades 1–2 @18	Pre–K @20	Pre–K @40	HS @20	CSR KIND @18	KIND @22	ESOL @15	METS @15	Special Education Services: School Based: HSM @13	School Based: ELEM LAD @13	Quad Cluster Based: ELC @10	Quad Cluster Based: LANG @12	Quad Cluster Based: LFI @10	Quad Cluster Based: SCB @6	Quad Cluster Based: AAC@7	County & Regional Based: AUT @6	BRIDGE @10	DHOH @7	ED @10	EXTENSIONS @6	GT/LD @13	PD @7	PEP@6	PEP @12	PEP @18	VISION (Elementary) @7	OTHER
Northwest HS	9-12	2241	102		98																				4							
Roberto Clemente MS	6-8	1231	60		56								1						2								1						
Kingsview MS	6-8	1041	49		49																												
Lakelands Park MS	6-8	1122	57		51								1							3						2							
Clopper Mill ES	HS-5	417	28	5		4	9		1	1	4				1							3											
Darnestown ES	K-5	471	25	4		18						2			1																		
Diamond ES	K-5	463	28	4		14						5			1							3											1
Germantown ES	K-5	333	22	4		10						3			1					3									1				
Great Seneca Creek ES	K-5	566	34	4		11	9				6				1										3								
Spark M. Matsunaga ES	K-5	652	34	4		23						5			1																		1
Ronald McNair ES	PreK-5	623	32	5		20			1			5			1																		

Facility Characteristics of Schools 2014–2015

Schools	Year Facility Opened	Year Reopened/ Revitalized	Total Square Footage	Site Size Acres	Adjacent Park	Reloc-atable Classrooms	Linkages to Learning Program	Home School Model
Northwest HS	1998		340,867	34.6	Yes			
Roberto Clemente MS	1992		148,246	19.9				
Kingsview MS	1997		140,398	18.5	Yes			
Lakelands Park MS	2005		153,588	8.11	Yes			
Clopper Mill ES	1986		64,851	9	Yes	4		Yes
Darnestown ES	1954	1980	64,840	7.2				Yes
Diamond ES	1975		64,950	10	Yes	5		Yes
Germantown ES	1935	1978	57,668	7.8				Yes
Great Seneca Creek ES	2006		82,511	13.71		3		Yes
Spark M. Matsunaga ES	2001		90,718	11.8		15		Yes
Ronald McNair ES	1990		78,275	10	Yes	6		Yes

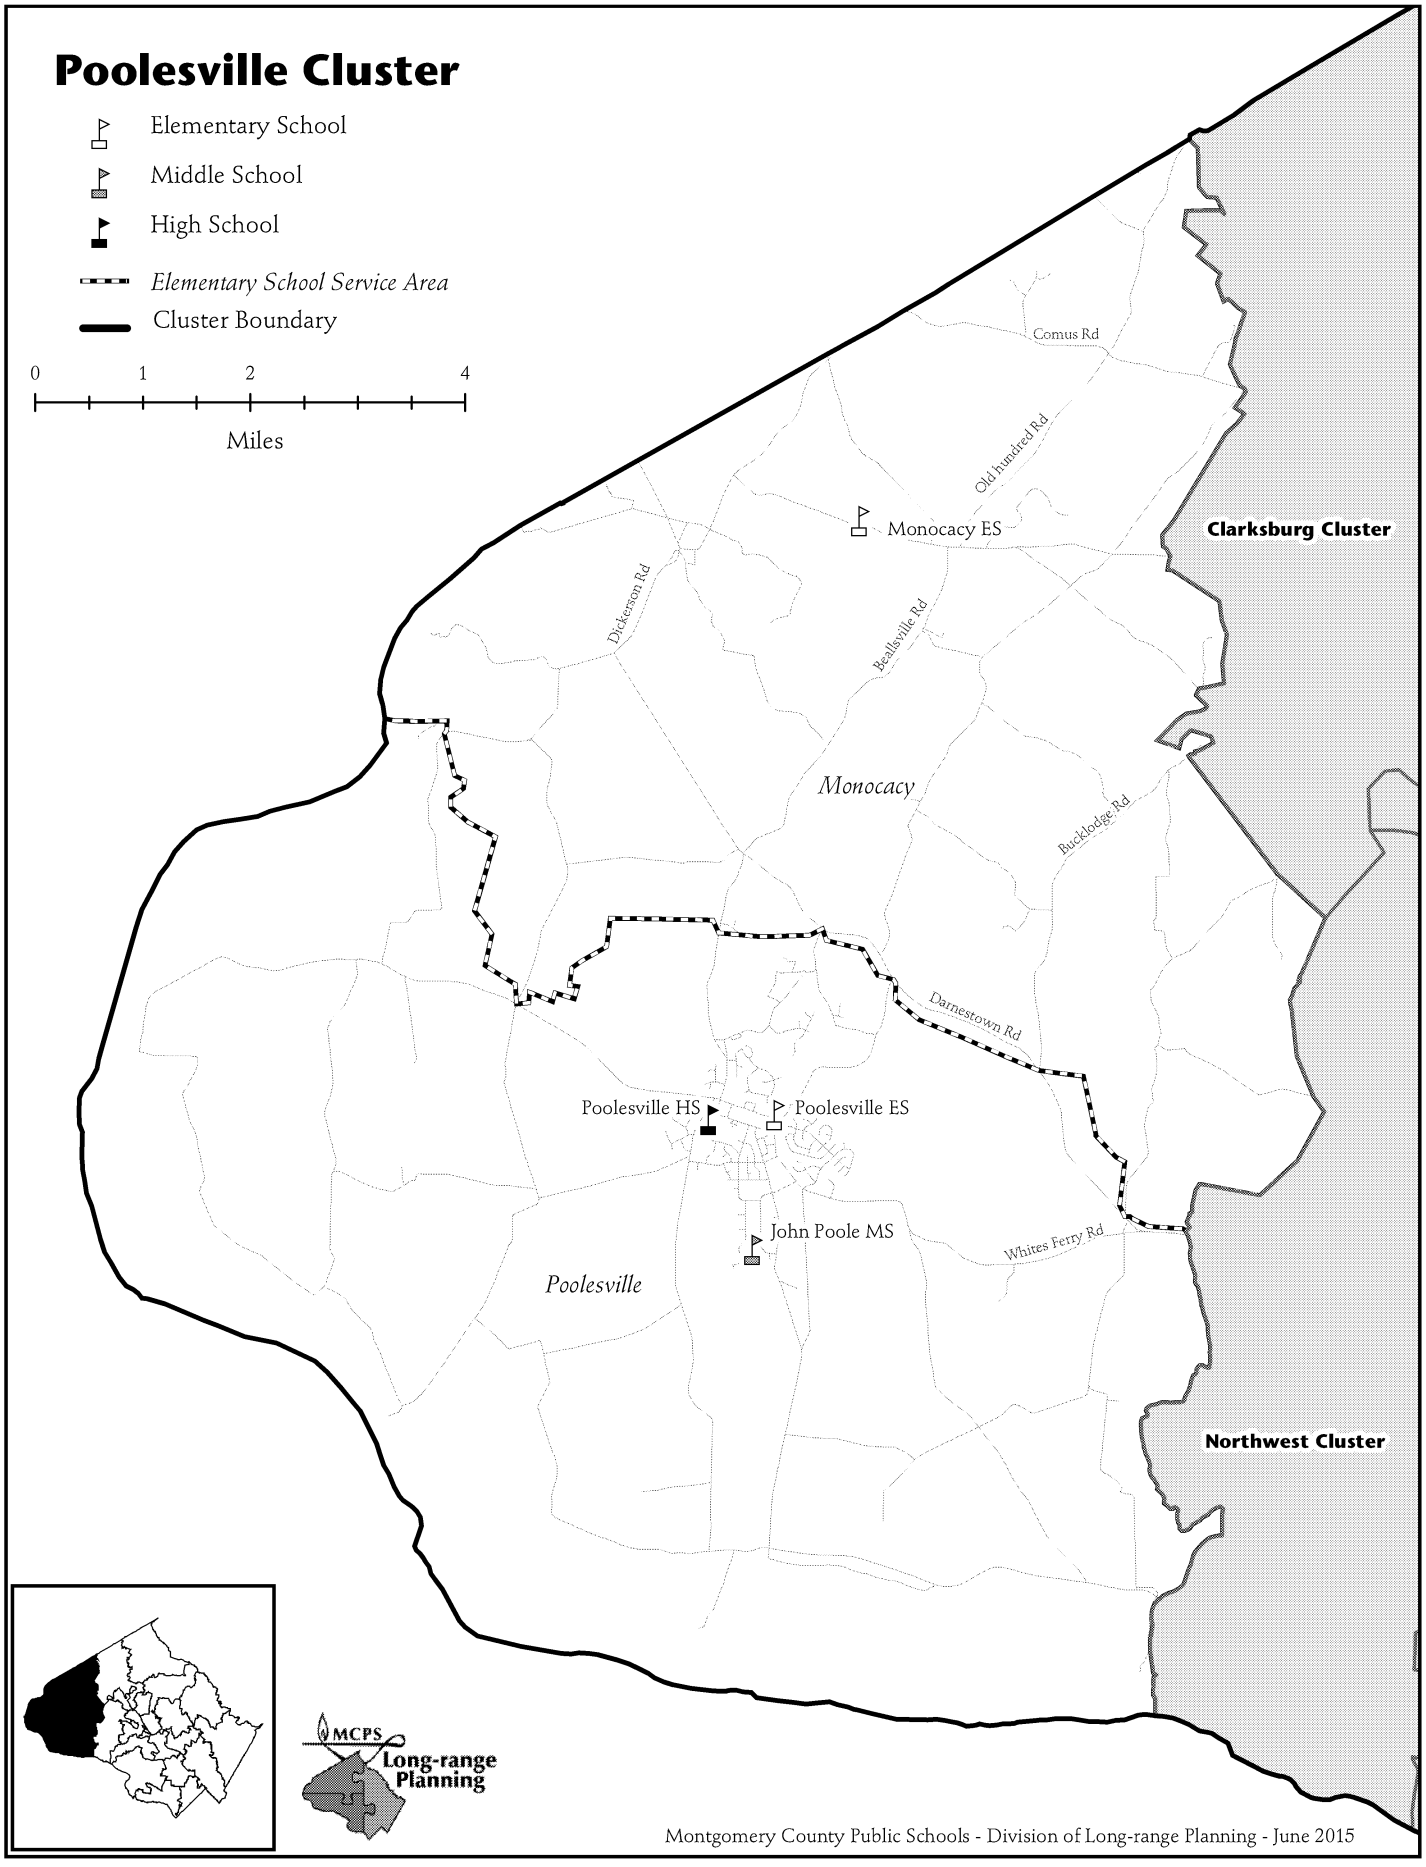
Poolesville Cluster
Elementary School
Middle School
High School
Elementary School Service Area
Cluster Boundary
0
1
2
4
Miles
Comus Rd
Old Hundred Rd
Monocacy ES
Clarksburg Cluster
Dickerson Rd
Beallsville Rd
Monocacy
Buckeystown Rd
Darnestown Rd
Poolesville HS
Poolesville ES
John Poole MS
Whites Ferry Rd
Poolesville
Northwest Cluster
MCPS
Long-range Planning
Montgomery County Public Schools - Division of Long-range Planning - June 2015

SCHOOLS

Poolesville High School

Capital Project: A revitalization/expansion project is scheduled for this school. Although the Board of Education requested a completion date of August 2022, the County Council maintained the approved FY 2015–2020 CIP completion date of August 2023. FY 2017 expenditures are programmed for facility planning funds to determine the scope and cost of the project. In order for this project to be completed on this schedule, county and state funding must be provided at levels approved in this CIP.

CAPITAL PROJECTS


School	Project	Project Status*	Date of Completion
Poolesville HS	Revitalization/ expansion	Programmed	Aug. 2023, building Aug. 2024, site

"Approved"— Project has an FY 2015 or FY 2016 appropriation approved in the FY 2015–2020 CIP.

"Deferred"—Funds have been deferred for a future CIP.

"Programmed"—Project has expenditures programmed in a future year of the CIP for planning and/or construction funds.

"Proposed"—Project has facility planning funds approved for FY 2015 or approved for FY 2016 for a feasibility study.

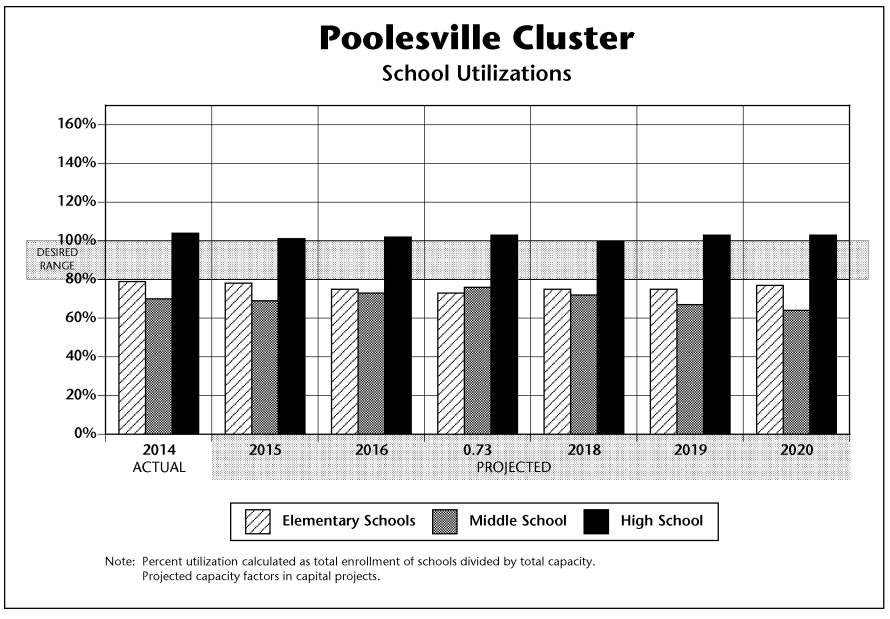

Projected Enrollment and Space Availability

Effects of the Amended FY2015–2020 CIP and Non–CIP Actions on Space Available

Schools			Actual 14–15	Projections 15–16	16–17	17–18	18–19	19–20	20–21	2024	2029
Poolesville HS		Program Capacity	1170	1170	1170	1170	1170	1170	1170	1170	1170
		Enrollment	**1222**	**1180**	**1189**	**1201**	**1169**	**1204**	**1208**	**1250**	**1200**
		Available Space	*(52)*	*(10)*	*(19)*	*(31)*	*1*	*(34)*	*(38)*	*(80)*	*(30)*
		Comments			Facility Planning for Rev/Ex		Planning for Revitalization/ Expansion				
John Poole MS		Program Capacity	468	468	468	468	468	468	468	468	468
		Enrollment	**327**	**324**	**341**	**355**	**339**	**315**	**300**	**350**	**300**
		Available Space	*140*	*144*	*126*	*112*	*128*	*152*	*168*	*118*	*168*
		Comments									
Monocacy ES		Program Capacity	219	219	219	219	219	219	219		
		Enrollment	**161**	**158**	**151**	**147**	**143**	**146**	**150**		
		Available Space	*58*	*61*	*68*	*72*	*76*	*73*	*69*		
		Comments									
Poolesville ES		Program Capacity	539	539	539	539	539	539	539		
		Enrollment	**441**	**433**	**416**	**409**	**425**	**426**	**433**		
		Available Space	*98*	*106*	*123*	*130*	*114*	*113*	*106*		
		Comments									
Cluster Information		HS Utilization	104%	101%	102%	103%	100%	103%	103%	107%	103%
		HS Enrollment	1222	1180	1189	1201	1169	1204	1208	1250	1200
		MS Utilization	70%	69%	73%	76%	72%	67%	64%	75%	64%
		MS Enrollment	327	324	341	355	339	315	300	350	300
		ES Utilization	79%	78%	75%	73%	75%	75%	77%	79%	79%
		ES Enrollment	602	591	567	556	568	572	583	600	600

Demographic Characteristics of Schools

Schools	2014–2015 Total Enrollment	Two or more races %	Black or Afr. Amer. %	Asian%	Hispanic %	White %	2014–2015 FARMS%*	ESOL%**	2013–2014 Mobility Rate%***
Poolesville HS	1222	6.5%	5.7%	25.9%	6.9%	54.6%	6.8%	≤ 5.0%	≤ 5.0%
John Poole MS	327	5.8%	≤ 5.0%	5.8%	11.3%	72.2%	14.1%	≤ 5.0%	≤ 5.0%
Monocacy ES	161	5.6%	6.8%	≤ 5.0%	10.6%	74.5%	16.1%	≤ 5.0%	≤ 5.0%
Poolesville ES	441	≤ 5.0%	≤ 5.0%	≤ 5.0%	11.8%	74.4%	12.7%	≤ 5.0%	10.9%
Elementary Cluster Total	**602**	**≤ 5.0%**	**5.5%**	**≤ 5.0%**	**11.5%**	**74.4%**	**14.6%**	**5.3%**	**9.1%**
Elementary County Total	**75,144**	**≤ 5.0%**	**21.2%**	**13.9%**	**30.4%**	**29.3%**	**40.2%**	**23.3%**	**13.3%**

**Percent of students approved for Free and Reduced-priced Meals Program (FARMS) during the 2014–2015 school year.*

***Percent of English for Speakers of Other Languages (ESOL) during the 2014–2015 school year. High School students are served in regional ESOL centers.*

****Mobility Rate is the number of entries plus withdrawals during the 2013–2014 school year compared to total enrollment.*
Notes: Native Hawaiian/Pacific Islander and American Indian/Alaskan Native categories total less than 1% and were therefore excluded from the table.

Due to federal and state guidelines, demographic characteristics of schools of less than or equal to 5.0% are reported as ≤ 5.0%.


Program Capacity Table

(School Year 2014–2015)

Schools	Grades Served	Capacity (HS @90% MS@85%)	Total Rooms	Support Rooms	Regular Secondary @25	Regular Elementary @23	CSR Grades 1–2 @18	Pre–K @20	Pre–K @40	HS @20	CSR KIND @18	KIND @22	ESOL @15	METS @15	Special Education Services: School Based: HSM @13	School Based: ELEM LAD @13	Cluster Based: ELC @10	Quad Cluster Based: LANG @12	Quad Cluster Based: LFI @10	Quad Cluster Based: SCB @6	County & Regional Based: AAC@7	AUT @6	BRIDGE @10	DHOH @7	ED @10	EXTENSIONS @6	GT/LD @13	PD @7	PEP@6	PEP @12	PEP @18	VISION (Elementary) @7	OTHER
Poolesville HS	9-12	1170	52		52																										
John Poole MS	6-8	468	22		22																										
Monocacy ES	K-5	219	13	3		8						1			1																
Poolesville ES	K-5	539	28	4		20						3			1																

Facility Characteristics of Schools 2014–2015

Schools	Year Facility Opened	Year Reopened/ Revitalized	Total Square Footage	Site Size Acres	Adjacent Park	Reloc-atable Classrooms	Linkages to Learning Program	Home School Model
Poolesville HS	1953	1978	165,056	37.2				
John Poole MS	1997		85,669	20.5				
Monocacy ES	1961	1989	42,482	27		1		Yes
Poolesville ES	1960	1978	64,803	12.3				Yes

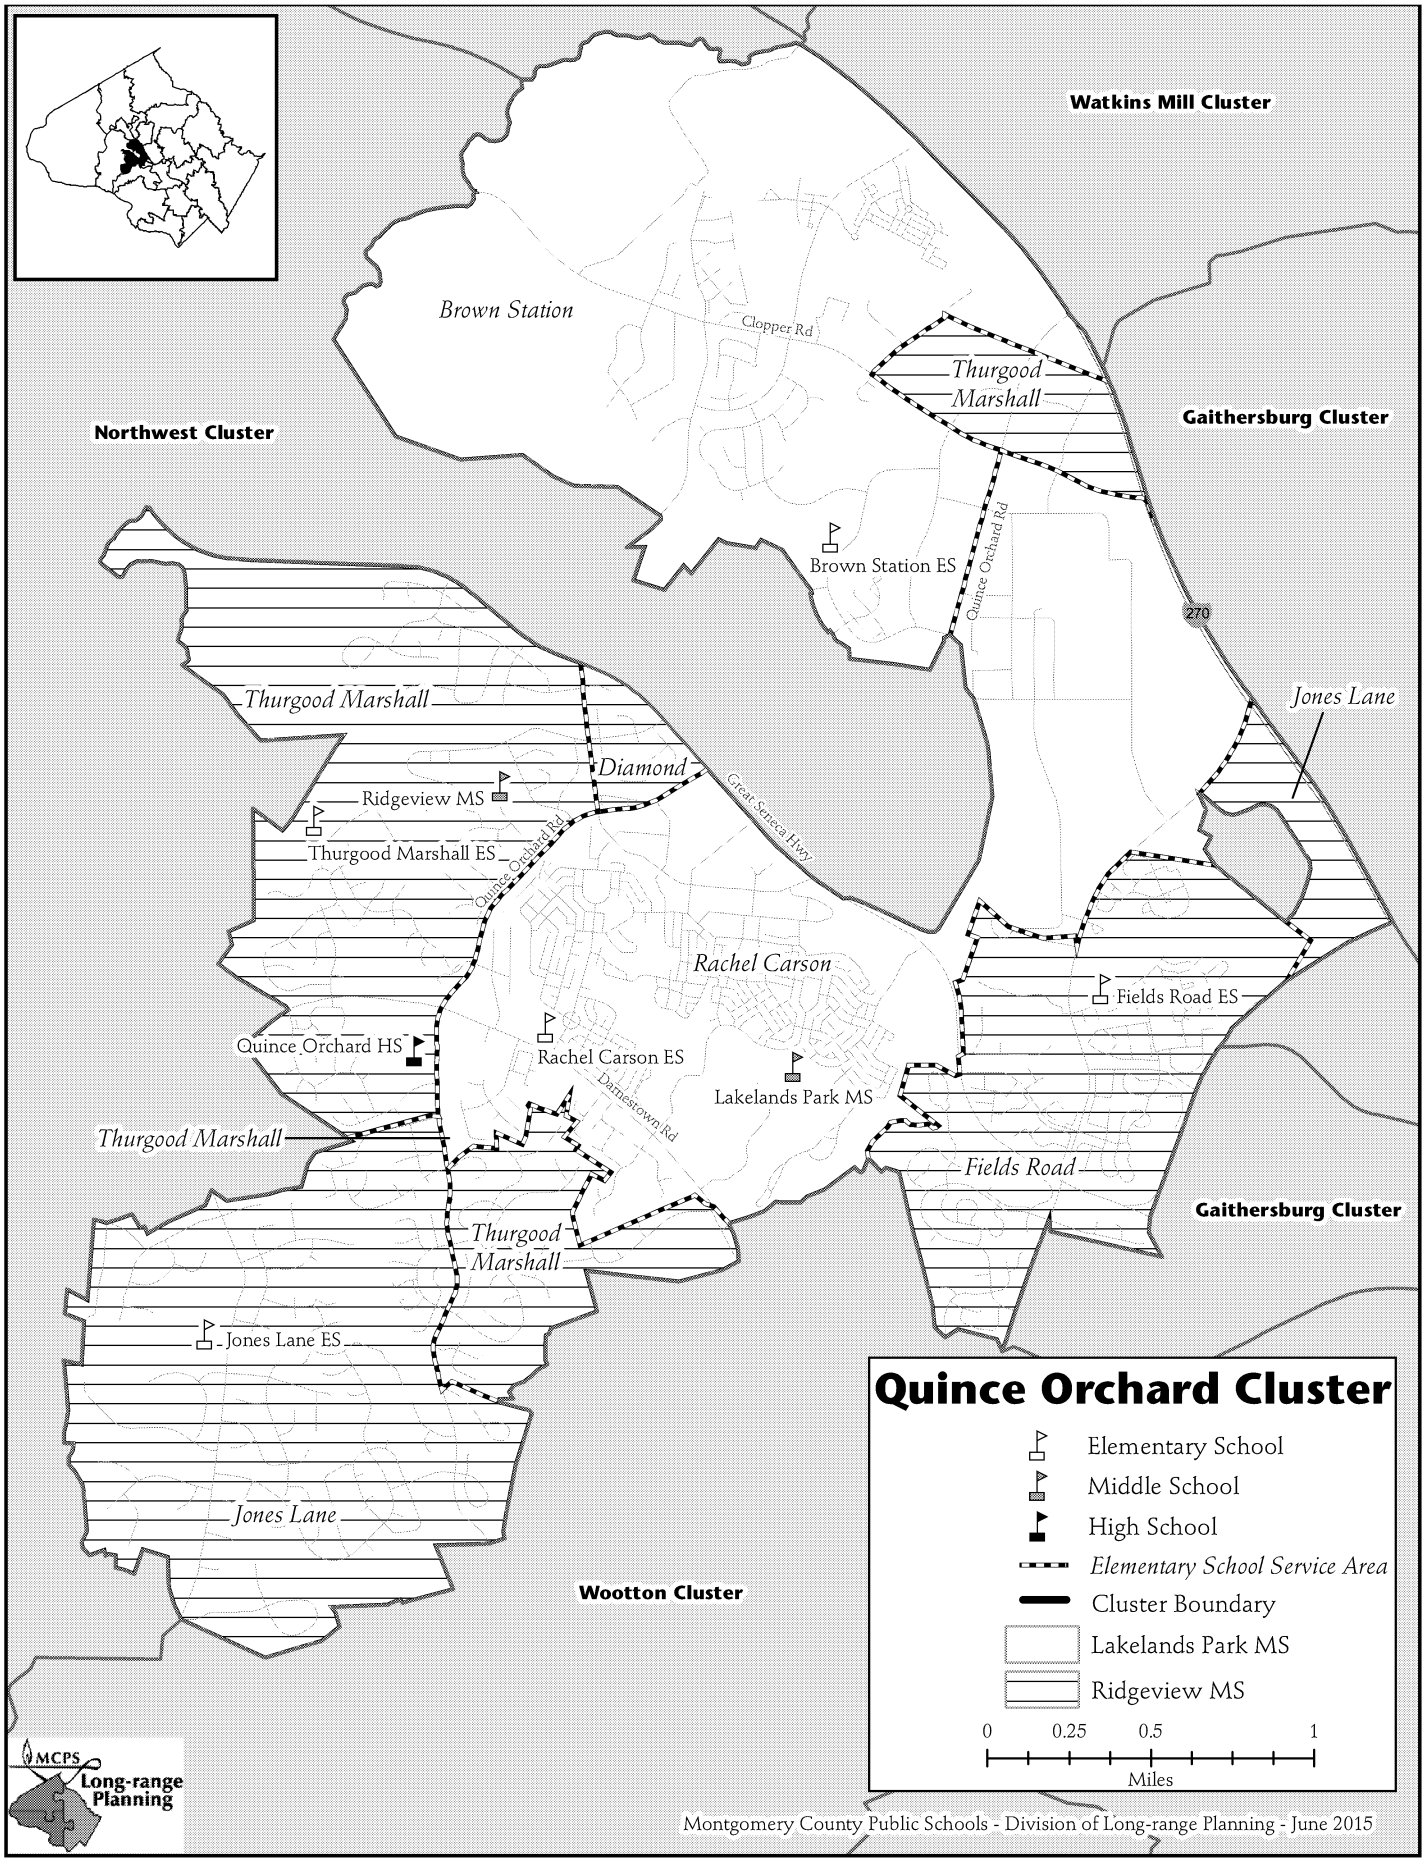
Watkins Mill Cluster
Brown Station
Clopper Rd
Thurgood Marshall
Gaithersburg Cluster
Northwest Cluster
Brown Station ES
Quince Orchard Rd
270
Jones Lane
Thurgood Marshall
Diamond
Ridgeview MS
Great Seneca Hwy
Thurgood Marshall ES
Quince Orchard Rd
Rachel Carson
Fields Road ES
Quince Orchard HS
Rachel Carson ES
Lakelands Park MS
Darnestown Rd
Thurgood Marshall
Fields Road
Gaithersburg Cluster
Thurgood Marshall
Jones Lane ES
Jones Lane
Wootton Cluster
Quince Orchard Cluster
Elementary School
Middle School
High School
Elementary School Service Area
Cluster Boundary
Lakelands Park MS
Ridgeview MS
0
0.25
0.5
1
Miles
MCPS
Long-range Planning
Montgomery County Public Schools - Division of Long-range Planning - June 2015

SCHOOLS

Brown Station Elementary School

Planning Issue: Projections indicate enrollment at Brown Station Elementary School will exceed capacity by 92 seats or more by the end of the six-year CIP period. Relocatable classrooms will be utilized until additional capacity can be added as part of the revitalization/expansion project. Funding was approved in the Department of Health and Human Services Capital Budget to construct a child care classroom as part of the project.

Capital Project: A revitalization/expansion project is scheduled for this school. Although the approved FY 2015–2020 CIP had a completion of August 2018 for the revitalization/expansion project, the County Council approved the Board of Education's request to complete the project in August 2017. An FY 2016 appropriation is approved to construct this project.

Rachel Carson Elementary School

Planning Issue: Projections indicate that enrollment at Rachel Carson Elementary School will exceed capacity by 92 seats or more by the end of the six-year CIP period. To address the high enrollment at Rachel Carson Elementary School the Board of Education approved the following studies to explore additional capacity to address the overutilization at Rachel Carson Elementary School:

- The feasibility study that was conducted in 2007 for an addition at Jones Lane Elementary School to relieve Carson Elementary School be updated to determine if a larger addition could be constructed at Jones Lane Elementary School;
- The feasibility study that is planned for the revitalization/expansion project at DuFief Elementary School during the 2014–2015 school year include the possibility of additional capacity;
- The feasibility study that is planned for an addition at Fields Road Elementary School include the possibility of additional capacity; and
- The consideration of a new elementary school in the Quince Orchard Cluster be included in the analysis of options to relieve Rachel Carson Elementary School.

The interim superintendent will make a recommendation to address the overutilization of Rachel Carson Elementary School as part of the FY 2017–2022 CIP.

Fields Road Elementary School

Capital Project: Projections indicate enrollment at Fields Road Elementary School will exceed capacity by 92 seats or more by the end of the six-year CIP period. An FY 2016 appropriation is approved for facility planning to determine the feasibility, scope, and cost for a classroom addition. Projections indicate that enrollment at Rachel Carson Elementary School will exceed capacity by 92 seats or more by the end of the six-year CIP period. To address the high enrollment at Rachel Carson Elementary School the Board of Education approved the following studies to explore additional capacity to address the overutilization at Rachel Carson Elementary School:

- The feasibility study that was conducted in 2007 for an addition at Jones Lane Elementary School to relieve Carson Elementary School be updated to determine if a larger addition could be constructed at Jones Lane Elementary School;
- The feasibility study that is planned for the revitalization/expansion project at DuFief Elementary School during

Quince Orchard Cluster Articulation*

Quince Orchard High School


Lakelands Park MS	Ridgeview MS
Brown Station ES Rachel Carson ES	Diamond ES (South of Great Seneca Highway) Fields Road ES Jones Lane ES Thurgood Marshall ES

* "Cluster" is defined as the collection of elementary schools that articulate to the same high school.

* Diamond (north of Great Seneca Highway) and Darnestown elementary schools also articulate to Lakelands Park Middle School, but thereafter to Northwest High School.

Quince Orchard Cluster

School Utilizations

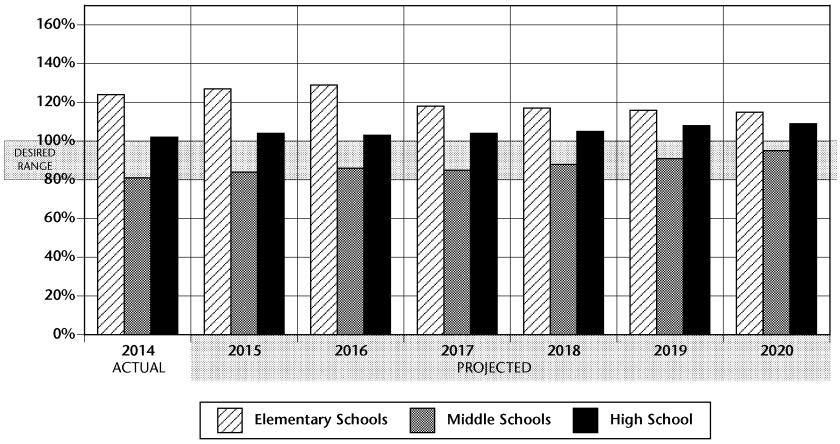

Note: Percent utilization calculated as total enrollment of schools divided by total capacity. Projected capacity factors in capital projects.

the 2014–2015 school year include the possibility of additional capacity;
- The feasibility study that is planned for an addition at Fields Road Elementary School include the possibility of additional capacity; and
- The consideration of a new elementary school in the Quince Orchard Cluster be included in the analysis of options to relieve Rachel Carson Elementary School.

The interim superintendent will make a recommendation to address the overutilization of Rachel Carson Elementary School as part of the FY 2017–2022 CIP.

Jones Lane Elementary School

Planning Issue: Projections indicate that enrollment at Rachel Carson Elementary School will exceed capacity by 92 seats or more by the end of the six-year CIP period. To address the high enrollment at Rachel Carson Elementary School the Board of Education approved the following studies to explore additional capacity to address the overutilization at Rachel Carson Elementary School:

- The feasibility study that was conducted in 2007 for an addition at Jones Lane Elementary School to relieve Carson Elementary School be updated to determine if a larger addition could be constructed at Jones Lane Elementary School;
- The feasibility study that is planned for the revitalization/expansion project at DuFief Elementary School during the 2014–2015 school year include the possibility of additional capacity;
- The feasibility study that is planned for an addition at Fields Road Elementary School include the possibility of additional capacity; and
- The consideration of a new elementary school in the Quince Orchard Cluster be included in the analysis of options to relieve Rachel Carson Elementary School.

The interim superintendent will make a recommendation to address the overutilization of Rachel Carson Elementary School as part of the FY 2017–2022 CIP.

Thurgood Marshall Elementary School

Capital Project: Projections indicate that Thurgood Marshall Elementary School will exceed capacity by 92 seats or more by the end of the six-year planning period. A feasibility study was conducted in FY 2008 to determine the feasibility, cost, and scope of an addition to Thurgood Marshall Elementary School. A completion date for an addition to this school will be determined in a future CIP. Relocatable classrooms will be utilized until additional capacity can be added.

CAPITAL PROJECTS

School	Project	Project Status*	Date of Completion
Brown Station ES	Revitalization/ expansion	Approved	Aug. 2017
Fields Road ES	Classroom addition	Approved	TBD
Thurgood Marshall ES	Classroom addition	Proposed	TBD

"Approved"— Project has an FY 2015 or FY 2016 appropriation approved in the FY 2015–2020 CIP.

"Deferred"—Funds have been deferred for a future CIP.

"Programmed"—Project has expenditures programmed in a future year of the CIP for planning and/or construction funds.

"Proposed"—Project has facility planning funds approved for FY 2015 or approved for FY 2016 for a feasibility study.

Projected Enrollment and Space Availability

Effects of the Amended FY2015–2020 CIP and Non–CIP Actions on Space Available

Schools			Actual	Projections							
			14–15	15–16	16–17	17–18	18–19	19–20	20–21	2024	2029
Quince Orchard HS		Program Capacity	1857	1857	1857	1857	1857	1857	1857	1857	1857
		Enrollment	**1899**	**1923**	**1918**	**1924**	**1959**	**2011**	**2019**	**2200**	**2100**
		Available Space	*(42)*	*(66)*	*(61)*	*(67)*	*(102)*	*(154)*	*(162)*	*(343)*	*(243)*
		Comments									
Lakelands Park MS		Program Capacity	1122	1122	1122	1122	1122	1122	1122	1122	1122
		Enrollment	**1011**	**1048**	**1063**	**1062**	**1106**	**1135**	**1184**	**1300**	**1200**
		Available Space	*111*	*74*	*59*	*60*	*16*	*(13)*	*(62)*	*(178)*	*(78)*
		Comments									
Ridgeview MS		Program Capacity	995	979	963	963	963	963	963	963	963
		Enrollment	**702**	**727**	**727**	**709**	**728**	**768**	**793**	**850**	**800**
		Available Space	*293*	*252*	*236*	*254*	*235*	*195*	*170*	*113*	*163*
		Comments		+1 AUT	+1 AUT						
Brown Station ES	CSR	Program Capacity	436	436	436	709	709	709	709		
		Enrollment	**513**	**531**	**559**	**588**	**600**	**623**	**633**		
		Available Space	*(77)*	*(95)*	*(123)*	*121*	*109*	*86*	*76*		
		Comments			@ Emory Grove	Rev/Ex Complete Aug. 2017					
Rachel Carson ES		Program Capacity	667	667	667	667	667	667	667		
		Enrollment	**1013**	**1039**	**1033**	**1034**	**995**	**988**	**968**		
		Available Space	*(346)*	*(372)*	*(366)*	*(367)*	*(328)*	*(321)*	*(301)*		
		Comments	See text								
Fields Road ES	CSR	Program Capacity	419	419	419	419	419	419	419		
		Enrollment	**484**	**504**	**528**	**540**	**537**	**526**	**529**		
		Available Space	*(65)*	*(85)*	*(109)*	*(121)*	*(118)*	*(107)*	*(110)*		
		Comments	Fac. Plng. for Addition See text								
Jones Lane ES		Program Capacity	441	441	441	441	441	441	441		
		Enrollment	**470**	**448**	**438**	**426**	**420**	**416**	**408**		
		Available Space	*(29)*	*(7)*	*3*	*15*	*21*	*25*	*33*		
		Comments	See text								
Thurgood Marshall ES		Program Capacity	534	534	534	534	534	534	534		
		Enrollment	**624**	**641**	**653**	**669**	**678**	**663**	**656**		
		Available Space	*(90)*	*(107)*	*(119)*	*(135)*	*(144)*	*(129)*	*(122)*		
		Comments	See text								
Cluster Information		HS Utilization	102%	104%	103%	104%	105%	108%	109%	118%	113%
		HS Enrollment	1899	1923	1918	1924	1959	2011	2019	2200	2100
		MS Utilization	81%	84%	86%	85%	88%	91%	95%	103%	96%
		MS Enrollment	1713	1775	1790	1771	1834	1903	1977	2150	2000
		ES Utilization	124%	127%	129%	118%	117%	116%	115%	119%	119%
		ES Enrollment	3104	3163	3211	3257	3230	3216	3194	3300	3300

Demographic Characteristics of Schools

Schools	2014–2015 Total Enrollment	Two or more races %	Black or Afr. Amer. %	Asian%	Hispanic %	White %	2014–2015 FARMS%*	2014–2015 ESOL%**	2013–2014 Mobility Rate%***
Quince Orchard HS	1899	≤ 5.0%	14.7%	12.4%	23.2%	44.9%	22.3%	6.4%	10.5%
Lakelands Park MS	1011	≤ 5.0%	12.5%	14.4%	18.9%	49.8%	22.0%	5.4%	8.9%
Ridgeview MS	702	≤ 5.0%	14.0%	16.0%	23.8%	41.5%	25.8%	5.1%	9.1%
Brown Station ES	513	5.1%	34.9%	7.6%	43.9%	8.4%	67.1%	26.5%	25.6%
Rachel Carson ES	1013	6.9%	7.1%	13.6%	18.6%	53.8%	20.2%	12.3%	6.5%
Fields Road ES	484	6.4%	17.8%	16.3%	30.2%	28.9%	38.6%	21.5%	16.0%
Jones Lane ES	470	5.1%	12.3%	9.8%	23.4%	48.9%	27.4%	14.9%	6.2%
Thurgood Marshall ES	624	≤ 5.0%	13.5%	16.8%	28.4%	36.2%	29.8%	14.1%	17.2%
Elementary Cluster Total	**3104**	**5.7%**	**15.4%**	**13.1%**	**27.3%**	**38.1%**	**34.0%**	**16.9%**	**13.4%**
Elementary County Total	**75,144**	**≤ 5.0%**	**21.2%**	**13.9%**	**30.4%**	**29.3%**	**40.2%**	**23.3%**	**13.3%**

**Percent of students approved for Free and Reduced-priced Meals Program (FARMS) during the 2014–2015 school year.*

***Percent of English for Speakers of Other Languages (ESOL) during the 2014–2015 school year. High School students are served in regional ESOL centers.*

****Mobility Rate is the number of entries plus withdrawals during the 2013–2014 school year compared to total enrollment.*

Notes: Native Hawaiian/Pacific Islander and American Indian/Alaskan Native categories total less than 1% and were therefore excluded from the table.

Due to federal and state guidelines, demographic characteristics of schools of less than or equal to 5.0% are reported as ≤ 5.0%.


Program Capacity Table

(School Year 2014–2015)

Schools	Grades Served	Capacity (HS @90% MS@85%)	Total Rooms	Support Rooms	Regular Secondary @25	Regular Elementary @23	CSR Grades 1–2 @18	Pre–K @20	Pre–K @40	HS @20	CSR KIND @18	KIND @22	ESOL @15	METS @15	Special Education Services: School Based: HSM @13	ELEM LAD @13	Cluster Based	Quad Cluster Based: ELC @10	LANG @12	LFI @10	SCB @6	County & Regional Based: AAC@7	AUT @6	BRIDGE @10	DHOH @7	ED @10	EXTENSIONS @6	GT/LD @13	PD @7	PEP@6	PEP @12	PEP @18	VISION (Elementary) @7	OTHER
Quince Orchard HS	9-12	1857	86		80								3								1						2							
Lakelands Park MS	6-8	1122	57		51								1								3						2							
Ridgeview MS	6-8	995	48		46								1										1											
Brown Station ES	HS-5	436	27	4		3	9		1	1	5				1															1		2		
Rachel Carson ES	PreK-5	667	35	5		20			1			7			1																			1
Fields Road ES	PreK-5	419	30	5		4	10	1			5				1								4											
Jones Lane ES	K-5	441	27	5		14						3			1			4																
Thurgood Marshall ES	K-5	534	32	4		15						5			1																1	3		3

Facility Characteristics of Schools 2014–2015

Schools	Year Facility Opened	Year Reopened/ Revitalized	Total Square Footage	Site Size Acres	Adjacent Park	Reloc-atable Classrooms	Linkages to Learning Program	Home School Model
Quince Orchard HS	1988		284,912	30.1				
Lakelands Park MS	2005		153,588	8.11	Yes			
Ridgeview MS	1975		139,742	20		4		
Brown Station ES	1969		58,338	9	Yes	6		Yes
Rachel Carson ES	1990		78,547	12.4		11		Yes
Fields Road ES	1973		72,302	10		4		Yes
Jones Lane ES	1987		60,679	12.1		4		Yes
Thurgood Marshall ES	1993		77,798	12		5		Yes

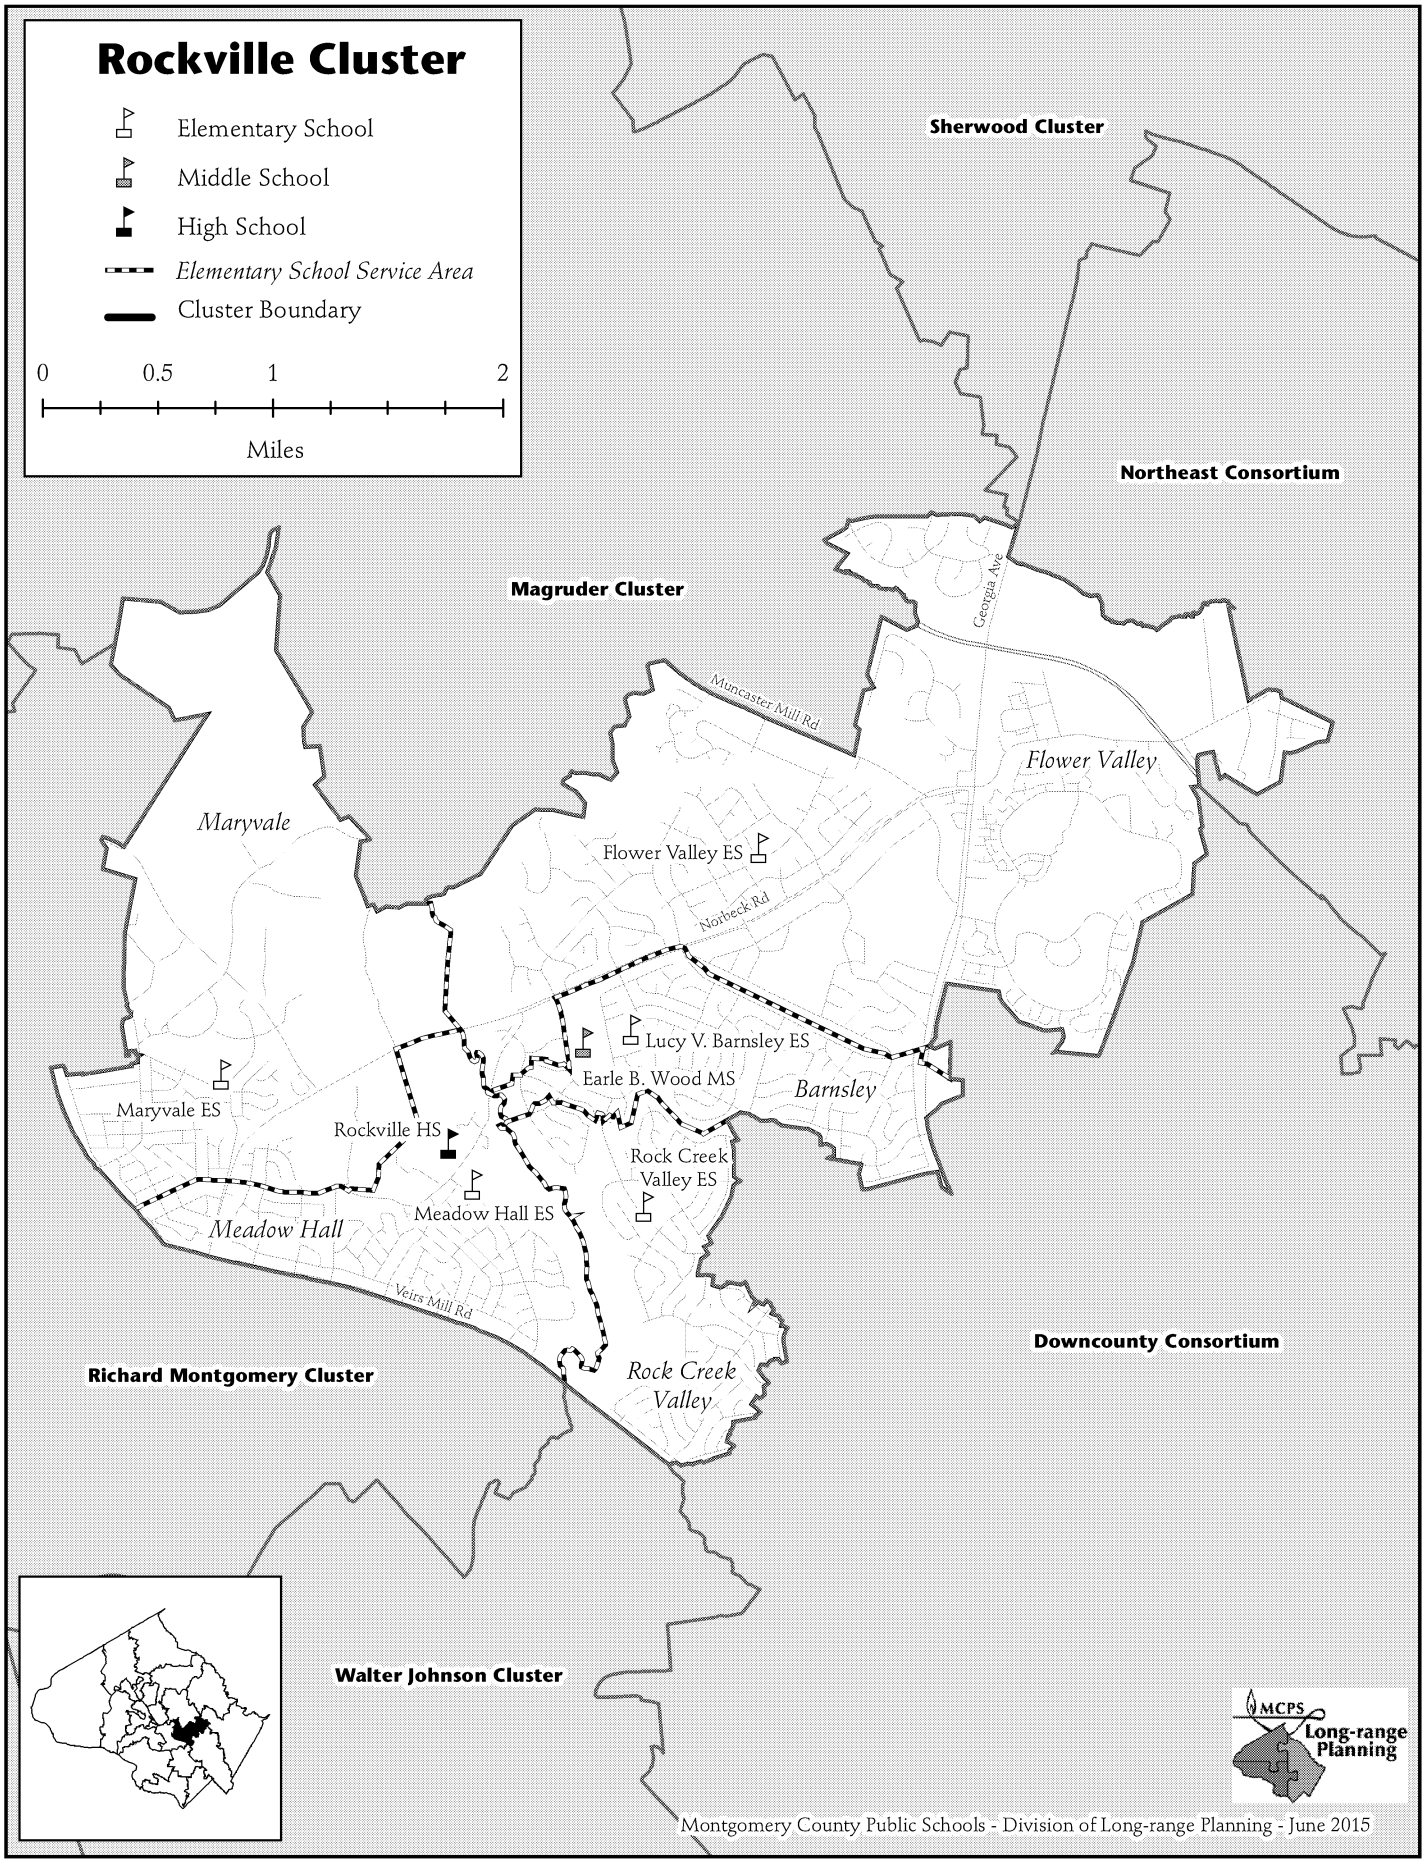
Rockville Cluster
Elementary School
Middle School
High School
Elementary School Service Area
Cluster Boundary
0
0.5
1
2
Miles
Sherwood Cluster
Northeast Consortium
Magruder Cluster
Georgia Ave
Muncaster Mill Rd
Flower Valley
Maryvale
Flower Valley ES
Notbeck Rd
Lucy V. Barnsley ES
Earle B. Wood MS
Barnsley
Maryvale ES
Rockville HS
Rock Creek Valley ES
Meadow Hall ES
Meadow Hall
Veirs Mill Rd
Downcounty Consortium
Richard Montgomery Cluster
Rock Creek Valley
Walter Johnson Cluster
MCPS
Long-range Planning
Montgomery County Public Schools - Division of Long-range Planning - June 2015

SCHOOLS

Lucy V. Barnsley Elementary School

Capital Project: Projections indicate enrollment at Lucy V. Barnsley Elementary School will exceed capacity by 92 seats or more by the end of the six-year CIP period. A classroom addition is approved for the school. Although the Board of Education requested a completion date of August 2017, the County Council maintained the approved FY 2015–2020 CIP completion date of August 2018. FY 2017 expenditures are programmed to construct the classroom addition. In order for this project to be completed on schedule, county and state funding must be provided at the levels approved in this CIP.

Maryvale Elementary School

Capital Project: A revitalization/expansion project is scheduled for this school. Although the Board of Education requested a completion date of January 2019, the County Council maintained the approved FY 2015–2020 CIP completion date of January 2020. An FY 2016 appropriation for planning funds is approved to begin the architectural design for this project. In order for this project to be completed on this schedule, county and state funding must be provided at the levels approved in this CIP. On November 17, 2011, the Board of Education approved the collocation of Carl Sandburg Learning Center on the Maryvale Elementary School campus when the revitalization/expansion project is complete.

Meadow Hall Elementary School

Capital Project: Previous projections indicated that enrollment at Meadow Hall Elementary School would exceed capacity by 92 seats or more by the end of the six-year CIP planning period. Therefore, an FY 2013 appropriation was approved for facility planning to determine the feasibility, scope, and cost for a classroom addition. However, due to fiscal constraints in the county and because the enrollment did not exceed capacity by more than 150 seats by the end of the six-year planning period when the FY 2015–202 CIP was prepared in the fall 2013, no funds are approved in this CIP for a classroom addition. A date for an addition will be considered in a future CIP if the enrollment exceeds 92 seats or more by the end of the six-year planning period. Relocatable classrooms will be utilized until additional capacity can be added.

CAPITAL PROJECTS


School	Project	Project Status*	Date of Completion
Lucy V. Barnsley ES	Addition	Programmed	Aug. 2018
Maryvale ES	Revitalization/ expansion, with collocation of Carl Sandburg LC	Approved	Jan. 2020
Meadow Hall ES	Classroom addition	Proposed	TBD

"Approved"— Project has an FY 2015 or FY 2016 appropriation approved in the FY 2015–2020 CIP.

"Deferred"—Funds have been deferred for a future CIP.

"Programmed"—Project has expenditures programmed in a future year of the CIP for planning and/or construction funds.

"Proposed"—Project has facility planning funds approved for FY 2015 or approved for FY 2016 for a feasibility study.

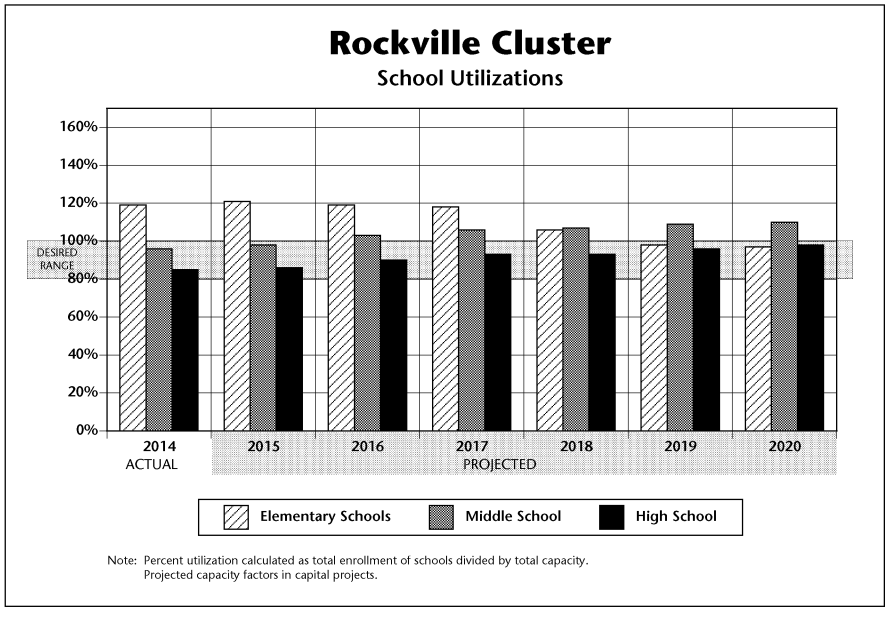

Projected Enrollment and Space Availability

Effects of the Amended FY2015–2020 CIP and Non–CIP Actions on Space Available

Schools			Actual 14–15	Projections 15–16	16–17	17–18	18–19	19–20	20–21	2024	2029
Rockville HS		Program Capacity	1570	1570	1570	1570	1570	1570	1570	1570	1570
		Enrollment	**1339**	**1358**	**1415**	**1459**	**1454**	**1512**	**1536**	**1650**	**1550**
		Available Space	*232*	*212*	*156*	*112*	*116*	*58*	*34*	*(80)*	*20*
		Comments									
Earle B. Wood MS		Program Capacity	961	961	961	961	961	961	961	961	961
		Enrollment	**927**	**943**	**988**	**1020**	**1025**	**1043**	**1053**	**1150**	**1050**
		Available Space	*34*	*18*	*(28)*	*(60)*	*(64)*	*(82)*	*(92)*	*(189)*	*(89)*
		Comments									
Lucy V. Barnsley ES	CSR	Program Capacity	404	404	404	404	673	673	673		
		Enrollment	**691**	**685**	**644**	**642**	**646**	**632**	**619**		
		Available Space	*(287)*	*(281)*	*(240)*	*(238)*	*27*	*41*	*54*		
		Comments	Planning for Addition				Addition Complete				
Flower Valley ES		Program Capacity	429	429	429	429	429	429	429		
		Enrollment	**480**	**477**	**450**	**458**	**445**	**437**	**437**		
		Available Space	*(51)*	*(48)*	*(21)*	*(29)*	*(16)*	*(8)*	*(8)*		
		Comments									
Maryvale ES	CSR	Program Capacity	626	626	626	626	626	778	778		
		Enrollment	**613**	**660**	**662**	**676**	**675**	**670**	**657**		
		Available Space	*13*	*(34)*	*(36)*	*(50)*	*(49)*	*108*	*121*		
		Comments		Planning for Revitalization/ Expansion			@ North Lake	Rev/Ex Complete Jan. 2020			
Meadow Hall ES	CSR	Program Capacity	370	370	370	370	370	370	370		
		Enrollment	**428**	**431**	**429**	**421**	**428**	**421**	**413**		
		Available Space	*(58)*	*(61)*	*(59)*	*(51)*	*(58)*	*(51)*	*(43)*		
		Comments									
Rock Creek Valley ES	CSR	Program Capacity	393	393	393	393	393	393	393		
		Enrollment	**437**	**441**	**451**	**426**	**437**	**426**	**428**		
		Available Space	*(44)*	*(48)*	*(58)*	*(33)*	*(44)*	*(33)*	*(35)*		
		Comments									
Cluster Information		HS Utilization	85%	86%	90%	93%	93%	96%	98%	105%	99%
		HS Enrollment	1339	1358	1415	1459	1454	1512	1536	1650	1550
		MS Utilization	96%	98%	103%	106%	107%	109%	110%	120%	109%
		MS Enrollment	927	943	988	1020	1025	1043	1053	1150	1050
		ES Utilization	119%	121%	119%	118%	106%	98%	97%	98%	98%
		ES Enrollment	2649	2694	2636	2623	2631	2586	2554	2600	2600

Demographic Characteristics of Schools

Schools	2014–2015 Total Enrollment	Two or more races %	Black or Afr. Amer. %	Asian%	Hispanic %	White %	2014–2015 FARMS%*	ESOL%**	2013–2014 Mobility Rate%***
Rockville HS	1339	≤ 5.0%	13.9%	11.0%	36.9%	34.1%	31.4%	9.5%	8.7%
Earle B. Wood MS	927	≤ 5.0%	12.8%	10.0%	38.8%	33.5%	36.1%	8.6%	9.9%
Lucy V. Barnsley ES	691	6.2%	10.1%	14.0%	30.8%	38.8%	29.1%	13.7%	10.6%
Flower Valley ES	480	≤ 5.0%	12.1%	11.5%	21.5%	50.2%	24.4%	7.7%	10.9%
Maryvale ES	613	7.3%	28.4%	8.0%	29.2%	26.6%	43.7%	25.6%	10.1%
Meadow Hall ES	428	≤ 5.0%	11.0%	11.2%	54.4%	18.0%	53.7%	23.1%	11.8%
Rock Creek Valley ES	437	7.3%	10.3%	11.9%	40.0%	30.2%	37.5%	24.0%	9.1%
Elementary Cluster Total	**2649**	**6.2%**	**14.9%**	**11.4%**	**34.1%**	**33.3%**	**37.1%**	**18.7%**	**10.5%**
Elementary County Total	75,144	≤ 5.0%	21.2%	13.9%	30.4%	29.3%	40.2%	23.3%	13.3%

**Percent of students approved for Free and Reduced-priced Meals Program (FARMS) during the 2014–2015 school year.*

***Percent of English for Speakers of Other Languages (ESOL) during the 2014–2015 school year. High School students are served in regional ESOL centers.*

****Mobility Rate is the number of entries plus withdrawals during the 2013–2014 school year compared to total enrollment.*
Notes: Native Hawaiian/Pacific Islander and American Indian/Alaskan Native categories total less than 1% and were therefore excluded from the table.

Due to federal and state guidelines, demographic characteristics of schools of less than or equal to 5.0% are reported as ≤ 5.0%.


Program Capacity Table

(School Year 2014–2015)

Schools	Grades Served	Capacity (HS @90% MS@85%)	Total Rooms	Support Rooms	Regular Secondary @25	Regular Elementary @23	CSR Grades 1–2 @18	Pre–K @20	Pre–K @40	HS @20	CSR KIND @18	KIND @22	ESOL @15	METS @15	Special Education Services: School Based: HSM @13	Cluster Based: ELEM LAD @13	Quad Cluster Based: ELC @10	LANG @12	LFI @10	SCB @6	County & Regional Based: AAC@7	AUT @6	BRIDGE @10	DHOH @7	ED @10	EXTENSIONS @6	GT/LD @13	PD @7	PEP@6	PEP @12	PEP @18	VISION (Elementary) @7	OTHER
Rockville HS	9-12	1571	78		65								2						5			2		4								
Earle B. Wood MS	6-8	961	50		43								1									2		4								
Lucy V. Barnsley ES	K-5	404	28	4		4	9				5													3			3					
Flower Valley ES	K-5	429	25	3		14						3												3	2							
Maryvale ES	HS-5	626	36	4		12	9		1	2	5											3										
Meadow Hall ES	K-5	370	25	3		4	8				5					2						3										
Rock Creek Valley ES	K-5	393	29	4		4	9				5													7								

Facility Characteristics of Schools 2014–2015

Schools	Year Facility Opened	Year Reopened/ Revitalized	Total Square Footage	Site Size Acres	Adjacent Park	Reloc-atable Classrooms	Linkages to Learning Program	Home School Model
Rockville HS	1968	2004	316,973	29.61				
Earle B. Wood MS	1965	2001	152,588	8.5	Yes			
Lucy V. Barnsley ES	1965	1998	72,024	10		10		
Flower Valley ES	1967	1996	61,567	9.3		1		
Maryvale ES	1969		92,050	17.7		1		
Meadow Hall ES	1956	1994	61,694	8.4	Yes	5		
Rock Creek Valley ES	1964	2001	76,692	10.4		4		

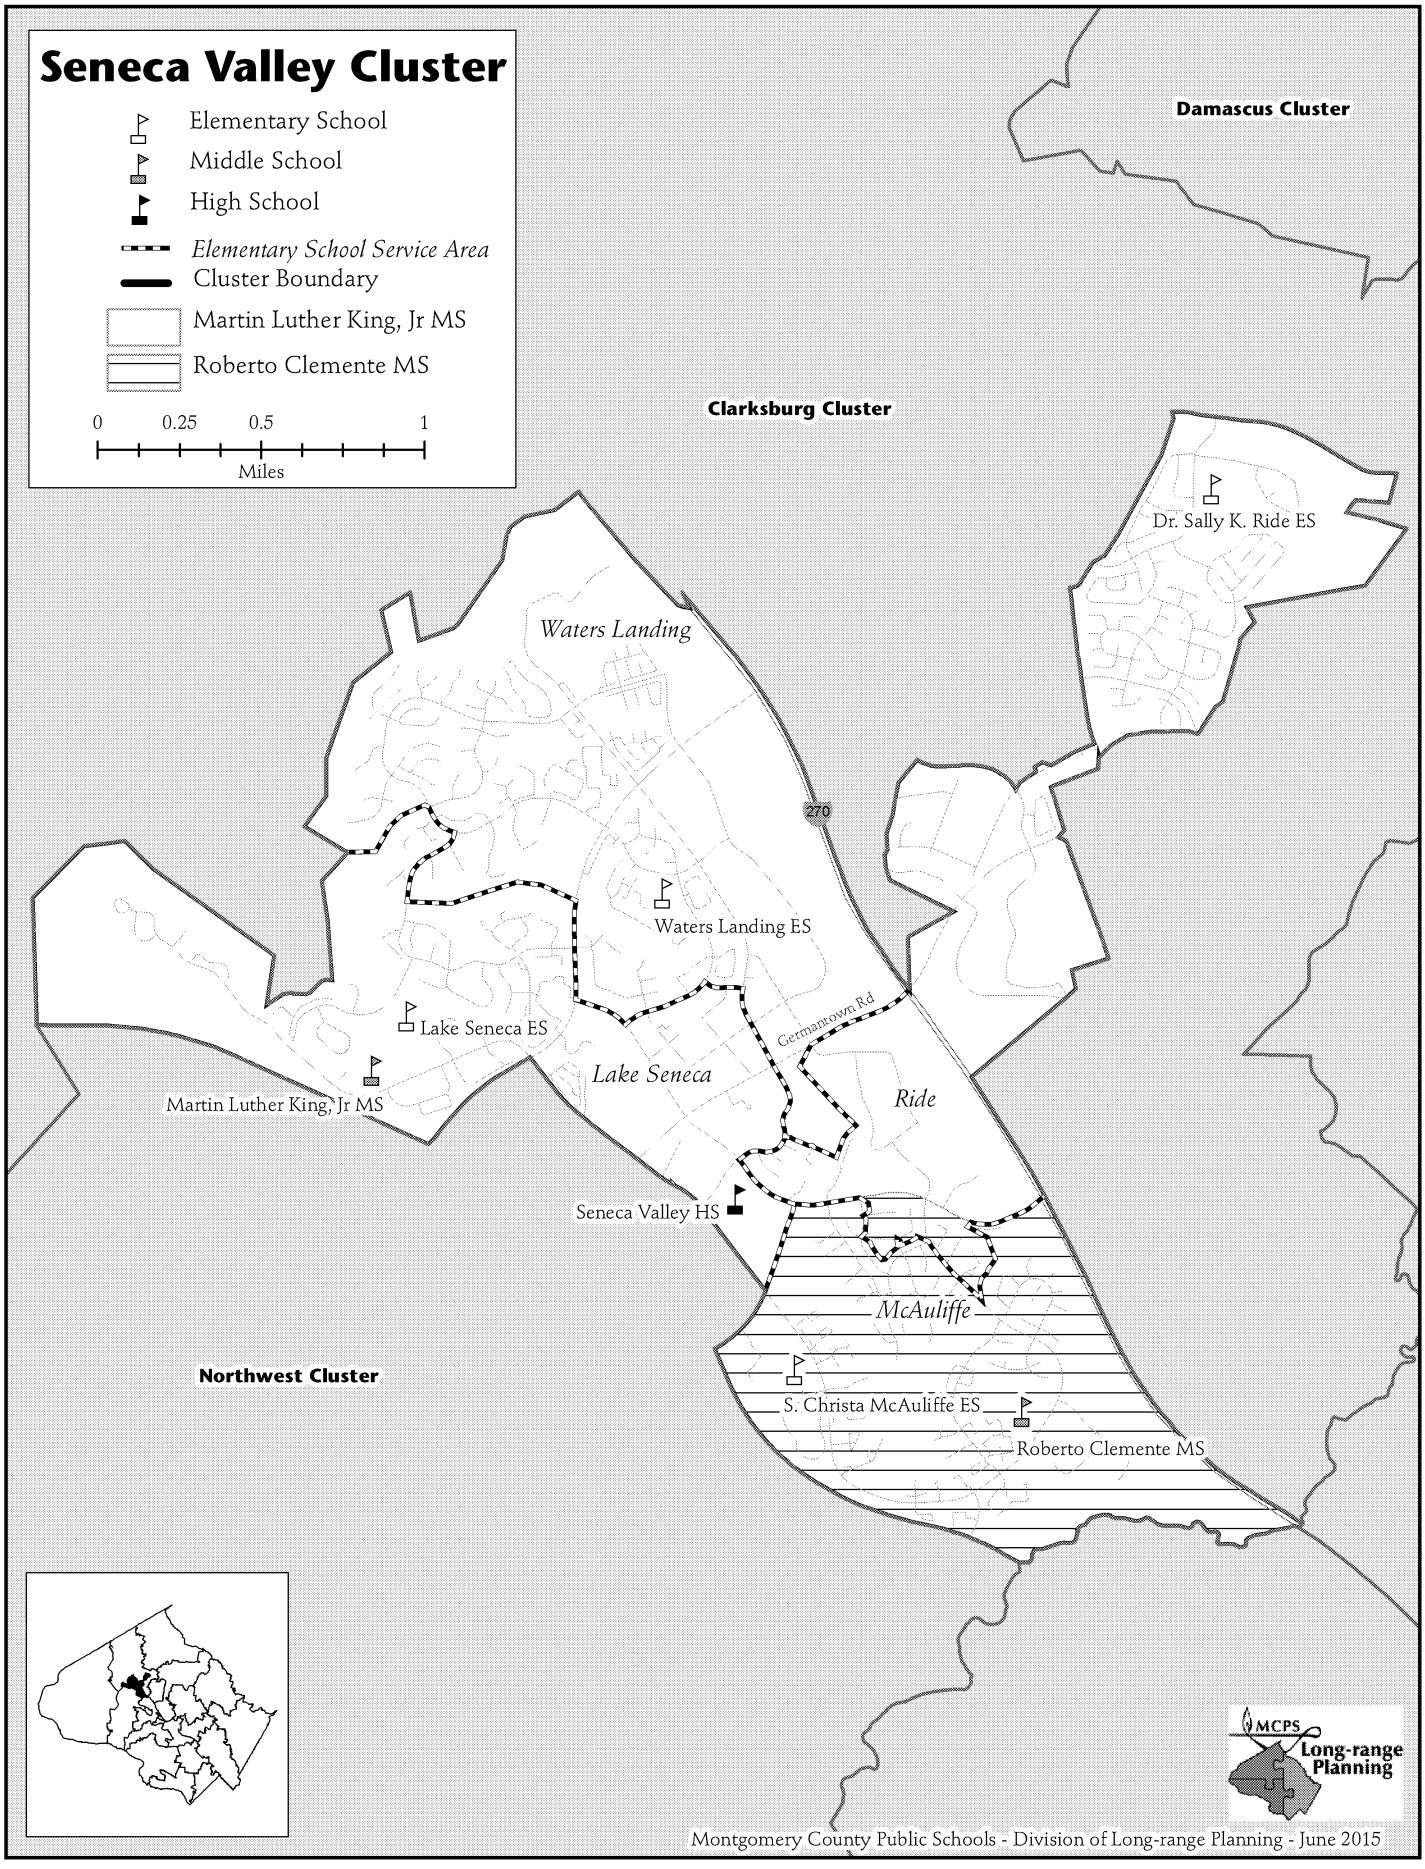
Seneca Valley Cluster
Elementary School
Middle School
High School
Elementary School Service Area
Cluster Boundary
Martin Luther King, Jr MS
Roberto Clemente MS
0
0.25
0.5
1
Miles
Damascus Cluster
Clarksburg Cluster
Dr. Sally K. Ride ES
Waters Landing
270
Waters Landing ES
Lake Seneca ES
Germantown Rd
Lake Seneca
Martin Luther King, Jr MS
Ride
Seneca Valley HS
McAuliffe
Northwest Cluster
S. Christa McAuliffe ES
Roberto Clemente MS
MCPS
Long-range Planning
Montgomery County Public Schools - Division of Long-range Planning - June 2015

CLUSTER PLANNING ISSUES

Planning Issues: The 2009 adopted Germantown Forward Sector Plan provides for up to 10,200 mostly multi-family residential units. The majority of planned residential development is located in the Seneca Valley Cluster. The plan requires some redevelopment of shopping centers and some other commercial uses. In addition, the plan anticipates construction of the Corridor Cities Transitway to support the higher housing densities. It is anticipated that the plan will take 20 to 30 years to build-out. The pace of construction will be market driven. A future elementary school site is included in the plan.

SCHOOLS

Seneca Valley High School

Capital Project: A revitalization/expansion project is scheduled for this school. Although the Board of Education requested a completion date of August 2018, the County Council maintained the approved FY 2015–2020 CIP completion date of August 2019. An FY 2014 appropriation was approved for planning funds to begin the architectural design for the project. In order for this project to be completed on schedule, county and state funding must be provided at the levels approved in this CIP.

Planning Issue: Although a classroom addition is scheduled to open in August 2015 to accommodate the overutilization at Clarksburg High School, student enrollment will continue to exceed capacity by nearly 500 students by the end of the six-year CIP planning period. Enrollment also is projected to exceed capacity at Northwest High School by nearly 300 students. The Seneca Valley High School service area is adjacent to the Clarksburg and Northwest high school service areas. A revitalization/expansion project of Seneca Valley High School, approved for completion in August 2019, will be designed and constructed with a capacity for 2400 students. The enrollment at Seneca Valley High School is projected to be 1395 students by the end of the six-year planning period. With a capacity of 2400 seats, there will be approximately 1000 seats available to accommodate students from Clarksburg and Northwest high schools when the project is complete.

Lake Seneca Elementary School

Capital Project: Projections indicate enrollment at Lake Seneca Elementary School will exceed capacity by 92 seats or more by the end of the six-year CIP period. An FY 2014 appropriation was approved for facility planning to determine the feasibility, scope, and cost for a classroom addition. A date for the addition will be considered in a future CIP. Relocatable classrooms will be utilized until additional capacity can be added.

S. Christa McAuliffe Elementary School

Capital Project: Projections indicate enrollment at S. Christa McAuliffe Elementary School will exceed capacity by 92 seats or more by the end of the six-year CIP period. A classroom addition is approved for this school. Although the Board of Education requested a completion date of August 2019, the County Council maintained the approved FY 2015–2020 CIP completion date of August 2020. FY 2017 expenditures are programmed for planning funds to begin the architectural design for a classroom addition. Relocatable classrooms will be utilized until additional capacity can be added. In order for this project to be completed on schedule, county and state funding must be provided at the levels approved in this CIP.


Seneca Valley Cluster Articulation*

Seneca Valley High School

Roberto Clemente MS	Dr. Martin Luther King, Jr. MS
S. Christa McAuliffe ES Dr. Sally K. Ride ES (South of Middlebrook Road)	Lake Seneca ES Dr. Sally K. Ride ES (North of Middlebrook Road) Waters Landing ES

* "Cluster" is defined as the collection of elementary schools that articulate to the same high school.

* Clopper Mill, Germantown, and a portion of Great Seneca Creek elementary schools also articulate to Roberto Clemente Middle School, but thereafter articulate to Northwest High School.

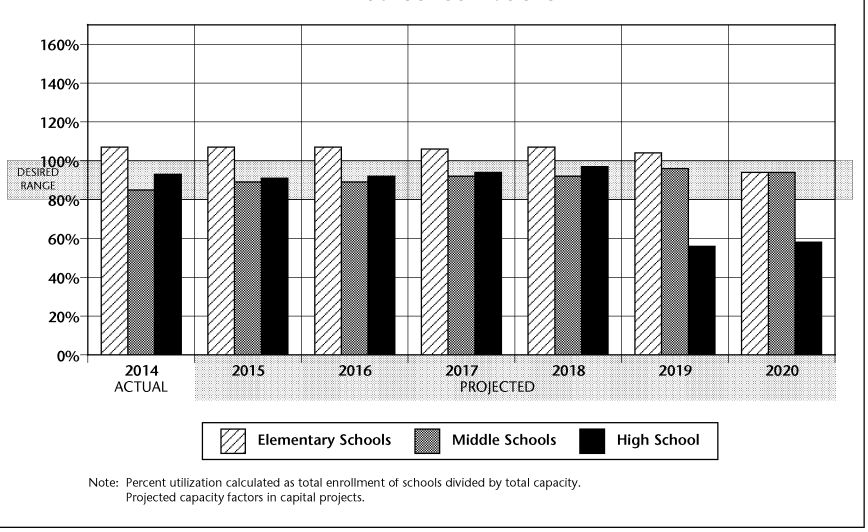

CAPITAL PROJECTS

School	Project	Project Status*	Date of Completion
Seneca Valley HS	Revitalization/ expansion	Programmed	Aug. 2019, building Aug. 2020, site
Lake Seneca ES	Classroom addition	Proposed	TBD
S. Christa McAuliffe ES	Classroom addition	Programmed	Aug. 2020

"Approved"— Project has an FY 2015 or FY 2016 appropriation approved in the FY 2015–2020 CIP.

"Deferred"—Funds have been deferred for a future CIP.

"Programmed"—Project has expenditures programmed in a future year of the CIP for planning and/or construction funds.

"Proposed"—Project has facility planning funds approved for FY 2015 or approved for FY 2016 for a feasibility study.

Projected Enrollment and Space Availability

Effects of the Amended FY2015–2020 CIP and Non–CIP Actions on Space Available

Schools			Actual 14–15	Projections 15–16	16–17	17–18	18–19	19–20	20–21	2024	2029
Seneca Valley HS		Program Capacity	1374	1361	1361	1361	1347	2400	2400	2400	2400
		Enrollment	**1284**	**1233**	**1258**	**1285**	**1309**	**1350**	**1395**	**1500**	**1400**
		Available Space	*90*	*128*	*103*	*76*	*38*	*1050*	*1005*	*900*	*1000*
		Comments	Planning for Revitalization/Expansion See text	+1 LFI		Revitalization/ Expansion in Progress		Rev/Ex Complete Aug. 2019			
Roberto Clemente MS		Program Capacity	1231	1231	1231	1231	1231	1231	1231	1231	1231
		Enrollment	**1208**	**1268**	**1297**	**1279**	**1279**	**1291**	**1286**	**1350**	**1250**
		Available Space	*23*	*(37)*	*(66)*	*(48)*	*(48)*	*(60)*	*(55)*	*(119)*	*(19)*
		Comments									
Martin Luther King, Jr. MS		Program Capacity	905	905	905	905	905	905	905	905	905
		Enrollment	**612**	**640**	**612**	**682**	**686**	**753**	**728**	**800**	**750**
		Available Space	*293*	*265*	*293*	*223*	*219*	*152*	*177*	*105*	*155*
		Comments									
Lake Seneca ES	CSR	Program Capacity	410	410	410	410	410	410	410		
		Enrollment	**536**	**540**	**533**	**523**	**532**	**517**	**510**		
		Available Space	*(126)*	*(130)*	*(123)*	*(113)*	*(122)*	*(107)*	*(100)*		
		Comments	Facility Planning for Addition								
S. Christa McAuliffe ES	CSR	Program Capacity	526	526	526	526	526	526	785		
		Enrollment	**629**	**635**	**647**	**655**	**655**	**654**	**665**		
		Available Space	*(103)*	*(109)*	*(121)*	*(129)*	*(129)*	*(128)*	*120*		
		Comments			Planning for Addition				Addition Complete		
Dr. Sally K. Ride ES	CSR	Program Capacity	523	523	523	523	523	523	523		
		Enrollment	**527**	**520**	**519**	**508**	**506**	**493**	**494**		
		Available Space	*(4)*	*3*	*4*	*15*	*17*	*30*	*29*		
		Comments									
Waters Landing ES	CSR	Program Capacity	*776*	*776*	*776*	*776*	*776*	*776*	*776*		
		Enrollment	**691**	**691**	**700**	**694**	**691**	**670**	**675**		
		Available Space	*85*	*85*	*76*	*82*	*85*	*106*	*101*		
		Comments									
Cluster Information		HS Utilization	93%	91%	92%	94%	97%	56%	58%	63%	58%
		HS Enrollment	1284	1233	1258	1285	1309	1350	1395	1500	1400
		MS Utilization	85%	89%	89%	92%	92%	96%	94%	101%	94%
		MS Enrollment	1820	1908	1909	1961	1965	2044	2014	2150	2000
		ES Utilization	107%	107%	107%	106%	107%	104%	94%	96%	96%
		ES Enrollment	2383	2386	2399	2380	2384	2334	2344	2400	2400

Demographic Characteristics of Schools

Schools	2014–2015 Total Enrollment	Two or more races %	Black or Afr. Amer. %	Asian%	Hispanic %	White %	2014–2015 FARMS%*	ESOL%**	2013–2014 Mobility Rate%***
Seneca Valley HS	1284	≤ 5.0%	35.7%	11.1%	27.0%	21.3%	37.7%	9.0%	18.7%
Roberto Clemente MS	1208	5.3%	25.4%	26.4%	25.6%	17.1%	33.2%	≤ 5.0%	11.0%
Martin Luther King, Jr MS	612	6.2%	32.5%	14.2%	28.6%	18.5%	46.7%	10.9%	16.9%
Lake Seneca ES	536	≤ 5.0%	37.7%	8.0%	30.0%	19.4%	51.9%	21.8%	20.4%
S. Christa McAuliffe ES	629	7.5%	34.8%	8.4%	32.6%	16.4%	50.4%	19.4%	16.8%
Dr. Sally K. Ride ES	528	5.1%	38.3%	18.2%	25.8%	12.5%	48.5%	17.2%	15.1%
Waters Landing ES	691	6.9%	34.9%	6.1%	34.2%	17.4%	52.8%	23.4%	24.3%
Elementary Cluster Total	**2384**	**6.2%**	**36.2%**	**9.8%**	**31.0%**	**16.5%**	**50.7%**	**20.5%**	**19.2%**
Elementary County Total	75,144	≤ 5.0%	21.2%	13.9%	30.4%	29.3%	40.2%	23.3%	13.3%

**Percent of students approved for Free and Reduced-priced Meals Program (FARMS) during the 2014–2015 school year.*

***Percent of English for Speakers of Other Languages (ESOL) during the 2014–2015 school year. High School students are served in regional ESOL centers.*

****Mobility Rate is the number of entries plus withdrawals during the 2013–2014 school year compared to total enrollment.*
Notes: Native Hawaiian/Pacific Islander and American Indian/Alaskan Native categories total less than 1% and were therefore excluded from the table.

Due to federal and state guidelines, demographic characteristics of schools of less than or equal to 5.0% are reported as ≤ 5.0%.


Program Capacity Table

(School Year 2014–2015)

Schools	Grades Served	Capacity (HS @90% MS@85%)	Total Rooms	Support Rooms	Regular Secondary @25	Regular Elementary @23	CSR Grades 1–2 @18	Pre–K @20	Pre–K @40	HS @20	CSR KIND @18	KIND @22	ESOL @15	METS @15	Special Education Services: School Based: HSM @13	School Based: ELEM LAD @13	Quad Cluster Based: ELC @10	Quad Cluster Based: LANG @12	Quad Cluster Based: LFI @10	Quad Cluster Based: SCB @6	County & Regional Based: AAC@7	AUT @6	BRIDGE @10	DHOH @7	ED @10	EXTENSIONS @6	GT/LD @13	PD @7	PEP@6	PEP @12	PEP @18	VISION (Elementary) @7	OTHER
Seneca Valley HS	9-12	1374	66		57								3	1					3	2													
Roberto Clemente MS	6-8	1231	60		56								1						2								1						
Martin Luther King, Jr MS	6-8	905	43		42								1																				
Lake Seneca ES	K-5	410	26	4		2	10		1		5																		1	1	2		
S. Christa McAuliffe ES	HS-5	526	33	5		6	13			1	6					2																	
Dr. Sally K. Ride ES	HS-5	523	33	5		8	8		1	1	4					1	5																
Waters Landing ES	K-5	776	43	3		16	14				7								3														

Facility Characteristics of Schools 2014–2015

Schools	Year Facility Opened	Year Reopened/ Revitalized	Total Square Footage	Site Size Acres	Adjacent Park	Reloc-atable Classrooms	Linkages to Learning Program	Home School Model
Seneca Valley HS	1974		251,278	29.4		1		
Roberto Clemente MS	1992		148,246	19.9				
Martin Luther King, Jr MS	1996		135,867	19				
Lake Seneca ES	1985		58,770	9.4		9		
S. Christa McAuliffe ES	1987		77,240	10.6	Yes	8		
Dr. Sally K. Ride ES	1994		78,686	13.5		4		
Waters Landing ES	1988		101,352	10				Yes

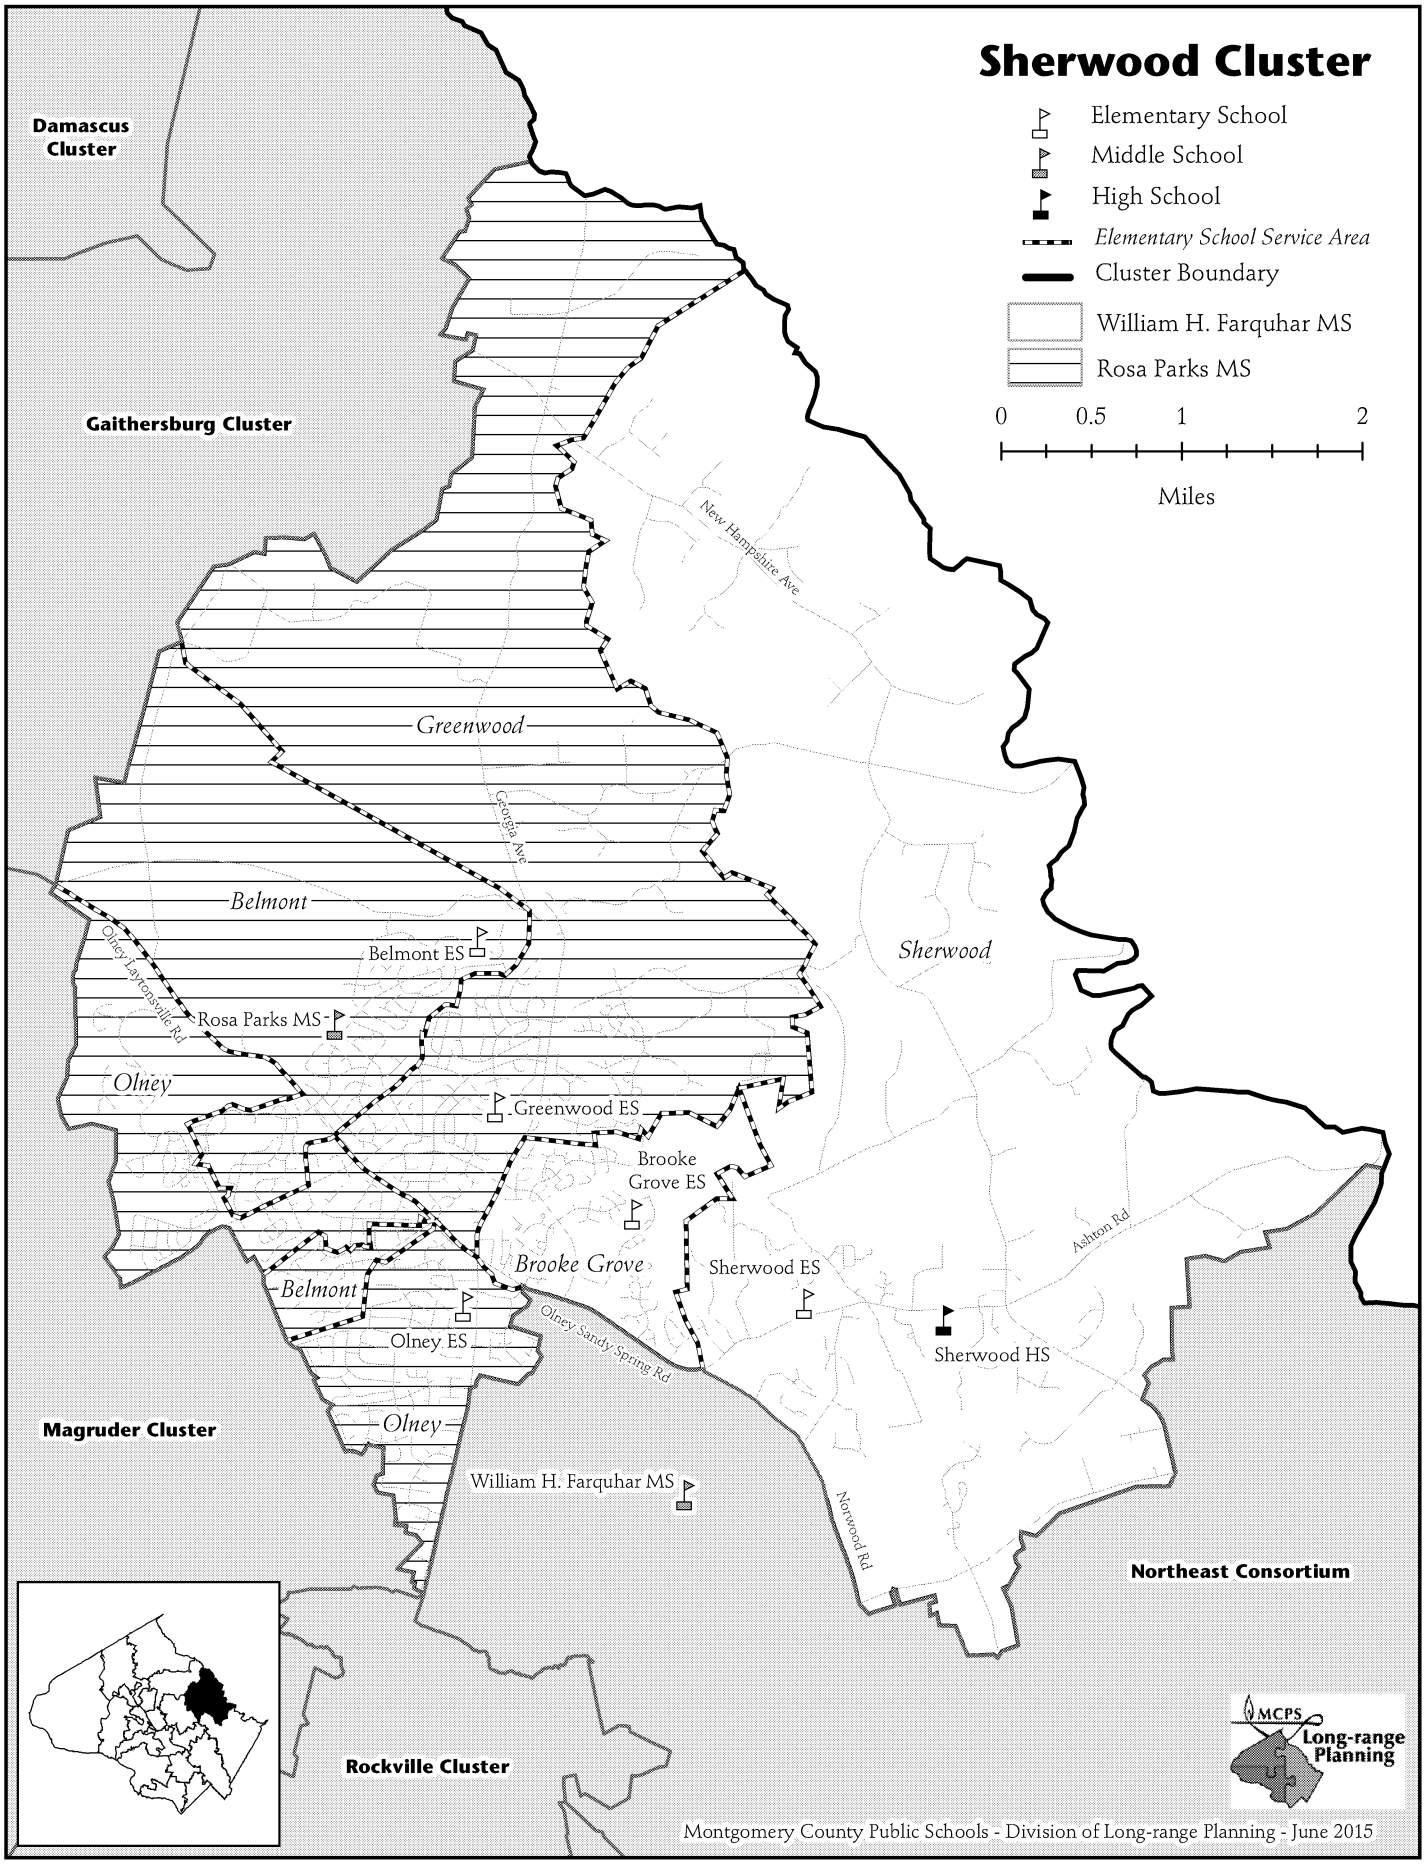
Sherwood Cluster
Elementary School
Middle School
High School
Elementary School Service Area
Cluster Boundary
William H. Farquhar MS
Rosa Parks MS
0
0.5
1
2
Miles
Damascus Cluster
Gaithersburg Cluster
Magruder Cluster
Rockville Cluster
Northeast Consortium
New Hampshire Ave
Greenwood
Georgia Ave
Belmont
Olney-Laytonsville Rd
Belmont ES
Rosa Parks MS
Olney
Greenwood ES
Brooke Grove ES
Brooke Grove
Belmont
Olney ES
Olney Sandy Spring Rd
Olney
William H. Farquhar MS
Sherwood
Sherwood ES
Ashton Rd
Sherwood HS
Norwood Rd
MCPS
Long-range Planning
Montgomery County Public Schools - Division of Long-range Planning - June 2015

SCHOOLS

William H. Farquhar Middle School

Capital Project: A revitalization/expansion project is scheduled for this school with a completion date of August 2016. An FY 2015 appropriation for construction funds is approved to construct the project on an adjacent property.

Belmont Elementary School

Capital Project: A revitalization/expansion project is scheduled for this school. Although the Board of Education requested a completion date of August 2020, the County Council maintained the approved FY 2015–2020 CIP completion date of August 2021. An FY 2015 appropriation was approved for facility planning for a feasibility study to determine the scope and cost of the project. In order for this project to be completed on this schedule, county and state funding must be provided at the levels approved in this CIP.

CAPITAL PROJECTS


School	Project	Project Status*	Date of Completion
Farquhar MS	Revitalization/ expansion	Approved	Aug. 2016
Belmont ES	Revitalization/ expansion	Approved	Aug. 2021

"Approved"— Project has an FY 2015 or FY 2016 appropriation approved in the FY 2015–2020 CIP.

"Deferred"—Funds have been deferred for a future CIP.

"Programmed"—Project has expenditures programmed in a future year of the CIP for planning and/or construction funds.

"Proposed"—Project has facility planning funds approved for FY 2015 or approved for FY 2016 for a feasibility study.

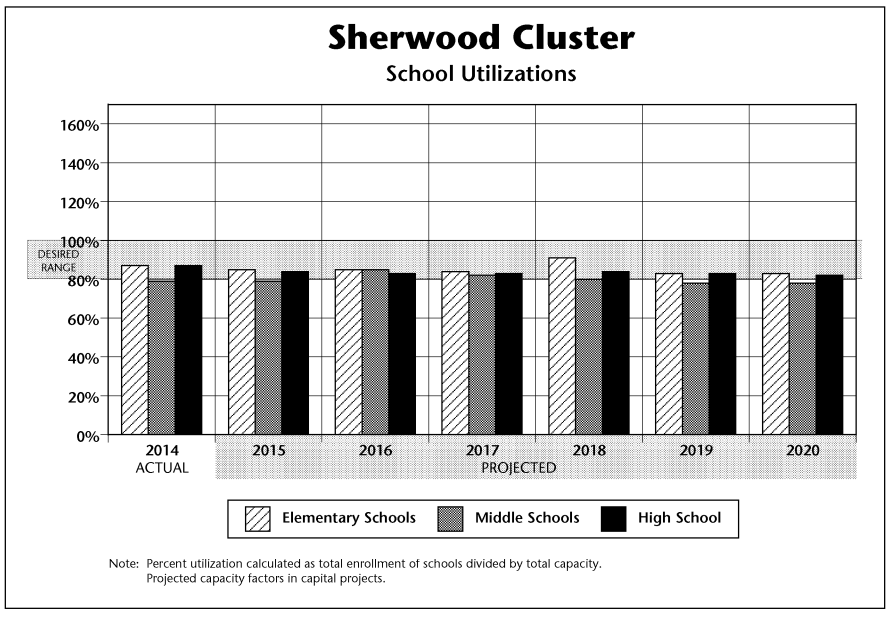

Projected Enrollment and Space Availability

Effects of the Amended FY2015–2020 CIP and Non–CIP Actions on Space Available

Schools			Actual 14–15	Projections 15–16	16–17	17–18	18–19	19–20	20–21	2024	2029
Sherwood HS		Program Capacity	2166	2166	2166	2166	2166	2166	2166	2166	2166
		Enrollment	**1891**	**1827**	**1804**	**1807**	**1821**	**1802**	**1772**	**1800**	**1700**
		Available Space	*275*	*339*	*362*	*359*	*345*	*364*	*394*	*366*	*466*
		Comments									
William H. Farquhar MS		Program Capacity	906	906	752	752	752	752	752	752	752
		Enrollment	**586**	**589**	**615**	**593**	**592**	**577**	**580**	**650**	**600**
		Available Space	*320*	*317*	*137*	*159*	*160*	*175*	*172*	*102*	*152*
		Comments	Revitalization/ Expansion in Progress		Rev/Ex Complete						
Rosa Parks MS		Program Capacity	978	978	978	978	978	978	978	978	978
		Enrollment	**904**	**891**	**854**	**824**	**792**	**780**	**770**	**800**	**750**
		Available Space	*74*	*86*	*124*	*154*	*186*	*198*	*208*	*178*	*228*
		Comments									
Belmont ES		Program Capacity	424	424	424	424	424	424	424		
		Enrollment	**310**	**309**	**329**	**339**	**353**	**355**	**360**		
		Available Space	*114*	*115*	*95*	*85*	*71*	*69*	*64*		
		Comments	Facility Planning for Rev/Ex		Planning for Revitalization/ Expansion			Move to North Lake Jan. 2020	@ North Lake		
Brooke Grove ES		Program Capacity	531	531	531	531	531	531	531		
		Enrollment	**398**	**382**	**378**	**381**	**380**	**375**	**369**		
		Available Space	*133*	*149*	*153*	*150*	*151*	*156*	*162*		
		Comments									
Greenwood ES		Program Capacity	585	585	585	585	585	585	585		
		Enrollment	**505**	**475**	**472**	**452**	**436**	**439**	**450**		
		Available Space	*80*	*110*	*113*	*133*	*149*	*146*	*135*		
		Comments									
Olney ES		Program Capacity	585	585	585	585	585	585	585		
		Enrollment	**629**	**613**	**614**	**594**	**590**	**583**	**566**		
		Available Space	*(44)*	*(28)*	*(29)*	*(9)*	*(5)*	*2*	*19*		
		Comments									
Sherwood ES		Program Capacity	569	569	569	569	569	569	569		
		Enrollment	**499**	**510**	**507**	**499**	**419**	**484**	**482**		
		Available Space	*70*	*59*	*62*	*70*	*150*	*85*	*87*		
		Comments									
Cluster Information		HS Utilization	87%	84%	83%	83%	84%	83%	82%	83%	78%
		HS Enrollment	1891	1827	1804	1807	1821	1802	1772	1800	1700
		MS Utilization	79%	79%	85%	82%	80%	78%	78%	84%	78%
		MS Enrollment	1490	1480	1469	1417	1384	1357	1350	1450	1350
		ES Utilization	87%	85%	85%	84%	81%	83%	83%	89%	89%
		ES Enrollment	2341	2289	2300	2265	2178	2236	2227	2400	2400

Demographic Characteristics of Schools

Schools	2014–2015 Total Enrollment	Two or more races %	Black or Afr. Amer. %	Asian%	Hispanic %	White %	2014–2015 FARMS%*	ESOL%**	2013–2014 Mobility Rate%***
Sherwood HS	1891	≤ 5.0%	17.6%	12.0%	13.8%	52.7%	16.8%	8.1%	7.3%
William H. Farquhar MS	586	6.1%	15.7%	14.2%	13.8%	50.2%	11.8%	≤ 5.0%	5.7%
Rosa Parks MS	904	≤ 5.0%	10.0%	9.3%	11.8%	63.5%	10.2%	≤ 5.0%	≤ 5.0%
Belmont ES	310	≤ 5.0%	5.5%	6.1%	10.6%	74.8%	6.1%	≤ 5.0%	≤ 5.0%
Brooke Grove ES	398	≤ 5.0%	18.1%	16.6%	17.1%	45.5%	26.1%	13.1%	7.1%
Greenwood ES	505	5.3%	8.5%	8.5%	10.7%	66.9%	8.7%	8.7%	≤ 5.0%
Olney ES	629	7.2%	15.1%	12.2%	16.4%	49.0%	21.3%	9.4%	8.5%
Sherwood ES	499	≤ 5.0%	20.2%	11.6%	11.8%	51.9%	16.6%	7.2%	8.2%
Elementary Cluster Total	**2341**	**≤ 5.0%**	**14.0%**	**11.2%**	**13.5%**	**56.3%**	**16.4%**	**8.8%**	**6.8%**
Elementary County Total	75,144	≤ 5.0%	21.2%	13.9%	30.4%	29.3%	40.2%	23.3%	13.3%

**Percent of students approved for Free and Reduced-priced Meals Program (FARMS) during the 2014–2015 school year.*

***Percent of English for Speakers of Other Languages (ESOL) during the 2014–2015 school year. High School students are served in regional ESOL centers.*

****Mobility Rate is the number of entries plus withdrawals during the 2013–2014 school year compared to total enrollment.*
Notes: Native Hawaiian/Pacific Islander and American Indian/Alaskan Native categories total less than 1% and were therefore excluded from the table.

Due to federal and state guidelines, demographic characteristics of schools of less than or equal to 5.0% are reported as ≤ 5.0%.


Program Capacity Table

(School Year 2014–2015)

Schools	Grades Served	Capacity (HS @90% MS@85%)	Total Rooms	Support Rooms	Regular Secondary @25	Regular Elementary @23	CSR Grades 1–2 @18	Pre–K @20	Pre–K @40	HS @20	CSR KIND @18	KIND @22	ESOL @15	METS @15	Special Education Services: School Based: HSM @13	School Based: ELEM LAD @13	Quad Cluster Based: ELC @10	Quad Cluster Based: LANG @12	Quad Cluster Based: LFI @10	Quad Cluster Based: SCB @6	County & Regional Based: AAC@7	AUT @6	BRIDGE @10	DHOH @7	ED @10	EXTENSIONS @6	GT/LD @13	PD @7	PEP@6	PEP @12	PEP @18	VISION (Elementary) @7	OTHER
Sherwood HS	9-12	2166	101		93								4						1	2													1
William H. Farquhar MS	6-8	906	44		42														1	1													
Rosa Parks MS	6-8	978	46		46																												
Belmont ES	K-5	424	23	4		15						3			1																		
Brooke Grove ES	PreK-5	531	30	4		18		1				2			1		4																
Greenwood ES	K-5	585	29	3		22						3			1																		
Olney ES	K-5	585	30	4		22						3			1																		
Sherwood ES	K-5	569	31	3		20						3			1					1		1							1	1			

Facility Characteristics of Schools 2014–2015

Schools	Year Facility Opened	Year Reopened/ Revitalized	Total Square Footage	Site Size Acres	Adjacent Park	Reloc-atable Classrooms	Linkages to Learning Program	Home School Model
Sherwood HS	1950	1991	333,154	49.3				
William H. Farquhar MS	1968		116,300	20				
Rosa Parks MS	1992		137,469	24.1	Yes			
Belmont ES	1974		49,279	10.5		1		Yes
Brooke Grove ES	1990		72,582	10.96				Yes
Greenwood ES	1970		64,609	10	Yes			Yes
Olney ES	1954	1990	68,755	9.9				Yes
Sherwood ES	1977		81,727	10.85		1		Yes

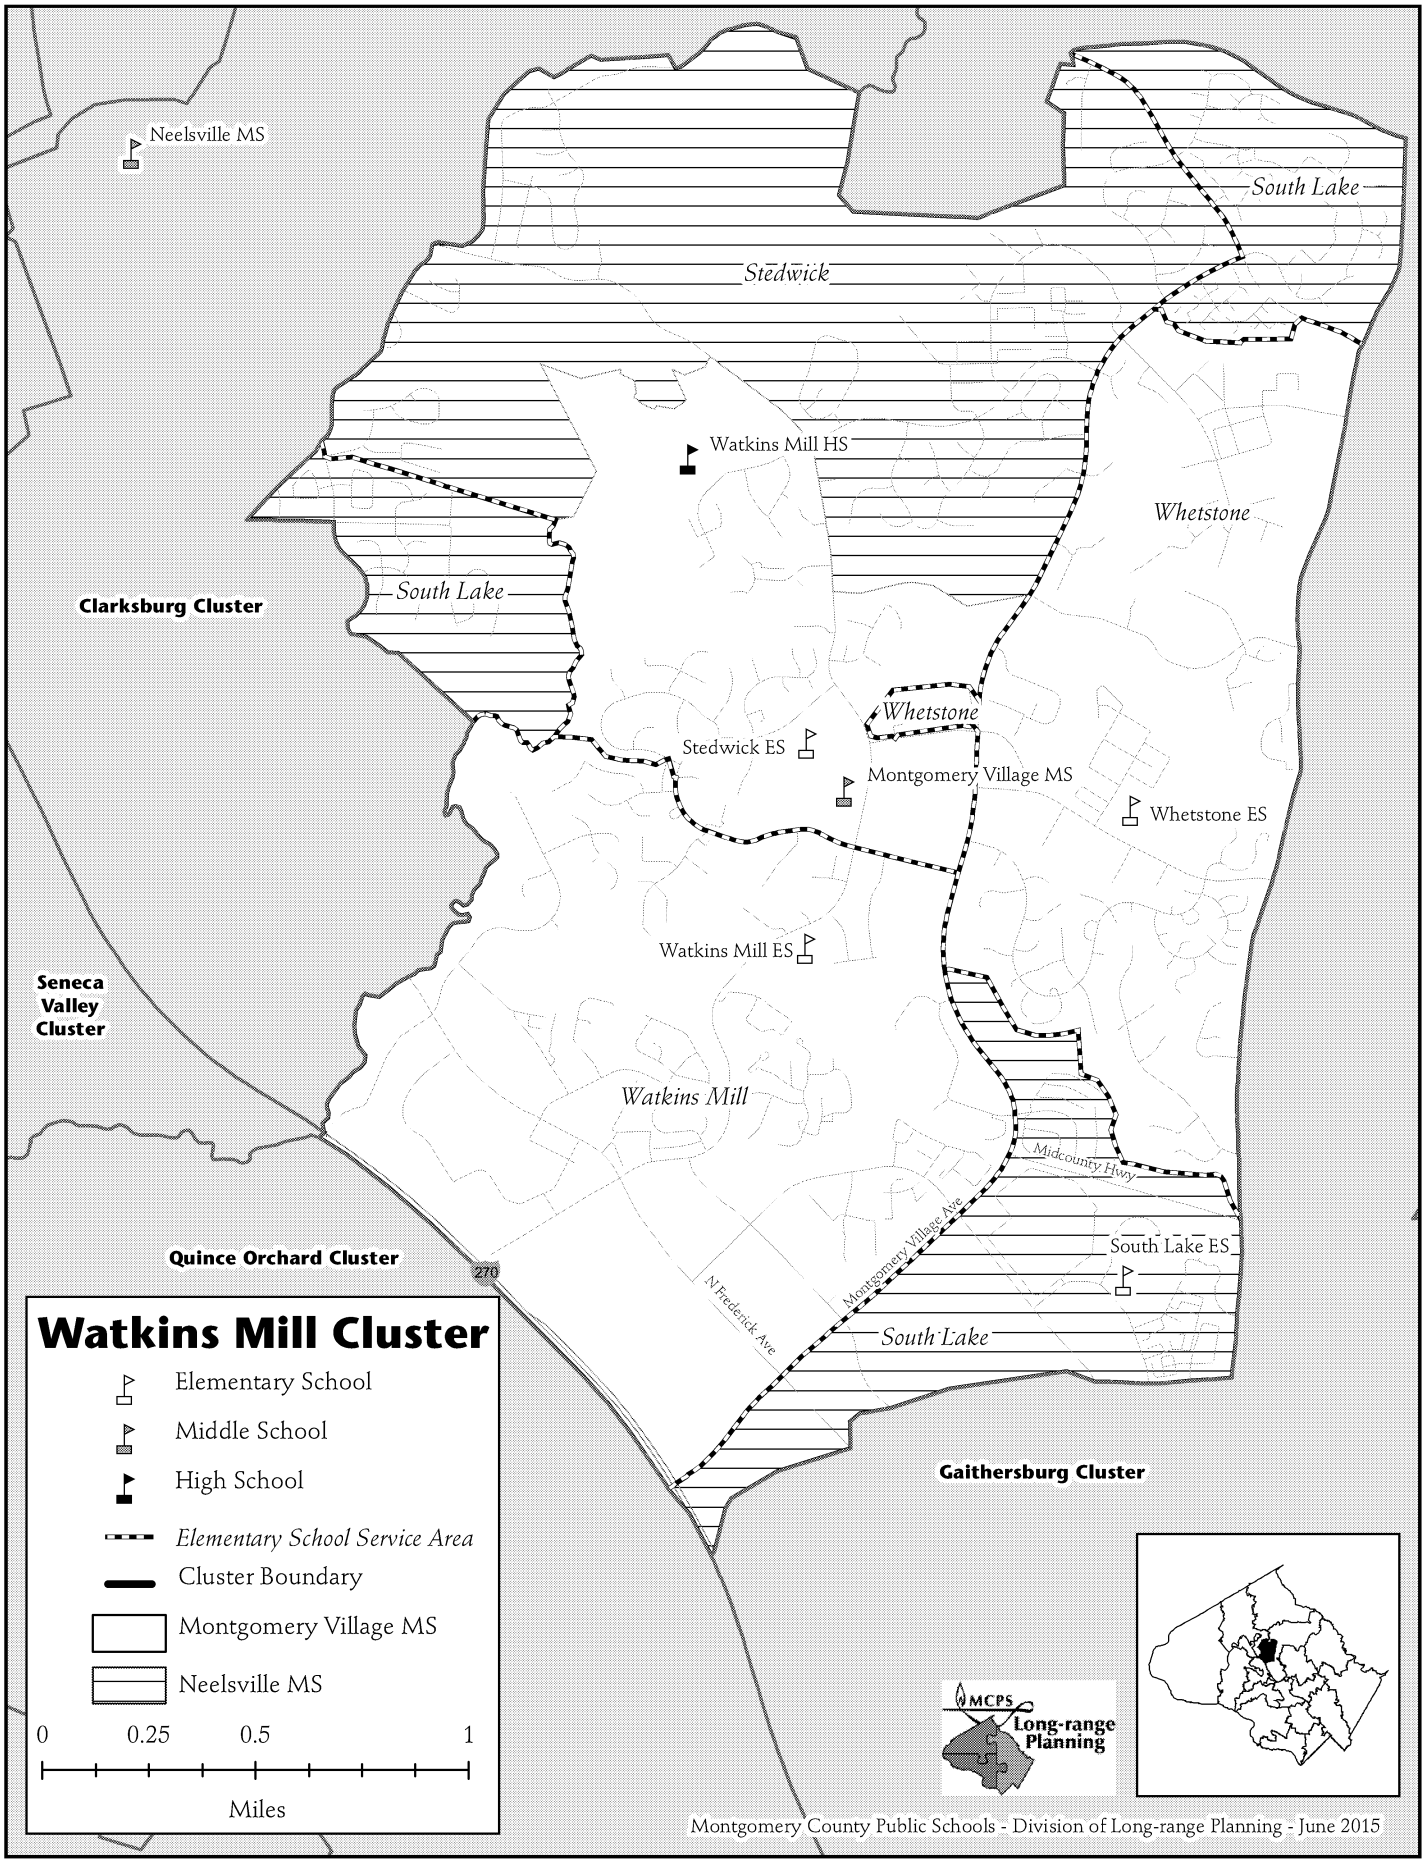
Neelsville MS
South Lake
Stedwick
Watkins Mill HS
Whetstone
Clarksburg Cluster
South Lake
Whetstone
Stedwick ES
Montgomery Village MS
Whetstone ES
Watkins Mill ES
Seneca Valley Cluster
Watkins Mill
Midcounty Hwy
Montgomery Village Ave
South Lake ES
Quince Orchard Cluster
270
N Frederick Ave
South Lake
Gaithersburg Cluster
Watkins Mill Cluster
Elementary School
Middle School
High School
Elementary School Service Area
Cluster Boundary
Montgomery Village MS
Neelsville MS
0
0.25
0.5
1
Miles
MCPS
Long-range Planning
Montgomery County Public Schools - Division of Long-range Planning - June 2015

SCHOOLS

Montgomery Village Middle School

Planning Study: A boundary study was conducted in spring 2015 to review the service area for Clarksburg/Damascus Middle School. Representatives from Montgomery Village, Neelsville, and Rocky Hill middle schools participated on the Boundary Advisory Committee. The interim superintendent will make a recommendation in October 2015 for Board of Education action in November 2015.

Neelsville Middle School

Capital Project: Projections indicate enrollment at Neelsville Middle School will exceed capacity by 150 seats or more by the end of the six-year period. An FY 2015 appropriation was approved for facility planning to determine the feasibility, scope, and cost for a classroom addition. The need for the addition will determined after the outcome of the boundary study for the Clarksburg/Damascus Middle School. If enrollment continues to exceed capacity by 150 seats or more after the boundaries are set for the new school, a date for the addition will be considered in a future CIP. Relocatable classrooms will be utilized until additional capacity can be added.

Planning Study: A boundary study is approved to determine the service area for Clarksburg/Damascus Middle School. Representatives from Montgomery Village, Neelsville, and Rocky Hill middle schools will participate in the boundary advisory study. The boundary advisory study will take place in spring 2015 with Board of Education action in November 2015.

South Lake Elementary School

Capital Project: Projections indicate enrollment at South Lake Elementary School will exceed capacity by 92 seats or more by the end of the six-year CIP period. An FY 2014 appropriation was approved for facility planning to determine the feasibility, scope, and cost for a classroom addition. A date for the addition will be considered in a future CIP. Relocatable classrooms will be utilized until additional capacity can be added. A school-based health center will be included in the feasibility study. Funding for the school-based health center will be included in the Department of Health and Human Services capital budget.

CAPITAL PROJECTS

School	Project	Project Status*	Date of Completion
Neelsville MS	Classroom addition	Proposed	TBD
South Lake ES	Classroom addition	Proposed	TBD
	SBHC	Proposed	TBD


"Approved"— Project has an FY 2015 or FY 2016 appropriation approved in the FY 2015–2020 CIP.

"Deferred"—Funds have been deferred for a future CIP.

"Programmed"—Project has expenditures programmed in a future year of the CIP for planning and/or construction funds.

"Proposed"—Project has facility planning funds approved for FY 2015 or approved for FY 2016 for a feasibility study.

Watkins Mill Cluster Articulation*




* "Cluster" is defined as the collection of elementary schools that articulate to the same high school.

* Capt. James Daly Elementary School and Fox Chapel Elementary School also articulate to Neelsville Middle School but thereafter to Clarksburg High School.

** A portion of Stedwick Elementary School articulates to Montgomery Village Middle School, and another portion articulates to Neelsville Middle School.

Watkins Mill Cluster

School Utilizations

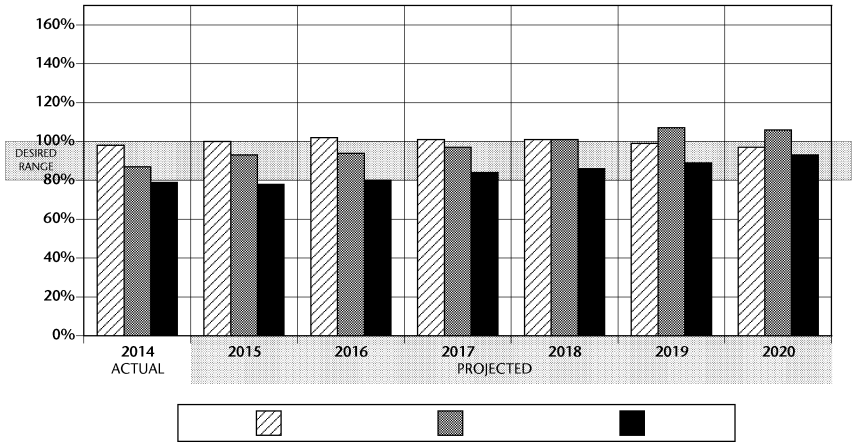

Note: Percent utilization calculated as total enrollment of schools divided by total capacity. Projected capacity factors in capital projects.

Projected Enrollment and Space Availability

Effects of the Amended FY2015–2020 CIP and Non–CIP Actions on Space Available

Schools			Actual 14–15	Projections 15–16	16–17	17–18	18–19	19–20	20–21	2024	2029
Watkins Mill HS		Program Capacity	1906	1906	1906	1906	1906	1906	1906	1906	1906
		Enrollment	**1499**	**1488**	**1516**	**1598**	**1632**	**1700**	**1779**	**1900**	**1800**
		Available Space	*407*	*418*	*390*	*308*	*274*	*206*	*127*	*6*	*106*
		Comments									
Montgomery Village MS		Program Capacity	894	878	878	878	878	878	878	878	878
		Enrollment	**658**	**715**	**720**	**748**	**762**	**786**	**782**	**850**	**800**
		Available Space	*236*	*163*	*158*	*130*	*116*	*92*	*96*	*28*	*78*
		Comments	Boundary Study	+1 AUT							
Neelsville MS		Program Capacity	922	922	922	922	922	922	922	922	922
		Enrollment	**914**	**953**	**977**	**997**	**1060**	**1132**	**1128**	**1200**	**1100**
		Available Space	*8*	*(31)*	*(55)*	*(75)*	*(138)*	*(210)*	*(206)*	*(278)*	*(178)*
		Comments	Fac. Plng. Bound. Study See text								
South Lake ES	CSR	Program Capacity	716	716	716	716	716	716	716		
		Enrollment	**862**	**874**	**898**	**903**	**884**	**855**	**845**		
		Available Space	*(146)*	*(158)*	*(182)*	*(187)*	*(168)*	*(139)*	*(129)*		
		Comments	Facility Planning for Additior								
Stedwick ES	CSR	Program Capacity	639	639	639	639	639	639	639		
		Enrollment	**573**	**576**	**601**	**597**	**606**	**593**	**591**		
		Available Space	*66*	*63*	*38*	*42*	*33*	*46*	*48*		
		Comments									
Watkins Mill ES	CSR	Program Capacity	*746*	733	733	733	733	733	733		
		Enrollment	**635**	**656**	**652**	**640**	**637**	**640**	**630**		
		Available Space	*111*	*77*	*81*	*93*	*96*	*93*	*103*		
		Comments		+1 ELC							
Whetstone ES	CSR	Program Capacity	783	783	783	783	783	783	783		
		Enrollment	**758**	**768**	**778**	**769**	**760**	**743**	**733**		
		Available Space	*25*	*15*	*5*	*14*	*23*	*40*	*50*		
		Comments									
Cluster Information		HS Utilization	79%	78%	80%	84%	86%	89%	93%	100%	94%
		HS Enrollment	1499	1488	1516	1598	1632	1700	1779	1900	1800
		MS Utilization	87%	93%	94%	97%	101%	107%	106%	114%	106%
		MS Enrollment	1572	1668	1697	1745	1822	1918	1910	2050	1900
		ES Utilization	98%	100%	102%	101%	101%	99%	97%	101%	101%
		ES Enrollment	2828	2874	2929	2909	2887	2831	2799	2900	2900

Demographic Characteristics of Schools

Schools	2014–2015 Total Enrollment	Two or more races %	Black or Afr. Amer. %	Asian%	Hispanic %	White %	2014–2015 FARMS%*	ESOL%**	2013–2014 Mobility Rate%***
Watkins Mill HS	1499	≤ 5.0%	34.7%	9.7%	40.4%	10.9%	52.9%	13.5%	16.3%
Montgomery Village MS	658	≤ 5.0%	32.1%	9.6%	45.7%	8.5%	62.3%	14.3%	18.1%
Neelsville MS	914	≤ 5.0%	34.6%	7.9%	44.6%	8.5%	64.0%	16.7%	16.7%
South Lake ES	862	≤ 5.0%	26.2%	8.2%	59.7%	≤ 5.0%	81.9%	49.2%	25.2%
Stedwick ES	573	5.6%	35.1%	7.3%	35.8%	15.5%	56.2%	32.3%	23.6%
Watkins Mill ES	635	≤ 5.0%	35.0%	10.4%	45.8%	≤ 5.0%	71.0%	41.6%	27.3%
Whetstone ES	758	≤ 5.0%	26.4%	7.7%	50.7%	11.1%	64.5%	38.4%	17.2%
Elementary Cluster Total	**2828**	**≤ 5.0%**	**30.0%**	**8.4%**	**49.3%**	**8.2%**	**70.4%**	**41.7%**	**23.2%**
Elementary County Total	75,144	≤ 5.0%	21.2%	13.9%	30.4%	29.3%	40.2%	23.3%	13.3%

**Percent of students approved for Free and Reduced-priced Meals Program (FARMS) during the 2014–2015 school year.*

***Percent of English for Speakers of Other Languages (ESOL) during the 2014–2015 school year. High School students are served in regional ESOL centers.*

****Mobility Rate is the number of entries plus withdrawals during the 2013–2014 school year compared to total enrollment.*
Notes: Native Hawaiian/Pacific Islander and American Indian/Alaskan Native categories total less than 1% and were therefore excluded from the table.

Due to federal and state guidelines, demographic characteristics of schools of less than or equal to 5.0% are reported as ≤ 5.0%.


Program Capacity Table

(School Year 2014–2015)

Schools	Grades Served	Capacity (HS @90% MS@85%)	Total Rooms	Support Rooms	Regular Secondary @25	Regular Elementary @23	CSR Grades 1–2 @18	Pre–K @20	Pre–K @40	HS @20	CSR KIND @18	KIND @22	ESOL @15	METS @15	Special Education Services: School Based: HSM @13	School Based: ELEM LAD @13	Quad Cluster Based: ELC @10	Quad Cluster Based: LANG @12	Quad Cluster Based: LFI @10	Quad Cluster Based: SCB @6	County & Regional Based: AAC@7	AUT @6	BRIDGE @10	DHOH @7	ED @10	EXTENSIONS @6	GT/LD @13	PD @7	PEP@6	PEP @12	PEP @18	VISION (Elementary) @7	OTHER
Watkins Mill HS	9-12	1906	90		80								4	1					3								1						1
Montgomery Village MS	6-8	894	46		39								2	1					2			2											
Neelsville MS	6-8	922	45		41								3	1																			
South Lake ES	HS-5	716	39	5		16	10		1	1	6																						
Stedwick ES	PreK-5	639	39	6		13	10		1		5								3														1
Watkins Mill ES	HS-5	746	42	4		18	9	1		1	5						4																
Whetstone ES	PreK-5	783	43	4		15	12		1		6					2														1	2		

Facility Characteristics of Schools 2014–2015

Schools	Year Facility Opened	Year Reopened/ Revitalized	Total Square Footage	Site Size Acres	Adjacent Park	Reloc-atable Classrooms	Linkages to Learning Program	Home School Model
Watkins Mill HS	1989		305,288	50.99	Yes			
Montgomery Village MS	1968	2003	141,615	15.1				
Neelsville MS	1981		131,432	29.2				
South Lake ES	1972		83,038	10.2		3		
Stedwick ES	1974		109,677	10				
Watkins Mill ES	1970		80,923	10	Yes			
Whetstone ES	1968		96,946	8.8	Yes			

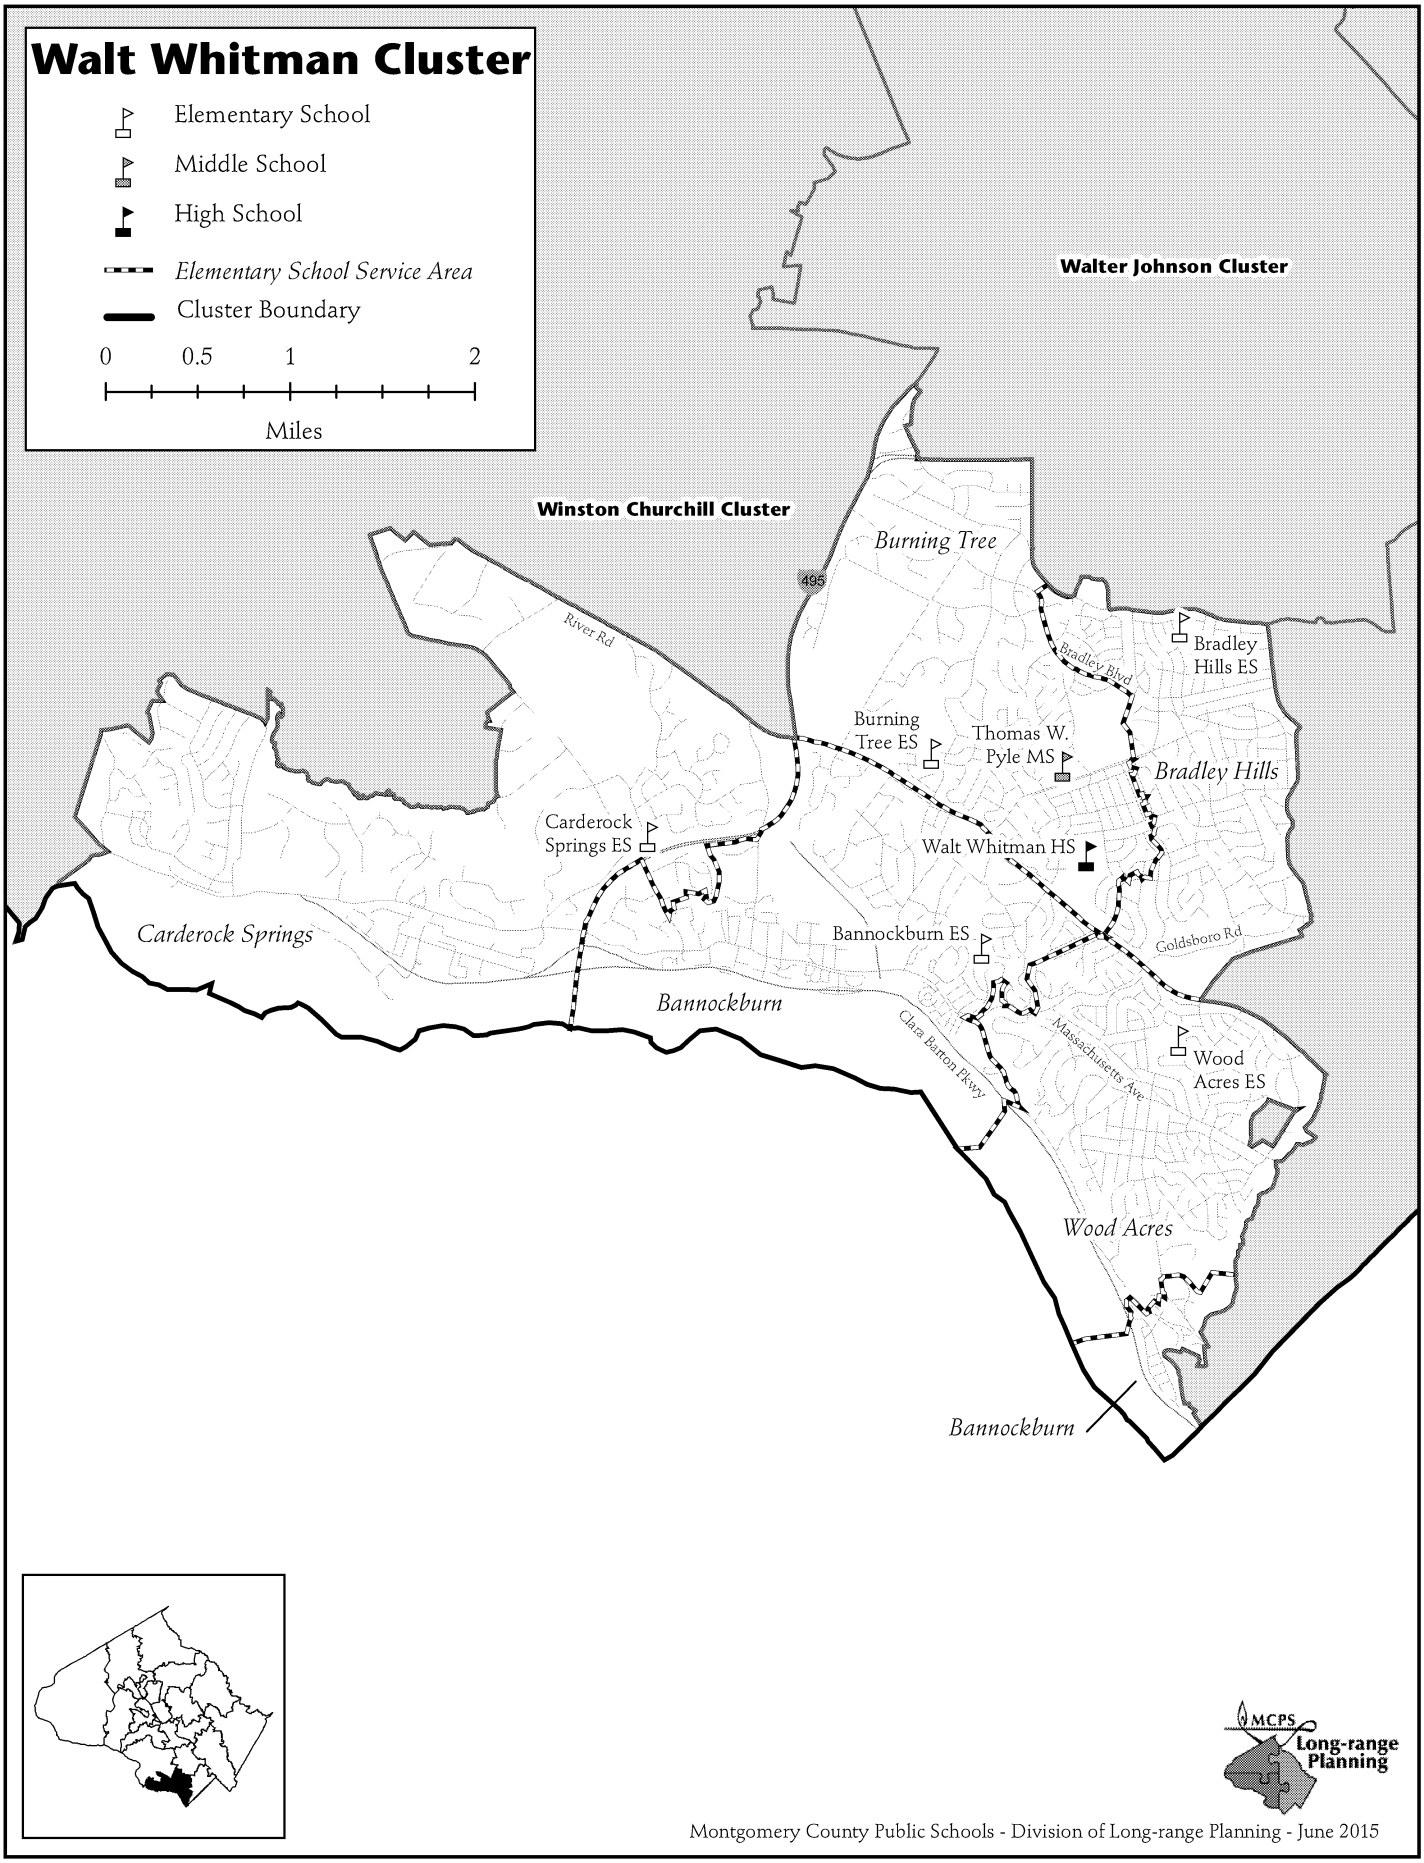

Montgomery County Public Schools - Division of Long-range Planning - June 2015

SCHOOLS

Walt Whitman High School

Capital Project: Projections indicate enrollment at Walt Whitman High School will exceed capacity by more 200 seats or more by the end of the six-year CIP period. An FY 2014 appropriation was approved for facility planning funds for a feasibility study to determine the feasibility, cost, and scope of an addition. A date for the addition will be considered in a future CIP. Relocatable classrooms will be utilized until additional capacity can be added.

Thomas W. Pyle Middle School

Capital Project: Projections for Thomas W. Pyle Middle School indicate that enrollment will exceed capacity by 150 seats or more throughout the six-year CIP planning period. An FY 2015 appropriation was approved in the Building Modifications and Program Improvements project for planning and construction of a third auxiliary gymnasium at the school to accommodate the high enrollment and meet the physical education facility requirements for middle schools. However, due to recent changes in the middle school physical education space requirements that add a second gymnasium to the program, the overutilization at the school, and the need for additional cafeteria space to accommodate the student enrollment, an FY 2016 appropriation is approved for a feasibility study to determine the feasibility, scope, and cost of an addition and core improvements to the school. The core improvements will include the physical education and cafeteria spaces. A date for the addition will be considered in a future CIP. Relocatable classrooms will be utilized, if needed, until additional capacity can be added.

Burning Tree Elementary School

Capital Project: Previous projections indicated enrollment at Burning Tree Elementary School would exceed capacity by 92 seats or more by the end of the six-year CIP period. Therefore, an FY 2014 appropriation was approved for facility planning to determine the feasibility, scope, and cost for a classroom addition. A date for the addition will be considered in a future CIP. Relocatable classrooms will be utilized until additional capacity can be added.

Wood Acres Elementary School

Capital Project: Projections indicate enrollment at Wood Acres Elementary School will exceed capacity by 92 seats or more by the end of the six-year CIP planning period. An FY 2015 appropriation was approved to begin the construction of the classroom addition. The school is located at the Radnor Holding Facility during construction. The scheduled completion date for the addition is August 2016.

CAPITAL PROJECTS


School	Project	Project Status*	Date of Completion
Walt Whitman HS	Classroom addition	Proposed	TBD
Thomas W. Pyle MS	Classroom addition/core improvements	Proposed	TBD
Burning Tree ES	Classroom addition	Proposed	TBD
Wood Acres ES	Classroom addition	Approved	Aug. 2016

"Approved"— Project has an FY 2015 or FY 2016 appropriation approved in the FY 2015–2020 CIP.

"Deferred"—Funds have been deferred for a future CIP.

"Programmed"—Project has expenditures programmed in a future year of the CIP for planning and/or construction funds.

"Proposed"—Project has facility planning funds approved for FY 2015 or approved for FY 2016 for a feasibility study.

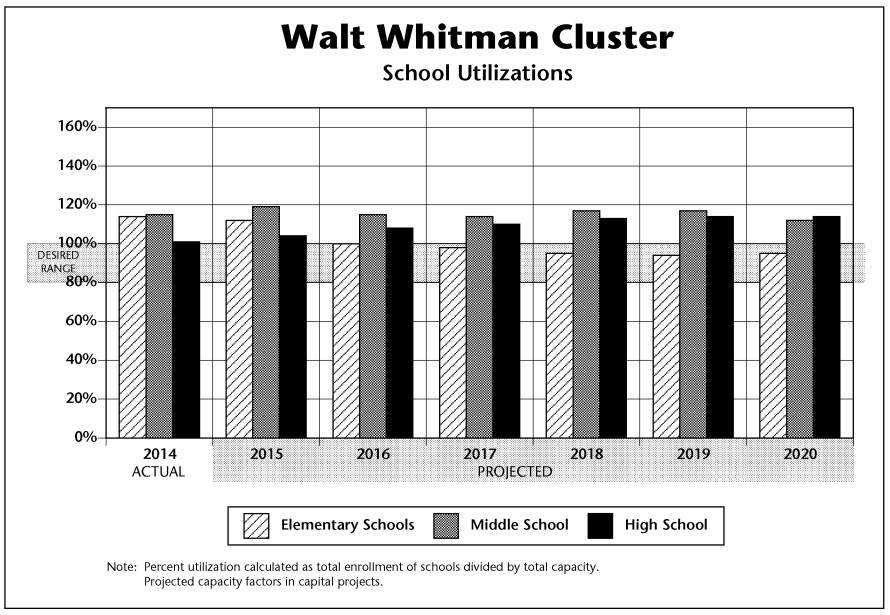

Projected Enrollment and Space Availability

Effects of the Amended FY2015–2020 CIP and Non–CIP Actions on Space Available

Schools			Actual 14–15	Projections 15–16	16–17	17–18	18–19	19–20	20–21	2024	2029
Walt Whitman HS		Program Capacity	1891	1891	1891	1891	1891	1891	1891	1891	1891
		Enrollment	**1912**	**1969**	**2034**	**2073**	**2142**	**2148**	**2155**	**2300**	**2200**
		Available Space	*(21)*	*(78)*	*(143)*	*(182)*	*(251)*	*(257)*	*(264)*	*(409)*	*(309)*
		Comments	Facility Planning for Addition								
Thomas W. Pyle MS		Program Capacity	1289	1289	1289	1289	1289	1289	1289	1289	1289
		Enrollment	**1483**	**1532**	**1478**	**1470**	**1502**	**1509**	**1443**	**1500**	**1400**
		Available Space	*(194)*	*(243)*	*(189)*	*(181)*	*(213)*	*(220)*	*(154)*	*(211)*	*(111)*
		Comments		Facility Planning for Addition							
Bannockburn ES		Program Capacity	365	365	365	365	365	365	365		
		Enrollment	**407**	**408**	**398**	**395**	**384**	**376**	**373**		
		Available Space	*(42)*	*(43)*	*(33)*	*(30)*	*(19)*	*(11)*	*(8)*		
		Comments									
Bradley Hills ES		Program Capacity	663	663	663	663	663	663	663		
		Enrollment	**632**	**643**	**616**	**615**	**587**	**569**	**565**		
		Available Space	*31*	*20*	*47*	*48*	*76*	*94*	*98*		
		Comments									
Burning Tree ES		Program Capacity	379	379	379	379	379	379	379		
		Enrollment	**492**	**480**	**469**	**447**	**437**	**428**	**432**		
		Available Space	*(113)*	*(101)*	*(90)*	*(68)*	*(58)*	*(49)*	*(53)*		
		Comments	Facility Planning for Addition								
Carderock Springs ES		Program Capacity	407	407	407	407	407	407	407		
		Enrollment	**418**	**395**	**388**	**376**	**361**	**356**	**364**		
		Available Space	*(11)*	*12*	*19*	*31*	*46*	*51*	*43*		
		Comments									
Wood Acres ES		Program Capacity	527	527	757	757	757	757	757		
		Enrollment	**718**	**696**	**693**	**691**	**678**	**683**	**705**		
		Available Space	*(191)*	*(169)*	*64*	*66*	*79*	*74*	*52*		
		Comments	Move to Radnor	@ Radnor	Addition Complete						
Cluster Information		HS Utilization	101%	104%	108%	110%	113%	114%	114%	122%	116%
		HS Enrollment	1912	1969	2034	2073	2142	2148	2155	2300	2200
		MS Utilization	115%	119%	115%	114%	117%	117%	112%	116%	109%
		MS Enrollment	1483	1532	1478	1470	1502	1509	1443	1500	1400
		ES Utilization	114%	112%	100%	98%	95%	94%	95%	97%	97%
		ES Enrollment	2667	2622	2564	2524	2447	2412	2439	2500	2500

Demographic Characteristics of Schools

Schools	2014–2015 Total Enrollment	Two or more races %	Black or Afr. Amer. %	Asian%	Hispanic %	White %	2014–2015 FARMS%*	ESOL%**	2013–2014 Mobility Rate%***
Walt Whitman HS	1912	5.6%	≤ 5.0%	12.3%	9.0%	69.2%	≤ 5.0%	≤ 5.0%	6.1%
Thomas W. Pyle MS	1483	5.5%	≤ 5.0%	11.8%	7.8%	72.8%	≤ 5.0%	≤ 5.0%	≤ 5.0%
Bannockburn ES	407	9.6%	≤ 5.0%	11.3%	9.1%	66.8%	≤ 5.0%	9.8%	5.8%
Bradley Hills ES	632	10.9%	≤ 5.0%	10.3%	9.5%	67.6%	≤ 5.0%	5.9%	5.8%
Burning Tree ES	492	7.5%	≤ 5.0%	19.7%	6.3%	62.4%	≤ 5.0%	10.8%	6.6%
Carderock Springs ES	418	≤ 5.0%	≤ 5.0%	16.3%	8.1%	67.5%	≤ 5.0%	5.3%	5.4%
Wood Acres ES	718	6.1%	≤ 5.0%	11.7%	9.7%	69.2%	≤ 5.0%	5.3%	5.9%
Elementary Cluster Total	**2667**	**7.8%**	**≤ 5.0%**	**13.5%**	**8.7%**	**66.9%**	**≤ 5.0%**	**7.0%**	**5.9%**
Elementary County Total	75,144	≤ 5.0%	21.2%	13.9%	30.4%	29.3%	40.2%	23.3%	13.3%

**Percent of students approved for Free and Reduced-priced Meals Program (FARMS) during the 2014–2015 school year.*

***Percent of English for Speakers of Other Languages (ESOL) during the 2014–2015 school year. High School students are served in regional ESOL centers.*

****Mobility Rate is the number of entries plus withdrawals during the 2013–2014 school year compared to total enrollment.*
Notes: Native Hawaiian/Pacific Islander and American Indian/Alaskan Native categories total less than 1% and were therefore excluded from the table.

Due to federal and state guidelines, demographic characteristics of schools of less than or equal to 5.0% are reported as ≤ 5.0%.


Program Capacity Table

(School Year 2014–2015)

Schools	Grades Served	Capacity (HS @90% MS@85%)	Total Rooms	Support Rooms	Regular Secondary @25	Regular Elementary @23	CSR Grades 1–2 @18	Pre–K @20	Pre–K @40	HS @20	CSR KIND @18	KIND @22	ESOL @15	METS @15	Special Education Services: School Based: HSM @13	Cluster Based: ELEM LAD @13	Quad Cluster Based: ELC @10	LANG @12	LFI @10	SCB @6	County & Regional Based: AAC@7	AUT @6	BRIDGE @10	DHOH @7	ED @10	EXTENSIONS @6	GT/LD @13	PD @7	PEP@6	PEP @12	PEP @18	VISION (Elementary) @7	OTHER
Walt Whitman HS	9-12	1891	88		81								2						2	1					2							
Thomas W. Pyle MS	6-8	1289	63		59								1								1				2							
Bannockburn ES	K-5	365	20	4		13						3																				
Bradley Hills ES	K-5	663	33	4		25						4																				
Burning Tree ES	K-5	379	24	4		11						3					6															
Carderock Springs ES	K-5	407	24	4		15						2										3										
Wood Acres ES	K-5	527	28	4		17						5				2																

Facility Characteristics of Schools 2014–2015

Schools	Year Facility Opened	Year Reopened/ Revitalized	Total Square Footage	Site Size Acres	Adjacent Park	Reloc-atable Classrooms	Linkages to Learning Program	Home School Model
Walt Whitman HS	1962	1992	261,295	30.7	Yes			
Thomas W. Pyle MS	1962	1993	153,824	14.3				
Bannockburn ES	1957	1988	54,234	8.3		2		
Bradley Hills ES	1951	1984	76,745	6.7	Yes			
Burning Tree ES	1958	1991	68,119	6.8	Yes	4		
Carderock Springs ES	1966	2010	75,351	9				
Wood Acres ES	1952	2002	73,138	4.78	Yes	7		

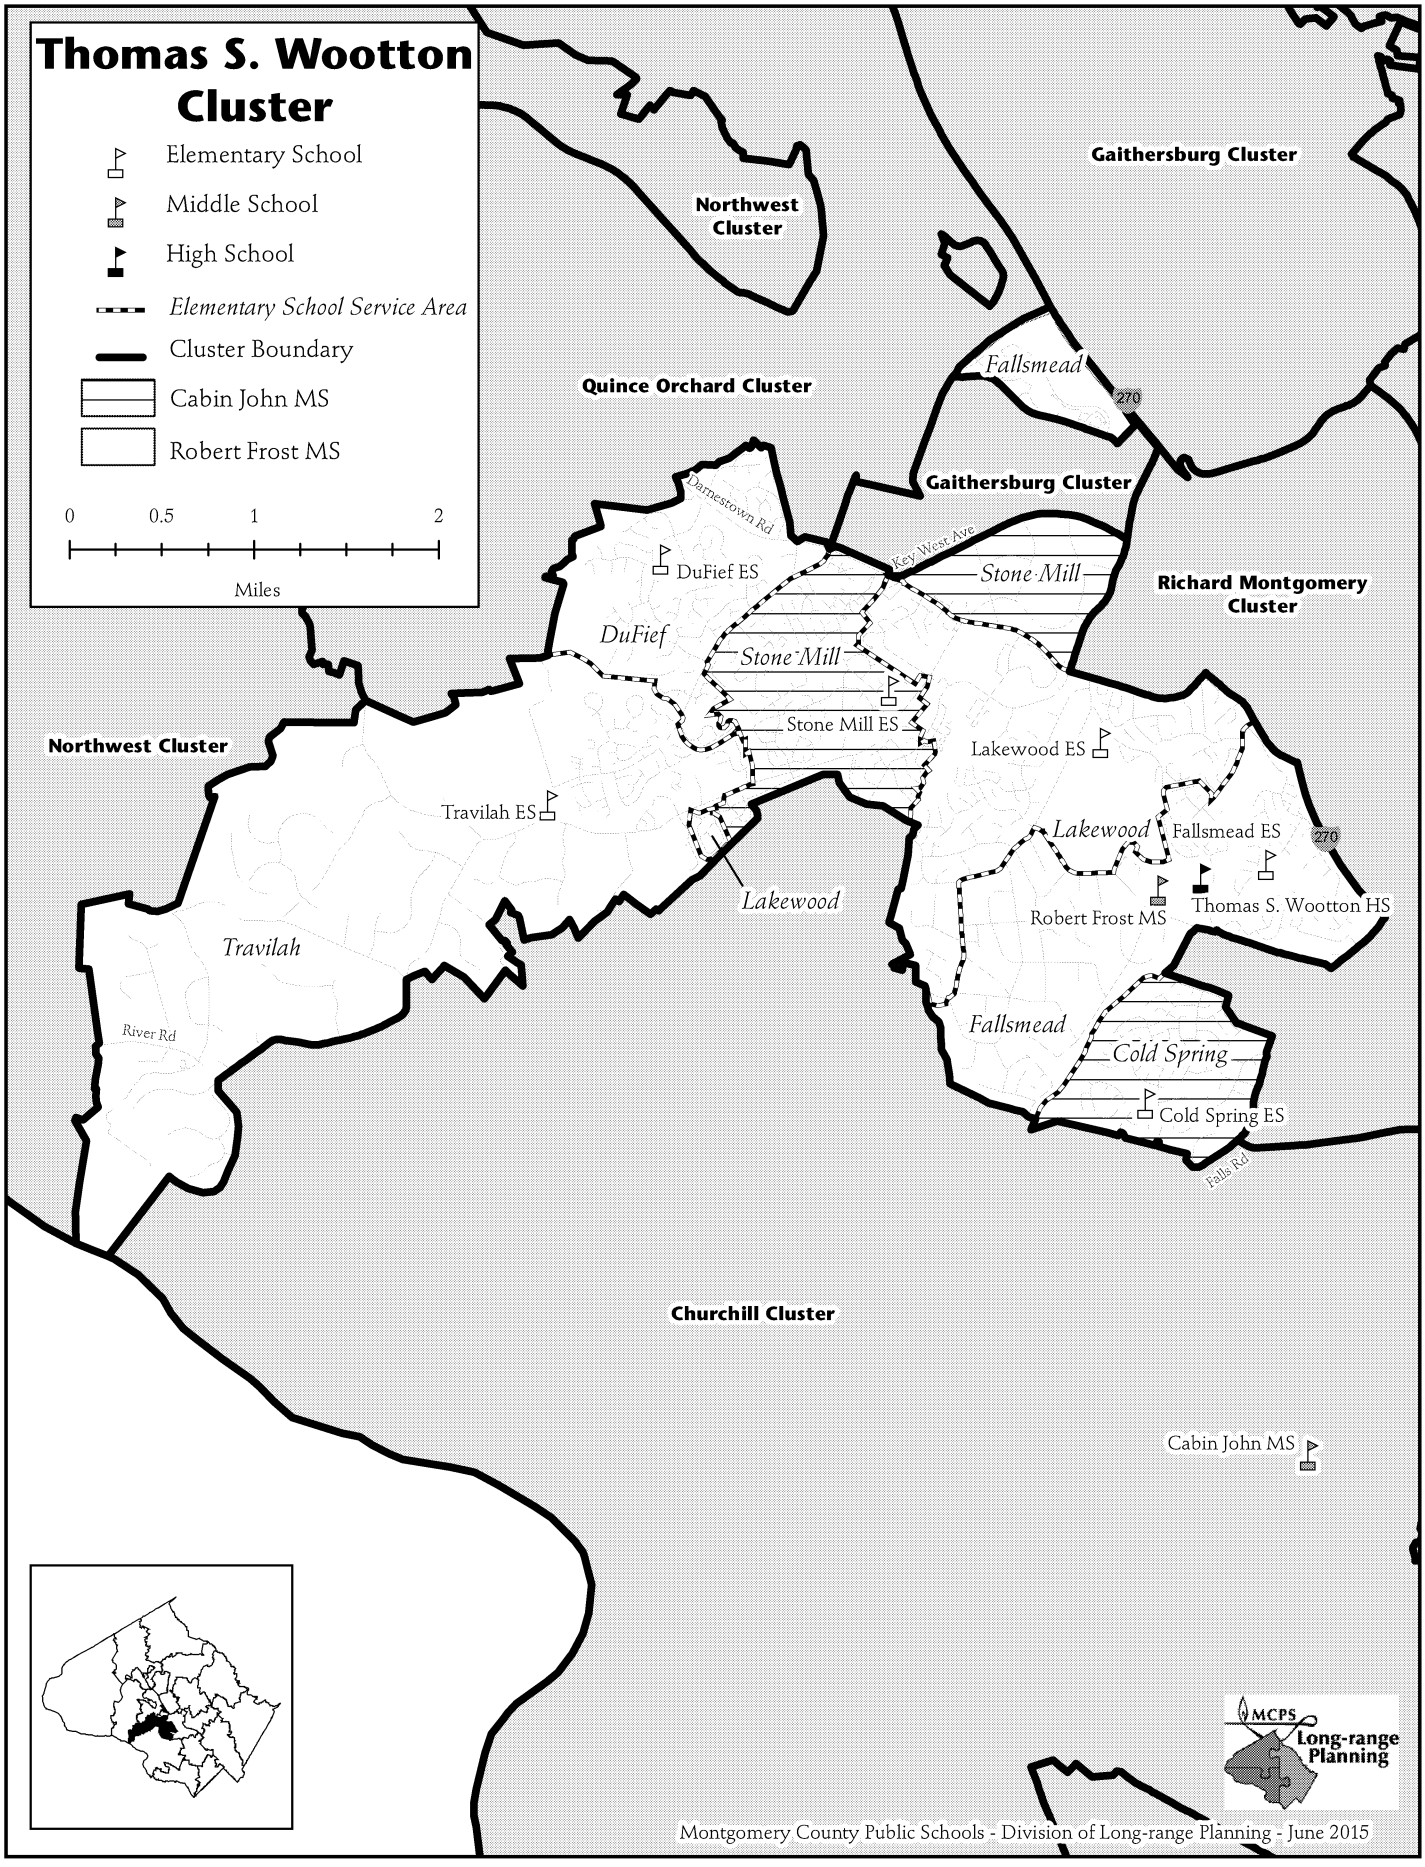
Thomas S. Wootton Cluster
Elementary School
Middle School
High School
Elementary School Service Area
Cluster Boundary
Cabin John MS
Robert Frost MS
0
0.5
1
2
Miles
Gaithersburg Cluster
Northwest Cluster
Quince Orchard Cluster
Fallsmead
270
Gaithersburg Cluster
Darnestown Rd
DuFief ES
Key West Ave
Stone Mill
Richard Montgomery Cluster
DuFief
Stone Mill
Stone Mill ES
Northwest Cluster
Lakewood ES
Travilah ES
Lakewood
Fallsmead ES
270
Lakewood
Robert Frost MS
Thomas S. Wootton HS
Travilah
River Rd
Fallsmead
Cold Spring
Cold Spring ES
Falls Rd
Churchill Cluster
Cabin John MS
MCPS
Long-range Planning
Montgomery County Public Schools - Division of Long-range Planning - June 2015

CLUSTER PLANNING ISSUES

Planning Issue: The 2010 adopted Great Seneca Science Corridor Master Plan provides for up to 5,750 residential units. Most of the residential development is in the Thomas S. Wootton Cluster. The majority of planned units require funding to be secured for construction of the Corridor Cities Transit Way. The pace of construction will be market driven. A future elementary school site is included in the plan.

SCHOOLS

Thomas S. Wootton High School

Capital Project: A revitalization/expansion project is scheduled for this school. Although the Board of Education requested a completion date of August 2020, the County Council maintained the approved FY 2015–2020 CIP completion date of August 2021. An FY 2015 appropriation was approved for facility planning funds to determine the scope and cost of the project. An FY 2016 appropriation is approved for planning funds to begin the architectural design for the revitalization/expansion project of this school. In order for this project to be completed on this schedule, county and state funding must be provided at levels approved in this CIP.

Cold Spring Elementary School

Capital Project: A revitalization/expansion project is scheduled for this school. Although the Board of Education requested a completion date of August 2020, the County Council maintained the approved FY 2015–2020 CIP completion date of August 2021. An FY 2015 appropriation was approved for facility planning for a feasibility study to determine the scope and cost of the project. In order for this project to be completed on this schedule, county and state funding must be provided at the levels approved in this CIP.

DuFief Elementary School

Capital Project: A revitalization/expansion project is scheduled for this school. Although the Board of Education requested a completion date of August 2020, the County Council maintained the approved FY 2015–2020 CIP completion date of August 2021. An FY 2015 appropriation was approved for facility planning for a feasibility study to determine the scope and cost of the project. In order for this project to be completed on this schedule, county and state funding must be provided at the levels approved in this CIP.

Planning Issue: Projections indicate that enrollment at Rachel Carson Elementary School will exceed capacity by 92 seats or more by the end of the six-year CIP period. To address the high enrollment at Rachel Carson Elementary School the Board of Education approved the following studies to explore additional capacity to address the overutilization at Rachel Carson Elementary School:

- The feasibility study that was conducted in 2007 for an addition at Jones Lane Elementary School to relieve Carson Elementary School be updated to determine if a larger addition could be constructed at Jones Lane Elementary School;
- The feasibility study that is planned for the revitalization/expansion project at DuFief Elementary School during the 2014–2015 school year include the possibility of additional capacity;
- The feasibility study that is planned for an addition at Fields Road Elementary School include the possibility of additional capacity; and
- The consideration of a new elementary school in the Quince Orchard Cluster be included in the analysis of options to relieve Rachel Carson Elementary School.

The interim superintendent will make a recommendation to address the overutilization of Rachel Carson Elementary School as part of the FY 2017–2022 CIP.

CAPITAL PROJECTS


School	Project	Project Status*	Date of Completion
Wootton HS	Revitalization/ expansion	Approved	Aug. 2021, building Aug. 2022, site
Cold Spring ES	Revitalization/ expansion	Approved	Aug. 2021
DuFief ES	Revitalization/ expansion	Approved	Aug. 2021

"Approved"— Project has an FY 2015 or FY 2016 appropriation approved in the FY 2015–2020 CIP.

"Deferred"—Funds have been deferred for a future CIP.

"Programmed"—Project has expenditures programmed in a future year of the CIP for planning and/or construction funds.

"Proposed"—Project has facility planning funds approved for FY 2015 or approved for FY 2016 for a feasibility study.

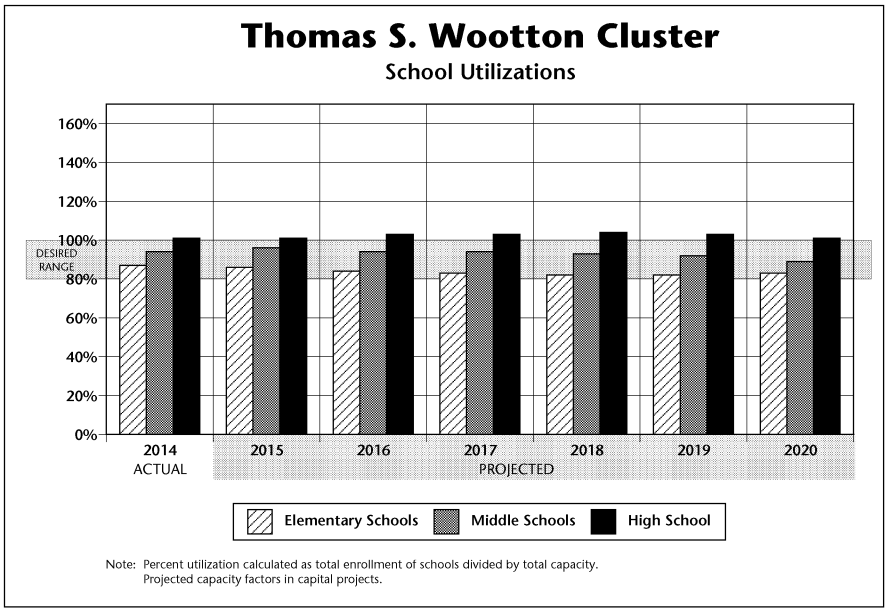

Projected Enrollment and Space Availability

Effects of the Amended FY2015–2020 CIP and Non–CIP Actions on Space Available

Schools			Actual 14–15	Projections 15–16	16–17	17–18	18–19	19–20	20–21	2024	2029
Thomas S. Wootton HS		Program Capacity	2184	2167	2167	2167	2167	2167	2167	2167	2167
		Enrollment	**2195**	**2194**	**2225**	**2238**	**2245**	**2230**	**2188**	**2300**	**2200**
		Available Space	*(11)*	*(27)*	*(58)*	*(71)*	*(78)*	*(63)*	*(21)*	*(133)*	*(33)*
		Comments	Facility Planning for Rev/Ex	+1 AUT	Planning for Revitalization/ Expansion			Revitalization/ Expansion in Progress			
Cabin John MS		Program Capacity	1129	1113	1113	1113	1113	1113	1113	1113	1113
		Enrollment	**943**	**954**	**965**	**996**	**1002**	**1032**	**1029**	**1100**	**1000**
		Available Space	*186*	*159*	*148*	*117*	*111*	*81*	*84*	*13*	*113*
		Comments		+1 AUT							
Robert Frost MS		Program Capacity	1075	1075	1075	1075	1075	1075	1075	1075	1075
		Enrollment	**1139**	**1137**	**1088**	**1069**	**1029**	**981**	**928**	**1000**	**900**
		Available Space	*(64)*	*(62)*	*(13)*	*6*	*46*	*94*	*147*	*75*	*175*
		Comments									
Cold Spring ES		Program Capacity	458	458	458	458	458	458	458		
		Enrollment	**335**	**335**	**324**	**324**	**331**	**332**	**340**		
		Available Space	*123*	*123*	*134*	*134*	*127*	*126*	*118*		
		Comments	Facility Planning for Rev/Ex		Planning for Revitalization/ Expansion			Move to Grosvenor Jan. 2020	@ Grosvenor		
DuFief ES		Program Capacity	428	428	428	428	428	428	428		
		Enrollment	**328**	**332**	**333**	**323**	**336**	**341**	**348**		
		Available Space	*100*	*96*	*95*	*105*	*92*	*87*	*80*		
		Comments	Facility Planning See text		Planning for Revitalization/ Expansion			Move to Emory Grove	@ Emory Grove		
Fallsmead ES		Program Capacity	598	598	598	598	598	598	598		
		Enrollment	**566**	**531**	**526**	**524**	**497**	**495**	**505**		
		Available Space	*32*	*67*	*72*	*74*	*101*	*103*	*93*		
		Comments									
Lakewood ES		Program Capacity	569	569	569	569	569	569	569		
		Enrollment	**549**	**526**	**501**	**483**	**474**	**470**	**475**		
		Available Space	*20*	*43*	*68*	*86*	*95*	*99*	*94*		
		Comments									
Stone Mill ES		Program Capacity	654	654	654	654	654	654	654		
		Enrollment	**619**	**632**	**627**	**620**	**609**	**607**	**606**		
		Available Space	*35*	*22*	*27*	*34*	*45*	*47*	*48*		
		Comments									
Travilah ES		Program Capacity	517	517	517	517	517	517	517		
		Enrollment	**413**	**409**	**394**	**400**	**397**	**405**	**412**		
		Available Space	*104*	*108*	*123*	*117*	*120*	*112*	*105*		
		Comments									
Cluster Information		HS Utilization	101%	101%	103%	103%	104%	103%	101%	106%	102%
		HS Enrollment	2195	2194	2225	2238	2245	2230	2188	2300	2200
		MS Utilization	94%	96%	94%	94%	93%	92%	89%	96%	87%
		MS Enrollment	2082	2091	2053	2065	2031	2013	1957	2100	1900
		ES Utilization	87%	86%	84%	83%	82%	82%	83%	87%	87%
		ES Enrollment	2810	2765	2705	2674	2644	2650	2686	2800	2800

Demographic Characteristics of Schools

Schools	2014–2015 Total Enrollment	Two or more races %	Black or Afr. Amer. %	Asian%	Hispanic %	White %	2014–2015 FARMS%*	ESOL%**	2013–2014 Mobility Rate%***
Thomas S. Wootton HS	2195	≤ 5.0%	6.8%	35.5%	7.7%	46.1%	5.1%	≤ 5.0%	≤ 5.0%
Cabin John MS	943	≤ 5.0%	10.7%	27.1%	9.1%	48.7%	8.7%	≤ 5.0%	≤ 5.0%
Robert Frost MS	1139	5.4%	≤ 5.0%	35.0%	6.4%	48.6%	5.4%	≤ 5.0%	5.4%
Cold Spring ES	335	6.9%	≤ 5.0%	39.7%	7.2%	43.3%	≤ 5.0%	≤ 5.0%	≤ 5.0%
DuFief ES	328	5.8%	6.1%	31.1%	12.5%	44.5%	14.9%	13.7%	11.4%
Fallsmead ES	566	≤ 5.0%	7.2%	33.7%	7.8%	46.6%	8.3%	10.4%	11.6%
Lakewood ES	549	5.5%	8.7%	45.2%	6.2%	34.2%	6.6%	10.0%	13.5%
Stone Mill ES	619	≤ 5.0%	11.5%	50.2%	5.8%	28.6%	9.0%	13.4%	8.2%
Travilah ES	413	5.6%	6.1%	43.8%	≤ 5.0%	39.7%	6.3%	9.7%	6.0%
Elementary Cluster Total	**2810**	**5.1%**	**7.7%**	**41.5%**	**7.0%**	**38.6%**	**7.6%**	**10.4%**	**9.3%**
Elementary County Total	75,144	≤ 5.0%	21.2%	13.9%	30.4%	29.3%	40.2%	23.3%	13.3%

**Percent of students approved for Free and Reduced-priced Meals Program (FARMS) during the 2014–2015 school year.*

***Percent of English for Speakers of Other Languages (ESOL) during the 2014–2015 school year. High School students are served in regional ESOL centers.*

****Mobility Rate is the number of entries plus withdrawals during the 2013–2014 school year compared to total enrollment.*

Notes: Native Hawaiian/Pacific Islander and American Indian/Alaskan Native categories total less than 1% and were therefore excluded from the table.

Due to federal and state guidelines, demographic characteristics of schools of less than or equal to 5.0% are reported as ≤ 5.0%.

Program Capacity Table


(School Year 2014–2015)

Schools	Grades Served	Capacity (HS @90% MS@85%)	Total Rooms	Support Rooms	Regular Secondary @25	Regular Elementary @23	CSR Grades 1–2 @18	Pre–K @20	Pre–K @40	HS @20	CSR KIND @18	KIND @22	ESOL @15	METS @15	Special Education Services: School Based: HSM @13	ELEM LAD @13	Cluster Based: ELC @10	LANG @12	LFI @10	SCB @6	Quad Cluster Based: AAC@7	AUT @6	BRIDGE @10	DHOH @7	ED @10	EXTENSIONS @6	GT/LD @13	PD @7	PEP@6	PEP @12	PEP @18	VISION (Elementary) @7	County & Regional Based: OTHER
Thomas S. Wootton HS	9-12	2184	99		96								1							2													
Cabin John MS	6-8	1129	57		51								1						2	1		2											
Robert Frost MS	6-8	1075	51		50								1																				
Cold Spring ES	K-5	458	24	4		18						2																					
DuFief ES	K-5	428	26	4		14						2					5	1															
Fallsmead ES	K-5	598	30	3		22						3				2																	
Lakewood ES	K-5	569	30	4		21						3							2														
Stone Mill ES	K-5	654	36	5		22						4																2	1	2			
Travilah ES	K-5	517	26	3		19						2																		2			

Facility Characteristics of Schools 2014–2015

Schools	Year Facility Opened	Year Reopened/ Revitalized	Total Square Footage	Site Size Acres	Adjacent Park	Reloc-atable Classrooms	Linkages to Learning Program	Home School Model
Thomas S. Wootton HS	1970		295,620	27.4		8		
Cabin John MS	1967	2011	159,514	18.2				
Robert Frost MS	1971		143,757	24.8				
Cold Spring ES	1972		55,158	12.4		1		
DuFief ES	1975		59,013	10	Yes	2		
Fallsmead ES	1974		67,472	9	Yes			
Lakewood ES	1968	2003	77,526	13.1				
Stone Mill ES	1988		78,617	11.8				
Travilah ES	1960	1992	65,378	9.3				

Special Education Centers

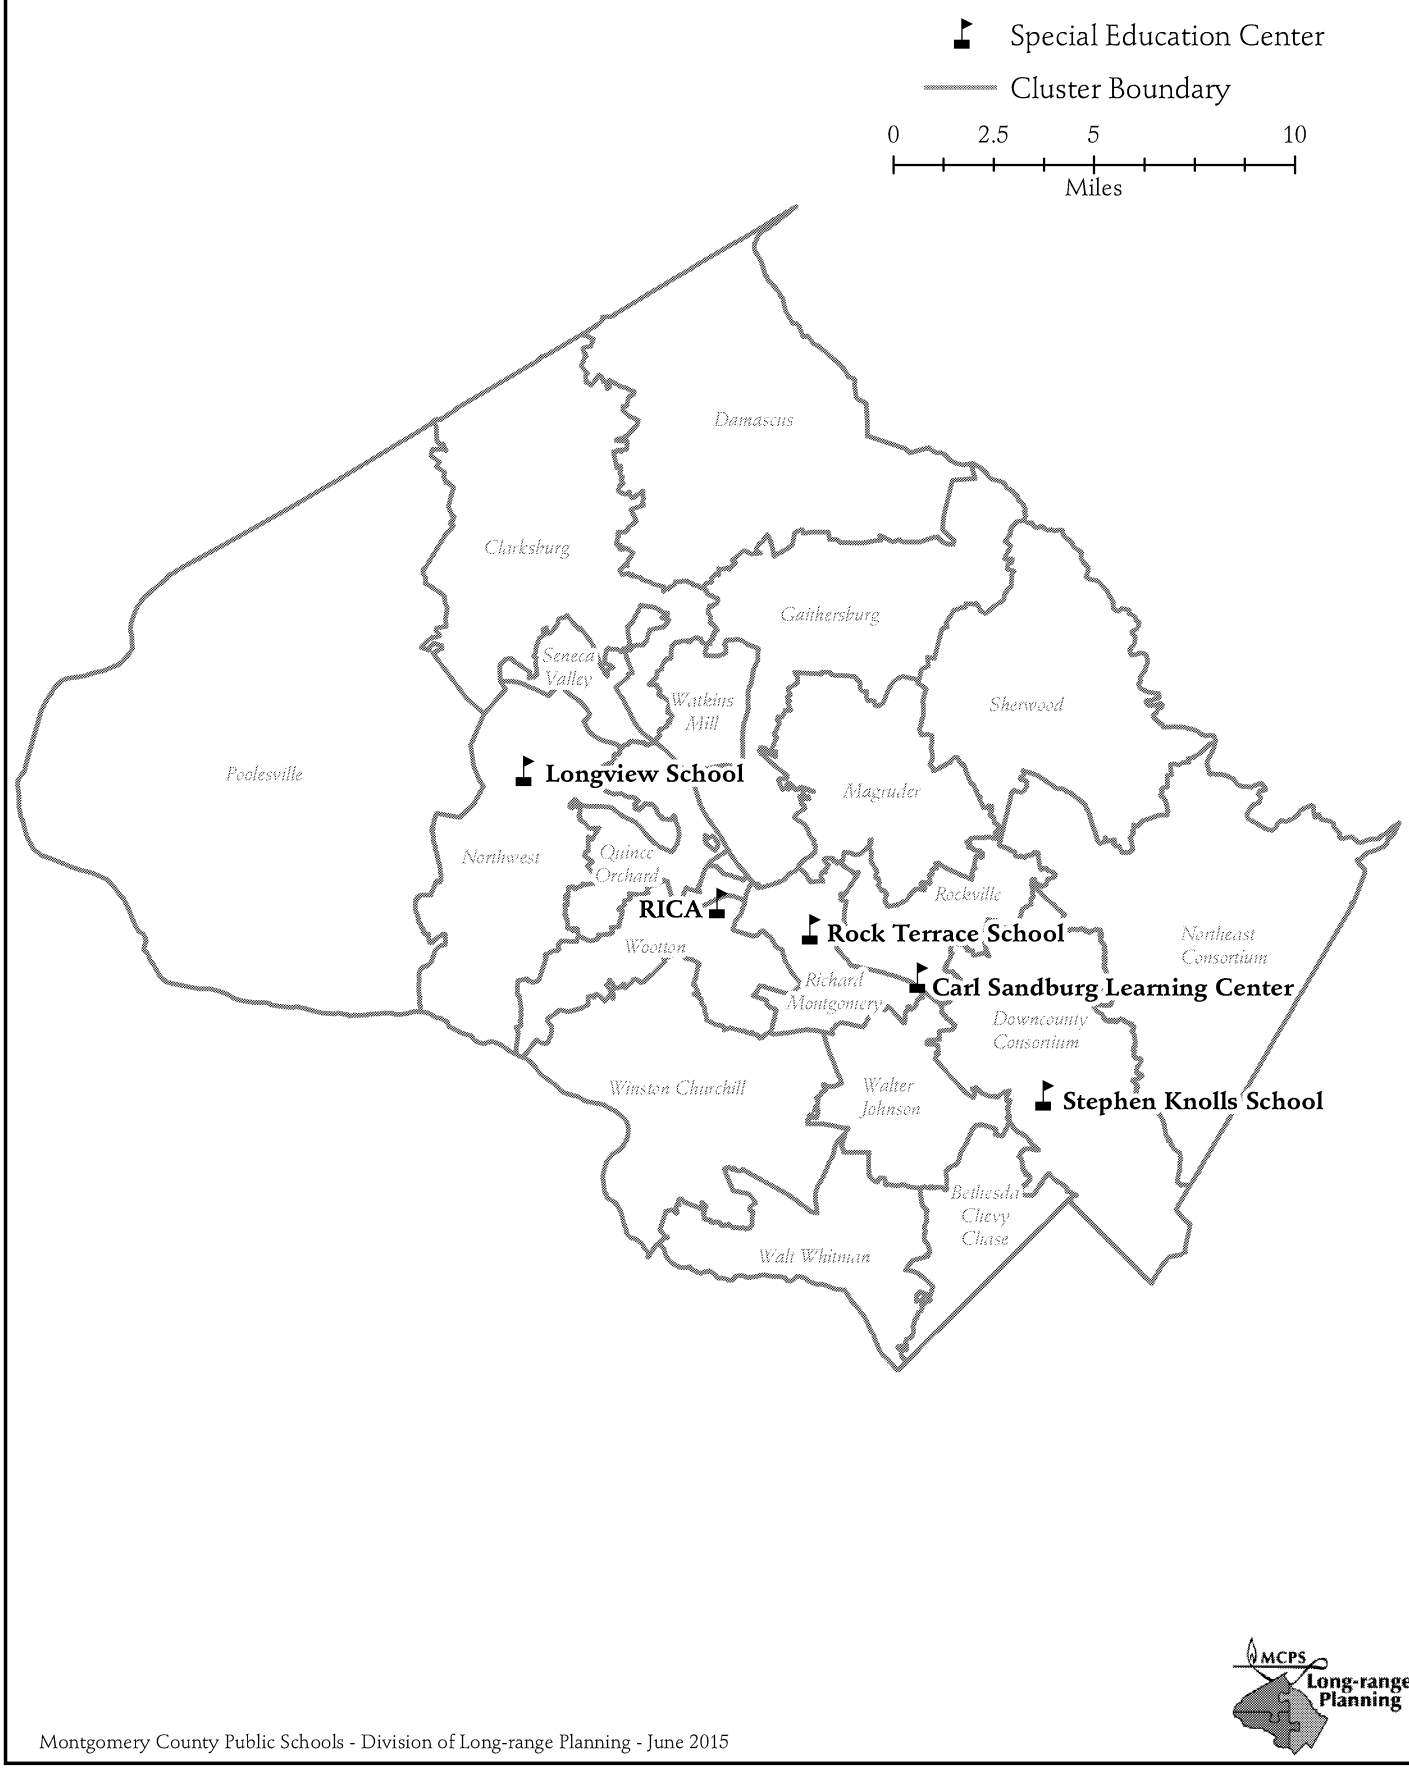

Montgomery County Public Schools - Division of Long-range Planning - June 2015

SPECIAL EDUCATION CENTERS

Longview School

Longview School provides services to students aged 5–21 with severe to profound intellectual disabilities and multiple disabilities. Alternative Academic Learning Outcomes aligned with Curriculum 2.0 are utilized to provide students with skills in the areas of communication, mobility, self-help, functional academics, and transition services. Longview School is collocated with Spark Matsunaga Elementary School in the Northwest Cluster.

John L. Gildner Regional institute for Children and Adolescents (RICA)

The John L. Gildner Regional Institute for Children and Adolescents (RICA), in collaboration with the Maryland State Department of Health and Mental Hygiene, provides appropriate educational and treatment services to students and their families through highly-structured intensive special education services with therapy integrated in a day and residential treatment facility. An interdisciplinary treatment team, comprised of school, clinical, residential, and related service providers, develops the student's total educational plan and monitors progress. Consulting psychiatrists, a full time pediatrician, and a school community health nurse also are on staff.

RICA offers fully accredited special education services which emphasize rigorous academic and vocational/occupational opportunities; day and residential treatment; and individual, group, and family therapy. The RICA program promotes acquisition of grade and age appropriate social and emotional skills and allows students to access the general education curriculum.

Rock Terrace School

Planning Study: On November 17, 2015, the Board of Education approved a Roundtable Discussion Group to explore the possible collocation of Rock Terrace School with Tilden Middle School on the Tilden Lane site. With an upcoming revitalization/expansion project, Tilden Middle School was identified because of its central location in the Walter Johnson Cluster its large site size and accessibility to accommodate the two schools, and the long history of the Walter Johnson cluster serving special education students.

Board of Education policy IOB, Education of Students with Disabilities, states that MCPS is committed to providing students with disabilities the opportunity to interact with non-disabled peers to the maximum extent possible. The Maryland State Department of Education (MSDE) has stated that state funding would be very difficult to acquire for stand-alone special education centers because students in these centers are not provided opportunities to receive instruction in the general education setting to the maximum extent appropriate. The collocation of special education centers with general education schools, such as the Longview School at Matsunaga Elementary School, allows the school system to address the facility needs of the stand-alone special education centers while meeting the goal to provide special education students with opportunities to receive instruction in the general education environment to the maximum extent appropriate.

Rock Terrace School, which serves students ages 12–21 throughout the county, and focuses on school-to-work programs, was assessed for revitalization/expansion using the Facilities Assessment with Criteria and Testing (FACT) methodology in the 2010–2011 school year. Of the secondary schools assessed that year, Rock Terrace School received the highest score and was in the greatest need of revitalization/expansion. (See Appendices E and F for additional information.)

The Roundtable Discussion Group included parents and staff from Rock Terrace School and Tilden Middle School as well as a representative from the MCCPTA Special Education Committee and the Walter Johnson Cluster. Staff from the Department of Special Education Services, the Division of Long-range Planning, and Division of Construction also participated in the process. To support the activities, an architect was hired to develop concept plans for the possible collocation of the two schools. The activities of the Roundtable included the following:

- Identify opportunities for special education students to receive instruction in the general education environment to the maximum extent appropriate
- Discuss the facility and site implications
- Conduct site visits and engage in discussions with parents and staff at other collocated or soon to be collocated schools in the county and state.

The Roundtable Discussion Group met from December 2014 through February 2015 and submitted a report to the interim superintendent of schools in March 2015. Following input from the Roundtable Discussion Group and the community at large, the interim superintendent of schools recommended and the Board of Education approved the collocation of Rock Terrace School and Tilden Middle School on May 12, 2015.

Capital Project: With the approval of the collocation, the school will be added to the revitalization/expansion schedule to coincide with the Tilden Middle School revitalization/expansion project. Although the Board of Education requested a completion date of August 2019 for this project, the County Council maintained the FY 2015–2020 approved completion date of August 2020.

Tilden Middle School is currently located in the Woodward facility on Old Georgetown Road. Rather than revitalize/expand the Woodward facility for Rock Terrace School and Tilden Middle School, the current Tilden Holding Facility, located on Tilden Lane, will be revitalized/expanded to house both Rock Terrace School and Tilden Middle School. The Woodward facility will then become a secondary school

holding facility for school revitalization/expansion projects scheduled after Tilden Middle School. Although an FY 2014 appropriation was approved for facility planning funds for a feasibility study to determine the scope for facility planning and cost for the revitalization/expansion project of Tilden Middle School, the feasibility study for Rock Terrace School and Tilden Middle School will begin in summer 2015. An FY 2016 appropriation for planning funds is approved to begin the architectural design for the project which will occur after the completion of the feasibility study. In order for this project to be completed on this schedule, county and state funding must be provided at the levels approved in this CIP.

Carl Sandburg Learning Center

Carl Sandburg Learning Center is a special education school that serves students with multiple disabilities in kindergarten through Grade 5, including intellectual disabilities, autism spectrum disorders, language disabilities, and emotional or other learning disabilities. Services are designed for elementary students who need a highly structured setting, small student-to-teacher ratio, and access to the MCPS Curriculum 2.0 or Alternate Learning Outcomes aligned with Curriculum 2.0. Modification of curriculum materials and instructional strategies, based on students' needs, is the basis of all instruction. Emphasis is placed on the development of language and academic and social skills provided through an in-class transdisciplinary model of service delivery in which all staff members implement the recommendations of related service providers. Special emphasis is placed on meeting the sensory and motor needs of students in their classroom setting. To address behavioral goals, services may include a behavior management system, psychological consultation, and crisis intervention.

Capital Project: A revitalization/expansion project is scheduled for this school. Although the Board of Education requested a completion date of August 2019, the County Council maintained the approved FY 2015–2020 CIP completion date of August 2020. An FY 2016 appropriation for planning funds is approved to begin the architectural design for this project. In order for this project to be completed on this schedule, county and state funding must be provided at the levels approved in this CIP. On November 17, 2011, the Board of Education approved the collocation of Carl Sandburg Learning Center on the Maryvale Elementary School campus when the revitalization/expansion project is complete.

Stephen Knolls School

The Stephen Knolls School services students aged 5–21 with severe to profound intellectual disabilities and multiple disabilities. Alternate Learning Outcomes aligned with Curriculum 2.0 are utilized to provide students with skills in the areas of communication, mobility, self-help, functional academics, and transition.

Capital Project: Stephen Knolls School was assessed as part of the Facilities Assessment with Criteria and Testing (FACT) process during the 2010–2011 school year. (See Appendix F for the FACT score of this facility.) To address facilities needs at this school, an FY 2013 appropriation for facility planning was approved in the Modification to Holding, Special Education and Alternative Centers Project for a feasibility study to identify improvement for this building. A recommendation for facility improvements will be made in a future CIP.

CAPITAL PROJECTS

School	Project	Project Status*	Date of Completion
Rock Terrace School	Revitalization/ expansion with collocation at Tilden Middle School	Approved	Aug. 2020
Carl Sandberg Learning Center	Revitalization/ expansion with collocation at Maryvale ES	Approved	Jan. 2020
Stephen Knolls School	Facility Improvements	Proposed	TBD

"Approved"— Project has an FY 2015 or FY 2016 appropriation approved in the FY 2015–2020 CIP.

"Deferred"—Funds have been deferred for a future CIP.

"Programmed"—Project has expenditures programmed in a future year of the CIP for planning and/or construction funds.

"Proposed"—Project has facility planning funds approved for FY 2015 or approved for FY 2016 for a feasibility study.

Projected Enrollment and Space Availability

Effects of the Amended FY2015–2020 CIP and Non–CIP Actions on Space Available

Schools			Actual 14–15	Projections 15–16	16–17	17–18	18–19	19–20	20–21	2024	2029
Stephen Knolls		Program Capacity	190	190	190	190	190	190	190		
		Enrollment	**88**	**88**	**88**	**88**	**88**	**88**	**88**		
		Available Space	*102*	*102*	*102*	*102*	*102*	*102*	*102*		
		Comments									
Longview		Program Capacity	48	48	48	48	48	48	48		
		Enrollment	**48**	**48**	**48**	**48**	**48**	**48**	**48**		
		Available Space	*0*	*0*	*0*	*0*	*0*	*0*	*0*		
		Comments									
RICA		Program Capacity	180	180	180	180	180	180	180		
		Enrollment	**116**	**116**	**116**	**116**	**116**	**116**	**116**		
		Available Space	*64*	*64*	*64*	*64*	*64*	*64*	*64*		
		Comments									
Rock Terrace		Program Capacity	100	100	100	100	100	100	100		
		Enrollment	**83**	**83**	**83**	**83**	**83**	**83**	**83**		
		Available Space	*17*	*17*	*17*	*17*	*17*	*17*	*17*		
		Comments	See text	Planning for Revitalization/ Expansion					Rev/Ex Complete Aug. 2020		
Carl Sandburg		Program Capacity	79	79	79	79	79	135	135		
		Enrollment	**92**	**92**	**92**	**92**	**92**	**92**	**92**		
		Available Space	*(13)*	*(13)*	*(13)*	*(13)*	*(13)*	*43*	*43*		
		Comments		Planning for Revitalization/ Expansion				Rev/Ex Complete Jan. 2020			
Cluster Information		Utilization	72%	72%	72%	72%	72%	65%	65%		
		Enrollment	427	427	427	427	427	427	427		

Demographic Characteristics of Schools

Schools	2014–2015						2014–2015		2013–2014
	Total Enrollment	Two or more races %	Black or Afr. Amer. %	Asian%	Hispanic %	White %	FARMS%*	ESOL%**	Mobility Rate%***
Stephen Knolls School	91	≤ 5.0%	35.2%	6.6%	36.3%	19.8%	47.3%	≤ 5.0%	12.8%
Longview School	48	≤ 5.0%	22.9%	14.6%	31.2%	27.1%	31.2%	≤ 5.0%	14.3%
RICA	120	8.3%	29.2%	≤ 5.0%	20.0%	39.2%	42.5%	≤ 5.0%	72.5%
Rock Terrace School	82	7.3%	32.9%	8.5%	22.0%	29.3%	35.4%	7.3%	10.5%
Carl Sandburg School	91	≤ 5.0%	27.5%	11.0%	29.7%	28.6%	39.6%	23.1%	22.9%
Elementary County Total	75,144	≤ 5.0%	21.2%	13.9%	30.4%	29.3%	40.2%	23.3%	13.3%

**Percent of students approved for Free and Reduced-priced Meals Program (FARMS) during the 2014–2015 school year.*

***Percent of English for Speakers of Other Languages (ESOL) during the 2014–2015 school year. High School students are served in regional ESOL centers.*

****Mobility Rate is the number of entries plus withdrawals during the 2013–2014 school year compared to total enrollment.*

Notes: Native Hawaiian/Pacific Islander and American Indian/Alaskan Native categories total less than 1% and were therefore excluded from the table.

Due to federal and state guidelines, demographic characteristics of schools of less than or equal to 5.0% are reported as ≤ 5.0%.

Program Capacity Table


(School Year 2014–2015)

Schools	Grades or Ages Served	Capacity (HS @90% MS@85%)	Total Rooms	Support Rooms	Regular Secondary @25	Regular Elementary @23	CSR Grades 1–2 @18	Pre–K @20	Pre–K @40	HS @20	CSR KIND @18	KIND @22	ESOL @15	METS @15	Special Education Services: School Based: HSM @13	School Based: ELEM LAD @13	Quad Cluster Based: ELC @10	Quad Cluster Based: LANG @12	Quad Cluster Based: LFI @10	Quad Cluster Based: SCB @6	County & Regional Based: AAC@7	AUT @6	SPECIAL SCHOOLS @ 6	DHOH @7	ED @10	EXTENSIONS @6	GT/LD @13	PD @7	PEP@6	PEP @12	PEP @18	VISION (Elementary) @7	OTHER
Stephen Knolls School	N/A	190	19	4					1																			7		6		1
Longview School	N/A	48	10	2																								8				
RICA	N/A	180	18																					18								
Rock Terrace School	N/A	100	16	2															10													4
Carl Sandburg School	N/A	79	16	3																	1	12										

Facility Characteristics of Schools 2014–2015

Schools	Year Facility Opened	Year Reopened/ Revitalized	Total Square Footage	Site Size Acres	Adjacent Park	Reloc-atable Classrooms	Linkages to Learning Program	Home School Model
Stephen Knolls School	1958	1979	48,872	6.6				
Longview School	2001		40,362	10				
RICA	1977		95,000	14.3				
Rock Terrace School	1950	1974	48,024	10.3				
Carl Sandburg Learning Center	1962		31,252	7.6		2		

Other Educational Facilities

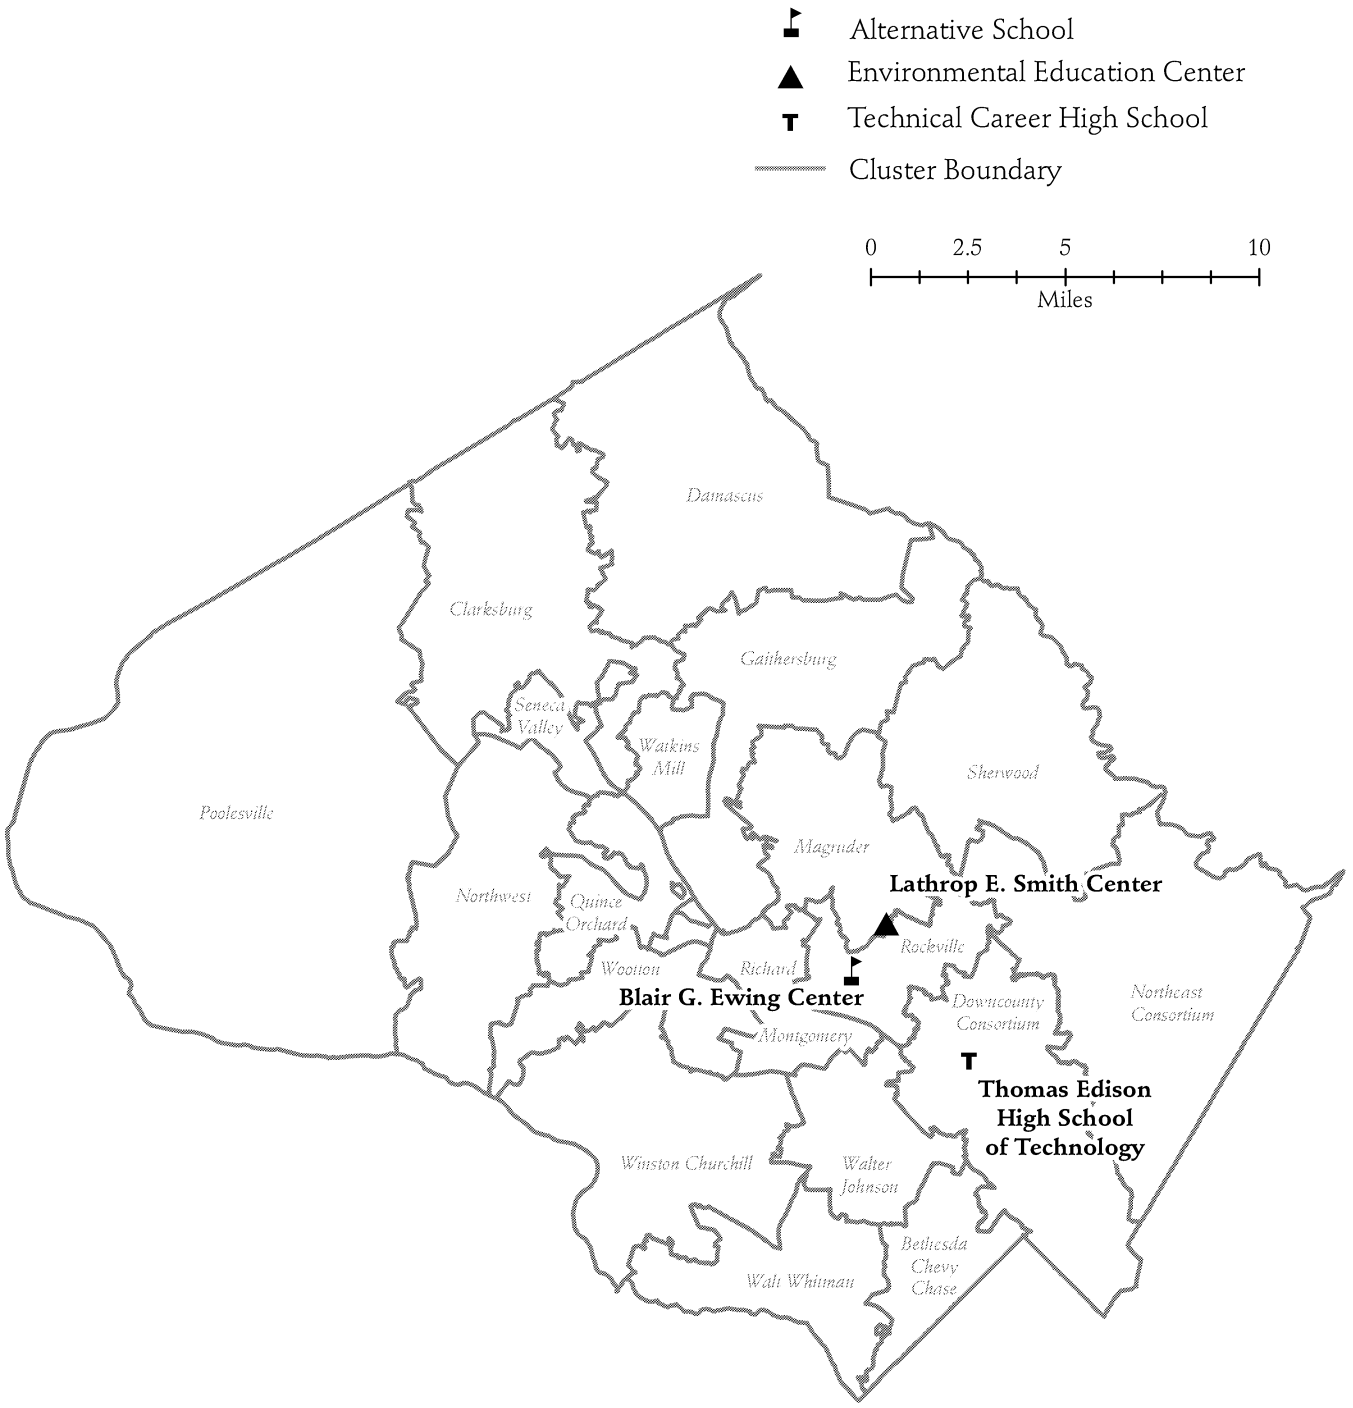

Montgomery County Public Schools - Division of Long-range Planning - June 2015

ALTERNATIVE EDUCATION PROGRAMS

In 2013, the superintendent of schools initiated a district-wide redesign of the Alternative Education Program (AEP) to provide specific supports and interventions to meet the needs of the unique student population so that the students can achieve success. The redesign is intended to ensure that academic performance is not predicted by race, ethnicity, or socioeconomic status. A three-year phase plan was developed by the AEP redesign committee comprised of central services and alternative education staff. In February 2014, the Board of Education approved the redesign plan for the AEP. Following the approval, a redesign implementation committee was tasked with the oversight and monitoring of the three-year phase plan.

The three major bedrocks of the redesign plan focus on:

- Creating Personalized Learning Plans (PLP) for each student
- Providing expanded social emotional learning and services
- Providing instructional focus through Universal Design of Learning (UDL), and PLATO online virtual pathway to learning

Montgomery County Public Schools operates two AEP programs—one for middle school students and one for high school students. The programs are intended to support students who have been unsuccessful in their home schools for a variety of reasons. AEP strives to provide positive and effective educational supports and services that address the academic, social, emotional and physical health of adolescents. Beginning in August 2014, all students attending AEP are located at the Blair Ewing Center.

The High School Program (grades 9–12) and the Middle School Program (grades 6–8) serve students who are not achieving at their potential for a wide variety of reasons. These reasons include behavior and/or attendance problems, as well as students who have been involved in a serious disciplinary action that warrants a recommendation for expulsion and placement by the Office of the Chief Operating Officer in lieu of expulsion.

In addition to the middle and high school programs, the 45-day Interim Placement Program serves students in grades 6–12 receiving special education services. Students are placed in the program after a central office review and as a result of their involvement with controlled substances, serious bodily injury, and/or weapons. Students remain enrolled in their home school, and the home school provides daily assignments and assessments.

Blair G. Ewing Center

Capital Project: Blair G. Ewing Center was assessed as part of the Facilities Assessment with Criteria and Testing (FACT) in FY 2012 to determine the condition of the facility. The facility was ranked in second worst condition of all the secondary schools assessed that year. As a result of the poor condition of the facility, a feasibility study was conducted in the 2012–2013 school year to identify facility improvements to the current Blair G. Ewing Center. At that time, the Blair G. Ewing Center housed all of the high school Alternative Education Programs (AEP) and only some of the middle school AEP. The Glenmont and Hadley Farms facilities housed the other middle school AEP. Subsequent to the feasibility study, an AEP project team was charged to develop a new vision and design for the AEP in MCPS. A result of the new vision was to locate all of the middle and high school AEP at Blair G. Ewing Center, beginning in the 2014–2015 school year.

Although an FY 2015 appropriation was approved to begin the architectural design to make improvements at the Blair G. Ewing Center facility, the new vision for AEP required a second look at the current facility to ensure that the middle and high schools AEP were appropriately accommodated with the funds approved. The Blair G. Ewing Center facility, which was constructed in the early 1970s with a pod organization, does not have an ideal configuration to support the new vision for alternative education in MCPS. The building remains less than ideal to support the redesigned program for middle and high school students and it is difficult to supervise students due to the pod configuration. Furthermore, although the $16.6 million approved in the CIP will address the systemic renovations in the facility, it will not be possible to address all of the configuration issues in the facility that make it a challenge to deliver the educational program.

In order to provide the AEP with a facility that will support the program and students, in October 2014, the superintendent of schools recommended that the AEP, currently housed at the Blair G. Ewing Center, be relocated to the former English Manor Elementary School site and the facility be renovated and expanded to accommodate the Blair G. Ewing Center AEP. On November 17, 2014, the Board of Education submitted a request for approval of a supplemental appropriation to change the project scope and conduct a feasibility study for the English Manor site. On February 10, 2015, the County Council approved that two feasibility studies be conducted for the redesigned AEP—one study at the current Avery Road site and a second study at another site determined to be appropriate by the Board of Education. Subsequent to the County Council action, on April 14, 2015, the Board approved a feasibility study at the current Avery Road site and a study of closed school sites in the central part of the county and Carl Sandburg and Rock Terrace School sites to determine the second site to study. The list of closed school sites includes: Aspen Hill, English Manor, Holiday Park, Lone Oak, Montrose, North Lake, Rocking Horse Road, Woodley Gardens

elementary schools, and Edwin W. Broome and Randolph junior high schools. The feasibility study and study of sites will begin in summer 2015. The completion date is scheduled for August 2018.

Lathrop E. Smith Center

The Lathrop E. Smith Center is owned and operated by Montgomery County Public Schools and hosts the Outdoor Environmental Education Programs (OEEP) that includes the Grade 6 residential program and Grades K–5 day program. The programs provide outdoor learning experiences through the MCPS curriculum that increase students' content and process knowledge; nurture awareness, appreciation, and stewardship for the natural environment; and build the capacity of MCPS educators to teach environmental education using the outdoors as a classroom.

Grade 6 students participate in a three-day, two-night residential outdoor environmental education program. While in residence, students study various aspects of the local watershed as they participate in outdoor field investigations that are directly connected to the Grade 6 curriculum and the MSDE environmental education standards. The teaching and learning that occurs at school and during the residential program create a meaningful watershed environmental experience for each Grade 6 student, which culminates in an environmental student service learning project. Students are accompanied by their teachers, who, in collaboration with an OEEP staff member, provide instruction and supervision during their stay. The environment is used as an integrating context for learning; therefore, instruction incorporates many content areas as students explore and investigate the local watershed.

The day program serves students in Grades K–5. Each program is directly linked to the school curriculum at each grade level with a focus on STEM relationships. Schools also may request an in-school visit from an environmental educator to provide assistance and guidance in the integration of environmental education at the local school site. The center also provides professional development to teachers in the content and pedagogy of environmental education.

CAPITAL PROJECTS

School	Project	Project Status*	Date of Completion
Blair G. Ewing Center	Facility Improvements	Approved	Aug. 2018

"Approved"— Project has an FY 2015 or FY 2016 appropriation approved in the FY 2015–2020 CIP.

"Deferred"—Funds have been deferred for a future CIP.

"Programmed"—Project has expenditures programmed in a future year of the CIP for planning and/or construction funds.

"Proposed"—Project has facility planning funds approved for FY 2015 or approved for FY 2016 for a feasibility study.

Facility Characteristics of Schools 2014–2015

Schools	Year Facility Opened	Year Reopened/ Revitalized	Total Square Footage	Site Size Acres	Adjacent Park	Reloc- atable Classrooms	Linkages to Learning Program	Home School Model
Thomas Edison HS of Technology	1982		114,310	28.2	Yes			
Blair G. Ewing Center	1970		85,400	22.5				
Lathrop E. Smith Center			20,345	9.78	Yes			

Career Technology Education Programs

Career and Technology Education (CTE) Programs of Study (POS) prepare students for college, careers, and lifelong learning. Montgomery County Public Schools currently offers College/Career Research Development in addition to over 35 POS organized within the following 11 career clusters:

- Arts, Humanities, Media, and Communications;
- Biosciences, Health Science, and Medicine;
- Business Management and Finance;
- Construction and Development;
- Education, Training, and Child Studies;
- Engineering, Scientific Research, and Manufacturing Technologies;
- Environmental, Agricultural, and Natural Resources;
- Human and Consumer Services, Hospitality, and Tourism;
- Information Technology;
- Law, Government, Public Safety, and Administration; and
- Transportation, Distribution, and Logistics.

Over 22,000 MCPS students are enrolled in at least one CTE POS pathway course at comprehensive high schools throughout the county or at Thomas Edison High School of Technology (TEHST). CTE POS focus on challenging and engaging instruction that provide academic and technical knowledge and skills and prepare students for college and careers. Most POS provide opportunities for students to earn college credit through college courses or articulation agreements with select postsecondary institutions. These agreements allow students to earn college credit for identified high school courses that are successfully completed with a grade of 'B' or better. Internship experiences connect students with the world of work, enhancing the rigor and relevance of the POS. Students take and pass industry credentialing examinations in areas, such as business, information technology, hospitality, and cosmetology.

There are regional hubs, like the TEHST location, that give students from all high schools equitable access to select POS. Students report to the identified location for half a day and spend the other half of the school day at their home high school. To ensure relevance to college and industry, CTE staff members have established a Program Advisory Committee (PAC) for each career cluster. The PAC includes representatives from the business community and secondary and postsecondary institutions. PACs strive to provide seamless experiences for students as they move from middle school to high school and postsecondary experiences.

Foundations Office Programs

The Montgomery County Student Trades Foundations Office is composed of the following three separate non-profit educational foundations: Automotive Trades Foundation (ATF), Construction Trades Foundation (CTF), and Information Technology Foundation (ITF). The Foundations Office is a liaison between the business/professional community in these three industry areas and MCPS. This relationship promotes the advancement of college and career education and prepares students for a full range of careers within each industry. In MCPS, there are currently 15 POS supervised by staff in the Foundations Office. Articulation agreements are in place for all Foundation programs with select postsecondary institutions; however, students may also earn college credit by enrolling in and successfully completing pre-approved college courses that align with their respective POS.

The ATF operates as a licensed used-car dealership. ATF programs are located at Damascus, Gaithersburg, and Seneca Valley high schools in addition to TEHST. The programs are nationally certified by the National Automotive Technicians Education Foundation (NATEF), an affiliation of Automotive Service of Excellence (ASE). The programs also are affiliated with Automotive Youth Education System (AYES), which is the highest level of achievement for automotive technology programs. Automotive instructors maintain industry standard certifications in ASE areas relevant to their programs.

The CTF operates as a licensed Residential Home Builder and supports a variety of construction industry trades that include the following: Carpentry, Electricity, Masonry, Plumbing, HVAC, Principles of Architecture and CAD Technology, Interior Design, and Foundations of Building and Construction Technology. The CTF programs are located at Damascus High School and TEHST. The Foundation also has established a partnership with Associated Builders and Contractors, Metro Washington Chapter (ABC Metro). ABC Metro has certified the instructors, accredited the facility, and formalized articulation agreements. This program provides a nationally recognized apprenticeship from the National Center for Construction Education and Research (NCCER). The CTF also has aligned with the construction programs at Montgomery College, allowing students further opportunities for professional development and advancement in the construction industry.

The ITF provides a POS in Network Operations at Clarksburg High School and TEHST, both of which are Computing Technology Industry Association (CompTIA) Academy and Microsoft DreamSpark member programs. The ITFs unique public/private partnership promotes computer education and provides entrepreneurial experiences to high school students throughout Montgomery County, preparing students for seamless transitions into the computer technology industry and college or other postsecondary education.

Additional POS pathways in information technology and/or computer science are provided at Bethesda-Chevy Chase, Damascus, Gaithersburg, John F. Kennedy, Northwest, Northwood, Paint Branch, Rockville, Quince Orchard, Seneca Valley, Springbrook, Wheaton, and Thomas S. Wootton high schools. Two additional high schools are slated to begin offering programs next school year. Programs offered include computer science, programming, networking and web development. Each program is aligned with national partners and/or national

academies. These include the National Academy Foundations' Academy of Information Technology, Cisco Networking Academy, and a partnership program with Code.org.

Seneca Valley High school has a revitalization/expansion project scheduled that includes the Automotive Technology Dealership/Training POS, Cisco Academy, and the Academy of Information Technology pathways in Programming, Networking and Information Resource Design.

Thomas Edison High School of Technology

Planning Study: Wheaton High School and Thomas Edison High School of Technology (TEHST) are located on the same site and share one facility. These schools are scheduled for revitalization/expansion projects. During the past several years, two major planning studies were conducted to prepare for the revitalization/expansion projects of these schools. During the fall and winter 2010–2011, a Roundtable Discussion Group, with broad stakeholder involvement, met to explore various approaches for the future relationship between the two schools. Following the Roundtable Discussion Group review, the Board of Education took action on March 28, 2011, to keep the two schools separate with distinct identities and directed staff to conduct a feasibility study to review two options—a one-building option and a two-building option. At the conclusion of the feasibility study, on September 13, 2011, the Board of Education adopted a two-building option for the revitalization/expansion projects of Wheaton High School and Thomas Edison High School of Technology.

Capital Project: An FY 2014 appropriation for construction funds was approved to construct the replacement facilities for Wheaton High School. An FY 2016 appropriation is approved to construct Thomas Edison High School of Technology. The completion dates for these schools are scheduled for January 2016 for the Wheaton High School facility, August 2017 for the Thomas Edison High School of Technology facility, and August 2018 for restoration of the site. In order for these projects to be completed on schedule, county and state funding must be provided at levels approved in this CIP.

Capital Project: On September 22, 2014, the Board of Education approved a plan to offer a financial literacy program at Thomas Edison High School of Technology to all Grade 7 students in Montgomery County Public Schools (MCPS). An agreement between MCPS and Junior Achievement of Greater Washington has been reached to proceed with the construction of a Junior Achievement Finance Park at Thomas Edison High School of Technology. A fourth floor will be added to Thomas Edison High School of Technology to accommodate the Junior Achievement Finance Park. Grade 7 students not only will benefit from the lifelong knowledge and skills gained at Junior Achievement Finance Park, they also will have the opportunity to learn about the exciting programs available at Thomas Edison High School of Technology.

The Junior Achievement Finance Park experience begins in the classroom with four weeks of classroom curriculum and culminates with a day at the Junior Achievement Finance Park. At Junior Achievement Finance Park, students immerse themselves in a reality-based, decision-making process that addresses aspects of individual and family budgeting-including housing, transportation, food, utilities, health care, investments, philanthropy, and banking. The on-site activities are designed to allow students the opportunity to "put into action" what they learned in the classroom and to understand the basic steps of maintaining a realistic personal budget. Two weeks of classroom follow-up activities will allow students to use their new financial knowledge to explore career options and to set future goals.

Junior Achievement of Greater Washington has agreed to contribute up to $2,500,000 for the construction of the Junior Achievement Finance Park. An FY 2015 supplemental appropriation was approve for the amount of $2,500,000 to be expended over a period of three fiscal years. The scheduled completion date for the Junior Achievement Finance Park will coincide with the completion of Thomas Edison High School of Technology, which is scheduled for August 2017.

CAPITAL PROJECTS


School	Project	Project Status*	Date of Completion
Thomas Edison HS of Technology	Revitalization/ expansion and Junior Achievement Finance Park	Approved	Aug. 2017, Building Aug. 2018, Site

"Approved"— Project has an FY 2015 or FY 2016 appropriation approved in the FY 2015–2020 CIP.

"Deferred"—Funds have been deferred for a future CIP.

"Programmed"—Project has expenditures programmed in a future year of the CIP for planning and/or construction funds.

"Proposed"—Project has facility planning funds approved for FY 2015 or approved for FY 2016 for a feasibility study.

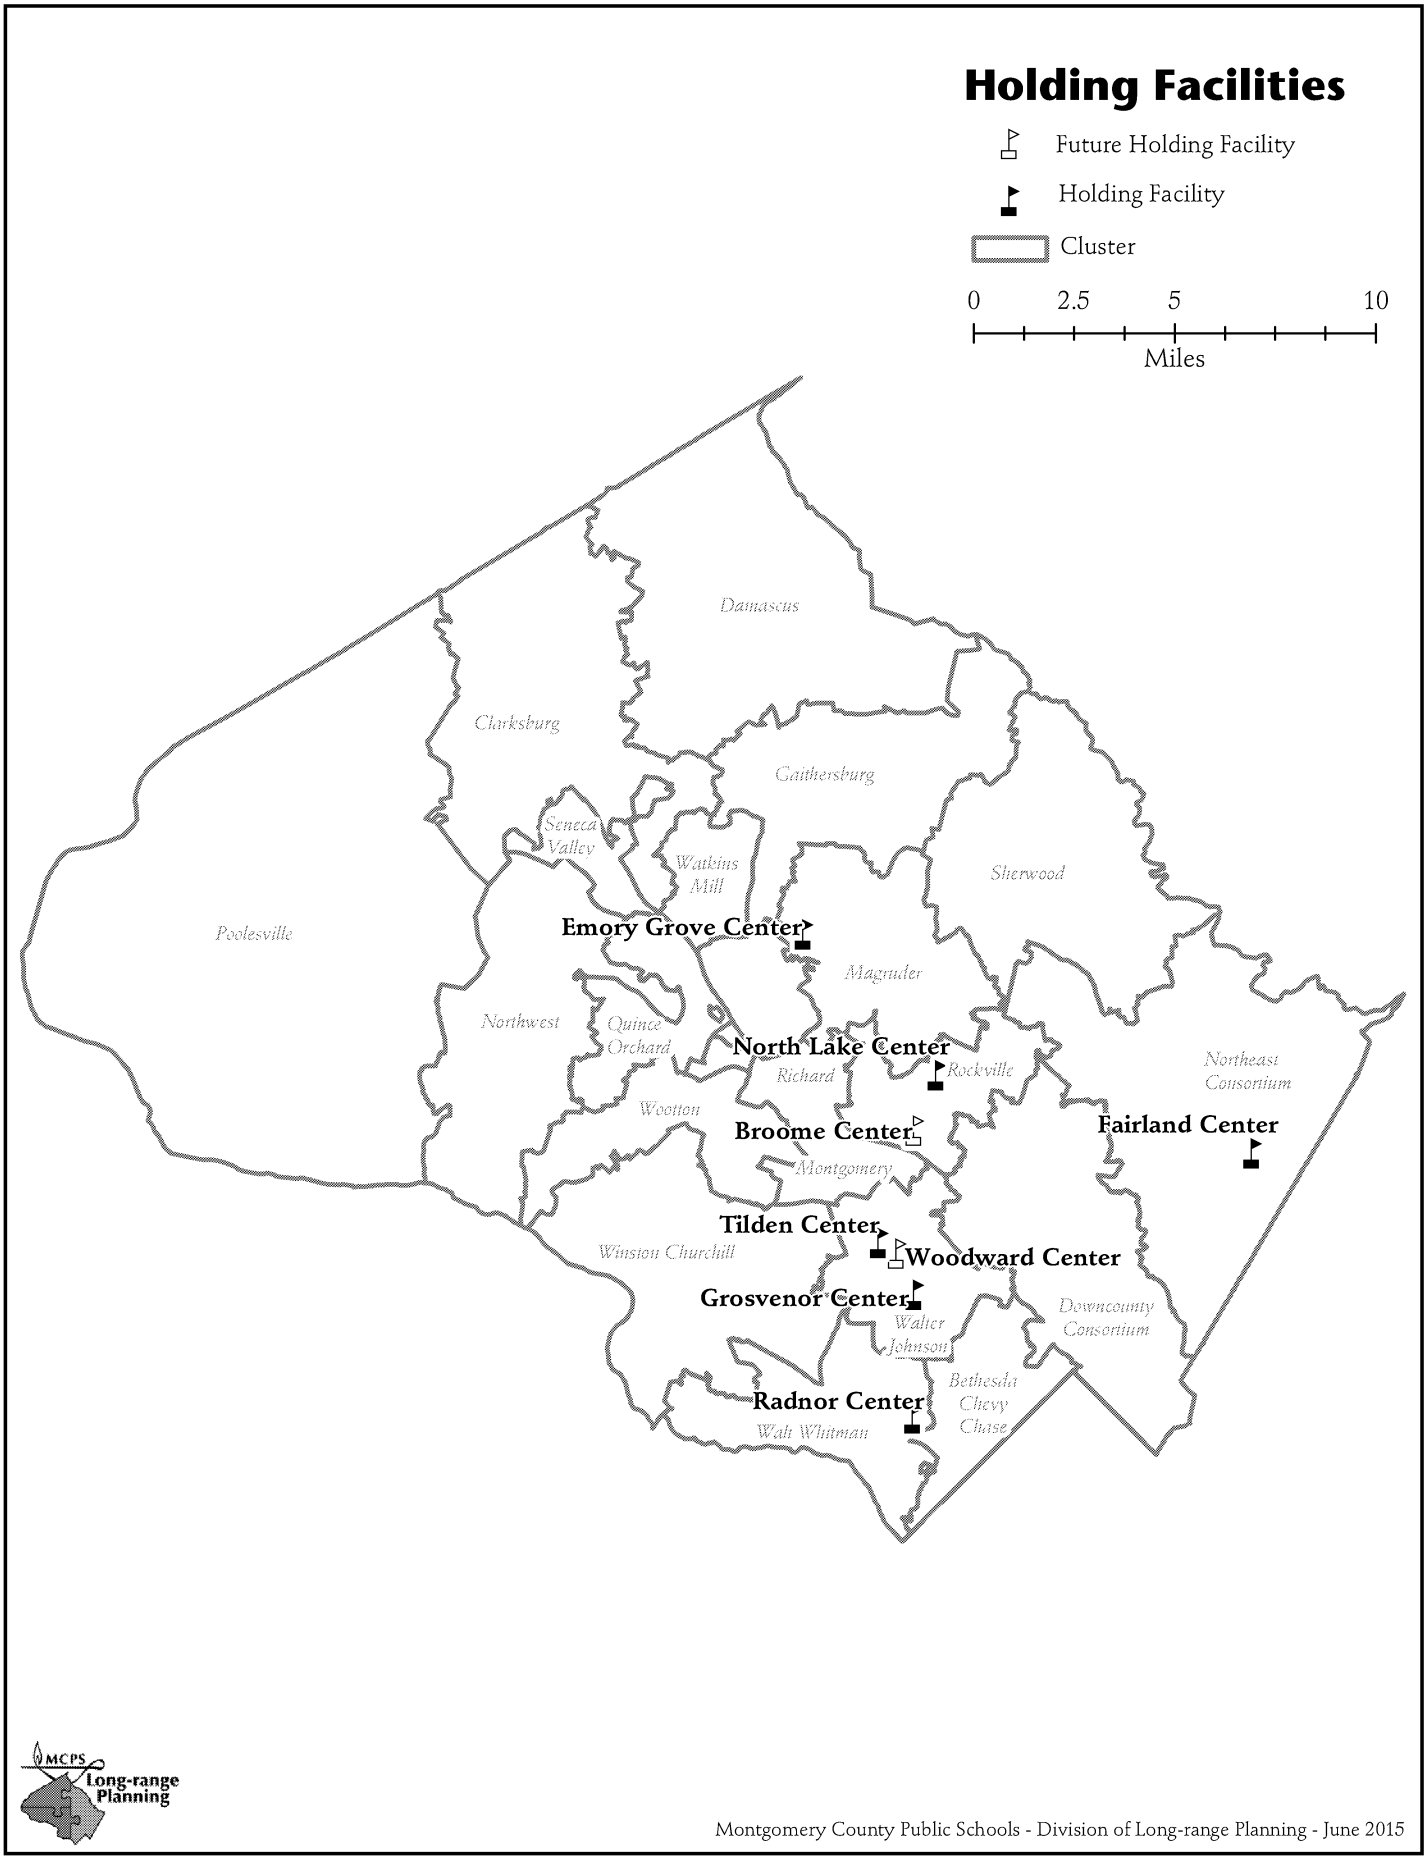
Holding Facilities
Future Holding Facility
Holding Facility
Cluster
0
2.5
5
10
Miles
Damascus
Clarksburg
Gaithersburg
Seneca Valley
Watkins Mill
Sherwood
Poolesville
Emory Grove Center
Magruder
Northwest
Quince Orchard
North Lake Center
Richard
Rockville
Northeast Consortium
Wootton
Broome Center
Fairland Center
Montgomery
Tilden Center
Winston Churchill
Woodward Center
Grosvenor Center
Walter Johnson
Downcounty Consortium
Bethesda Chevy Chase
Radnor Center
Walt Whitman
MCPS
Long-range Planning
Montgomery County Public Schools - Division of Long-range Planning - June 2015

Holding Facilities

Holding facilities are utilized for capital projects, such as revitalization/expansion projects and large-scale addition projects to house students and staff during construction. By relocating students and staff to a holding facility, MCPS is able to reduce the length of time required for construction and provide a safe and secure environment for the students and staff. Currently, MCPS utilizes the following facilities as holding schools for revitalization/expansion projects and large-scale addition projects.

Elementary School Holding Facilities

The elementary school holding facilities were assessed as part of the Facilities Assessment with Criteria and Testing (FACT) process during the 2010–2011 school year. To address needs at these facilities, an FY 2013 appropriation for facility planning was approved in the Modifications to Holding, Special Education, and Alternative Centers Project for feasibility studies to identify improvements for these buildings. Due to fiscal constraints in the county, a recommendation for facility improvements will be made in a future CIP. The following facilities are utilized for elementary school projects:

- Emory Grove
- Fairland
- Grosvenor
- North Lake
- Radnor

Secondary School Holding Facilities

Broome Holding Facility

Capital Project: The Broome facility is currently owned by Montgomery County. Although FY 2015 expenditures for planning funds were programmed to reopen the facility for use as a middle school holding facility, due to fiscal constraints in the county, these funds have been deferred until a recommendation can be made in a future CIP.

Tilden Holding Facility

A recommendation for funds to replace the Tilden Holding Facility with the Woodward Holding Facility will be made in a future CIP. This site will be used for the Rock Terrace School and Tilden Middle School revitalization/expansion project which is scheduled for completion in August 2020.

Woodward Holding Facility

Capital Project: With the reopening of Northwood High School in 2004, there has been no high school holding facility. Tilden Middle School is currently located at the former Woodward High School facility, which is located on Old Georgetown Road. Tilden Middle School has a revitalization/expansion project scheduled for completion in August 2020. Although the school is currently located in the Woodward facility, the current Tilden Holding Facility, located on Tilden Lane, will be revitalized to house Rock Terrace School and Tilden Middle School. The Woodward facility will then become a secondary school holding facility for school revitalization/expansion projects scheduled after Rock Terrace School and Tilden Middle School. Tilden Middle School will remain at the Woodward facility until the revitalization/expansion project of the Tilden Lane facility is complete. Although FY 2017 expenditures were programmed in the CIP to design the renovations of the Woodward facility for use as a secondary holding facility, due to fiscal constraints in the county, the funds have been deferred until a recommendation can be made in a future CIP.

CAPITAL PROJECTS

School	Project	Project Status*	Date of Completion
Broome Holding Facility	Renovations	Deferred	TBD
Woodward Holding Facility	Renovations	Deferred	TBD

"Approved"— Project has an FY 2015 or FY 2016 appropriation approved in the FY 2015–2020 CIP.

"Deferred"—Funds have been deferred for a future CIP.

"Programmed"—Project has expenditures programmed in a future year of the CIP for planning and/or construction funds.

"Proposed"—Project has facility planning funds approved for FY 2015 or approved for FY 2016 for a feasibility study.

Holding Facility Schedule

Holding Facility	SY 14–15	SY 15–16	SY 16–17	SY 17–18	SY 18–19	SY 19–20	SY 20–21
ELEMENTARY SCHOOLS							
Emory Grove Center	Candle-wood		Brown Station			DuFief	
Fairland Center						Stonegate	
Grosvenor Center			Wayside		Luxmanor	Cold Spring	
North Lake Center			Wheaton Woods		Maryvale	Belmont	
Radnor Center	Rock Creek Forest	Wood Acres			Potomac		
MIDDLE SCHOOLS							
Tilden Center/ Woodward Center*					*To be revitalized/expanded*		Eastern

** Tilden Middle School is currently located in the Woodward Center. A revitalization/expansion for Tilden Center is scheduled for completion in August 2020 which will house Tilden Middle School. The Woodward Center will then become a secondary holding school facility for school revitalization/expansion projects scheduled after Tilden Middle School.*

Holding Facility Data (2014–2015 School Year)

Holding Facility	Level	Facility Address	Rooms	Total Square Footage	Site Size Acres	Relocatable Classrooms
Emory Grove Center	Elementary	18100 Washington Grove Lane	19	49,858	10.17	7
Fairland Center	Elementary	13313 Old Columbia Pike	26	45,082	9.21	9
Grosvenor Center	Elementary	5701 Grosvenor Lane	19	36,770	10.21	21
North Lake Center	Elementary	15101 Bauer Drive	22	40,378	9.66	16
Radnor Center	Elementary	7000 Radnor Road	16	36,663	9.03	23
Tilden Center	Middle	6300 Tilden Lane	39	119,516	19.7	0

Chapter 5

Countywide Projects

Montgomery County Public Schools (MCPS) has many capital projects that are not for one particular school, but rather are programmed to meet the needs of many schools across the county. These projects involve multiyear plans with different schools scheduled each year, and projects are referred to as countywide projects. The assessment and selection process for many of these projects is carried out through an annual review process that involves school principals, maintenance, planning, and construction staff.

The primary countywide projects that address the physical environment in schools include: compliance with the Americans with Disabilities Act (ADA); Asbestos Abatement; Fire Safety Code Upgrades; Heating, Ventilation and Air Conditioning (HVAC); Indoor Air Quality (IAQ); Planned Life-cycle Asset Replacement (PLAR); and Roof Replacement. These projects require an assessment of each school relative to the needs of other schools and the development of schedules based on available funding. Some projects, such as ADA, Asbestos Abatement, Fuel Tank Management, and Stormwater Management are driven by mandates that require an evaluation and action plan in order to meet federal, state, and local regulations.

Maintenance and replacement projects are critical to keep aging school facilities operational. As schools age, they are placed on a maintenance and repair ladder, moving from minor repairs to outright replacement of major systems. PLAR and the countywide projects that focus on roof replacements and mechanical system rehabilitations are essential to the preservation of the school systems' infrastructure. Intensive maintenance and rehabilitation efforts to extend the useful life of schools occur through the following projects: HVAC, PLAR, and Roof Replacement.

A brief description of each countywide project follows.

Americans with Disabilities Act (ADA) Compliance

Funds from this project support compliance with federal and state laws and regulations regarding the accessibility of school facilities for persons with disabilities. The items most frequently provided are ramps, elevators, and wider door openings for wheelchair accessibility. Accessible bathrooms and water fountains also are funded as part of this program. The goal is to provide access to all spaces in MCPS buildings. In some cases, programs have been relocated to accommodate students until full accessibility can be met. Funding for this program will continue beyond the six–year planning period.

Asbestos Abatement

Federal and state regulations require the management and ultimately, the removal of asbestos from schools. Funds from this project support compliance with these mandates. As a cost saving measure, a special group of MCPS employees has been trained to remove asbestos in a manner that complies with strict safety requirements. However, projects that are larger than this group can accommodate are competitively bid and are funded through this project. Funding for this program will continue beyond the six–year planning period.

Building Modifications and Program Improvements

This project will provide facility modifications and program improvements to schools that are not scheduled for a revitalization/expansion project or addition in the foreseeable future.

Current Revitalizations/Expansions

This is a summary project for all revitalization/expansion projects that have planning or construction expenditures for either FY 2015 or FY 2016. Revitalization/Expansion projects are moved from the Future Revitalization/Expansion project to this project when expenditures are approved by the County Council in the first two years of the CIP. Appendix E of this document lists the priority order of revitalizations/expansions, based on FACT and Educational Program assessments.

Design and Construction Management

This project provides funding for the MCPS staff necessary to assure the successful planning, design, and construction of the capital projects contained in the six–year CIP.

Energy Conservation

This project funds the materials necessary to develop strategies to reduce energy consumption. These strategies include improving building mechanical systems, retrofitting building lighting, and updating associated temperature control systems. This project will continue indefinitely.

Facility Planning

In order to assure the availability of accurate cost estimates for facility construction, a feasibility study process has been instituted. Architects are hired for each new or revitalization/expansion project to develop and evaluate several feasible options that meet the project's needs. For each option, a cost estimate is prepared and an analysis is performed to determine the most cost–effective solution. The study of options is presented to the Board of Education and the project cost is established. This "preplanning" information is then used to develop a budget for submission to the County Council for funding. The feasibility study process helps to produce a clear understanding of the feasibility, scope, and cost for each project.

Fire Safety Code Upgrades

This project funds building modifications to meet Fire Marshall and life safety code requirements. Facility modifications to be addressed in this project are sprinklers, escape windows, exit signs, fire alarm devices, and exit stairs.

Future Revitalizations/Expansions

This is a summary of all revitalization/expansion projects that do not have expenditures in the first two years of the CIP. The priority order for revitalizations/expansions is determined by the FACT and Educational Program assessments, and is detailed in Appendix E. Schools are added to the schedule in the out–years of the CIP as the County Council approves funding. Projects shown within this project will be moved to the Current Revitalizations/Expansions project once the County Council approves expenditures for a revitalization/expansion in either the first or second fiscal year of the CIP.

Heating, Ventilation, and Air Conditioning (HVAC) Mechanical Systems Replacement

This project provides an orderly replacement of heating, ventilation, and air conditioning systems in MCPS facilities not scheduled for revitalization/expansion.

Improved (Safe) Access to Schools

This project addresses vehicular access to schools. Projects may involve the widening of a street or road, obtaining rights–of–way for vehicular access, or the addition of entrances to school sites. The list of specific school projects is approved annually by the County Council.

Indoor Air Quality Improvements

This project provides mechanical retrofits and building envelope modifications necessary to address Indoor Air Quality (IAQ) problems at schools. In the past, funds in this project also addressed lead abatement remediation at identified schools and will be used to develop specific remediation and work plans for schools that have complete test results and lead source assessment.

Land Acquisition

The Land Acquisition project is used to acquire land for new schools and the expansion of smaller school sites. Sites are initially identified through the Comprehensive Master Plan process administered by the Maryland National Capital Park and Planning Commission. Prior to site selection, a Site Selection Advisory Committee (SSAC) is convened.

Planned Life-cycle Asset Replacement (PLAR)

This project provides funding for the repair or replacement of major site improvements and building systems that have reached the end of their useful life. Some of the items that this project covers are field rehabilitation, exterior resurfacing (including driveways and tennis courts), interior partitions, doors, lighting, windows, security gates, bleachers, communications systems, and flooring. All projects are evaluated, and a six–year plan is in place for the repair of needed items. The list of projects is evaluated annually.

Rehabilitation and Renovation of Closed Schools (RROCS)

MCPS has retained some closed schools for use as office space, holding schools, or alternative schools. Some of these facilities have reopened as schools. Funds from this project are used to rehabilitate buildings to meet current codes and to provide appropriate educational spaces.

Relocatable Classrooms

MCPS utilizes relocatable classrooms on an interim basis to accommodate student enrollment in overutilized facilities and for class–size reduction initiatives until a long–term solution is in place. Some are owned by MCPS, some are owned by the State of Maryland, and others are leased. This project provides funding for the relocation, leasing, acquisition, and repair of relocatable classroom units.

Restroom Renovations

The project will provide needed modifications to specific areas of restroom facilities. A study was conducted to evaluate restrooms for all schools that were built or renovated before 1985. A second study was conducted in FY 2010 to provide restroom renovations at additional schools. Schools were rated based on an evaluation method using a preset number scale for the assessment of the existing plumbing fixtures, accessories, and room finish materials. See Appendix G for the list of schools in the project.

Roof Replacement

Roofs that are in need of repair or replacement are funded through this project. The schedule of yearly repairs/replacements is determined according to priority. The roofs are expected to have a life cycle of approximately 20 years.

School Security Systems

This project provides funding for security camera systems at MCPS high school facilities. Currently, all high schools have security systems. At this time, no middle schools have security camera systems. Consideration is being given to install security systems in middle schools.

Shady Grove Transportation Depot Replacement

The 2006 adoption of the Shady Grove Sector Plan signaled the future transformation of the existing County Service Park (CSP) along Crabbs Branch Way into a mixed-use community with a residential focus at the Shady Grove Metro Station. Services located at the CSP were relocated to other parts of the county, with the exception of the Shady Grove Transportation Depot. Funds approved in the FY 2015–2020 Amended CIP will be used to conduct feasibility studies to determine a new location for the depot.

Stormwater Discharge and Water Quality Management

This project will provide funding to plan and implement a variety of pollution prevention measures related to stormwater discharge from our school facilities as required by federal and state laws. Also, this project will provide funding to meet State of Maryland requirements that all industrial sites be surveyed and a plan developed to mitigate stormwater runoff.

Technology Modernization

This project will provide needed technology updates for the original Global Access program schools. This project will provide a better student to computer ratio, best practices for dynamic access to information networks, modern methodologies for teacher training, and application of current theory and practice to prepare students for the 21st century.

Chapter 6

Project Description Forms

SAMPLE FORM -- No. 999999

Category	**MCPS**	Date Last Modified	**October 21, 1997**
Agency	**Public Schools**	Previous PDF Page Number	-
Planning Area	**Bethesda-Chevy Chase**	Required Adequate Public Facility	**NO**
Relocation Impact	**None.**		

EXPENDITURE SCHEDULE ($000)

Cost Element	Total	Thru FY97	Estimate FY98	Total 6 Years	FY99	FY00	FY01	FY02	FY03	FY04	Beyond 6 Years
Planning, Design and Supervision	0	0	0	0	0	0	0	0	0	0	0
Land	0	0	0	0	0	0	0	0	0	0	0
Site Improvements and Utilities	0	0	0	0	0	0	0	0	0	0	0
Construction	0	0	0	0	0	0	0	0	0	0	0
Other	0	0	0	0	0	0	0	0	0	0	0
Total	0	0	0	0	0	0	0	0	0	0	0

FUNDING SCHEDULE ($000)

G.O. Bonds	0	0	0	0	0	0	0	0	0	0	0
State Aid	0	0	0	0	0	0	0	0	0	0	0

ANNUAL OPERATING BUDGET IMPACT ($000)

Maintenance				0	0	0	0	0	0	0	0
Energy				0	0	0	0	0	0	0	0
Program-Staff				0	0	0	0	0	0	0	0
Program-Other				0	0	0	0	0	0	0	0
Net Impact				0	0	0	0	0	0	0	0
Workyears				0	0	0	0	0	0	0	0

DESCRIPTION
This is a sample form for a Project Description Form (PDF). This form is a summary of the project and provides costs information, description, and justification for the project.
STATUS
Planning

9 8 7 10 12

11

How to Read a Project Description Form

The following page provides a diagram of the PDF. Each section of the form is described as follows:

1. Initial Cost Estimate—The estimated cost at the time the project name first appears in the Capital Improvements Program (CIP). This cost remains the same regardless of any changes in the project, such as scope, timing, inflation, code changes, etc.
2. First Cost Estimate—Current Scope—The estimated cost of the project as currently planned.
3. Last Fiscal Year's Cost Estimate—The cost approved in last year's CIP.
4. Present Cost Estimate—The current cost based on a detailed review of construction costs, scope, design, and program of the project.
5. Appropriation Request—The legal authority for the total amount of funds needed to award an entire contract for goods/services. To award a contract, this authority is required, even though funds typically are spent year by year, as shown in the expenditure schedule.
6. Cumulative Appropriation—The Council-approved total appropriation from prior years.
7. Expenditure Schedule—Year One Total—The actual anticipated cash flow in the first year of the requested capital budget.
8. Expenditure Schedule—Total Six Years—The totals for the six-year CIP in current-year dollars.
9. Expenditure Schedule—Total—The grand total in current-year dollars.
10. Funding Schedule—County Bonds—The source of funding, including state, county, or other sources.
11. Description and Justification—The text that describes the project and why it is needed.
12. Operating Budget Impact—Displays new annual costs that represent additional operating budget expenditures required for a new or expanded school building.

APPROPRIATION AND EXPENDITURE DATA

Date First Appropriation	FY99	($000)
Initial Cost Estimate		0
First Cost Estimate Current Scope	FY99	0
Last FY's Cost Estimate		0
Present Cost Estimate		0
Appropriation Request	FY99	0
Supplemental Appropriation Request	FY98	0
Cumulative Appropriation		0
Expenditures/ Encumbrances		0
Unencumbered Balance		0
Capitalization Thru	FY96	0
New Capitalization	FY97	0
Total Capitalization		0

COORDINATION

MAP

1 2 3 4 5 6

Background

The Project Description Form (PDF) is the official, county-authorized budget form that is used for many purposes in the capital budget and the CIP. A PDF is assigned to a project in its earliest planning stages and remains the document of record until the project is closed out. The PDF is used for recommending planning, requesting and documenting appropriations and expenditure schedules, estimating operating budget impact, and providing a description and justification for the project. Because most projects span multiple years, from initial planning to project close out, the PDF may be revised many times by the County Council throughout all phases of the project.

SAMPLE FORM (999999) - Approved Data

PDF - Page 1

#2 - MCPS CIP amendments and Capital Budget: this resolution requires 6 affirmative votes.

Resolution No.: 18-142
Introduced: May 21, 2015
Adopted: May 21, 2015

COUNTY COUNCIL
FOR MONTGOMERY COUNTY, MARYLAND

By: County Council

SUBJECT: Approval of Amendments to the Approved FY 2015-2020 Capital Improvements Program, and Approval of and Appropriation for the FY 2016 Capital Budget of the Montgomery County Public School System

Background

1. As required by the Education Article, Sections 5-306, 5-101, and 5-102 of the Maryland Code, the Board of Education sent to the County Executive a FY 2016 capital budget and amendments to the approved FY 2015-2020 capital improvements program for the Montgomery County Public School system.

2. Section 302 of the County Charter requires the County Executive to send to the County Council by January 15 in each even-numbered calendar year a six-year capital improvements program, which the County Executive did on January 15, 2014 for the six year period FY 2015-2020. Section 302 requires the affirmative vote of at least 5 Councilmembers to approve or modify the Executive's Recommended Capital Improvements Program. On May 22, 2014, the Council approved a Capital Improvements Program for FY 2015-2020 in Resolution 17-1103. After the Council approves a Capital Improvements Program, Section 302 permits the Council to amend it at any time with the affirmative vote of at least 6 Councilmembers.

3. Section 303 of the County Charter requires the County Executive to send to the County Council by January 15 in each year a recommended capital budget, which the County Executive did on January 15, 2015 for FY 2016. The Executive also made recommendations with regard to the Board of Education's requested amendments to the approved FY 2015-2020 Capital Improvements Program in his transmittal dated January 15, 2015.

4. As required by Section 304 of the County Charter, the County Council held public hearings on February 24, April 14, 15, 16, and May 12 on the capital budget for FY 2016 and on requested amendments to the Approved Capital Improvements Program for FY 2015-2020.

Action

The County Council for Montgomery County, Maryland approves the following resolution:

1. For FY 2016, the Council approves the capital budget of the Montgomery County Public Schools and appropriates the amounts by project which is shown in part I.

2. The expenditure of funds for each item in the capital budget must comply with all restrictions and requirements in the project description form for that item, as the form is contained in the approved Capital Improvements Program as amended by this resolution, and as the Capital Improvements Program is amended by the Council under Charter Section 302 after this resolution is adopted.

3. This resolution reappropriates the appropriations made in prior years for all capital projects:
   a) except as specifically reflected elsewhere in this resolution;
   b) in the amounts and for the purposes specified in the approved Capital Improvements Program for FY 2015-2020; and
   c) to the extent that those appropriations are not expended or encumbered.

4. The Council approves those projects shown in Part II as amendments to the Approved FY 2015-2020 Capital Improvements Program.

5. The Council approves the close out of the projects in part III.

6. The Council approves the partial closeout of the projects in part IV.

7. If a sign recognizing the contribution of any Federal, State, or local government or agency is displayed at any project for which funds are appropriated in this resolution, as a condition of spending those funds each sign must also expressly recognize the contribution of the County and the County's taxpayers.

This is a correct copy of Council action.

Linda M. Lauer

Linda M. Lauer, Clerk of the Council

PART I: FY2016 CAPITAL BUDGET FOR

Montgomery County Public Schools

The appropriation for FY 2016 in this Part are made to implement the projects in the Capital Improvements Program for FY 2015 - 2020. When the total appropriation for a project includes State funds, the total appropriation for the project is contingent on the availability of funds from the State.

Project Title (Project #)	FY 16 Appropriation	Cumulative Appropriation	Total Appropriation
Clarksburg/Damascus MS (New) (P116506)	1,400,000	51,364,000	52,764,000
Bethesda-Chevy Chase MS #2 (P136502)	47,916,000	2,698,000	50,614,000
Julius West MS Addition (P136507)	688,000	14,615,000	15,303,000
Wood Acres ES Addition (P136508)	342,000	8,264,000	8,606,000
Sargent Shriver ES Addition (DCC Solution) (P651501)	341,000	0	341,000
Kemp Mill ES Addition (DCC Solution) (P651506)	774,000	0	774,000
Highland ES Addition (DCC Solution) (P651508)	713,000	0	713,000
Glen Haven ES Addition (DCC Solution) (P651509)	367,000	0	367,000
Brookhaven ES Addition (DCC Solution) (P651512)	481,000	0	481,000
Indoor Air Quality Improvements: MCPS (P006503)	2,147,000	19,926,000	22,073,000
Fire Safety Code Upgrades (P016532)	2,000,000	10,215,000	12,215,000
Technology Modernization (P036510)	23,538,000	185,795,000	209,333,000
Restroom Renovations (P056501)	1,000,000	10,735,000	11,735,000
Building Modifications and Program Improvements (P076506)	3,500,000	25,994,000	29,494,000
Design and Construction Management (P746032)	4,900,000	41,275,000	46,175,000
Roof Replacement: MCPS (P766995)	8,000,000	32,356,000	40,356,000
Energy Conservation: MCPS (P796222)	2,057,000	19,465,000	21,522,000
ADA Compliance: MCPS (P796235)	3,000,000	16,593,000	19,593,000
HVAC (Mechanical Systems) Replacement: MCPS (P816633)	16,000,000	70,967,000	86,967,000
Asbestos Abatement: MCPS (P816695)	1,145,000	9,795,000	10,940,000
Planned Life Cycle Asset Repl: MCPS (P896586)	9,750,000	64,651,000	74,401,000
Stormwater Discharge & Water Quality Mgmt: MCPS (P956550)	616,000	6,287,000	6,903,000
Facility Planning: MCPS (P966553)	550,000	8,307,000	8,857,000
Improved (Safe) Access to Schools (P975051)	1,200,000	9,143,000	10,343,000
Current Revitalizations/Expansions(P926575)	168,639,000	676,002,000	844,641,000
Shady Grove Transportation Depot Replacement (P651641)	700,000	0	700,000
Montgomery County Public Schools	**301,764,000**	**1,284,447,000**	**1,586,211,000**

Arcola ES Addition (P136500)

Category	Montgomery County Public Schools	Date Last Modified	11/17/14
Sub Category	Individual Schools	Required Adequate Public Facility	No
Administering Agency	Public Schools (AAGE18)	Relocation Impact	None
Planning Area	Silver Spring	Status	Planning Stage

	Total	Thru FY14	Rem FY14	Total 6 Years	FY 15	FY 16	FY 17	FY 18	FY 19	FY 20	Beyond 6 Yrs
EXPENDITURE SCHEDULE ($000s)											
Planning, Design and Supervision	281	141	84	56	56	0	0	0	0	0	0
Land	0	0	0	0	0	0	0	0	0	0	0
Site Improvements and Utilities	543	0	434	109	109	0	0	0	0	0	0
Construction	2,887	0	578	2,309	866	1,443	0	0	0	0	0
Other	130	0	0	130	26	104	0	0	0	0	0
Total	**3,841**	**141**	**1,096**	**2,604**	**1,057**	**1,547**	**0**	**0**	**0**	**0**	**0**
FUNDING SCHEDULE ($000s)											
G.O. Bonds	3,804	141	1,096	2,567	1,057	1,510	0	0	0	0	0
School Facilities Payment	37	0	0	37	0	37	0	0	0	0	0
Total	**3,841**	**141**	**1,096**	**2,604**	**1,057**	**1,547**	**0**	**0**	**0**	**0**	**0**
OPERATING BUDGET IMPACT ($000s)											
Energy				80	0	16	16	16	16	16	
Maintenance				220	0	44	44	44	44	44	
Net Impact				**300**	**0**	**60**	**60**	**60**	**60**	**60**	

APPROPRIATION AND EXPENDITURE DATA (000s)

Appropriation Request	FY 16	0
Supplemental Appropriation Request		0
Transfer		0
Cumulative Appropriation		3,841
Expenditure / Encumbrances		141
Unencumbered Balance		3,700

Date First Appropriation FY 13	
First Cost Estimate	
Current Scope	0
Last FY's Cost Estimate	3,841

Description

Enrollment projections at Arcola Elementary School reflect a need for an addition. Arcola Elementary School has a program capacity for 486 students. Enrollment is expected to reach 745 students by the 2015-2016 school year. A feasibility study was conducted in FY 2011 to determine the cost and scope of the project. An FY 2013 appropriation was approved to begin planning this addition. An FY 2014 appropriation was approved for construction funds. An FY 2015 appropriation was approved to complete this project. This project is scheduled to be completed by August 2015.

Capacity

Program Capacity After Addition: 624

Coordination

Mandatory Referral - M-NCPPC, Department of Environmental Protection, Building Permits, Code Review, Fire Marshall, Department of Transportation, Inspections, Sediment Control, Stormwater Management, WSSC Permits

Ashburton ES Addition (P651514)

Category	Montgomery County Public Schools	Date Last Modified	11/17/14
Sub Category	Individual Schools	Required Adequate Public Facility	No
Administering Agency	Public Schools (AAGE18)	Relocation Impact	None
Planning Area	Rockville	Status	Planning Stage

	Total	Thru FY14	Rem FY14	Total 6 Years	FY 15	FY 16	FY 17	FY 18	FY 19	FY 20	Beyond 6 Yrs
EXPENDITURE SCHEDULE ($000s)											
Planning, Design and Supervision	640	0	0	640	0	0	256	192	128	64	0
Land	0	0	0	0	0	0	0	0	0	0	0
Site Improvements and Utilities	1,657	0	0	1,165	0	0	0	0	874	291	492
Construction	4,777	0	0	3,137	0	0	0	0	986	2,151	1,640
Other	147	0	0	147	0	0	0	0	0	147	0
Total	**7,221**	**0**	**0**	**5,089**	**0**	**0**	**256**	**192**	**1,988**	**2,653**	**2,132**
FUNDING SCHEDULE ($000s)											
G.O. Bonds	7,221	0	0	5,089	0	0	256	192	1,988	2,653	2,132
Total	**7,221**	**0**	**0**	**5,089**	**0**	**0**	**256**	**192**	**1,988**	**2,653**	**2,132**

APPROPRIATION AND EXPENDITURE DATA (000s)

Appropriation Request	FY 16	0
Supplemental Appropriation Request		0
Transfer		0
Cumulative Appropriation		0
Expenditure / Encumbrances		0
Unencumbered Balance		0

Date First Appropriation	
First Cost Estimate	
Current Scope	7,221
Last FY's Cost Estimate	7,221

Description

Enrollment projections at Ashburton Elementary School reflect a need for an addition. Ashburton Elementary School has a program capacity for 628 students. Enrollment is expected to reach 835 students by the 2020-2021 school year. A feasibility study was conducted in FY 2013 to determine the cost and scope of the project. In the approved FY 2015-2020 CIP, while the planning funds for this project remain on the schedule requested by the Board of Education, due to fiscal constraints, the construction funds were programmed one year later, with a completion date of August 2020. The Board of Education's requested FY2015-2020 Amended CIP reinstated the construction schedule previously requested by the Board. Due to fiscal constraints, the County Council did not approve the Board's request. An FY 2017 appropriation will be requested for planning funds. This project is scheduled to be completed August 2020.

Disclosures

Coordination

Mandatory Referral - M-NCPPC, Department of Environmental Protection, Building Permits:, Code Review, Fire Marshall, Department of Transportation, Inspections, Sediment Control, Stormwater Management, WSSC Permits

Lucy V. Barnsley ES Addition (P651504)

Category	Montgomery County Public Schools	Date Last Modified	11/17/14
Sub Category	Individual Schools	Required Adequate Public Facility	No
Administering Agency	Public Schools (AAGE18)	Relocation Impact	None
Planning Area	Rockville	Status	Planning Stage

	Total	Thru FY14	Rem FY14	Total 6 Years	FY 15	FY 16	FY 17	FY 18	FY 19	FY 20	Beyond 6 Yrs
EXPENDITURE SCHEDULE ($000s)											
Planning, Design and Supervision	1,156	0	0	1,156	462	347	231	116	0	0	0
Land	0	0	0	0	0	0	0	0	0	0	0
Site Improvements and Utilities	1,660	0	0	1,660	0	0	1,245	415	0	0	0
Construction	9,349	0	0	9,349	0	0	1,870	6,545	934	0	0
Other	809	0	0	809	0	0	0	243	566	0	0
Total	**12,974**	**0**	**0**	**12,974**	**462**	**347**	**3,346**	**7,319**	**1,500**	**0**	**0**
FUNDING SCHEDULE ($000s)											
G.O. Bonds	10,922	0	0	10,922	450	0	3,346	5,626	1,500	0	0
School Facilities Payment	12	0	0	12	12	0	0	0	0	0	0
Schools Impact Tax	2,040	0	0	2,040	0	347	0	1,693	0	0	0
Total	**12,974**	**0**	**0**	**12,974**	**462**	**347**	**3,346**	**7,319**	**1,500**	**0**	**0**
OPERATING BUDGET IMPACT ($000s)											
Energy				94	0	0	0	0	47	47	
Maintenance				230	0	0	0	0	115	115	
Net Impact				**324**	**0**	**0**	**0**	**0**	**162**	**162**	

APPROPRIATION AND EXPENDITURE DATA (000s)

Appropriation Request	FY 16	0
Supplemental Appropriation Request		0
Transfer		0
Cumulative Appropriation		1,156
Expenditure / Encumbrances		0
Unencumbered Balance		1,156

Date First Appropriation FY 16	
First Cost Estimate	
Current Scope	12,974
Last FY's Cost Estimate	12,974

Description

Enrollment projections at Lucy V. Barnsley Elementary School reflect a need for an addition. Lucy V. Barnsley Elementary School has a program capacity for 411 students. Enrollment is expected to reach 619 students by the 2020-2021 school year. A feasibility study was conducted in FY 2013 to determine the cost and scope of the project. An FY 2015 appropriation was approved to begin planning this addition. While the planning funds remain on the schedule requested by the Board of Education, due to fiscal constraints, the construction funds were programmed one year later in the approved FY 2015-2020 CIP, with a completion date of August 2018. The Board of Education's requested FY 2015-2020 Amended CIP reinstated the construction schedule previoulsy requested by the Board. Due to fiscal constraints, the County Council did not approve the Board's request. An FY 2017 appropriation will be requested for construction funds. This project is scheduled to be completed by August 2018.

Disclosures

Coordination

Mandatory Referral - M-NCPPC, Department of Environmental Protection, Building Permits:, Code Review, Fire Marshall, Department of Transportation, Inspections, Sediment Control, Stormwater Management, WSSC Permits

Bethesda ES Addition (P136501)

Category	Montgomery County Public Schools	Date Last Modified	4/21/14
Sub Category	Individual Schools	Required Adequate Public Facility	No
Administering Agency	Public Schools (AAGE18)	Relocation Impact	None
Planning Area	Bethesda-Chevy Chase	Status	Planning Stage

	Total	Thru FY14	Rem FY14	Total 6 Years	FY 15	FY 16	FY 17	FY 18	FY 19	FY 20	Beyond 6 Yrs
EXPENDITURE SCHEDULE ($000s)											
Planning, Design and Supervision	286	143	86	57	57	0	0	0	0	0	0
Land	0	0	0	0	0	0	0	0	0	0	0
Site Improvements and Utilities	632	0	506	126	126	0	0	0	0	0	0
Construction	2,881	0	576	2,305	864	1,441	0	0	0	0	0
Other	171	0	0	171	35	136	0	0	0	0	0
Total	**3,970**	**143**	**1,168**	**2,659**	**1,082**	**1,577**	**0**	**0**	**0**	**0**	**0**
FUNDING SCHEDULE ($000s)											
G.O. Bonds	3,970	143	1,168	2,659	1,082	1,577	0	0	0	0	0
Total	**3,970**	**143**	**1,168**	**2,659**	**1,082**	**1,577**	**0**	**0**	**0**	**0**	**0**
OPERATING BUDGET IMPACT ($000s)											
Energy				45	0	9	9	9	9	9	
Maintenance				120	0	24	24	24	24	24	
Net Impact				**165**	**0**	**33**	**33**	**33**	**33**	**33**	

APPROPRIATION AND EXPENDITURE DATA (000s)

Appropriation Request	FY 16	0
Supplemental Appropriation Request		0
Transfer		0
Cumulative Appropriation		3,970
Expenditure / Encumbrances		143
Unencumbered Balance		3,827

Date First Appropriation FY 13	
First Cost Estimate	
Current Scope	0
Last FY's Cost Estimate	3,970

Description

Enrollment projections at Bethesda Elementary School reflect a need for an addition. Bethesda Elementary School has a program capacity for 384 students. Enrollment is expected to reach 515 students by the 2015-2016 school year. A feasibility study was conducted in FY 2011 to determine the cost and scope of the project. An FY 2013 appropriation was approved to begin planning this addition. An FY 2014 appropriation was approved for construction funds. An FY 2015 appropriation was approved to complete this project. This project is scheduled to be completed by August 2015.

Capacity

Program Capacity After Addition: 568

Coordination

Mandatory Referral - M-NCPPC, Department of Environmental Protection, Building Permits, Code Review, Fire Marshall, Department of Transportation, Inspections, Sediment Control, Stormwater Management, WSSC Permits

Bethesda-Chevy Chase HS Addition (P651513)

Category	Montgomery County Public Schools	Date Last Modified	11/17/14
Sub Category	Individual Schools	Required Adequate Public Facility	No
Administering Agency	Public Schools (AAGE18)	Relocation Impact	None
Planning Area	Bethesda-Chevy Chase	Status	Planning Stage

	Total	Thru FY14	Rem FY14	Total 6 Years	FY 15	FY 16	FY 17	FY 18	FY 19	FY 20	Beyond 6 Yrs
EXPENDITURE SCHEDULE ($000s)											
Planning, Design and Supervision	2,808	0	0	2,808	1,123	842	562	281	0	0	0
Land	0	0	0	0	0	0	0	0	0	0	0
Site Improvements and Utilities	5,170	0	0	5,170	0	0	3,878	1,292	0	0	0
Construction	21,569	0	0	21,569	0	0	3,314	10,099	8,156	0	0
Other	1,240	0	0	1,240	0	0	0	372	868	0	0
Total	**30,787**	**0**	**0**	**30,787**	**1,123**	**842**	**7,754**	**12,044**	**9,024**	**0**	**0**
FUNDING SCHEDULE ($000s)											
G.O. Bonds	27,572	0	0	27,572	698	691	7,754	9,405	9,024	0	0
School Facilities Payment	576	0	0	576	425	151	0	0	0	0	0
Schools Impact Tax	2,639	0	0	2,639	0	0	0	2,639	0	0	0
Total	**30,787**	**0**	**0**	**30,787**	**1,123**	**842**	**7,754**	**12,044**	**9,024**	**0**	**0**
OPERATING BUDGET IMPACT ($000s)											
Energy				250	0	0	0	0	125	125	
Maintenance				608	0	0	0	0	304	304	
Net Impact				**858**	**0**	**0**	**0**	**0**	**429**	**429**	

APPROPRIATION AND EXPENDITURE DATA (000s)

Appropriation Request	FY 16	0
Supplemental Appropriation Request		0
Transfer		0
Cumulative Appropriation		2,808
Expenditure / Encumbrances		0
Unencumbered Balance		2,808

Date First Appropriation FY 15	
First Cost Estimate	
Current Scope	30,787
Last FY's Cost Estimate	30,787

Description

Enrollment projections at Bethesda-Chevy Chase High School reflect a need for an addition. Bethesda-Chevy Chase High School has a program capacity for 1692 students. Enrollment is expected to reach 2286 students by the 2019-2020 school year. A feasibility study was conducted in FY 2013 to determine the cost and scope of the project. An FY 2015 appropriation was approved to begin planning this addition. While the planning funds for this project remain on the schedule requested by the Board of Education, due to fiscal constraints, the construction funds were programmed one year later in the approved FY 2015-2020 CIP. The Board of Education's requested FY 2015-2020 Amended CIP reinstated the construction schedule previously requested by the Board. Due to fiscal constraints, the County Council did not approve the Board's request. An FY 2017 appropriation will be requested for construction funds. This project is scheduled to be completed August 2018.

Disclosures

Coordination

Mandatory Referral - M-NCPPC, Department of Environmental Protection, Building Permits:, Code Review, Fire Marshall, Department of Transportation, Inspections, Sediment Control, Stormwater Management, WSSC Permits

Bethesda-Chevy Chase MS #2 (P136502)

Category	Montgomery County Public Schools	Date Last Modified	11/17/14
Sub Category	Individual Schools	Required Adequate Public Facility	No
Administering Agency	Public Schools (AAGE18)	Relocation Impact	None
Planning Area	Bethesda-Chevy Chase	Status	Planning Stage

	Total	Thru FY14	Rem FY14	Total 6 Years	FY 15	FY 16	FY 17	FY 18	FY 19	FY 20	Beyond 6 Yrs
EXPENDITURE SCHEDULE ($000s)											
Planning, Design and Supervision	2,698	0	250	2,448	829	809	540	270	0	0	0
Land	0	0	0	0	0	0	0	0	0	0	0
Site Improvements and Utilities	8,705	0	0	8,705	0	6,529	2,176	0	0	0	0
Construction	39,211	0	0	39,211	0	5,843	29,448	3,920	0	0	0
Other	1,700	0	0	1,700	0	0	510	1,190	0	0	0
Total	**52,314**	**0**	**250**	**52,064**	**829**	**13,181**	**32,674**	**5,380**	**0**	**0**	**0**
FUNDING SCHEDULE ($000s)											
G.O. Bonds	11,694	0	250	11,444	829	360	10,100	155	0	0	0
Schools Impact Tax	40,620	0	0	40,620	0	12,821	22,574	5,225	0	0	0
Total	**52,314**	**0**	**250**	**52,064**	**829**	**13,181**	**32,674**	**5,380**	**0**	**0**	**0**

APPROPRIATION AND EXPENDITURE DATA (000s)

Appropriation Request	FY 16	47,916
Supplemental Appropriation Request		0
Transfer		0
Cumulative Appropriation		2,698
Expenditure / Encumbrances		0
Unencumbered Balance		2,698

Date First Appropriation FY 15	
First Cost Estimate	
Current Scope	0
Last FY's Cost Estimate	52,314

Description

Enrollment projections at Westland Middle School and the plan to reassign Grade 6 students from Chevy Chase and North Chevy Chase elementary schools to the middle school level, will result in a total cluster middle school enrollment of approximately 1,600 students. This projected enrollment would far exceed the current capacity of Westland Middle School. Therefore, a new middle school is needed in the cluster to accommodate the projected enrollment. A feasibility study was conducted to determine the cost and scope of the project. An FY 2014 appropriation was approved to begin planning this new school. An FY 2016 appropriation was approved for construction funds. This project is scheduled to be completed by August 2017.

Capacity

Program Capacity: 944

Coordination

Mandatory Referral - M-NCPPC, Department of Environmental Protection, Building Permits, Code Review, Fire Marshall, Department of Transportation, Inspections, Sediment Control, Stormwater Management, WSSC Permits

Brookhaven ES Addition (DCC Solution) (P651512)

Category	Montgomery County Public Schools	Date Last Modified	11/17/14
Sub Category	Individual Schools	Required Adequate Public Facility	No
Administering Agency	Public Schools (AAGE18)	Relocation Impact	#MISSING
Planning Area	Silver Spring	Status	Planning Stage

	Total	Thru FY14	Rem FY14	Total 6 Years	FY 15	FY 16	FY 17	FY 18	FY 19	FY 20	Beyond 6 Yrs
EXPENDITURE SCHEDULE ($000s)											
Planning, Design and Supervision	481	0	0	481	0	192	144	96	49	0	0
Land	0	0	0	0	0	0	0	0	0	0	0
Site Improvements and Utilities	826	0	0	826	0	0	0	620	206	0	0
Construction	3,754	0	0	3,754	0	0	0	751	1,878	1,125	0
Other	320	0	0	320	0	0	0	0	96	224	0
Total	**5,381**	**0**	**0**	**5,381**	**0**	**192**	**144**	**1,467**	**2,229**	**1,349**	**0**
FUNDING SCHEDULE ($000s)											
G.O. Bonds	5,381	0	0	5,381	0	192	144	1,467	2,229	1,349	0
Total	**5,381**	**0**	**0**	**5,381**	**0**	**192**	**144**	**1,467**	**2,229**	**1,349**	**0**
OPERATING BUDGET IMPACT ($000s)											
Energy				22	0	0	0	0	0	22	
Maintenance				53	0	0	0	0	0	53	
Net Impact				**75**	**0**	**0**	**0**	**0**	**0**	**75**	

APPROPRIATION AND EXPENDITURE DATA (000s)

Appropriation Request	FY 16	481
Supplemental Appropriation Request		0
Transfer		0
Cumulative Appropriation		0
Expenditure / Encumbrances		0
Unencumbered Balance		0

Date First Appropriation	
First Cost Estimate	
Current Scope	5,381
Last FY's Cost Estimate	5,381

Description

A comprehensive capacity study to address overutilization at several elementary schools in the midsection of the Downcounty Consortium was conducted during the 2012-2013 school year. The following elementary schools were included in the study: Arcola, Brookhaven, Forest Knolls, Georgian Forest, Glen Haven, Glenallan, Harmony Hills, Highland, Kemp Mill, Sargent Shriver, Weller Road and Wheaton Woods. Based on the outcome of the study, additions will be constructed at the following elementary schools: Brookhaven, Glen Haven, Highland, Kemp MIll, and Sargent Shriver. While the planning funds for this project remain on the schedule requested by the Board of Education, due to fiscal constraints, the construction funds were programmed one year later in the approved FY 2015-2020 CIP. The Board of Education's requested FY 2015-2020 Amended CIP reinstated the construction schedule previously requested by the Board. Due to fiscal constraints, the County Council did not approve the Board's request. An FY 2016 appropriation was approved for planning. This project is scheduled to be completed August 2019.

Disclosures

Coordination

Mandatory Referral - M-NCPPC, Department of Environmental Protection, Building Permits:, Code Review, Fire Marshall, Department of Transportation, Inspections, Sediment Control, Stormwater Management, WSSC Permits

Burtonsville ES Addition (P651511)

Category	Montgomery County Public Schools	Date Last Modified	11/17/14
Sub Category	Individual Schools	Required Adequate Public Facility	No
Administering Agency	Public Schools (AAGE18)	Relocation Impact	None
Planning Area	Colesville-White Oak	Status	Planning Stage

	Total	Thru FY14	Rem FY14	Total 6 Years	FY 15	FY 16	FY 17	FY 18	FY 19	FY 20	Beyond 6 Yrs
EXPENDITURE SCHEDULE ($000s)											
Planning, Design and Supervision	1,172	0	0	1,172	0	0	469	352	234	117	0
Land	0	0	0	0	0	0	0	0	0	0	0
Site Improvements and Utilities	2,013	0	0	2,013	0	0	0	0	1,510	503	0
Construction	9,149	0	0	6,435	0	0	0	0	1,830	4,605	2,714
Other	484	0	0	146	0	0	0	0	0	146	338
Total	**12,818**	**0**	**0**	**9,766**	**0**	**0**	**469**	**352**	**3,574**	**5,371**	**3,052**
FUNDING SCHEDULE ($000s)											
G.O. Bonds	5,991	0	0	2,939	0	0	0	352	1,801	786	3,052
Schools Impact Tax	6,827	0	0	6,827	0	0	469	0	1,773	4,585	0
Total	**12,818**	**0**	**0**	**9,766**	**0**	**0**	**469**	**352**	**3,574**	**5,371**	**3,052**

APPROPRIATION AND EXPENDITURE DATA (000s)

Appropriation Request	FY 16	0
Supplemental Appropriation Request		0
Transfer		0
Cumulative Appropriation		0
Expenditure / Encumbrances		0
Unencumbered Balance		0

Date First Appropriation FY 16	
First Cost Estimate	
Current Scope	12,818
Last FY's Cost Estimate	12,818

Description

Enrollment projections at Burtonsville Elementary School reflect a need for an addition. Burtonsville Elementary School has a program capacity for 502 students. Enrollment is expected to reach 672 students by the 2019-2020 school year. A feasibility study was conducted in FY 2013 to determine the cost and scope of the project. While the planning funds remain on the schedule requested by the Board of Education, due to fiscal constraints, the construction funds were programmed one year later in the approved FY 2015-2020 CIP. The Board of Education's requested FY 2015-2020 Amended CIP reinstated the construction schedule previously requested by the Board. Due to fiscal constraints, the County Council did not approve the Board's request. An FY 2017 appropriation will be requested for planning funds. This project is scheduled to be completed by August 2020.

Disclosures

Coordination

Mandatory Referral - M-NCPPC, Department of Environmental Protection, Building Permits:, Code Review, Fire Marshall, Department of Transportation, Inspections, Sediment Control, Stormwater Management, WSSC Permits

Clarksburg Cluster ES (Clarksburg Village Site #1) (P116504)

Category	Montgomery County Public Schools	Date Last Modified	11/17/14
Sub Category	Individual Schools	Required Adequate Public Facility	No
Administering Agency	Public Schools (AAGE18)	Relocation Impact	None
Planning Area	Clarksburg	Status	Planning Stage

	Total	Thru FY14	Rem FY14	Total 6 Years	FY 15	FY 16	FY 17	FY 18	FY 19	FY 20	Beyond 6 Yrs
EXPENDITURE SCHEDULE ($000s)											
Planning, Design and Supervision	1,567	1,254	313	0	0	0	0	0	0	0	0
Land	0	0	0	0	0	0	0	0	0	0	0
Site Improvements and Utilities	3,998	1,599	1,599	800	800	0	0	0	0	0	0
Construction	21,703	4,341	6,511	10,851	10,851	0	0	0	0	0	0
Other	950	0	190	760	760	0	0	0	0	0	0
Total	**28,218**	**7,194**	**8,613**	**12,411**	**12,411**	**0**	**0**	**0**	**0**	**0**	**0**
FUNDING SCHEDULE ($000s)											
Current Revenue: Recordation Tax	65	0	0	65	65	0	0	0	0	0	0
G.O. Bonds	6,514	2,610	3,613	291	291	0	0	0	0	0	0
Schools Impact Tax	21,639	4,584	5,000	12,055	12,055	0	0	0	0	0	0
Total	**28,218**	**7,194**	**8,613**	**12,411**	**12,411**	**0**	**0**	**0**	**0**	**0**	**0**

APPROPRIATION AND EXPENDITURE DATA (000s)

Appropriation Request	FY 16	0
Supplemental Appropriation Request		0
Transfer		0
Cumulative Appropriation		28,218
Expenditure / Encumbrances		7,194
Unencumbered Balance		21,024

Date First Appropriation FY 16	
First Cost Estimate	
Current Scope	0
Last FY's Cost Estimate	28,218

Description

The Clarksburg Master Plan, approved in 1994, allows for the potential development of 15,000 housing units. Development of this community resulted in the formation of a new cluster of schools. Elementary school enrollment projections in the Clarksburg Cluster continue to increase dramatically throughout the FY 2011-2016 six-year CIP. This continued growth justifies the need for the opening of another elementary school in the Clarsksburg Cluster. The new elementary school is intended to relieve overutilization at Cedar Grove, Clarksburg, and Little Bennett elementary schools. An FY 2011 appropriation was requested for planning funds in the Board of Education's FY 2011-2016 CIP. However, due to fiscal constraints, the County Council, in the adopted FY 2011-2016 CIP, delayed this project one year. An FY 2012 appropriation was approved for planning funds. An FY 2013 appropriation was approved for construction funds. An FY 2014 appropriation was approved to complete this project. The project is now scheduled to be completed by August 2014.

Capacity

Program Capacity After Project: 740

Disclosures

Clarksburg HS Addition (P116505)

Category	Montgomery County Public Schools	Date Last Modified	11/17/14
Sub Category	Individual Schools	Required Adequate Public Facility	No
Administering Agency	Public Schools (AAGE18)	Relocation Impact	None
Planning Area	Clarksburg	Status	Planning Stage

	Total	Thru FY14	Rem FY14	Total 6 Years	FY 15	FY 16	FY 17	FY 18	FY 19	FY 20	Beyond 6 Yrs
EXPENDITURE SCHEDULE ($000s)											
Planning, Design and Supervision	755	377	226	152	152	0	0	0	0	0	0
Land	0	0	0	0	0	0	0	0	0	0	0
Site Improvements and Utilities	1,492	0	1,194	298	298	0	0	0	0	0	0
Construction	9,047	0	1,809	7,238	2,714	4,524	0	0	0	0	0
Other	529	0	0	529	105	424	0	0	0	0	0
Total	**11,823**	**377**	**3,229**	**8,217**	**3,269**	**4,948**	**0**	**0**	**0**	**0**	**0**
FUNDING SCHEDULE ($000s)											
G.O. Bonds	1,551	377	229	945	0	945	0	0	0	0	0
School Facilities Payment	3	0	0	3	0	3	0	0	0	0	0
Schools Impact Tax	10,269	0	3,000	7,269	3,269	4,000	0	0	0	0	0
Total	**11,823**	**377**	**3,229**	**8,217**	**3,269**	**4,948**	**0**	**0**	**0**	**0**	**0**
OPERATING BUDGET IMPACT ($000s)											
Energy				400	0	80	80	80	80	80	
Maintenance				760	0	152	152	152	152	152	
Net Impact				**1,160**	**0**	**232**	**232**	**232**	**232**	**232**	

APPROPRIATION AND EXPENDITURE DATA (000s)

Appropriation Request	FY 16	0
Supplemental Appropriation Request		0
Transfer		0
Cumulative Appropriation		11,823
Expenditure / Encumbrances		377
Unencumbered Balance		11,446

Date First Appropriation FY 13	
First Cost Estimate	
Current Scope	0
Last FY's Cost Estimate	11,823

Description

The Clasrksburg Master Plan, approved in 1994, allows for the potential development of 15,000 housing units. Development of this community resulted in the formation of a new cluster of schools. Enrollment projections at Clarksburg High School reflect a need for an 18-classroom addition. Clarksburg High School has a program capacity for 1,566 students. Enrollment is expected to reach 1,958 students by the 2014-2015 school year. A feasibility study was conducted in FY 2009 to determine the cost and scope of the project. An FY 2012 appropriation was included in the Board of Education's FY 2011-2016 CIP to begin planning this addition project. However, due to fiscal constraints, the County Council adopted FY 2011-2016 CIP delayed this project one year, from August 2014 to August 2015. An FY 2013 appropriation was approved to begin planning this addition project. An FY 2014 appropriation was approved for construction funds. An FY 2015 appropriation was approved to complete this project. This addition is scheduled to be completed by August 2015.

Capacity

Program Capacity after Project: 1,971

Coordination

Mandatory Referral - M-NCPPC, Department of Environment Protection, Building Permits, Code Review, Fire Marshall, Department of Transportation, Inspections, Sediment Control, Stormwater Management, WSSC Permits

Clarksburg/Damascus MS (New) (P116506)

Category	Montgomery County Public Schools	Date Last Modified	11/17/14
Sub Category	Individual Schools	Required Adequate Public Facility	No
Administering Agency	Public Schools (AAGE18)	Relocation Impact	None
Planning Area	Clarksburg	Status	Planning Stage

	Total	Thru FY14	Rem FY14	Total 6 Years	FY 15	FY 16	FY 17	FY 18	FY 19	FY 20	Beyond 6 Yrs
EXPENDITURE SCHEDULE ($000s)											
Planning, Design and Supervision	2,631	200	1,107	1,324	784	540	0	0	0	0	0
Land	0	0	0	0	0	0	0	0	0	0	0
Site Improvements and Utilities	7,690	0	0	7,690	5,514	2,176	0	0	0	0	0
Construction	40,813	0	0	40,813	6,335	27,020	7,458	0	0	0	0
Other	1,630	0	0	1,630	0	510	1,120	0	0	0	0
Total	**52,764**	**200**	**1,107**	**51,457**	**12,633**	**30,246**	**8,578**	**0**	**0**	**0**	**0**
FUNDING SCHEDULE ($000s)											
Current Revenue: Recordation Tax	17,086	0	0	17,086	0	16,086	1,000	0	0	0	0
G.O. Bonds	12,102	200	0	11,902	1,508	2,816	7,578	0	0	0	0
Schools Impact Tax	23,576	0	1,107	22,469	11,125	11,344	0	0	0	0	0
Total	**52,764**	**200**	**1,107**	**51,457**	**12,633**	**30,246**	**8,578**	**0**	**0**	**0**	**0**
OPERATING BUDGET IMPACT ($000s)											
Energy				932	0	0	233	233	233	233	
Maintenance				2,504	0	0	626	626	626	626	
Net Impact				**3,436**	**0**	**0**	**859**	**859**	**859**	**859**	

APPROPRIATION AND EXPENDITURE DATA (000s)

Appropriation Request	FY 16	1,400
Supplemental Appropriation Request		0
Transfer		0
Cumulative Appropriation		51,364
Expenditure / Encumbrances		200
Unencumbered Balance		51,164

Date First Appropriation FY 13	
First Cost Estimate	
Current Scope	0
Last FY's Cost Estimate	52,764

Description

The Clasrksburg Master Plan, approved in 1994, allows for the potential development of 15,000 housing units. Development of this community resulted in the formation of a new cluster of schools. Enrollment projections at Rocky Hill Middle School continue to increase dramatically throughout the FY 2011-2016 six-year CIP. This continued growth justifies the need for the opening of another middle school to serve the Clarksburg/Damascus service areas. Rocky Hill Middle School has a program capacity for 939 students. Enrollment is expected to reach 1,411 students by the 2015-2016 school year. A feasibility study was conducted in FY 2009 to determine the cost and scope of the project. The proposed middle school will have a program capacity of 988. Due to fiscal constraints, this project was delayed one year in the adopted FY 2013-2018 CIP. An FY 2013 appropriation was approved to begin planning this new middle school. An FY 2015 appropriation was approved for construction funds. An FY 2016 appropriation was approved to complete this project. This project is scheduled to be completed by August 2016.

Capacity

Program Capacity after Project: 988

Coordination

Mandatory Referral - M-NCPPC, Department of Environment Protection, Building Permits, Code Review, Fire Marshal, Department of Transportation, Inspections, Sediment Control, Stormwater Management, WSSC Permits

Diamond ES Addition (P651510)

Category	Montgomery County Public Schools	Date Last Modified	11/17/14
Sub Category	Individual Schools	Required Adequate Public Facility	No
Administering Agency	Public Schools (AAGE18)	Relocation Impact	None
Planning Area	Gaithersburg	Status	Planning Stage

	Total	Thru FY14	Rem FY14	Total 6 Years	FY 15	FY 16	FY 17	FY 18	FY 19	FY 20	Beyond 6 Yrs
EXPENDITURE SCHEDULE ($000s)											
Planning, Design and Supervision	804	0	0	804	322	241	161	80	0	0	0
Land	0	0	0	0	0	0	0	0	0	0	0
Site Improvements and Utilities	1,531	0	0	1,531	0	0	1,149	382	0	0	0
Construction	6,123	0	0	6,123	0	0	1,225	2,787	2,111	0	0
Other	468	0	0	468	0	0	0	141	327	0	0
Total	**8,926**	**0**	**0**	**8,926**	**322**	**241**	**2,535**	**3,390**	**2,438**	**0**	**0**
FUNDING SCHEDULE ($000s)											
G.O. Bonds	7,250	0	0	7,250	0	0	2,440	2,372	2,438	0	0
School Facilities Payment	658	0	0	658	322	241	95	0	0	0	0
Schools Impact Tax	1,018	0	0	1,018	0	0	0	1,018	0	0	0
Total	**8,926**	**0**	**0**	**8,926**	**322**	**241**	**2,535**	**3,390**	**2,438**	**0**	**0**
OPERATING BUDGET IMPACT ($000s)											
Energy				54	0	0	0	0	27	27	
Maintenance				132	0	0	0	0	66	66	
Net Impact				**186**	**0**	**0**	**0**	**0**	**93**	**93**	

APPROPRIATION AND EXPENDITURE DATA (000s)

Appropriation Request	FY 16	0
Supplemental Appropriation Request		0
Transfer		0
Cumulative Appropriation		804
Expenditure / Encumbrances		0
Unencumbered Balance		804

Date First Appropriation FY 16	
First Cost Estimate	
Current Scope	8,926
Last FY's Cost Estimate	8,926

Description

Enrollment projections at Diamond Elementary School reflect a need for an addition. Diamond Elementary School has a program capacity for 463 students. Enrollment is expected to reach 615 students by the 2020-2021 school year. A feasibility study was conducted in FY 2013 to determine the cost and scope of the project. An FY 2015 appropriation was approved to begin planning this addition. While the planning funds remain on the schedule requested by the Board of Education, due to fiscal constraints, the construction funds were programmed one year later in the approved FY2015-2020 CIP. The Board of Education's requested FY 2015-2020 Amended CIP reinstated the construction schedule previously requested by the Board. Due to fiscal constraints, the County Council did not approve the Board's request. An FY 2017 appropriation will be requested for construction funds. This project is scheduled to be completed by August 2018.

Disclosures

Coordination

Mandatory Referral - M-NCPPC, Department of Environmental Protection, Building Permits:, Code Review, Fire Marshal, Department of Transportation, Inspections, Sediment Control, Stormwater Management, WSSC Permits

Albert Einstein Cluster HS Solution (P651519)

Category	Montgomery County Public Schools	Date Last Modified	11/17/14
Sub Category	Individual Schools	Required Adequate Public Facility	No
Administering Agency	Public Schools (AAGE18)	Relocation Impact	None
Planning Area	Kensington-Wheaton	Status	Planning Stage

	Total	Thru FY14	Rem FY14	Total 6 Years	FY 15	FY 16	FY 17	FY 18	FY 19	FY 20	Beyond 6 Yrs
EXPENDITURE SCHEDULE ($000s)											
Planning, Design and Supervision	177	0	0	177	0	0	0	89	53	35	0
Land	0	0	0	0	0	0	0	0	0	0	0
Site Improvements and Utilities	190	0	0	190	0	0	0	0	152	38	0
Construction	1,757	0	0	1,230	0	0	0	0	351	879	527
Other	210	0	0	42	0	0	0	0	0	42	168
Total	**2,334**	**0**	**0**	**1,639**	**0**	**0**	**0**	**89**	**556**	**994**	**695**
FUNDING SCHEDULE ($000s)											
G.O. Bonds	2,334	0	0	1,639	0	0	0	89	556	994	695
Total	**2,334**	**0**	**0**	**1,639**	**0**	**0**	**0**	**89**	**556**	**994**	**695**

APPROPRIATION AND EXPENDITURE DATA (000s)

Appropriation Request	FY 16	0
Supplemental Appropriation Request		0
Transfer		0
Cumulative Appropriation		0
Expenditure / Encumbrances		0
Unencumbered Balance		0

Date First Appropriation	
First Cost Estimate	
Current Scope	0
Last FY's Cost Estimate	0

Description

Due to increasing enrollment growth, this project includes funds to design and construct six permanent high school classrooms serving Albert Einstein High School in the Downcounty Consortium. These additinal classrooms would meet capacity requirements under the Subdivision Staging Policy, avoiding a residential moratorium in the Albert Einstein Cluster. The County Council anticipates that ultimately, the Board of Education will request a specific project that will add at least these classrooms by the start of the 2020-2021 school year, at the latest, and that these funds would be used towards that purpose.

Blair Ewing Center Improvements (P651515)

Category	Montgomery County Public Schools	Date Last Modified	11/17/14
Sub Category	Individual Schools	Required Adequate Public Facility	#MISSING
Administering Agency	Public Schools (AAGE18)	Relocation Impact	#MISSING
Planning Area	Rockville	Status	#MISSING

	Total	Thru FY14	Rem FY14	Total 6 Years	FY 15	FY 16	FY 17	FY 18	FY 19	FY 20	Beyond 6 Yrs
EXPENDITURE SCHEDULE ($000s)											
Planning, Design and Supervision	1,512	0	0	1,512	605	454	302	151	0	0	0
Land	0	0	0	0	0	0	0	0	0	0	0
Site Improvements and Utilities	350	0	0	350	0	0	263	87	0	0	0
Construction	14,049	0	0	14,049	0	0	2,810	5,835	5,404	0	0
Other	668	0	0	668	0	0	0	201	467	0	0
Total	**16,579**	**0**	**0**	**16,579**	**605**	**454**	**3,375**	**6,274**	**5,871**	**0**	**0**
FUNDING SCHEDULE ($000s)											
G.O. Bonds	16,579	0	0	16,579	605	454	3,375	6,274	5,871	0	0
Total	**16,579**	**0**	**0**	**16,579**	**605**	**454**	**3,375**	**6,274**	**5,871**	**0**	**0**

APPROPRIATION AND EXPENDITURE DATA (000s)

Appropriation Request	FY 16	0
Supplemental Appropriation Request		0
Transfer		0
Cumulative Appropriation		1,512
Expenditure / Encumbrances		0
Unencumbered Balance		1,512

Date First Appropriation FY 15	
First Cost Estimate	
Current Scope	16,579
Last FY's Cost Estimate	16,579

Description

The Blair Ewing Center was assessed as part of the FACT process during the 2010-2011 school year. To address facilities needs at this school, an FY 2013 appropriation for facility planning was approved in the Modifications to Holding, Special Education and Alternative Centers project for a feasibility study to identify improvements for this building. An FY 2015 appropriation was approved to begin planning the modifications to this building. While the planning funds remain on the schedule requested by the Board of Education, due to fiscal constraints, the construction funds were programmed one year later in the approved FY2015-2020 CIP. The Board of Education's requested FY 2015-2020 Amended CIP reinstated the construction schedule previously requested by the Board. Also, the Board of Education's request included a scope change for the Blair Ewing Center. In order to provide the Alternative Education Programs (AEP) with a facility that will support the program and students, the Board's request relocated the AEP from the current site to the English Manor ES site. However, the County Council directed the Board to reevaluate the current Blair G. Ewing site, as well as another site deemed appropriate by the Board for the AEP. Subsequently, the Board directed MCPS staff to reevaluate the current Blair G. Ewing site, as well as other sites owned by the Board of Education. Therefore, the County Council did not approve the Board's request to accelerate the construction funds for this project, but instead kept this project on the approved schedule. An FY 2017 appropriation will be requested for construction funds. This project is scheduled to be completed August 2018.

Coordination

Mandatory Referral - M-NCPPC, Department of Environmental Protection, Building Permits:, Code Review, Fire Marshall, Department of Transportation, Inspections, Sediment Control, Stormwater Management, WSSC Permits

Gaithersburg Cluster ES Solution (P651518)

Category	Montgomery County Public Schools	Date Last Modified	11/17/14
Sub Category	Individual Schools	Required Adequate Public Facility	No
Administering Agency	Public Schools (AAGE18)	Relocation Impact	None
Planning Area	Gaithersburg Vicinity	Status	Planning Stage

	Total	Thru FY14	Rem FY14	Total 6 Years	FY 15	FY 16	FY 17	FY 18	FY 19	FY 20	Beyond 6 Yrs
EXPENDITURE SCHEDULE ($000s)											
Planning, Design and Supervision	294	0	0	294	0	0	0	147	88	59	0
Land	0	0	0	0	0	0	0	0	0	0	0
Site Improvements and Utilities	316	0	0	316	0	0	0	0	253	63	0
Construction	2,928	0	0	2,050	0	0	0	0	586	1,464	878
Other	350	0	0	70	0	0	0	0	0	70	280
Total	**3,888**	**0**	**0**	**2,730**	**0**	**0**	**0**	**147**	**927**	**1,656**	**1,158**
FUNDING SCHEDULE ($000s)											
G.O. Bonds	3,888	0	0	2,730	0	0	0	147	927	1,656	1,158
Total	**3,888**	**0**	**0**	**2,730**	**0**	**0**	**0**	**147**	**927**	**1,656**	**1,158**

APPROPRIATION AND EXPENDITURE DATA (000s)

Appropriation Request	FY 16	0
Supplemental Appropriation Request		0
Transfer		0
Cumulative Appropriation		0
Expenditure / Encumbrances		0
Unencumbered Balance		0

Date First Appropriation	
First Cost Estimate	
Current Scope	0
Last FY's Cost Estimate	0

Description

Due to increasing enrollment growth, this project includes funds to design and construct 10 elementary school classrooms in the Gaithersburg Cluster. These additional classrooms would meet capacity requirements under the Subdivision Staging Policy, avoiding a residential moratorium in the Gaithersburg Cluster. The County Council anticipates that ultimately, the Board of Education will request a specific project that wil add at least these classrooms by the start of the 2020-2021 school year at the latest and these funds would be used towards that purpose.

Glen Haven ES Addition (DCC Solution) (P651509)

Category	Montgomery County Public Schools	Date Last Modified	11/17/14
Sub Category	Individual Schools	Required Adequate Public Facility	No
Administering Agency	Public Schools (AAGE18)	Relocation Impact	None
Planning Area	Silver Spring	Status	Planning Stage

	Total	Thru FY14	Rem FY14	Total 6 Years	FY 15	FY 16	FY 17	FY 18	FY 19	FY 20	Beyond 6 Yrs
EXPENDITURE SCHEDULE ($000s)											
Planning, Design and Supervision	367	0	0	367	0	147	110	73	37	0	0
Land	0	0	0	0	0	0	0	0	0	0	0
Site Improvements and Utilities	905	0	0	905	0	0	0	679	226	0	0
Construction	2,585	0	0	2,585	0	0	0	517	1,060	1,008	0
Other	235	0	0	235	0	0	0	0	71	164	0
Total	**4,092**	**0**	**0**	**4,092**	**0**	**147**	**110**	**1,269**	**1,394**	**1,172**	**0**
FUNDING SCHEDULE ($000s)											
G.O. Bonds	4,092	0	0	4,092	0	147	110	1,269	1,394	1,172	0
Total	**4,092**	**0**	**0**	**4,092**	**0**	**147**	**110**	**1,269**	**1,394**	**1,172**	**0**
OPERATING BUDGET IMPACT ($000s)											
Energy				14	0	0	0	0	0	14	
Maintenance				34	0	0	0	0	0	34	
Net Impact				**48**	**0**	**0**	**0**	**0**	**0**	**48**	

APPROPRIATION AND EXPENDITURE DATA (000s)

Appropriation Request	FY 16	367
Supplemental Appropriation Request		0
Transfer		0
Cumulative Appropriation		0
Expenditure / Encumbrances		0
Unencumbered Balance		0

Date First Appropriation	
First Cost Estimate	
Current Scope	4,092
Last FY's Cost Estimate	4,092

Description

A comprehensive capacity study to address overutilization at several elementary schools in the midsection of the Downcounty Consortium was conducted during the 2012-2013 school year. The following elementary schools were included in the study: Arcola, Brookhaven, Forest Knolls, Georgian Forest, Glen Haven, Glenallan, Harmony Hills, Highland, Kemp Mill, Sargent Shriver, Weller Road and Wheaton Woods. Based on the outcome of the study, additions will be constructed at the following elementary schools: Brookhaven, Glen Haven, Highland, Kemp MIll, and Sargent Shriver. While the planning funds remain on the schedule requested by the Board of Education, due to fiscal constraints, the construction funds were programmed one year later in the approved FY2015-2020 CIP. The Board of Education's requested FY 2015-2020 Amended CIP reinstated the construction schedule previously requested by the Board. Due to fiscal constraints, the County Council did not approve the Board's request. An FY 2016 appropriation was approved for planning funds. This project is scheduled to be completed August 2019.

Disclosures

Coordination

Mandatory Referral - M-NCPPC, Department of Environmental Protection, Building Permits:, Code Review, Fire Marshall, Department of Transportation, Inspections, Sediment Control, Stormwater Management, WSSC Permits

Highland ES Addition (DCC Solution) (P651508)

Category	Montgomery County Public Schools	Date Last Modified	11/17/14
Sub Category	Individual Schools	Required Adequate Public Facility	No
Administering Agency	Public Schools (AAGE18)	Relocation Impact	None
Planning Area	Silver Spring	Status	Planning Stage

	Total	Thru FY14	Rem FY14	Total 6 Years	FY 15	FY 16	FY 17	FY 18	FY 19	FY 20	Beyond 6 Yrs
EXPENDITURE SCHEDULE ($000s)											
Planning, Design and Supervision	713	0	0	713	0	285	214	143	71	0	0
Land	0	0	0	0	0	0	0	0	0	0	0
Site Improvements and Utilities	1,358	0	0	1,358	0	0	0	1,019	339	0	0
Construction	5,432	0	0	5,432	0	0	0	1,087	2,803	1,542	0
Other	722	0	0	722	0	0	0	0	217	505	0
Total	**8,225**	**0**	**0**	**8,225**	**0**	**285**	**214**	**2,249**	**3,430**	**2,047**	**0**
FUNDING SCHEDULE ($000s)											
G.O. Bonds	2,444	0	0	2,444	0	0	214	0	1,301	929	0
Schools Impact Tax	5,781	0	0	5,781	0	285	0	2,249	2,129	1,118	0
Total	**8,225**	**0**	**0**	**8,225**	**0**	**285**	**214**	**2,249**	**3,430**	**2,047**	**0**
OPERATING BUDGET IMPACT ($000s)											
Energy				30	0	0	0	0	0	30	
Maintenance				73	0	0	0	0	0	73	
Net Impact				**103**	**0**	**0**	**0**	**0**	**0**	**103**	

APPROPRIATION AND EXPENDITURE DATA (000s)

Appropriation Request	FY 16	713
Supplemental Appropriation Request		0
Transfer		0
Cumulative Appropriation		0
Expenditure / Encumbrances		0
Unencumbered Balance		0

Date First Appropriation	
First Cost Estimate	
Current Scope	8,225
Last FY's Cost Estimate	8,225

Description

A comprehensive capacity study to address overutilization at several elementary schools in the midsection of the Downcounty Consortium was conducted during the 2012-2013 school year. The following elementary schools were included in the study: Arcola, Brookhaven, Forest Knolls, Georgian Forest, Glen Haven, Glenallan, Harmony Hills, Highland, Kemp Mill, Sargent Shriver, Weller Road and Wheaton Woods. Based on the outcome of the study, additions will be constructed at the following elementary schools: Brookhaven, Glen Haven, Highland, Kemp MIll, and Sargent Shriver. While the planning funds remain on the schedule requested by the Board of Education, due to fiscal constraints, the construction funds were programmed one year later in the FY2015-2020 CIP. The Board of Education's requested FY 2015-2020 Amended CIP reinstated the construction schedule previously requested by the Board. Due to fiscal constraints, the County Council did not approve the Board's request. An FY 2016 appropriation was approved for planning funds. This project is scheduled to be completed August 2019.

Disclosures

Coordination

Mandatory Referral - M-NCPPC, Department of Environmental Protection, Building Permits:, Code Review, Fire Marshall, Department of Transportation, Inspections, Sediment Control, Stormwater Management, WSSC Permits

Kemp Mill ES Addition (DCC Solution) (P651506)

Category	Montgomery County Public Schools	Date Last Modified	11/17/14
Sub Category	Individual Schools	Required Adequate Public Facility	No
Administering Agency	Public Schools (AAGE18)	Relocation Impact	None
Planning Area	Silver Spring	Status	Planning Stage

	Total	Thru FY14	Rem FY14	Total 6 Years	FY 15	FY 16	FY 17	FY 18	FY 19	FY 20	Beyond 6 Yrs
EXPENDITURE SCHEDULE ($000s)											
Planning, Design and Supervision	774	0	0	774	0	310	232	155	77	0	0
Land	0	0	0	0	0	0	0	0	0	0	0
Site Improvements and Utilities	1,473	0	0	1,473	0	0	0	1,105	368	0	0
Construction	5,890	0	0	5,890	0	0	0	1,178	2,623	2,089	0
Other	521	0	0	521	0	0	0	0	157	364	0
Total	**8,658**	**0**	**0**	**8,658**	**0**	**310**	**232**	**2,438**	**3,225**	**2,453**	**0**
FUNDING SCHEDULE ($000s)											
G.O. Bonds	232	0	0	232	0	0	232	0	0	0	0
Schools Impact Tax	8,426	0	0	8,426	0	310	0	2,438	3,225	2,453	0
Total	**8,658**	**0**	**0**	**8,658**	**0**	**310**	**232**	**2,438**	**3,225**	**2,453**	**0**
OPERATING BUDGET IMPACT ($000s)											
Energy				34	0	0	0	0	0	34	
Maintenance				83	0	0	0	0	0	83	
Net Impact				**117**	**0**	**0**	**0**	**0**	**0**	**117**	

APPROPRIATION AND EXPENDITURE DATA (000s)

Appropriation Request	FY 16	774
Supplemental Appropriation Request		0
Transfer		0
Cumulative Appropriation		0
Expenditure / Encumbrances		0
Unencumbered Balance		0

Date First Appropriation FY 16	
First Cost Estimate	
Current Scope	8,658
Last FY's Cost Estimate	8,658

Description

A comprehensive capacity study to address overutilization at several elementary schools in the midsection of the Downcounty Consortium was conducted during the 2012-2013 school year. The following elementary schools were included in the study: Arcola, Brookhaven, Forest Knolls, Georgian Forest, Glen Haven, Glenallan, Harmony Hills, Highland, Kemp Mill, Sargent Shriver, Weller Road and Wheaton Woods. Based on the outcome of the study, additions will be constructed at the following elementary schools: Brookhaven, Glen Haven, Highland, Kemp MIll, and Sargent Shriver. While the planning funds remain on the schedule requested by the Board of Education, due to fiscal constraints, the construction funds were programmed one year later in the approved FY2015-2020 CIP. The Board of Education's requested FY 2015-2020 Amended CIP reinstated the construction schedule previously requested by the Board. Due to fiscal constraints, the County Council did not approve the Board's request. An FY 2016 appropriation was approved for planning funds. This project is scheduled to be completed August 2019.

Disclosures

Coordination

Mandatory Referral - M-NCPPC, Department of Environmental Protection, Building Permits:, Code Review, Fire Marshall, Department of Transportation, Inspections, Sediment Control, Stormwater Management, WSSC Permits

Kensington-Parkwood ES Addition (P651505)

Category	Montgomery County Public Schools	Date Last Modified	11/17/14
Sub Category	Individual Schools	Required Adequate Public Facility	No
Administering Agency	Public Schools (AAGE18)	Relocation Impact	None
Planning Area	Kensington-Wheaton	Status	Planning Stage

	Total	Thru FY14	Rem FY14	Total 6 Years	FY 15	FY 16	FY 17	FY 18	FY 19	FY 20	Beyond 6 Yrs
EXPENDITURE SCHEDULE ($000s)											
Planning, Design and Supervision	998	0	0	998	399	299	200	100	0	0	0
Land	0	0	0	0	0	0	0	0	0	0	0
Site Improvements and Utilities	1,900	0	0	1,900	0	0	1,425	475	0	0	0
Construction	7,597	0	0	7,597	0	0	1,520	5,318	759	0	0
Other	661	0	0	661	0	0	0	199	462	0	0
Total	**11,156**	**0**	**0**	**11,156**	**399**	**299**	**3,145**	**6,092**	**1,221**	**0**	**0**
FUNDING SCHEDULE ($000s)											
G.O. Bonds	11,156	0	0	11,156	399	299	3,145	6,092	1,221	0	0
Total	**11,156**	**0**	**0**	**11,156**	**399**	**299**	**3,145**	**6,092**	**1,221**	**0**	**0**
OPERATING BUDGET IMPACT ($000s)											
Energy				72	0	0	0	0	36	36	
Maintenance				176	0	0	0	0	88	88	
Net Impact				**248**	**0**	**0**	**0**	**0**	**124**	**124**	

APPROPRIATION AND EXPENDITURE DATA (000s)

Appropriation Request	FY 16	0
Supplemental Appropriation Request		0
Transfer		0
Cumulative Appropriation		998
Expenditure / Encumbrances		0
Unencumbered Balance		998

Date First Appropriation FY 15	
First Cost Estimate	
Current Scope	11,156
Last FY's Cost Estimate	11,156

Description

Enrollment projections at Kensington-Parkwood Elementary School reflect a need for an addition. Kensington-Parkwood Elementary School has a program capacity for 471students. Enrollment is expected to reach 674 students by the 2017-2018 school year. A feasibility study was conducted in FY 2013 to determine the cost and scope of the project. An FY 2015 appropriation was approved to begin planning this addition. While the planning funds remain on the schedule requested by the Board of Education, due to fiscal constraints, the construction funds were programmed one year later in the approved FY2015-2020 CIP. The Board of Education's requested FY 2015-2020 Amended CIP reinstated the construction schedule previously requested by the Board. Due to fiscal constraints, the County Council did not approve the Board's request. An FY 2017 appropriation will be requested for construction funds. This project is scheduled to be completed by August 2018.

Disclosures

Coordination

Mandatory Referral - M-NCPPC, Department of Environmental Protection, Building Permits:, Code Review, Fire Marshall, Department of Transportation, Inspections, Sediment Control, Stormwater Management, WSSC Permits

S. Christa McAuliffe ES Addition (P651502)

Category	Montgomery County Public Schools	Date Last Modified	11/17/14
Sub Category	Individual Schools	Required Adequate Public Facility	No
Administering Agency	Public Schools (AAGE18)	Relocation Impact	None
Planning Area	Germantown	Status	Planning Stage

	Total	Thru FY14	Rem FY14	Total 6 Years	FY 15	FY 16	FY 17	FY 18	FY 19	FY 20	Beyond 6 Yrs
EXPENDITURE SCHEDULE ($000s)											
Planning, Design and Supervision	910	0	0	910	0	0	364	273	182	91	0
Land	0	0	0	0	0	0	0	0	0	0	0
Site Improvements and Utilities	1,733	0	0	1,733	0	0	0	0	1,300	433	0
Construction	6,930	0	0	4,937	0	0	0	0	1,386	3,551	1,993
Other	598	0	0	180	0	0	0	0	0	180	418
Total	**10,171**	**0**	**0**	**7,760**	**0**	**0**	**364**	**273**	**2,868**	**4,255**	**2,411**
FUNDING SCHEDULE ($000s)											
G.O. Bonds	2,684	0	0	273	0	0	0	273	0	0	2,411
Schools Impact Tax	7,487	0	0	7,487	0	0	364	0	2,868	4,255	0
Total	**10,171**	**0**	**0**	**7,760**	**0**	**0**	**364**	**273**	**2,868**	**4,255**	**2,411**

APPROPRIATION AND EXPENDITURE DATA (000s)

Appropriation Request	FY 16	0
Supplemental Appropriation Request		0
Transfer		0
Cumulative Appropriation		0
Expenditure / Encumbrances		0
Unencumbered Balance		0

Date First Appropriation	
First Cost Estimate	
Current Scope	10,171
Last FY's Cost Estimate	10,171

Description

Enrollment projections at S. Christa McAuliffe Elementary School reflect a need for an addition. S. Christa McAuliffe Elementary School has a program capacity for 533 students. Enrollment is expected to reach 697 students by the 2019-2020 school year. A feasibility study was conducted in FY 2013 to determine the cost and scope of the project. While the planning funds remain on the schedule requested by the Board of Education, due to fiscal constraints, the construction funds were programmed one year later in the approved FY 2015-2020 CIP. The Board of Education's requested FY 2015-2020 Amended CIP reinstated the construction schedule previously requested by the Board. Due to fiscal constraints, the County Council did not approve the Board's request. An FY 2017 appropriation will be requested for planning funds. This project is scheduled to be completed by August 2020.

Disclosures

Coordination

Mandatory Referral - M-NCPPC, Department of Environmental Protection, Building Permits:, Code Review, Fire Marshall, Department of Transportation, Inspections, Sediment Control, Stormwater Management, WSSC Permits

North Bethesda MS Addition (P651503)

Category	Montgomery County Public Schools	Date Last Modified	11/17/14
Sub Category	Individual Schools	Required Adequate Public Facility	No
Administering Agency	Public Schools (AAGE18)	Relocation Impact	None
Planning Area	Bethesda-Chevy Chase	Status	Planning Stage

	Total	Thru FY14	Rem FY14	Total 6 Years	FY 15	FY 16	FY 17	FY 18	FY 19	FY 20	Beyond 6 Yrs
EXPENDITURE SCHEDULE ($000s)											
Planning, Design and Supervision	1,691	0	0	1,691	676	507	338	170	0	0	0
Land	0	0	0	0	0	0	0	0	0	0	0
Site Improvements and Utilities	2,903	0	0	2,903	0	0	2,178	725	0	0	0
Construction	13,195	0	0	13,195	0	0	2,639	5,237	5,319	0	0
Other	821	0	0	821	0	0	0	247	574	0	0
Total	**18,610**	**0**	**0**	**18,610**	**676**	**507**	**5,155**	**6,379**	**5,893**	**0**	**0**
FUNDING SCHEDULE ($000s)											
G.O. Bonds	18,341	0	0	18,341	438	476	5,155	6,379	5,893	0	0
School Facilities Payment	269	0	0	269	238	31	0	0	0	0	0
Total	**18,610**	**0**	**0**	**18,610**	**676**	**507**	**5,155**	**6,379**	**5,893**	**0**	**0**
OPERATING BUDGET IMPACT ($000s)											
Energy				152	0	0	0	0	76	76	
Maintenance				372	0	0	0	0	186	186	
Net Impact				**524**	**0**	**0**	**0**	**0**	**262**	**262**	

APPROPRIATION AND EXPENDITURE DATA (000s)

Appropriation Request	FY 16	0
Supplemental Appropriation Request		0
Transfer		0
Cumulative Appropriation		1,691
Expenditure / Encumbrances		0
Unencumbered Balance		1,691

Date First Appropriation FY 15	
First Cost Estimate	
Current Scope	18,610
Last FY's Cost Estimate	18,610

Description

Enrollment projections at North Bethesda Middle School reflect a need for an addition. North Bethesda Middle School has a program capacity for 864 students. Enrollment is expected to reach 1156 students by the 2017-2018 school year. A feasibility study was conducted in FY 2013 to determine the cost and scope of the project. An FY 2015 appropriation was approved to begin planning this addition. While the planning funds remain on the schedule requested by the Board of Education, due to fiscal constraints, the construction funds were programmed one year later in the approved FY2015-2020 CIP. The Board of Education's requested FY 2015-2020 Amended CIP reinstated the construction schedule previously requested by the Board. Due to fiscal constraints, the County Council did not approve the Board's request. An FY 2017 appropriation will be requested for construction funds. This project is scheduled to be completed by August 2018.

Disclosures

Coordination

Mandatory Referral - M-NCPPC, Department of Environmental Protection, Building Permits:, Code Review, Fire Marshall, Department of Transportation, Inspections, Sediment Control, Stormwater Management, WSSC Permits

North Chevy Chase ES Addition (P136504)

Category	Montgomery County Public Schools	Date Last Modified	4/21/14
Sub Category	Individual Schools	Required Adequate Public Facility	No
Administering Agency	Public Schools (AAGE18)	Relocation Impact	None
Planning Area	Bethesda-Chevy Chase	Status	Planning Stage

	Total	Thru FY14	Rem FY14	Total 6 Years	FY 15	FY 16	FY 17	FY 18	FY 19	FY 20	Beyond 6 Yrs
EXPENDITURE SCHEDULE ($000s)											
Planning, Design and Supervision	459	230	138	91	91	0	0	0	0	0	0
Land	0	0	0	0	0	0	0	0	0	0	0
Site Improvements and Utilities	939	0	751	188	188	0	0	0	0	0	0
Construction	5,162	0	1,032	4,130	1,549	2,581	0	0	0	0	0
Other	260	0	0	260	52	208	0	0	0	0	0
Total	**6,820**	**230**	**1,921**	**4,669**	**1,880**	**2,789**	**0**	**0**	**0**	**0**	**0**
FUNDING SCHEDULE ($000s)											
G.O. Bonds	4,776	66	1,921	2,789	0	2,789	0	0	0	0	0
School Facilities Payment	164	164	0	0	0	0	0	0	0	0	0
Schools Impact Tax	1,880	0	0	1,880	1,880	0	0	0	0	0	0
Total	**6,820**	**230**	**1,921**	**4,669**	**1,880**	**2,789**	**0**	**0**	**0**	**0**	**0**
OPERATING BUDGET IMPACT ($000s)											
Energy				45	0	9	9	9	9	9	
Maintenance				120	0	24	24	24	24	24	
Net Impact				**165**	**0**	**33**	**33**	**33**	**33**	**33**	

APPROPRIATION AND EXPENDITURE DATA (000s)

Appropriation Request	FY 16	0
Supplemental Appropriation Request		0
Transfer		0
Cumulative Appropriation		6,820
Expenditure / Encumbrances		230
Unencumbered Balance		6,590

Date First Appropriation FY 13	
First Cost Estimate	
Current Scope	0
Last FY's Cost Estimate	6,820

Description

Enrollment projections at North Chevy Chase Elementary School reflect a need for an addition. North Chevy Chase Elementary School has a program capacity for 220 students. Enrollment is expected to reach 330 students by the 2017-2018 school year. The reassignment of Grade 6 students out of North Chevy Chase Elementary School will relieve some, but not all, of the projected space deficit. A feasibility study was conducted in FY 2011 to determine the cost and scope of the project. An FY 2013 appropriation was approved to begin planning this addition. An FY 2014 appropriation was approved for construction funds. An FY 2015 appropriation was approved to complete this project. This project is scheduled to be completed by August 2015.

Capacity

Program Capacity After Addition: 358

Coordination

Mandatory Referral - M-NCPPC, Department of Environmental Protection, Building Permits, Code Review, Fire Marshal, Department of Transportation, Inspections, Sediment Control, Stormwater Management, WSSC Permits

Northwest ES #8 (New) (P136505)

Category	Montgomery County Public Schools	Date Last Modified	11/17/14
Sub Category	Individual Schools	Required Adequate Public Facility	No
Administering Agency	Public Schools (AAGE18)	Relocation Impact	None
Planning Area	Germantown	Status	Planning Stage

	Total	Thru FY14	Rem FY14	Total 6 Years	FY 15	FY 16	FY 17	FY 18	FY 19	FY 20	Beyond 6 Yrs
EXPENDITURE SCHEDULE ($000s)											
Planning, Design and Supervision	2,979	0	0	2,979	1,192	894	596	297	0	0	0
Land	0	0	0	0	0	0	0	0	0	0	0
Site Improvements and Utilities	3,776	0	0	3,776	0	0	2,690	1,086	0	0	0
Construction	24,595	0	0	24,595	0	0	4,374	11,819	8,402	0	0
Other	1,100	0	0	1,100	0	0	0	330	770	0	0
Total	**32,450**	**0**	**0**	**32,450**	**1,192**	**894**	**7,660**	**13,532**	**9,172**	**0**	**0**
FUNDING SCHEDULE ($000s)											
Current Revenue: Recordation Tax	3,000	0	0	3,000	0	0	3,000	0	0	0	0
G.O. Bonds	21,103	0	0	21,103	0	894	974	10,063	9,172	0	0
School Facilities Payment	630	0	0	630	630	0	0	0	0	0	0
Schools Impact Tax	7,717	0	0	7,717	562	0	3,686	3,469	0	0	0
Total	**32,450**	**0**	**0**	**32,450**	**1,192**	**894**	**7,660**	**13,532**	**9,172**	**0**	**0**
OPERATING BUDGET IMPACT ($000s)											
Energy				294	0	0	0	0	147	147	
Maintenance				788	0	0	0	0	394	394	
Net Impact				**1,082**	**0**	**0**	**0**	**0**	**541**	**541**	

APPROPRIATION AND EXPENDITURE DATA (000s)

Appropriation Request	FY 16	0
Supplemental Appropriation Request		0
Transfer		0
Cumulative Appropriation		2,979
Expenditure / Encumbrances		0
Unencumbered Balance		2,979

Date First Appropriation FY 15	
First Cost Estimate	
Current Scope	0
Last FY's Cost Estimate	32,450

Description

Projections indicate enrollment at Spark M. Matsunaga and Ronald McNair elementary schools will exceed the capacities at each school. Spark M. Matsunaga Elementary School has a program capacity of 650 with a 2017-2018 projected enrollment of 1,016 students. Ronald McNair Elementary School has a program capacity of 623 with a 2017-2018 projected enrollment of 732 students. In order to provide relief of the overutilization at both schools, a new elementary school is needed. An FY 2015 appropriation was approved to begin planning this new school. While planning funds remain on schedule, due to fiscal constraints, the construction funds for this project were delayed one year in the approved FY2015-2020 CIP. The Board of Education's requested FY 2015-2020 Amended CIP reinstated the construction schedule previously requested by the Board. Due to fiscal constraints, the County Council did not approve the Board's request. An FY 2017 appropriation will be requested for construction funds. This project is scheduled to be completed by August 2018.

Capacity

Program Capacity: 740

Coordination

Mandatory Referral - M-NCPPC, Department of Environmental Protection, Building Permits, Code Review, Fire Marshal, Department of Transportation, Inspections, Sediment Control, Stormwater Management, WSSC Permits

Northwood Cluster HS Solution (P651517)

Category	Montgomery County Public Schools	Date Last Modified	11/17/14
Sub Category	Individual Schools	Required Adequate Public Facility	No
Administering Agency	Public Schools (AAGE18)	Relocation Impact	None
Planning Area	Kensington-Wheaton	Status	Planning Stage

	Total	Thru FY14	Rem FY14	Total 6 Years	FY 15	FY 16	FY 17	FY 18	FY 19	FY 20	Beyond 6 Yrs
EXPENDITURE SCHEDULE ($000s)											
Planning, Design and Supervision	294	0	0	294	0	0	0	147	88	59	0
Land	0	0	0	0	0	0	0	0	0	0	0
Site Improvements and Utilities	316	0	0	316	0	0	0	0	253	63	0
Construction	2,928	0	0	2,050	0	0	0	0	586	1,464	878
Other	350	0	0	70	0	0	0	0	0	70	280
Total	**3,888**	**0**	**0**	**2,730**	**0**	**0**	**0**	**147**	**927**	**1,656**	**1,158**
FUNDING SCHEDULE ($000s)											
G.O. Bonds	3,888	0	0	2,730	0	0	0	147	927	1,656	1,158
Total	**3,888**	**0**	**0**	**2,730**	**0**	**0**	**0**	**147**	**927**	**1,656**	**1,158**

APPROPRIATION AND EXPENDITURE DATA (000s)

Appropriation Request	FY 16	0
Supplemental Appropriation Request		0
Transfer		0
Cumulative Appropriation		0
Expenditure / Encumbrances		0
Unencumbered Balance		0

Date First Appropriation	
First Cost Estimate	
Current Scope	0
Last FY's Cost Estimate	0

Description

Due to increasing enrollment growth, this project includes funds to design and construct 10 high school classrooms serving Northwood High School in the Downcounty Consortium. These additional classrooms would meet capacity requirements under the Subdivision Staging Policy, avoiding a residential moratorium in the Northwood Cluster. The County Council anticipates that ultimately, the Board of Education will request a specific project that will add, at least, these classrooms by the start of the 2020-2021 school year at the latest and these funds would be used towards that purpose.

Judith Resnik ES Addition (P651507)

Category	Montgomery County Public Schools	Date Last Modified	11/17/14
Sub Category	Individual Schools	Required Adequate Public Facility	No
Administering Agency	Public Schools (AAGE18)	Relocation Impact	None
Planning Area	Germantown	Status	Planning Stage

	Total	Thru FY14	Rem FY14	Total 6 Years	FY 15	FY 16	FY 17	FY 18	FY 19	FY 20	Beyond 6 Yrs
EXPENDITURE SCHEDULE ($000s)											
Planning, Design and Supervision	1,032	0	0	1,032	0	0	413	310	206	103	0
Land	0	0	0	0	0	0	0	0	0	0	0
Site Improvements and Utilities	2,751	0	0	1,966	0	0	0	0	1,475	491	785
Construction	7,533	0	0	5,277	0	0	0	0	1,573	3,704	2,256
Other	196	0	0	196	0	0	0	0	0	196	0
Total	**11,512**	**0**	**0**	**8,471**	**0**	**0**	**413**	**310**	**3,254**	**4,494**	**3,041**
FUNDING SCHEDULE ($000s)											
G.O. Bonds	3,351	0	0	310	0	0	0	310	0	0	3,041
Schools Impact Tax	8,161	0	0	8,161	0	0	413	0	3,254	4,494	0
Total	**11,512**	**0**	**0**	**8,471**	**0**	**0**	**413**	**310**	**3,254**	**4,494**	**3,041**

APPROPRIATION AND EXPENDITURE DATA (000s)

Appropriation Request	FY 16	0
Supplemental Appropriation Request		0
Transfer		0
Cumulative Appropriation		0
Expenditure / Encumbrances		0
Unencumbered Balance		0

Date First Appropriation FY 16	
First Cost Estimate	
Current Scope	11,512
Last FY's Cost Estimate	11,512

Description

Enrollment projections at Judith Resnik Elementary School reflect a need for an addition. Judith Resnik Elementary School has a program capacity for 503 students. Enrollment is expected to reach 655 students by the 2019-2020 school year. A feasibility study was conducted in FY 2013 to determine the cost and scope of the project. While the planning funds remain on the schedule requested by the Board of Education, due to fiscal constraints, the construction funds were programmed one year later in the approved FY2015-2020 CIP. The Board of Education's requested FY2015-2020 Amended CIP reinstated the construction schedule previously requested by the Board. Due to fiscal constraints, the County Council did not approvedthe Board's request. An FY 2017 appropriation will be requested for planning funds. This project is scheduled to be completed by August 2020.

Disclosures

Coordination

Mandatory Referral - M-NCPPC, Department of Environmental Protection, Building Permits:, Code Review, Fire Marshall, Department of Transportation, Inspections, Sediment Control, Stormwater Management, WSSC Permits

Rosemary Hills ES Addition (P136506)

Category	Montgomery County Public Schools	Date Last Modified	4/21/14
Sub Category	Individual Schools	Required Adequate Public Facility	No
Administering Agency	Public Schools (AAGE18)	Relocation Impact	None
Planning Area	Bethesda-Chevy Chase	Status	Planning Stage

	Total	Thru FY14	Rem FY14	Total 6 Years	FY 15	FY 16	FY 17	FY 18	FY 19	FY 20	Beyond 6 Yrs
EXPENDITURE SCHEDULE ($000s)											
Planning, Design and Supervision	396	198	119	79	79	0	0	0	0	0	0
Land	0	0	0	0	0	0	0	0	0	0	0
Site Improvements and Utilities	868	0	694	174	174	0	0	0	0	0	0
Construction	4,274	0	855	3,419	1,282	2,137	0	0	0	0	0
Other	170	0	0	170	34	136	0	0	0	0	0
Total	**5,708**	**198**	**1,668**	**3,842**	**1,569**	**2,273**	**0**	**0**	**0**	**0**	**0**
FUNDING SCHEDULE ($000s)											
G.O. Bonds	4,139	198	1,668	2,273	0	2,273	0	0	0	0	0
Schools Impact Tax	1,569	0	0	1,569	1,569	0	0	0	0	0	0
Total	**5,708**	**198**	**1,668**	**3,842**	**1,569**	**2,273**	**0**	**0**	**0**	**0**	**0**
OPERATING BUDGET IMPACT ($000s)											
Energy				130	0	26	26	26	26	26	
Maintenance				355	0	71	71	71	71	71	
Net Impact				**485**	**0**	**97**	**97**	**97**	**97**	**97**	

APPROPRIATION AND EXPENDITURE DATA (000s)

Appropriation Request	FY 16	0
Supplemental Appropriation Request		0
Transfer		0
Cumulative Appropriation		5,708
Expenditure / Encumbrances		198
Unencumbered Balance		5,510

Date First Appropriation FY 13	
First Cost Estimate	
Current Scope	0
Last FY's Cost Estimate	5,708

Description

Enrollment projections at Rosemary Hills Elementary School reflect a need for an addition. Rosemary Hills Elementary School has a program capacity for 476 students. Enrollment is expected to reach 571 students by the 2015-2016 school year. A feasibility study was conducted in FY 2011 to determine the cost and scope of the project. An FY 2013 appropriation was approved to begin planning this addition. An FY 2014 appropriation was approved for construction funds. An FY 2015 appropriation was approved to complete this project. This project is scheduled to be completed by August 2015.

Capacity

Program Capacity After Addition: 615

Coordination

Mandatory Referral - M-NCPPC, Department of Environmental Protection, Building Permits, Code Review, Fire Marshal, Department of Transportation, Inspections, Sediment Control, Stormwater Management, WSSC Permits

Sargent Shriver ES Addition (DCC Solution) (P651501)

Category	Montgomery County Public Schools	Date Last Modified	11/17/14
Sub Category	Individual Schools	Required Adequate Public Facility	No
Administering Agency	Public Schools (AAGE18)	Relocation Impact	None
Planning Area	Silver Spring	Status	Planning Stage

	Total	Thru FY14	Rem FY14	Total 6 Years	FY 15	FY 16	FY 17	FY 18	FY 19	FY 20	Beyond 6 Yrs
EXPENDITURE SCHEDULE ($000s)											
Planning, Design and Supervision	341	0	0	341	0	136	102	68	35	0	0
Land	0	0	0	0	0	0	0	0	0	0	0
Site Improvements and Utilities	649	0	0	649	0	0	0	487	162	0	0
Construction	2,593	0	0	2,593	0	0	0	519	1,816	258	0
Other	298	0	0	298	0	0	0	0	90	208	0
Total	**3,881**	**0**	**0**	**3,881**	**0**	**136**	**102**	**1,074**	**2,103**	**466**	**0**
FUNDING SCHEDULE ($000s)											
Current Revenue: Recordation Tax	1,501	0	0	1,501	0	0	0	1,000	501	0	0
G.O. Bonds	2,380	0	0	2,380	0	136	102	74	1,602	466	0
Total	**3,881**	**0**	**0**	**3,881**	**0**	**136**	**102**	**1,074**	**2,103**	**466**	**0**
OPERATING BUDGET IMPACT ($000s)											
Energy				15	0	0	0	0	0	15	
Maintenance				37	0	0	0	0	0	37	
Net Impact				**52**	**0**	**0**	**0**	**0**	**0**	**52**	

APPROPRIATION AND EXPENDITURE DATA (000s)

Appropriation Request	FY 16	341
Supplemental Appropriation Request		0
Transfer		0
Cumulative Appropriation		0
Expenditure / Encumbrances		0
Unencumbered Balance		0

Date First Appropriation FY 16	
First Cost Estimate	
Current Scope	3,881
Last FY's Cost Estimate	3,881

Description

A comprehensive capacity study to address overutilization at several elementary schools in the midsection of the Downcounty Consortium was conducted during the 2012-2013 school year. The following elementary schools were included in the study: Arcola, Brookhaven, Forest Knolls, Georgian Forest, Glen Haven, Glenallan, Harmony Hills, Highland, Kemp Mill, Sargent Shriver, Weller Road and Wheaton Woods. Based on the outcome of the study, additions will be constructed at the following elementary schools: Brookhaven, Glen Haven, Highland, Kemp MIll, and Sargent Shriver. While the planning funds remain on the schedule requested by the Board of Education, due to fiscal constraints, the construction funds were programmed one year later in the approved FY2015-2020 CIP. The Board of Education's requested FY2015-2020 Amended CIP reinstated the construction schedule previously requested by the Board. Due to fiscal constraints, the County Council did not approve the Board' s request. An FY 2016 appropriation was approved for planning funds. This project is scheduled to be completed August 2019.

Disclosures

Coordination

Mandatory Referral - M-NCPPC, Department of Environmental Protection, Building Permits:, Code Review, Fire Marshall, Department of Transportation, Inspections, Sediment Control, Stormwater Management, WSSC Permits

Waters Landing ES Addition (P116511)

Category	Montgomery County Public Schools	Date Last Modified	4/21/14
Sub Category	Individual Schools	Required Adequate Public Facility	No
Administering Agency	Public Schools (AAGE18)	Relocation Impact	None
Planning Area	Germantown	Status	Planning Stage

	Total	Thru FY14	Rem FY14	Total 6 Years	FY 15	FY 16	FY 17	FY 18	FY 19	FY 20	Beyond 6 Yrs
EXPENDITURE SCHEDULE ($000s)											
Planning, Design and Supervision	669	535	134	0	0	0	0	0	0	0	0
Land	0	0	0	0	0	0	0	0	0	0	0
Site Improvements and Utilities	1,277	766	511	0	0	0	0	0	0	0	0
Construction	6,481	493	2,592	3,396	3,396	0	0	0	0	0	0
Other	400	0	250	150	150	0	0	0	0	0	0
Total	**8,827**	**1,794**	**3,487**	**3,546**	**3,546**	**0**	**0**	**0**	**0**	**0**	**0**
FUNDING SCHEDULE ($000s)											
G.O. Bonds	3,281	1,794	1,487	0	0	0	0	0	0	0	0
Schools Impact Tax	5,546	0	2,000	3,546	3,546	0	0	0	0	0	0
Total	**8,827**	**1,794**	**3,487**	**3,546**	**3,546**	**0**	**0**	**0**	**0**	**0**	**0**
OPERATING BUDGET IMPACT ($000s)											
Energy				228	38	38	38	38	38	38	
Maintenance				474	79	79	79	79	79	79	
Net Impact				**702**	**117**	**117**	**117**	**117**	**117**	**117**	

APPROPRIATION AND EXPENDITURE DATA (000s)

Appropriation Request	FY 16	0
Supplemental Appropriation Request		0
Transfer		0
Cumulative Appropriation		8,827
Expenditure / Encumbrances		1,794
Unencumbered Balance		7,033

Date First Appropriation FY 12	
First Cost Estimate	
Current Scope	0
Last FY's Cost Estimate	8,827

Description

Due to enrollment growth at the elementary school level, the Seneca Valley Cluster is in a housing moratorium according to the county's Annual Growth Policy. To lift the moratorium, additional elementary school capacity must be built. Enrollment projections at Waters Landing Elementary School reflect a need for a 11-classroom addition. Waters Landing Elementary School has a program capacity for 499 students. Enrollment is expected to reach 630 students by the 2013-2014 school year. An FY 2011 appropriation was requested as part of the Board of Education's FY 2011-2016 CIP to begin planning this addition. However, due to fiscal constraints, the County Council's adopted FY 2011-2016 CIP delayed this addition project one year. An FY 2012 appropriation was approved for planning funds. An FY 2013 appropriation was approved for construction funds. An FY 2014 appropriation was approved to complete this project. This project is now scheduled to be completed by August 2014.

Capacity

Program Capacity after Addition: 736

Coordination

Mandatory Referral - M-NCPPC, Department of Environmental Protection, Building Permits, Code Review, Fire Marshal, Department of Transportation, Inspections, Sediment Control, Stormwater Management, WSSC Permits

Julius West MS Addition (P136507)

Category	Montgomery County Public Schools	Date Last Modified	11/17/14
Sub Category	Individual Schools	Required Adequate Public Facility	No
Administering Agency	Public Schools (AAGE18)	Relocation Impact	None
Planning Area	Rockville	Status	Planning Stage

	Total	Thru FY14	Rem FY14	Total 6 Years	FY 15	FY 16	FY 17	FY 18	FY 19	FY 20	Beyond 6 Yrs
EXPENDITURE SCHEDULE ($000s)											
Planning, Design and Supervision	1,389	0	409	980	445	335	200	0	0	0	0
Land	0	0	0	0	0	0	0	0	0	0	0
Site Improvements and Utilities	2,646	0	0	2,646	1,984	662	0	0	0	0	0
Construction	10,580	0	0	10,580	2,235	7,350	995	0	0	0	0
Other	688	0	0	688	0	207	481	0	0	0	0
Total	**15,303**	**0**	**409**	**14,894**	**4,664**	**8,554**	**1,676**	**0**	**0**	**0**	**0**
FUNDING SCHEDULE ($000s)											
G.O. Bonds	7,563	0	409	7,154	0	5,478	1,676	0	0	0	0
Schools Impact Tax	7,740	0	0	7,740	4,664	3,076	0	0	0	0	0
Total	**15,303**	**0**	**409**	**14,894**	**4,664**	**8,554**	**1,676**	**0**	**0**	**0**	**0**
OPERATING BUDGET IMPACT ($000s)											
Energy				200	0	0	50	50	50	50	
Maintenance				536	0	0	134	134	134	134	
Net Impact				**736**	**0**	**0**	**184**	**184**	**184**	**184**	

APPROPRIATION AND EXPENDITURE DATA (000s)

Appropriation Request	FY 16	688
Supplemental Appropriation Request		0
Transfer		0
Cumulative Appropriation		14,615
Expenditure / Encumbrances		0
Unencumbered Balance		14,615

Date First Appropriation FY 15	
First Cost Estimate	
Current Scope	0
Last FY's Cost Estimate	15,303

Description

Enrollment projections at Julius West Middle School reflect a need for an addition. Julius West Middle School has a program capacity for 986 students. Enrollment is expected to reach 1,313 students by the 2016-2017 school year. A feasibility study was conducted in FY 2011 to determine the cost and scope of the project. An FY 2014 appropriation was approved to begin planning this addition. An FY 2015 appropriation was approved for construction funds. An FY 2016 appropriation was approved to complete this project. This project is scheduled to be completed by August 2016.

Capacity

Program Capacity After Addition: 1,444

Coordination

Mandatory Referral - M-NCPPC, Department of Environmental Protection, Building Permits, Code Review, Fire Marshal, Department of Transportation, Inspections, Sediment Control, Stormwater Management, WSSC Permits

Wheaton Cluster MS Solution (P651516)

Category	Montgomery County Public Schools	Date Last Modified	11/17/14
Sub Category	Individual Schools	Required Adequate Public Facility	No
Administering Agency	Public Schools (AAGE18)	Relocation Impact	None
Planning Area	Kensington-Wheaton	Status	Planning Stage

	Total	Thru FY14	Rem FY14	Total 6 Years	FY 15	FY 16	FY 17	FY 18	FY 19	FY 20	Beyond 6 Yrs
EXPENDITURE SCHEDULE ($000s)											
Planning, Design and Supervision	118	0	0	118	0	0	0	59	35	24	0
Land	0	0	0	0	0	0	0	0	0	0	0
Site Improvements and Utilities	126	0	0	126	0	0	0	0	101	25	0
Construction	1,172	0	0	820	0	0	0	0	234	586	352
Other	140	0	0	28	0	0	0	0	0	28	112
Total	**1,556**	**0**	**0**	**1,092**	**0**	**0**	**0**	**59**	**370**	**663**	**464**
FUNDING SCHEDULE ($000s)											
G.O. Bonds	1,556	0	0	1,092	0	0	0	59	370	663	464
Total	**1,556**	**0**	**0**	**1,092**	**0**	**0**	**0**	**59**	**370**	**663**	**464**

APPROPRIATION AND EXPENDITURE DATA (000s)

Appropriation Request	FY 16	0
Supplemental Appropriation Request		0
Transfer		0
Cumulative Appropriation		0
Expenditure / Encumbrances		0
Unencumbered Balance		0

Date First Appropriation	
First Cost Estimate	
Current Scope	0
Last FY's Cost Estimate	0

Description

Due to increasing enrollment growth, this project includes funds to design and construct four middle school classrooms serving A. Mario Loiderman Middle School or Parkland Middle School in the Wheaton High School portion of the Downcounty Consortium. These additional classrooms would meet capacity requirements under the Subdivision Staging Policy, avoiding a residential moratorium in the Wheaton Cluster. The County Council anticipates that ultimately, the Board of Education will request a specific project that will add at least these classrooms by the start of the 2020-2021 school year at the latest and these funds would be used towards that purpose.

Wood Acres ES Addition (P136508)

Category	Montgomery County Public Schools	Date Last Modified	11/17/14
Sub Category	Individual Schools	Required Adequate Public Facility	No
Administering Agency	Public Schools (AAGE18)	Relocation Impact	None
Planning Area	Bethesda-Chevy Chase	Status	Planning Stage

	Total	Thru FY14	Rem FY14	Total 6 Years	FY 15	FY 16	FY 17	FY 18	FY 19	FY 20	Beyond 6 Yrs
EXPENDITURE SCHEDULE ($000s)											
Planning, Design and Supervision	786	0	232	554	318	157	79	0	0	0	0
Land	0	0	0	0	0	0	0	0	0	0	0
Site Improvements and Utilities	1,496	0	0	1,496	1,122	374	0	0	0	0	0
Construction	5,982	0	0	5,982	1,197	4,188	597	0	0	0	0
Other	342	0	0	342	0	103	239	0	0	0	0
Total	**8,606**	**0**	**232**	**8,374**	**2,637**	**4,822**	**915**	**0**	**0**	**0**	**0**
FUNDING SCHEDULE ($000s)											
G.O. Bonds	5,969	0	232	5,737	0	4,822	915	0	0	0	0
Schools Impact Tax	2,637	0	0	2,637	2,637	0	0	0	0	0	0
Total	**8,606**	**0**	**232**	**8,374**	**2,637**	**4,822**	**915**	**0**	**0**	**0**	**0**
OPERATING BUDGET IMPACT ($000s)											
Energy				136	0	0	34	34	34	34	
Maintenance				368	0	0	92	92	92	92	
Net Impact				**504**	**0**	**0**	**126**	**126**	**126**	**126**	

APPROPRIATION AND EXPENDITURE DATA (000s)

Appropriation Request	FY 16	342
Supplemental Appropriation Request		0
Transfer		0
Cumulative Appropriation		8,264
Expenditure / Encumbrances		0
Unencumbered Balance		8,264

Date First Appropriation FY 15	
First Cost Estimate	
Current Scope	0
Last FY's Cost Estimate	8,606

Description

Enrollment projections at Wood Acres Elementary School reflect a need for an addition. Wood Acres Elementary School has a program capacity for 551 students. Enrollment is expected to reach 696 students by the 2016-2017 school year. A feasibility study was conducted in FY 2011 to determine the cost and scope of the project. An FY 2014 appropriation was approved to begin planning this addition. An FY 2015 appropriation was approved for construction funds. An FY2016 appropriation was approved to complete this project. This project is scheduled to be completed by August 2016.

Capacity

Program Capacity After Addition: 735

Coordination

Mandatory Referral - M-NCPPC, Department of Environmental Protection, Building Permits, Code Review, Fire Marshall, Department of Transportation, Inspections, Sediment Control, Stormwater Management, WSSC Permits

ADA Compliance: MCPS (P796235)

Category	Montgomery County Public Schools	Date Last Modified	11/17/14
Sub Category	Countywide	Required Adequate Public Facility	No
Administering Agency	Public Schools (AAGE18)	Relocation Impact	None
Planning Area	Countywide	Status	Ongoing

	Total	Thru FY14	Rem FY14	Total 6 Years	FY 15	FY 16	FY 17	FY 18	FY 19	FY 20	Beyond 6 Yrs
EXPENDITURE SCHEDULE ($000s)											
Planning, Design and Supervision	5,740	1,844	960	2,936	810	810	329	329	329	329	0
Land	0	0	0	0	0	0	0	0	0	0	0
Site Improvements and Utilities	0	0	0	0	0	0	0	0	0	0	0
Construction	18,653	8,549	2,240	7,864	2,190	2,190	871	871	871	871	0
Other	0	0	0	0	0	0	0	0	0	0	0
Total	**24,393**	**10,393**	**3,200**	**10,800**	**3,000**	**3,000**	**1,200**	**1,200**	**1,200**	**1,200**	**0**
FUNDING SCHEDULE ($000s)											
G.O. Bonds	24,393	10,393	3,200	10,800	3,000	3,000	1,200	1,200	1,200	1,200	0
Total	**24,393**	**10,393**	**3,200**	**10,800**	**3,000**	**3,000**	**1,200**	**1,200**	**1,200**	**1,200**	**0**

APPROPRIATION AND EXPENDITURE DATA (000s)

Appropriation Request	FY 16	3,000
Supplemental Appropriation Request		0
Transfer		0
Cumulative Appropriation		16,593
Expenditure / Encumbrances		10,393
Unencumbered Balance		6,200

Date First Appropriation	FY 79	
First Cost Estimate		
Current Scope	FY 96	16,615
Last FY's Cost Estimate		24,393
Partial Closeout Thru		17,216
New Partial Closeout		0
Total Partial Closeout		17,216

Description
Federal and State laws require MCPS to provide program accessibility for all of its activities and to consider various forms of accessibility improvements at existing facilities on a continuing basis. While MCPS provides program accessibility in a manner consistent with current laws, a significant number of existing facilities not scheduled for modernization in the current six-year CIP are at least partially inaccessible for a variety of disabling conditions. Some combination of elevators, wheelchair lifts, restroom modifications, and other site-specific improvements are required at many of these facilities. Since disabilities of eligible individuals must be considered on a case-by-case basis, additional modifications such as automatic door openers, access ramps, and curb cuts may be required on an ad hoc basis even in facilities previously considered accessible. The increased mainstreaming of special education students has contributed to modifications to existing facilities. Certain ADA modifications results in significant cost avoidance, since transportation may have to be provided for individuals to other venues or programs. On September 15, 2010, the Department of Justice approved revisions to Title II of the Americans with Disabilities Act (ADA), thw will require local and state government agencies to comply with theses reviesions. An FY 2013 appropriation was approved to begin the assessment of MCPS facilities to comply with the approved rrevision ot Title II of the ADA. An FY 2014 appropriation was approved to continue this level of effort project. An FY 2015 appropriation was approved to continue remediation to address the revisions to Title II of the ADA. An FY 2016 appropriation was approved to continue this level of effort project.

Other
ADA requirements are addressed in other projects, including many transportation and renovation projects.

Fiscal Note
State Reimbursement: Not eligible

Disclosures
Expenditures will continue indefinitely.

Coordination
Advisory Committee for the Handicapped

Asbestos Abatement: MCPS (P816695)

Category	Montgomery County Public Schools	Date Last Modified	11/17/14
Sub Category	Countywide	Required Adequate Public Facility	No
Administering Agency	Public Schools (AAGE18)	Relocation Impact	None
Planning Area	Countywide	Status	Ongoing

	Total	Thru FY14	Rem FY14	Total 6 Years	FY 15	FY 16	FY 17	FY 18	FY 19	FY 20	Beyond 6 Yrs
EXPENDITURE SCHEDULE ($000s)											
Planning, Design and Supervision	10,992	5,350	806	4,836	806	806	806	806	806	806	0
Land	0	0	0	0	0	0	0	0	0	0	0
Site Improvements and Utilities	0	0	0	0	0	0	0	0	0	0	0
Construction	4,528	2,155	339	2,034	339	339	339	339	339	339	0
Other	0	0	0	0	0	0	0	0	0	0	0
Total	**15,520**	**7,505**	**1,145**	**6,870**	**1,145**	**1,145**	**1,145**	**1,145**	**1,145**	**1,145**	**0**
FUNDING SCHEDULE ($000s)											
G.O. Bonds	15,520	7,505	1,145	6,870	1,145	1,145	1,145	1,145	1,145	1,145	0
Total	**15,520**	**7,505**	**1,145**	**6,870**	**1,145**	**1,145**	**1,145**	**1,145**	**1,145**	**1,145**	**0**

APPROPRIATION AND EXPENDITURE DATA (000s)

Appropriation Request	FY 16	1,145
Supplemental Appropriation Request		0
Transfer		0
Cumulative Appropriation		9,795
Expenditure / Encumbrances		7,505
Unencumbered Balance		2,290

Date First Appropriation	FY 81	
First Cost Estimate		
Current Scope	FY 96	147,218
Last FY's Cost Estimate		15,520
Partial Closeout Thru		25,289
New Partial Closeout		0
Total Partial Closeout		25,289

Description

Comprehensive asbestos management services for all facilities in the school system ensure compliance with the existing Federal Asbestos Hazard Emergency Response Act (AHERA). MCPS has produced major cost savings for asbestos abatement by an innovative plan with an in-house team of licensed abatement technicians for its numerous small abatement projects and required semi-annual inspections. Cost containment measures, a more competitive bidding environment, and development of a comprehensive data base and management plan also have contributed to significant expenditure reductions. MCPS is participating in interdepartmental coordination of various improvement projects in order to share successful and cost effective approaches. This project is based on the approved management plan for all facilities in the system. Actual abatement and the subsequent restoration of facilities are funded through this project. An FY 2013 appropriation was approved to continue asbestos abatement projects as required by AHERA. An FY 2014 appropriation was approved to continue this project. An FY 2015 appropriation was approved to continue funding asbestos abatement projects systemwide. An FY 2016 appropriation was approved to continue this level of effort project.

Fiscal Note

State Reimbursement: Not eligible

Disclosures

Expenditures will continue indefinitely.

Coordination

Maryland Department of the Environment, Department of Environmental Protection, State Department of Education, Department of Health

$(000)	FY 15	FY 16-20
Salaries and Wages:	817	4085
Fringe Benefits:	376	1880
Workyears:	10	50

Building Modifications and Program Improvements (P076506)

Category	Montgomery County Public Schools	Date Last Modified	11/17/14
Sub Category	Countywide	Required Adequate Public Facility	No
Administering Agency	Public Schools (AAGE18)	Relocation Impact	None
Planning Area	Countywide	Status	Ongoing

	Total	Thru FY14	Rem FY14	Total 6 Years	FY 15	FY 16	FY 17	FY 18	FY 19	FY 20	Beyond 6 Yrs
EXPENDITURE SCHEDULE ($000s)											
Planning, Design and Supervision	4,572	2,442	690	1,440	720	720	0	0	0	0	0
Land	0	0	0	0	0	0	0	0	0	0	0
Site Improvements and Utilities	0	0	0	0	0	0	0	0	0	0	0
Construction	24,062	16,092	1,510	6,460	3,880	2,580	0	0	0	0	0
Other	860	360	100	400	200	200	0	0	0	0	0
Total	**29,494**	**18,894**	**2,300**	**8,300**	**4,800**	**3,500**	**0**	**0**	**0**	**0**	**0**
FUNDING SCHEDULE ($000s)											
Contributions	2,510	1,210	0	1,300	1,300	0	0	0	0	0	0
G.O. Bonds	26,984	17,684	2,300	7,000	3,500	3,500	0	0	0	0	0
Total	**29,494**	**18,894**	**2,300**	**8,300**	**4,800**	**3,500**	**0**	**0**	**0**	**0**	**0**

APPROPRIATION AND EXPENDITURE DATA (000s)

Appropriation Request	FY 16	3,500
Supplemental Appropriation Request		0
Transfer		0
Cumulative Appropriation		25,994
Expenditure / Encumbrances		18,894
Unencumbered Balance		7,100

Date First Appropriation	FY 07	
First Cost Estimate		
Current Scope	FY07	0
Last FY's Cost Estimate		28,194

Description

This project will provide facility modfications to support program offerings at schools that are not scheduled for capital improvements in the six-year CIP. These limited modifications to instruction and support spaces are needed to provide adequate space for new or expanded programs and administrative support space for schools that are not included in the revitalization/expansion program. An FY 2012 appropriation was approved to continue to provide facility modifications at various schools throughout the system. Facility modifications in FY 2013 and beyond will be determined based on the need for space modifications/upgrades to support new or modified program offerings. Due to fiscal constraints, expenditures requested in the Board of Education's FY 2011-2016 CIP for FYs 2013-2016 were removed by the County Council in the adopted FY 2011-2016 CIP. An FY 2013 appropriation was approved to renovate science laboratories at one high school and provide special education facility modifications for two elementary schools and two high schools. An FY 2014 appropriation was approved to continue to provide facility modifications and program improvements to various schools throughout the county. An FY 2015 appropriation was approved for modifications to schools due to special education program changes; science laboratory upgrades at secondary schools; space modifications for program requirements; as well as two specific one-time projects--the construction of an auxiliary gymnasium at Thomas Pyle Middle School and classroom modifications at the Whittier Woods Center to be used by Walt Whitman High School. An FY 2015 appropriation was approved for $1.3 million for the installation of artificial turf at Winston Churchill High School. An FY 2016 appropriation was approved for modifications to schools due to special education program changes, space modifications for program requirements, and computer lab conversions at various schools throughout the county.

Coordination

Mandatory Referral - M-NCPPC, Department of Environmental Protection, Building Permits, Code Review, Fire Marshall, Department of Transportation, Inspections, Sediment Control, Stormwater Management, WSSC Permits

Current Revitalizations/Expansions(P926575)

Category	Montgomery County Public Schools	Date Last Modified	11/17/14
Sub Category	Countywide	Required Adequate Public Facility	No
Administering Agency	Public Schools (AAGE18)	Relocation Impact	None
Planning Area	Countywide	Status	Ongoing

	Total	Thru FY14	Rem FY14	Total 6 Years	FY 15	FY 16	FY 17	FY 18	FY 19	FY 20	Beyond 6 Yrs
EXPENDITURE SCHEDULE ($000s)											
Planning, Design and Supervision	80,144	36,939	8,031	34,606	6,446	8,741	8,362	6,857	3,393	807	568
Land	0	0	0	0	0	0	0	0	0	0	0
Site Improvements and Utilities	178,234	60,095	13,806	95,971	16,342	17,359	10,434	19,430	22,981	9,425	8,362
Construction	900,812	219,730	94,682	534,223	75,221	91,276	92,394	75,404	102,214	97,714	52,177
Other	38,501	10,182	5,463	20,756	1,765	3,278	2,599	2,609	3,847	6,658	2,100
Total	**1,197,691**	**326,946**	**121,982**	**685,556**	**99,774**	**120,654**	**113,789**	**104,300**	**132,435**	**114,604**	**63,207**
FUNDING SCHEDULE ($000s)											
Contributions	2,791	291	0	2,500	2,500	0	0	0	0	0	0
Current Revenue: General	44	0	0	44	0	0	44	0	0	0	0
Current Revenue: Recordation Tax	147,474	14,582	19,082	113,810	2,478	1,984	23,047	26,891	29,197	30,213	0
G.O. Bonds	859,937	266,000	76,523	454,207	61,223	97,277	90,698	63,805	79,816	61,388	63,207
School Facilities Payment	655	0	0	655	517	138	0	0	0	0	0
Schools Impact Tax	83,185	14,352	5,132	63,701	3,672	0	0	13,604	23,422	23,003	0
State Aid	103,605	31,721	21,245	50,639	29,384	21,255	0	0	0	0	0
Total	**1,197,691**	**326,946**	**121,982**	**685,556**	**99,774**	**120,654**	**113,789**	**104,300**	**132,435**	**114,604**	**63,207**
OPERATING BUDGET IMPACT ($000s)											
Energy				6,016	1,191	1,310	869	1,178	734	734	
Maintenance				12,737	2,273	2,592	1,770	2,598	1,752	1,752	
Net Impact				**18,753**	**3,464**	**3,902**	**2,639**	**3,776**	**2,486**	**2,486**	

APPROPRIATION AND EXPENDITURE DATA (000s)

Appropriation Request	FY 16	168,639
Supplemental Appropriation Request		0
Transfer		0
Cumulative Appropriation		676,002
Expenditure / Encumbrances		326,946
Unencumbered Balance		349,056

Date First Appropriation	
First Cost Estimate	
Current Scope	331,923
Last FY's Cost Estimate	1,239,291
Partial Closeout Thru	446,000
New Partial Closeout	44,100
Total Partial Closeout	490,100

Description

This project combines all current revitalization/expansion projects as prioritized by the FACT assessments. Future projects with planning in FY 2017 or later are in PDF No. 886536. Due to fiscal constraints, the Board of Education's Requested FY 2015-2020 CIP includes a one-year delay of elementary school revitalization/expansion projects. Also, in the Board of Education's Requested FY 2015-2020 CIP, the name of this project changed from replacements/modernizations to revitalizations/expansions, to better reflect the scope of work done during these projects. Due to fiscal constraints, the County Council adopted FY 2015-2020 CIP includes a one year delay, beyond the Board of Education's request, for elementary school projects and a one year delay of secondary school projects beginning with Tilden Middle School and Seneca Valley High School; however, all planning funds remained on the Board of Education's requested schedule. An FY 2015 appropriation was approved to provide planning funds for two revitalization/expansion projects, construction funds for one revitalization/expansion project and the balance of funding for three revitalization/expansion projects. An FY 2015 supplemental appropriation of a $2.5 million contribution from Junior Acheivement of Greater Washington was approved to include a Junior Achievement Finance Park during the revitalization of Thomas Edison High School of Technology. The Board of Education's requested FY2015-2020 Amended CIP reinstated the construction schedule previously requested by the Board. Due to fiscal constraints, the County Council did not approve the Board's request. Therefore, revitalization/expansion projects beginning with Potomac ES, Tilden MS, and Seneca Valley HS will remain on their approved schedule. An FY 2016 appropriation was approved for the balance of funding for one project, construction funding for four projects, and planning funding for five projects.

Disclosures

Expenditures will continue indefinitely.

Public Schools (A18) asserts that this project conforms to the requirements of relevant local plans, as required by the Maryland Economic Growth, Resource Protection and Planning Act.

Coordination

Mandatory Referral - M-NCPPC, Department of Environmental Protection, Building Permits, Code Review, Fire Marshal Inspections, Department of Transportation, Sediment Control, Stormwater Management, WSSC Permits

Design and Construction Management (P746032)

Category	Montgomery County Public Schools	Date Last Modified	11/17/14
Sub Category	Countywide	Required Adequate Public Facility	No
Administering Agency	Public Schools (AAGE18)	Relocation Impact	None
Planning Area	Countywide	Status	Ongoing

	Total	Thru FY14	Rem FY14	Total 6 Years	FY 15	FY 16	FY 17	FY 18	FY 19	FY 20	Beyond 6 Yrs
EXPENDITURE SCHEDULE ($000s)											
Planning, Design and Supervision	65,775	31,475	4,900	29,400	4,900	4,900	4,900	4,900	4,900	4,900	0
Land	0	0	0	0	0	0	0	0	0	0	0
Site Improvements and Utilities	0	0	0	0	0	0	0	0	0	0	0
Construction	0	0	0	0	0	0	0	0	0	0	0
Other	0	0	0	0	0	0	0	0	0	0	0
Total	**65,775**	**31,475**	**4,900**	**29,400**	**4,900**	**4,900**	**4,900**	**4,900**	**4,900**	**4,900**	**0**
FUNDING SCHEDULE ($000s)											
G.O. Bonds	65,775	31,475	4,900	29,400	4,900	4,900	4,900	4,900	4,900	4,900	0
Total	**65,775**	**31,475**	**4,900**	**29,400**	**4,900**	**4,900**	**4,900**	**4,900**	**4,900**	**4,900**	**0**

APPROPRIATION AND EXPENDITURE DATA (000s)

Appropriation Request	FY 16	4,900
Supplemental Appropriation Request		0
Transfer		0
Cumulative Appropriation		41,275
Expenditure / Encumbrances		31,475
Unencumbered Balance		9,800

Date First Appropriation	FY 74	
First Cost Estimate		
Current Scope	FY 96	19,723
Last FY's Cost Estimate		65,775
Partial Closeout Thru		55,502
New Partial Closeout		0
Total Partial Closeout		55,502

Description

This project funds positions essential for implementation of the multiyear capital improvements program. Personnel provide project administration, in-house design, and engineering services in the Department of Facilities Management and the Division of Construction. An FY 2011 appropriation was approved for salaries of 41 current staff, legal fees and other non-reimburseable costs for MCPS real estate issues, as well as the transfer of three positions previously in the HVAC PDF. Due to fiscal constraints, $100,000 annually, for a total of $600,000 was removed from this PDF to reflect the reduction of COLAs and step increases for MCPS staff. An FY 2012 appropriation was approved. An FY 2013 appropriation was approved for salaries, legal fees and other non-reimburseable costs for MCPS related real estate issues. An FY 2014 appropriation was approved for this project. An FY 2015 appropriation was approved for salaries of 44 current staff, legal fees and other non-reimburseable costs for MCPS real estate issues. An FY 2016 appropriation was approved for salaries of current staff, legal fees and other non-reimburseable costs for MCPS real estate issues.

Fiscal Note

State Reimbursement: Not eligible

Disclosures

Expenditures will continue indefinitely.

Coordination

Mandatory Referral - M-NCPPC, Department of Environmental Protection, Building Permits, Code Review, Fire Marshall, Department of Transportation, Inspections, Sediment Control, Stormwater Management, WSSC Permits

$(000s)	FY 15	FYs 16-20
Salaries and Wages:	3,581	18,355
Fringe Benefits:	895	4,590
Workyears:	44	220

Energy Conservation: MCPS (P796222)

Category	Montgomery County Public Schools	Date Last Modified	11/17/14
Sub Category	Countywide	Required Adequate Public Facility	No
Administering Agency	Public Schools (AAGE18)	Relocation Impact	None
Planning Area	Countywide	Status	Ongoing

	Total	Thru FY14	Rem FY14	Total 6 Years	FY 15	FY 16	FY 17	FY 18	FY 19	FY 20	Beyond 6 Yrs
EXPENDITURE SCHEDULE ($000s)											
Planning, Design and Supervision	4,390	2,115	325	1,950	325	325	325	325	325	325	0
Land	0	0	0	0	0	0	0	0	0	0	0
Site Improvements and Utilities	0	0	0	0	0	0	0	0	0	0	0
Construction	24,565	12,756	1,687	10,122	1,687	1,687	1,687	1,687	1,687	1,687	0
Other	795	480	45	270	45	45	45	45	45	45	0
Total	**29,750**	**15,351**	**2,057**	**12,342**	**2,057**	**2,057**	**2,057**	**2,057**	**2,057**	**2,057**	**0**
FUNDING SCHEDULE ($000s)											
Federal Stimulus	1,624	1,624	0	0	0	0	0	0	0	0	0
G.O. Bonds	27,438	13,727	1,369	12,342	2,057	2,057	2,057	2,057	2,057	2,057	0
State Aid	688	0	688	0	0	0	0	0	0	0	0
Total	**29,750**	**15,351**	**2,057**	**12,342**	**2,057**	**2,057**	**2,057**	**2,057**	**2,057**	**2,057**	**0**
OPERATING BUDGET IMPACT ($000s)											
Energy				-1,992	-498	-498	-498	-498	0	0	
Maintenance				-1,856	-464	-464	-464	-464	0	0	
Net Impact				**-3,848**	**-962**	**-962**	**-962**	**-962**	**0**	**0**	

APPROPRIATION AND EXPENDITURE DATA (000s)

Appropriation Request	FY 16	2,057
Supplemental Appropriation Request		0
Transfer		0
Cumulative Appropriation		19,465
Expenditure / Encumbrances		13,202
Unencumbered Balance		6,263

Date First Appropriation	FY 79	
First Cost Estimate		
Current Scope	FY 96	8,061
Last FY's Cost Estimate		29,750
Partial Closeout Thru		19,208
New Partial Closeout		0
Total Partial Closeout		19,208

Description

The MCPS Energy Conservation Program has saved more than $34 million since the project began in FY 1978. The project has been reviewed by the Interagency Committee on Energy and Utility Management. The program is designed to reduce energy consumption by improving building mechanical systems, retrofitting building lighting and control systems, and controlling HVAC equipment through computer management systems. Computer systems currently control the operation of most MCPS facilities. New and modernized schools are built with the latest technological advances to achieve higher levels of energy savings. Energy conservation staff review new construction mechanical guidelines and designs. Staff also inspect and perform computer diagnostics of HVAC installations for operational efficiency and review certain aspects of indoor air quality. To date, 197 facilities have energy management system installations; to keep up with advances in computer technology, each is on a schedule for upgrade and/or replacement energy management system installations, 65 remain to be upgraded or replaced. Expenditures in the six-year period will address the controls system integration, the energy managment system upgrades, and continue the countywide lighting modernization schedule. An FY 2014 appropriation was approved to continue this project. An FY 2015 appropriation was approved to continue this level of effort project. An FY 2016 appropriation was approved to continue the upgrades/replacements necessary to reduce energy consumption at MCPS facilities.

Disclosures

Expenditures will continue indefinitely.

Public Schools (A18) asserts that this project conforms to the requirements of relevant local plans, as required by the Maryland Economic Growth, Resource Protection and Planning Act.

Coordination

Montgomery College, County Government, Comprehensive Facilities Plan, Interagency Committee - Energy and Utilities Management, MCPS Resource Conservation Plan, County Code 8-14a

$(000)	FY15	FY16-20
Salries and Wages:	140	700
Fringe Benefits:	65	325
Workyears:	1.5	7.5

Facility Planning: MCPS (P966553)

Category	Montgomery County Public Schools	Date Last Modified	11/17/14
Sub Category	Countywide	Required Adequate Public Facility	No
Administering Agency	Public Schools (AAGE18)	Relocation Impact	None
Planning Area	Countywide	Status	Ongoing

	Total	Thru FY14	Rem FY14	Total 6 Years	FY 15	FY 16	FY 17	FY 18	FY 19	FY 20	Beyond 6 Yrs
EXPENDITURE SCHEDULE ($000s)											
Planning, Design and Supervision	11,097	6,807	600	3,690	900	550	770	400	670	400	0
Land	0	0	0	0	0	0	0	0	0	0	0
Site Improvements and Utilities	0	0	0	0	0	0	0	0	0	0	0
Construction	0	0	0	0	0	0	0	0	0	0	0
Other	0	0	0	0	0	0	0	0	0	0	0
Total	**11,097**	**6,807**	**600**	**3,690**	**900**	**550**	**770**	**400**	**670**	**400**	**0**
FUNDING SCHEDULE ($000s)											
Current Revenue: General	4,312	3,060	180	1,072	270	152	220	120	190	120	0
Current Revenue: Recordation Tax	885	885	0	0	0	0	0	0	0	0	0
G.O. Bonds	5,900	2,862	420	2,618	630	398	550	280	480	280	0
Total	**11,097**	**6,807**	**600**	**3,690**	**900**	**550**	**770**	**400**	**670**	**400**	**0**

APPROPRIATION AND EXPENDITURE DATA (000s)

Appropriation Request	FY 16	550
Supplemental Appropriation Request		0
Transfer		0
Cumulative Appropriation		8,307
Expenditure / Encumbrances		8,001
Unencumbered Balance		306

Date First Appropriation	FY 96	
First Cost Estimate		
Current Scope	FY 96	1,736
Last FY's Cost Estimate		10,997
Partial Closeout Thru		4,891
New Partial Closeout		0
Total Partial Closeout		4,891

Description

The facility planning process provides preliminary programs of requirements (PORs), cost estimates, and budget documentation for selected projects. This project serves as the transition stage from the master plan or conceptual stage to inclusion of a stand-alone project in the CIP. There is a continuing need for the development of accurate cost estimates and an exploration of alternatives for proposed projects. Implementation of the facility planning process results in realistic cost estimates, fewer and less significant cost overruns, fewer project delays, and improved life-cycle costing of projects. In the past, this project was funded solely by current revenue; however, as a result of new environmental regulation changes, design of site development concept plans must be done during the facility planning phase in order to obtain necessary site permits in time for the construction phase. Therefore, the funding sources shown on this PDF reflect the appropriate portions for both current revenue and GO bonds.

Due to fiscal constraints, the County Council, in the adopted FY 2011-2016 CIP, reduced the expenditures in FYs 2013-2016 for this project. An FY 2012 appropriation was approved to continue this project. An FY 2013 appropriation was approved for the pre-planning of three elementary school revitalization/expansion projects, one middle school revitalization/expansion project, six elementary school additions, and one middle school addition. An FY 2014 apppropriation and amendment to the FY 2013-2018 CIP was approved to provide an additional $220,000 for this project to conduct feasibility studies to address overutilization at various school throughout the county. An FY 2015 appropriation was approved for the pre-planning of nine elementary school additions, five middle school additions, one high school addition, one new elementary school, and four elementary school and one high school revitalization/expansion projects. An FY 2016 appropriation and amendment to the adopted CIP was approved for the preplanning of two elementary school additions, five high school additions, and one middle school addition.

Disclosures

Expenditures will continue indefinitely.

Fire Safety Code Upgrades (P016532)

Category	Montgomery County Public Schools	Date Last Modified	11/17/14
Sub Category	Countywide	Required Adequate Public Facility	No
Administering Agency	Public Schools (AAGE18)	Relocation Impact	None
Planning Area	Countywide	Status	Ongoing

	Total	Thru FY14	Rem FY14	Total 6 Years	FY 15	FY 16	FY 17	FY 18	FY 19	FY 20	Beyond 6 Yrs
EXPENDITURE SCHEDULE ($000s)											
Planning, Design and Supervision	2,990	1,430	300	1,260	350	350	140	140	140	140	0
Land	0	0	0	0	0	0	0	0	0	0	0
Site Improvements and Utilities	0	0	0	0	0	0	0	0	0	0	0
Construction	12,493	5,282	1,203	6,008	1,650	1,650	677	677	677	677	0
Other	0	0	0	0	0	0	0	0	0	0	0
Total	**15,483**	**6,712**	**1,503**	**7,268**	**2,000**	**2,000**	**817**	**817**	**817**	**817**	**0**
FUNDING SCHEDULE ($000s)											
G.O. Bonds	15,483	6,712	1,503	7,268	2,000	2,000	817	817	817	817	0
Total	**15,483**	**6,712**	**1,503**	**7,268**	**2,000**	**2,000**	**817**	**817**	**817**	**817**	**0**

APPROPRIATION AND EXPENDITURE DATA (000s)

Appropriation Request	FY 16	2,000
Supplemental Appropriation Request		0
Transfer		0
Cumulative Appropriation		10,215
Expenditure / Encumbrances		8,652
Unencumbered Balance		1,563

Date First Appropriation FY 01	
First Cost Estimate	
Current Scope	0
Last FY's Cost Estimate	15,483

Description

This project addresses sprinklers, escape windows, exit signs, fire alarm devices, exit stairs, and hood and fire supression systems to comply with annual Fire Marshal inspections. An FY 2011 appropriation was approved to continue this program to maintain code compliance and life-cycle equipment replacement. An FY 2012 appropriation was approved to continue this level of effort project. An FY 2013 appropriation was approved to maintain life safety code compliance and equipment life-cycle replacements at MCPS facilities systemwide. An FY 2014 appropriation was approved to continue this project. An FY 2015 appropriation was approved to continue this level of effort project and maintain life safety code coomplaince through equipment replacement such as fire alarm systems that will be over 20 years old and will have exceeded their anticipated life-cycle. An FY 2016 appropriation was approved to continue this level of effort project.

Coordination

Fire Marshal

Future Revitalizations/Expansions(P886536)

Category	Montgomery County Public Schools	Date Last Modified	11/17/14
Sub Category	Countywide	Required Adequate Public Facility	No
Administering Agency	Public Schools (AAGE18)	Relocation Impact	None
Planning Area	Countywide	Status	Ongoing

	Total	Thru FY14	Rem FY14	Total 6 Years	FY 15	FY 16	FY 17	FY 18	FY 19	FY 20	Beyond 6 Yrs
EXPENDITURE SCHEDULE ($000s)											
Planning, Design and Supervision	28,576	0	0	14,128	0	0	0	3,368	5,532	5,228	14,448
Land	0	0	0	0	0	0	0	0	0	0	0
Site Improvements and Utilities	69,699	0	0	8,528	0	0	0	0	0	8,528	61,171
Construction	254,460	0	0	10,484	0	0	0	0	0	10,484	243,976
Other	13,108	0	0	0	0	0	0	0	0	0	13,108
Total	**365,843**	**0**	**0**	**33,140**	**0**	**0**	**0**	**3,368**	**5,532**	**24,240**	**332,703**
FUNDING SCHEDULE ($000s)											
G.O. Bonds	365,843	0	0	33,140	0	0	0	3,368	5,532	24,240	332,703
Total	**365,843**	**0**	**0**	**33,140**	**0**	**0**	**0**	**3,368**	**5,532**	**24,240**	**332,703**

APPROPRIATION AND EXPENDITURE DATA (000s)

Appropriation Request	FY 16	0
Supplemental Appropriation Request		0
Transfer		0
Cumulative Appropriation		0
Expenditure / Encumbrances		0
Unencumbered Balance		0

Date First Appropriation	
First Cost Estimate	
Current Scope	50,028
Last FY's Cost Estimate	365,843
Partial Closeout Thru	0
New Partial Closeout	0
Total Partial Closeout	0

Description

The Board of Education strongly supports the upgrading of facilities through comprehensive revitalization/expansion to replace major building systems and to bring schools up to current educational standards. As feasibility studies are completed and architectural planning is scheduled, individual schools move from this project to the Current Revitalization/Expansion PDF No. 926575. The adopted FY 2011-2016 CIP moved three elementary schools, one middle school, and one high school from this project to the Current Revitalization/Expansion project. Also, the adopted FY 2011-2016 CIP provided completion dates for one middle school and one high school. The Board of Education's Requested FY 2013-2018 CIP moves three elementary schools and one high school from this project to the Current Revitalization/Expansion project. Also, based on the new Facility Assessment with Criteria and Testing (FACT)conducted in 2010-2011, eight elementary schools were appended to the current revitalization/expansion schedule. Due to fiscal constraints, the County Council's adopted FY 2013-2018 CIP includes a two year delay for for middle school revitalizations/expansions beginning with Tilden Middle School and a two year delay for high school revitalizations/expansions beginning with Seneca Valley High School.
The Board of Education's Requested FY 2015-2020 CIP moved one middle and one high school from this project to the Current Revitalization/Expansion project. Due to fiscal constraints the County Council adopted FY 2015-2020 CIP delayed elementary school projects one year beyond the Board of Education's request and delayed secondary projects one year beginning with Tilden Middle School and Seneca Valley High School; however, all planning funds remained on the Board of Education's requested schedule. The Board of Education's requested FY 2015-2020 Amended CIP reinstated the construction schedule previously requested by the Board. Due to fiscal constraints, the County Council did not approve the Board's request. Therefore, the revitalization/expansion projects beginning with Potomac ES, Tilden MS, and Seneca Valley HS will remain on their approved schedules. A complete list of the revitalization/expansion schedule is in Appendix E of the FY 2016 Educational Facilities Master Plan.

Disclosures

Expenditures will continue indefinitely.

Coordination

Mandatory Referral - M-NCPPC, Department of Environmental Protection, Building Permits, Code Review, Fire Marshal, Department of Transportation, Inspections, Sediment Control, Stormwater Management, WSSC Permits

HVAC (Mechanical Systems) Replacement: MCPS (P816633)

Category	Montgomery County Public Schools	Date Last Modified	11/17/14
Sub Category	Countywide	Required Adequate Public Facility	No
Administering Agency	Public Schools (AAGE18)	Relocation Impact	None
Planning Area	Countywide	Status	Ongoing

	Total	Thru FY14	Rem FY14	Total 6 Years	FY 15	FY 16	FY 17	FY 18	FY 19	FY 20	Beyond 6 Yrs
EXPENDITURE SCHEDULE ($000s)											
Planning, Design and Supervision	27,200	5,900	2,000	19,300	5,200	4,100	2,500	2,500	2,500	2,500	0
Land	0	0	0	0	0	0	0	0	0	0	0
Site Improvements and Utilities	0	0	0	0	0	0	0	0	0	0	0
Construction	107,767	28,287	6,780	72,700	22,800	11,900	9,500	9,500	9,500	9,500	0
Other	0	0	0	0	0	0	0	0	0	0	0
Total	**134,967**	**34,187**	**8,780**	**92,000**	**28,000**	**16,000**	**12,000**	**12,000**	**12,000**	**12,000**	**0**
FUNDING SCHEDULE ($000s)											
G.O. Bonds	107,158	22,083	4,684	80,391	20,355	12,036	12,000	12,000	12,000	12,000	0
State Aid	27,809	12,104	4,096	11,609	7,645	3,964	0	0	0	0	0
Total	**134,967**	**34,187**	**8,780**	**92,000**	**28,000**	**16,000**	**12,000**	**12,000**	**12,000**	**12,000**	**0**

APPROPRIATION AND EXPENDITURE DATA (000s)

Appropriation Request	FY 16	16,000
Supplemental Appropriation Request		0
Transfer		0
Cumulative Appropriation		70,967
Expenditure / Encumbrances		34,187
Unencumbered Balance		36,780

Date First Appropriation	FY 81	
First Cost Estimate		
Current Scope	FY 96	16,388
Last FY's Cost Estimate		150,076
Partial Closeout Thru		75,396
New Partial Closeout		12,247
Total Partial Closeout		87,643

Description

This project provides for the systematic replacement of heating, ventilating, air conditioning, automated temperature controls, and plumbing systems for MCPS facilities. This replacement approach is based on indoor environmental quality (IEQ), energy performance, maintenance data, and the modernization schedule. Qualifying systems and/or components are selected based on the above criteria and are prioritized within the CIP through a rating system formula. MCPS is participating in interagency planning and review to share successful and cost effective approaches. For projects on the revitalization/expansion schedule, the scope is reduced to the minimum necessary to maintain the operation of the existing mechanical system. Any new equipment installations will be salvaged at the time of the revitalization/expansion project and will be re-used.

An FY 2012 appropriation and amendment to the FY 2011-2016 CIP was approved to provide an additional $6.52 million above the adopted CIP to reinstate funds that were removed by the County Council during reconciliation in May 2010. An FY 2013 appropriation was approved for mechanical systems upgrades and/or replacements at Damascus and Col. Zadok Magruder high schools, Neelesville Middle School, and Takoma Park, Waters Landing, Cold Spring, Rosemary Hills, Rachel Carson, Washington Grove, Bannockburn, Westbrook, East Silver Spring, and Piney Branch elementary schools. The County Council, in the adopted FY 2013-2018 CIP, significantly reduced the expenditures requested by the Board of Education for this project for FY 2014 and beyond. An FY 2014 appropriation and amendment to the FY 2013-2018 CIP was requested to provide an additional $11.46 million above the adopted CIP to reinstate funds that were removed by the County Council during reconciliation in May 2012. However, the County Council, in the adopted FY 2013-2018 Amended Cip, approved only $3.82 million of the $11.46 million requested by the Board.

Due to fiscal constraints, the County Council adopted FY 2015-2020 CIP reduced the FY 2016 expenditures requested by the Board of Education from $28 million to $16 million, but increased the outyears by a total of $8 million ($2 million in FYs 2017-2020). An FY 2015 appropriation was approved for mechanical systems upgrades and/or replacements at Damascus, Quince Orchard, and Watkins Mill high schools; Thomas Pyle, Shady Grove, and Silver Spring International middle schools; and Woodfield, Goshen, Whetsone, Summit Hall, S. Christa McAuliffe, Lake Seneca, Sligo Creek, Brooke Grove, Clearspring, Laytonsville, and New Hamsphire Estates elementary schools. An FY 2016 appropriation was approved for mechanical systems upgrades and/or replacements at Quince Orchard (Phase II) and Damscus (Phase III) high schools; Shady Grove (Phase II) Middle School; and Beall, Burning Tree, Captain Daly, Highland, and Rolling Terrace elementary schools.

Disclosures

Expenditures will continue indefinitely.

Public Schools (A18) asserts that this project conforms to the requirements of relevant local plans, as required by the Maryland Economic Growth, Resource Protection and Planning Act.

Coordination

CIP Master Plan for School Facilities

Improved (Safe) Access to Schools (P975051)

Category	Montgomery County Public Schools	Date Last Modified	11/17/14
Sub Category	Countywide	Required Adequate Public Facility	No
Administering Agency	Public Schools (AAGE18)	Relocation Impact	None
Planning Area	Countywide	Status	Ongoing

	Total	Thru FY14	Rem FY14	Total 6 Years	FY 15	FY 16	FY 17	FY 18	FY 19	FY 20	Beyond 6 Yrs
EXPENDITURE SCHEDULE ($000s)											
Planning, Design and Supervision	1,366	766	200	400	200	200	0	0	0	0	0
Land	0	0	0	0	0	0	0	0	0	0	0
Site Improvements and Utilities	8,977	5,977	1,000	2,000	1,000	1,000	0	0	0	0	0
Construction	0	0	0	0	0	0	0	0	0	0	0
Other	0	0	0	0	0	0	0	0	0	0	0
Total	**10,343**	**6,743**	**1,200**	**2,400**	**1,200**	**1,200**	**0**	**0**	**0**	**0**	**0**
FUNDING SCHEDULE ($000s)											
G.O. Bonds	10,343	6,743	1,200	2,400	1,200	1,200	0	0	0	0	0
Total	**10,343**	**6,743**	**1,200**	**2,400**	**1,200**	**1,200**	**0**	**0**	**0**	**0**	**0**

APPROPRIATION AND EXPENDITURE DATA (000s)

Appropriation Request	FY 16	1,200
Supplemental Appropriation Request		0
Transfer		0
Cumulative Appropriation		9,143
Expenditure / Encumbrances		6,743
Unencumbered Balance		2,400

Date First Appropriation	FY 97	
First Cost Estimate		
Current Scope	FY 97	1,185
Last FY's Cost Estimate		10,343
Partial Closeout Thru		13,126
New Partial Closeout		485
Total Partial Closeout		13,611

Description

This project addresses vehicular and pedestrian access to schools. It may involve the widening of a street or roadway, obtaining rights-of-way for school access or exit, or changing or adding entrance/exits at various schools. These problems may arise at schools where there are no construction projects or DOT road projects that could fund the necessary changes.

An FY 2011 appropriation was approved to address access, circulation, and vehicular and pedestrian traffic issues at schools throughout the county. Expenditures are shown for only the first two years of the CIP. Funding beyond the first two years will be reviewed during each on-year of the CIP cycle. An FY 2012 appropriation was approved to continue this project. An FY 2013 appropriation was approved to address access, circulation, and vehicular and pedestrian traffic issues at two high schools, one middle school, and one elementary school. An FY 2014 appropriation was approved to continue this project. An FY 2015 appropriation was approved to address access, circulation, and vehicular and pedestrian traffice issues at Julius West Middle School, North Bethesda Middle School, Ashburton Elementary School and Judith Resnik Elementary School. An FY 2016 appropriation was approved to continue this project.

Fiscal Note

State Reimbursement: not eligible

Disclosures

Expenditures will continue indefinitely.

Coordination

STEP Committee

Indoor Air Quality Improvements: MCPS (P006503)

Category	Montgomery County Public Schools	Date Last Modified	11/17/14
Sub Category	Countywide	Required Adequate Public Facility	No
Administering Agency	Public Schools (AAGE18)	Relocation Impact	None
Planning Area	Countywide	Status	Ongoing

	Total	Thru FY14	Rem FY14	Total 6 Years	FY 15	FY 16	FY 17	FY 18	FY 19	FY 20	Beyond 6 Yrs
EXPENDITURE SCHEDULE ($000s)											
Planning, Design and Supervision	11,766	4,476	942	6,348	1,290	1,290	942	942	942	942	0
Land	0	0	0	0	0	0	0	0	0	0	0
Site Improvements and Utilities	0	0	0	0	0	0	0	0	0	0	0
Construction	15,945	11,701	520	3,724	822	822	520	520	520	520	0
Other	350	105	35	210	35	35	35	35	35	35	0
Total	**28,061**	**16,282**	**1,497**	**10,282**	**2,147**	**2,147**	**1,497**	**1,497**	**1,497**	**1,497**	**0**
FUNDING SCHEDULE ($000s)											
G.O. Bonds	28,061	16,282	1,497	10,282	2,147	2,147	1,497	1,497	1,497	1,497	0
Total	**28,061**	**16,282**	**1,497**	**10,282**	**2,147**	**2,147**	**1,497**	**1,497**	**1,497**	**1,497**	**0**

APPROPRIATION AND EXPENDITURE DATA (000s)

Appropriation Request	FY 16	2,147
Supplemental Appropriation Request		0
Transfer		0
Cumulative Appropriation		19,926
Expenditure / Encumbrances		16,282
Unencumbered Balance		3,644

Date First Appropriation	FY 99	
First Cost Estimate		
Current Scope	FY02	3,800
Last FY's Cost Estimate		28,061

Description

This project funds mechanical retrofits and building envelope modifications necessary to address schools experiencing Indoor Air Quality (IAQ) problems. In the FY 2005-2010 CIP, the County Council approved a level of effort funding for the outyears of this project in order to adequately illustrate that this project will continue for the foreseeable future. Funds approved in FYs 2006-2010 were used to address indoor air quality issues systemwide. An FY 2011 appropriation was approved to continue to address indoor air quality issues through various remediation efforts including carpet removal, floor tile replacement, and minor mechanical retrofits. Due to fiscal constraints, the County Council's adopted FY 2011-2016 CIP reduced the expenditures, as requested in the Board of Education's FY 2011-2016 CIP for FYs 2012-2016 by approximately $2.8 million. The title of this PDF was change to more accurately reflect the work accomplished in this project.

An FY 2012 appropriation and amendment to the FY 2011-2016 CIP was approved to provide an additional $394,000 above the adopted CIP to reinstate funds that were removed by the County Council during reconciliation in May 2010. An FY 2013 appropriation was approved to continue to address indoor air quaility issues through remediation efforts such as carpet removal, floor and ceiling tile replacement, and minor mechanical retrofits. An FY 2014 appropriation was approved to continue this level of effort project. An FY 2015 appropriation was approved to address indoor air quality issues throughout the school system. The increase in for FY 2015 will provide funds for replacements of pipe insulation to improve indoor air quality where identified. An FY 2016 appropriation was approved to continue this level of effort project.

Fiscal Note

State reimbursement: not eligible

Coordination

Department of Environmental Protection, Department of Health and Human Services, American Lung Association

($000s)	FY 15	FY 16-20
Salaries and Wages	266	1330
Fringe Benefits	123	615
Workyears:	4	20

Planned Life Cycle Asset Repl: MCPS (P896586)

Category	Montgomery County Public Schools	Date Last Modified	11/17/14
Sub Category	Countywide	Required Adequate Public Facility	No
Administering Agency	Public Schools (AAGE18)	Relocation Impact	None
Planning Area	Countywide	Status	Ongoing

	Total	Thru FY14	Rem FY14	Total 6 Years	FY 15	FY 16	FY 17	FY 18	FY 19	FY 20	Beyond 6 Yrs
EXPENDITURE SCHEDULE ($000s)											
Planning, Design and Supervision	10,968	3,518	900	6,550	1,225	1,725	900	900	900	900	0
Land	0	0	0	0	0	0	0	0	0	0	0
Site Improvements and Utilities	11,345	7,395	500	3,450	725	725	500	500	500	500	0
Construction	71,052	38,907	4,569	27,576	6,912	7,300	3,341	3,341	3,341	3,341	0
Other	0	0	0	0	0	0	0	0	0	0	0
Total	**93,365**	**49,820**	**5,969**	**37,576**	**8,862**	**9,750**	**4,741**	**4,741**	**4,741**	**4,741**	**0**
FUNDING SCHEDULE ($000s)											
Aging Schools Program	6,361	5,155	603	603	603	0	0	0	0	0	0
G.O. Bonds	77,375	36,670	4,741	35,964	7,250	9,750	4,741	4,741	4,741	4,741	0
Qualified Zone Academy Funds	9,629	7,995	625	1,009	1,009	0	0	0	0	0	0
Total	**93,365**	**49,820**	**5,969**	**37,576**	**8,862**	**9,750**	**4,741**	**4,741**	**4,741**	**4,741**	**0**

APPROPRIATION AND EXPENDITURE DATA (000s)

Appropriation Request	FY 16	9,750
Supplemental Appropriation Request		0
Transfer		0
Cumulative Appropriation		64,651
Expenditure / Encumbrances		49,820
Unencumbered Balance		14,831

Date First Appropriation	FY 89	
First Cost Estimate		
Current Scope	FY 96	24,802
Last FY's Cost Estimate		90,506
Partial Closeout Thru		49,807
New Partial Closeout		1,253
Total Partial Closeout		51,060

Description

This project funds a comprehensive and ongoing plan to replace key facility and site components based on an inventory of their age and conditions. A comprehensive inventory of all such components has been assembled so that replacements can be anticipated and accomplished in a planned and orderly manner. Facility components included in this project are code corrections, physical education facility/field improvements, school facility exterior resurfacing, partitions, doors, lighting, media center security gates, bleachers, communication systems, and flooring.

An FY 2013 appropriation was approved to fund capital projects that will address MCPS infrastructure. The County Council, in the adopted FY 2013-2018 CIP significantly reduced the expenditures requested by the Board of Education for this project for FY 2014 and beyond. An FY 2014 appropriation and amendment to the FY 2013-2018 CIP was requested to provide an additional $2.49 million above the adopted CIP to reinstate funds that were removed by the County Council during reconciliation in May 2012. However, the County Council, in the adopted FY 2013-2018 Amended CIP did not approve the $2.49 million amendment as requested by the Board. An FY 2013 supplemental approporiation of $3.1 million was approved through the state's ASP program and an FY 2013 supplemental appropriation of $2.0 million was approved through the state's QZAB program. An FY 2015 appropriation was approved to reinstate funds that were removed by the County Council during the last full CIP approval process in order to address our aging infrastructure through the PLAR program. An FY 2015 supplemental appropriation of $603,000 was approved through the state's ASP program and $1.009 million was approved through the state's QZAB program.

An FY 2016 appropriation and amendment was approved to continue this level of effort project and also provide an additional $2.5 million in FY 2016 to address immediate facility issues at schools that are waiting for a major capital project. For a list of projects completed during the summer of 2014, see Appendix R of the FY 2016 Educational Facilities Master Plan.

Disclosures

Expenditures will continue indefinitely.

Public Schools (A18) asserts that this project conforms to the requirements of relevant local plans, as required by the Maryland Economic Growth, Resource Protection and Planning Act.

Coordination

CIP Master Plan for School Facilities,

	FY 15	FY 16-20
Salaries and Wages	361	1805
Fringe Benefits	161	805
Workyears	5	25

Rehab/Reno.Of Closed Schools- RROCS (P916587)

Category	Montgomery County Public Schools	Date Last Modified	11/17/14
Sub Category	Countywide	Required Adequate Public Facility	No
Administering Agency	Public Schools (AAGE18)	Relocation Impact	None
Planning Area	Countywide	Status	Ongoing

	Total	Thru FY14	Rem FY14	Total 6 Years	FY 15	FY 16	FY 17	FY 18	FY 19	FY 20	Beyond 6 Yrs
EXPENDITURE SCHEDULE ($000s)											
Planning, Design and Supervision	11,862	4,830	0	3,258	1,303	977	652	326	0	0	3,774
Land	0	0	0	0	0	0	0	0	0	0	0
Site Improvements and Utilities	17,565	9,660	0	2,905	0	0	2,179	726	0	0	5,000
Construction	134,886	57,043	0	28,118	0	0	5,624	19,683	2,811	0	49,725
Other	5,006	3,906	0	1,100	0	0	0	330	770	0	0
Total	**169,319**	**75,439**	**0**	**35,381**	**1,303**	**977**	**8,455**	**21,065**	**3,581**	**0**	**58,499**
FUNDING SCHEDULE ($000s)											
Current Revenue: General	2,765	2,765	0	0	0	0	0	0	0	0	0
G.O. Bonds	124,174	43,286	0	22,389	673	977	0	17,158	3,581	0	58,499
PAYGO	375	375	0	0	0	0	0	0	0	0	0
Recordation Tax - PAYGO	7,000	7,000	0	0	0	0	0	0	0	0	0
Schools Impact Tax	13,690	698	0	12,992	630	0	8,455	3,907	0	0	0
State Aid	21,315	21,315	0	0	0	0	0	0	0	0	0
Total	**169,319**	**75,439**	**0**	**35,381**	**1,303**	**977**	**8,455**	**21,065**	**3,581**	**0**	**58,499**
OPERATING BUDGET IMPACT ($000s)											
Energy				716	199	199	0	0	159	159	
Maintenance				1,616	381	381	0	0	427	427	
Net Impact				**2,332**	**580**	**580**	**0**	**0**	**586**	**586**	

APPROPRIATION AND EXPENDITURE DATA (000s)

Appropriation Request	FY 16	0
Supplemental Appropriation Request		0
Transfer		0
Cumulative Appropriation		78,697
Expenditure / Encumbrances		75,439
Unencumbered Balance		3,258

Date First Appropriation	
First Cost Estimate	
Current Scope	15,152
Last FY's Cost Estimate	169,319

Description

MCPS retained some closed schools for use for office space, as holding schools, or for alternative programs. Occasionally a closed school is reopened as an operating school to address increasing enrollment. Some rehabilitation is necessary to restore spaces for contemporary instructional use. An FY 2011 appropriation was approved for the construction funds for the reopening of McKenney Hills. An FY 2012 appropriation was approved for the balance of funding for the McKenney Hills Reopening project. This project is scheduled to be completed in August 2012.

Student enrollment at elementary schools in the Richard Montgomery Cluster has increased dramatically over the past four school years. The magnitude of enrollment growth in the cluster requires the opening of a new elementary school. A feasibility study was conducted during the 2010–2011 school year for a new elementary school at the site of the former Hungerford Park Elementary School. Based on the revised enrollment projections for Richard Montgomery Cluster elementary schools, the new elementary school will be sufficient to address the projected elementary enrollment in the cluster. An FY 2013 appropriation was requested by the Board of Education for planning funds for this new school; however, the County Council, in the adopted FY 2013-2108 CIP delayed this project two years. An FY 2012 transfer was approved to shift $4.5 million from the Downcounty Consortium Elementary School #29 to another project in the approved CIP. An FY 2015 appropriation was approved to begin planning the new Richard Montgomery Elementary School #5. However, due to fiscal constraints, the construction funds for this project were delayed one year in the approved FY2015-2020 CIP. The Board of Education's requested FY 2015-2020 Amended CIP reinstated the construction schedule previously requested by the Board. Due to fiscal constraints, the County Council did not approve the Board's request. An FY 2017 appropriation will be requested for construction funds. The completion date for this project is August 2018.

Public Schools (A18) asserts that this project conforms to the requirements of relevant local plans, as required by the Maryland Economic Growth, Resource Protection and Planning Act.

Coordination

Mandatory Referral - M-NCPPC, Department of Environmental Protection, Building Permits, Code Review, Fire Marshal, Department of Transportation, Inspections, Sediment Control, Stormwater Management, WSSC Permits

Relocatable Classrooms (P846540)

Category	Montgomery County Public Schools	Date Last Modified	11/17/14
Sub Category	Countywide	Required Adequate Public Facility	No
Administering Agency	Public Schools (AAGE18)	Relocation Impact	None
Planning Area	Countywide	Status	Ongoing

	Total	Thru FY14	Rem FY14	Total 6 Years	FY 15	FY 16	FY 17	FY 18	FY 19	FY 20	Beyond 6 Yrs
EXPENDITURE SCHEDULE ($000s)											
Planning, Design and Supervision	3,475	1,575	400	1,500	500	500	500	0	0	0	0
Land	0	0	0	0	0	0	0	0	0	0	0
Site Improvements and Utilities	0	0	0	0	0	0	0	0	0	0	0
Construction	42,336	25,236	3,600	13,500	4,500	4,500	4,500	0	0	0	0
Other	0	0	0	0	0	0	0	0	0	0	0
Total	**45,811**	**26,811**	**4,000**	**15,000**	**5,000**	**5,000**	**5,000**	**0**	**0**	**0**	**0**
FUNDING SCHEDULE ($000s)											
Current Revenue: General	41,387	26,333	4,000	11,054	1,054	5,000	5,000	0	0	0	0
Current Revenue: Recordation Tax	4,424	478	0	3,946	3,946	0	0	0	0	0	0
Total	**45,811**	**26,811**	**4,000**	**15,000**	**5,000**	**5,000**	**5,000**	**0**	**0**	**0**	**0**

APPROPRIATION AND EXPENDITURE DATA (000s)

Appropriation Request	FY 16	0
Supplemental Appropriation Request		0
Transfer		0
Cumulative Appropriation		35,811
Expenditure / Encumbrances		26,811
Unencumbered Balance		9,000

Date First Appropriation	FY 84	
First Cost Estimate		
Current Scope	FY02	21,470
Last FY's Cost Estimate		45,811
Partial Closeout Thru		56,588
New Partial Closeout		0
Total Partial Closeout		56,588

Description

MCPS currently has a total of 498 relocatable classrooms. Of the 498 relocatables, 382 are used to address over utilization at various schools throughout the system. The balance, 116 relocatables, are used at schools undergoing construction projects on-site, or at holding schools, or for other uses countywide. Units around 15-20 years old require general renovation if they are to continue in use as educational spaces.

An FY 2011 supplemental appropriation of $2.2 million was approved by the County Council to accelerate the FY 2012 appropriation requested by the Board of Education to allow MCPS to enter into contracts in order to have the relocatable units ready for the 2011-2012 school year. An FY 2012 supplemental appropriation of $4.0 million was approved to accelerate the FY 2013 appropriation requested by the Board of Education to allow MCPS to enter into contracts in order to have the relocatable units ready for the 2012-2013 school year. An FY 2013 supplemental approriation of $4.0 million was approved to accelerate the FY 2014 appropriation requested by the Board of Education to allow MCPS to enter into contracts in order to have the relocatables ready for the 2013-2014 school year. An FY 2014 supplemental appropriation of $5.0 million was approved to accelerate the FY 2015 appropriation requested by the Board of Education to allow MCPS to enter into contracts in order to have the relocatables ready for the 2014-2015 school year. An FY 2015 supplemental appropriation of $5.0 million was approved to accelerate the FY 2016 appropriation requested by the Board of Education to enter into contracts in order to have relocatables ready for the 2015-2016 school year.

Disclosures

Expenditures will continue indefinitely.

Coordination

CIP Master Plan for School Facilities

Restroom Renovations (P056501)

Category	Montgomery County Public Schools	Date Last Modified	11/17/14
Sub Category	Countywide	Required Adequate Public Facility	No
Administering Agency	Public Schools (AAGE18)	Relocation Impact	None
Planning Area	Countywide	Status	Ongoing

	Total	Thru FY14	Rem FY14	Total 6 Years	FY 15	FY 16	FY 17	FY 18	FY 19	FY 20	Beyond 6 Yrs
EXPENDITURE SCHEDULE ($000s)											
Planning, Design and Supervision	1,210	760	100	350	100	100	100	50	0	0	0
Land	0	0	0	0	0	0	0	0	0	0	0
Site Improvements and Utilities	0	0	0	0	0	0	0	0	0	0	0
Construction	11,875	7,975	900	3,000	900	900	900	300	0	0	0
Other	0	0	0	0	0	0	0	0	0	0	0
Total	**13,085**	**8,735**	**1,000**	**3,350**	**1,000**	**1,000**	**1,000**	**350**	**0**	**0**	**0**
FUNDING SCHEDULE ($000s)											
G.O. Bonds	13,085	8,735	1,000	3,350	1,000	1,000	1,000	350	0	0	0
Total	**13,085**	**8,735**	**1,000**	**3,350**	**1,000**	**1,000**	**1,000**	**350**	**0**	**0**	**0**

APPROPRIATION AND EXPENDITURE DATA (000s)

Appropriation Request	FY 16	1,000
Supplemental Appropriation Request		0
Transfer		0
Cumulative Appropriation		10,735
Expenditure / Encumbrances		8,735
Unencumbered Balance		2,000

Date First Appropriation	FY 05	
First Cost Estimate		
Current Scope	FY05	0
Last FY's Cost Estimate		13,085

Description

This project will provide needed modifications to specific areas of restroom facilities. A study was conducted in FY 2004 to evaluate restrooms for all schools that were built or renovated before 1985. Schools on the moderniation list with either planning or construction funding in the six-year CIP were excluded from this list. Ratings were based upon visual inspections of the existing materials and fixtures as of August 1, 2003. Ratings also were based on conversations with the building services managers, principals, vice principals, and staffs about the existing conditions of the restroom facilities. The numeric rating for each school was based on an evaluation method using a preset number scale for the assessment of the existing plumbing fixtures, accessories, and room finish materials.

An FY 2010 appropriation was approved to address the remaining schools identified on the list for restroom renovations. In FY 2010, a second round of assessments were completed, which included a total of 110 schools, including holding facilities. An FY 2011 appropriation was approved to begin the renovations of the schools identified in the second round of assessments. Based on the expenditures shown above, the first 71 schools are proposed for renovation in the FY 2011-2016 CIP. An FY 2012 appropriation was approved to continue this project. An FY 2013 appropriation was approved to continue the renovations of restroom facilities. An FY 2014 appropriation was approved to continue this project. An FY 2015 appropriation was approved to provide restroom renovations for school identified for this project. An FY 2016 appropriation was approved to continue this project. BY FY 2018, based on the expenditures shown above, all 110 schools assessed will be completed. The list of approved restroom renovations is shown in Appendix G of the FY 2016 Educational Facilities Master Plan.

Roof Replacement: MCPS (P766995)

Category	Montgomery County Public Schools	Date Last Modified	11/17/14
Sub Category	Countywide	Required Adequate Public Facility	No
Administering Agency	Public Schools (AAGE18)	Relocation Impact	None
Planning Area	Countywide	Status	Ongoing

	Total	Thru FY14	Rem FY14	Total 6 Years	FY 15	FY 16	FY 17	FY 18	FY 19	FY 20	Beyond 6 Yrs
EXPENDITURE SCHEDULE ($000s)											
Planning, Design and Supervision	4,945	990	495	3,460	740	740	495	495	495	495	0
Land	0	0	0	0	0	0	0	0	0	0	0
Site Improvements and Utilities	0	0	0	0	0	0	0	0	0	0	0
Construction	61,283	17,640	5,231	38,412	7,260	7,260	5,973	5,973	5,973	5,973	0
Other	0	0	0	0	0	0	0	0	0	0	0
Total	**66,228**	**18,630**	**5,726**	**41,872**	**8,000**	**8,000**	**6,468**	**6,468**	**6,468**	**6,468**	**0**
FUNDING SCHEDULE ($000s)											
G.O. Bonds	53,648	12,938	3,206	37,504	5,079	6,553	6,468	6,468	6,468	6,468	0
State Aid	12,580	5,692	2,520	4,368	2,921	1,447	0	0	0	0	0
Total	**66,228**	**18,630**	**5,726**	**41,872**	**8,000**	**8,000**	**6,468**	**6,468**	**6,468**	**6,468**	**0**

APPROPRIATION AND EXPENDITURE DATA (000s)

Appropriation Request	FY 16	8,000
Supplemental Appropriation Request		0
Transfer		0
Cumulative Appropriation		32,356
Expenditure / Encumbrances		18,630
Unencumbered Balance		13,726

Date First Appropriation	FY 76	
First Cost Estimate		
Current Scope	FY 96	19,470
Last FY's Cost Estimate		72,153
Partial Closeout Thru		64,212
New Partial Closeout		6,236
Total Partial Closeout		70,448

Description

The increasing age of buildings has created a backlog of work to replace roofs on their expected 20 year life cycle. Roofs are replaced when schools are not in session, and are scheduled during the summer. This is an annual request, funded since FY 1976.

An FY 2012 appropriation was approved and will provide funding for partial roof replacements at Broad Acres, Fairland, Oak View and Olney elementary schools, Sligo Middle School, and Damascus and Sherwood high schools. Also, the FY 2012 appropriation will provide funding for a full roof replacement at Rachel Carson Elementary School. An FY 2013 appropriation was approved for partial roof replacements at Pine Crest, Stedwick, Dr. Charles R. Drew, Summit Hall, and Whetstone elementary schools and full roof replacements at Damascus, Judith A. Resnick and Sequoyah elementary schools. An FY 2014 appropriation was approved to continue this project.

An FY 2015 appropriation was approved for partial roof replacements at Fields Road, Olney, and Rockwell elementary schools and Walt Whitman High School as well as full roof replacements at Briggs Chaney, White Oak, and Roberto Clemente middle schools. An FY 2016 appropriation was approved for partial roof replacements at Albert Einstein and Walt Whitman high schools; Newport Mill Middle School; Galway,Thurgood Marshall, Rock Creek Valley and Washington Grove elementary schools; and the Stephen Knolls Center.

Fiscal Note

State Reimbursement: reimbursement of the state share of eligible costs will continue to be pursued.

Disclosures

Expenditures will continue indefinitely.

Public Schools (A18) asserts that this project conforms to the requirements of relevant local plans, as required by the Maryland Economic Growth, Resource Protection and Planning Act.

Coordination

CIP Master Plan for School Facilities

($000s)	FY15	FY 16-20
Salaries and Wages	158	790
Fringe Benefits	73	365
Workyears	2	10

School Security Systems (P926557)

Category	Montgomery County Public Schools	Date Last Modified	11/17/14
Sub Category	Countywide	Required Adequate Public Facility	No
Administering Agency	Public Schools (AAGE18)	Relocation Impact	None
Planning Area	Countywide	Status	Ongoing

	Total	Thru FY14	Rem FY14	Total 6 Years	FY 15	FY 16	FY 17	FY 18	FY 19	FY 20	Beyond 6 Yrs
EXPENDITURE SCHEDULE ($000s)											
Planning, Design and Supervision	2,000	1,400	400	200	200	0	0	0	0	0	0
Land	0	0	0	0	0	0	0	0	0	0	0
Site Improvements and Utilities	0	0	0	0	0	0	0	0	0	0	0
Construction	16,610	8,214	5,460	2,936	2,936	0	0	0	0	0	0
Other	0	0	0	0	0	0	0	0	0	0	0
Total	**18,610**	**9,614**	**5,860**	**3,136**	**3,136**	**0**	**0**	**0**	**0**	**0**	**0**
FUNDING SCHEDULE ($000s)											
G.O. Bonds	14,424	9,614	1,674	3,136	3,136	0	0	0	0	0	0
State Aid	4,186	0	4,186	0	0	0	0	0	0	0	0
Total	**18,610**	**9,614**	**5,860**	**3,136**	**3,136**	**0**	**0**	**0**	**0**	**0**	**0**

APPROPRIATION AND EXPENDITURE DATA (000s)

Appropriation Request	FY 16	0
Supplemental Appropriation Request		0
Transfer		0
Cumulative Appropriation		18,610
Expenditure / Encumbrances		9,614
Unencumbered Balance		8,996

Date First Appropriation	FY 92	
First Cost Estimate		
Current Scope	FY 96	2,987
Last FY's Cost Estimate		18,610

Description

This project addresses four aspects of security throughout MCPS, and will serve to protect not only the student and community population, but also the extensive investment in educational facilities, equipment, and supplies in buildings. An FY 2009 appropriation was approved to provide additional funding for new initiatives for the school security program. The initiatives include design and installation of Closed Circuit Television (CCTV) camera systems in all middle schools, the replacement of existing outdated analog CCTV camera systems in all high schools, the installation of a visitor management system in all schools, and the installation of a visitor access system at elementary schools. An FY 2010 appropriation was approved to continue this project. An FY 2011 appropriation was approved to continue the roll out of the new initiatives that began in FY 2009. An FY 2012 appropriation was approved to continue this project. An FY 2013 appropriation was approved to continue the roll out the school security program initiative. An FY 2013 supplemental appropriation was approved to accelerate $364,000 from FY 2014 to FY 2013 to allow for the installation of acess control systems in the remaining 26 elemetnary schools, with a completion date of July 2013. An FY 2014 appropriation was approved to continue this project. An FY 2014 supplemental appropriation and amendment to the FY 2013-2018 CIP was approved to implement the state's School Security Initaitve. The supplemental appropriation approved $4.186 million from the state as well as $1.674 million from the county to provide additional security technology at schools as well as minor modifications to enhance security. Anticipated completion date for the initiative is summer 2014.

Fiscal Note

State Reimbursement: not eligible

Public Schools (A18) asserts that this project conforms to the requirements of relevant local plans, as required by the Maryland Economic Growth, Resource Protection and Planning Act.

Shady Grove Transportation Depot Replacement (P651641)

Category	Montgomery County Public Schools	Date Last Modified	11/17/14
Sub Category	Countywide	Required Adequate Public Facility	No
Administering Agency	Public Schools (AAGE18)	Relocation Impact	None
Planning Area	Countywide	Status	Planning Stage

	Total	Thru FY14	Rem FY14	Total 6 Years	FY 15	FY 16	FY 17	FY 18	FY 19	FY 20	Beyond 6 Yrs
EXPENDITURE SCHEDULE ($000s)											
Planning, Design and Supervision	700	0	0	700	0	700	0	0	0	0	0
Land	0	0	0	0	0	0	0	0	0	0	0
Site Improvements and Utilities	0	0	0	0	0	0	0	0	0	0	0
Construction	0	0	0	0	0	0	0	0	0	0	0
Other	0	0	0	0	0	0	0	0	0	0	0
Total	**700**	**0**	**0**	**700**	**0**	**700**	**0**	**0**	**0**	**0**	**0**
FUNDING SCHEDULE ($000s)											
Current Revenue: General	700	0	0	700	0	700	0	0	0	0	0
Total	**700**	**0**	**0**	**700**	**0**	**700**	**0**	**0**	**0**	**0**	**0**

APPROPRIATION AND EXPENDITURE DATA (000s)

Appropriation Request	FY 16	700
Supplemental Appropriation Request		0
Transfer		0
Cumulative Appropriation		0
Expenditure / Encumbrances		0
Unencumbered Balance		0

Date First Appropriation	
First Cost Estimate	
Current Scope	0
Last FY's Cost Estimate	0

Description

The Shady Grove Transportation Depot is located in the County Service Park along Crabbs Branch Way in Rockville. The Smart Growth Initiative included the relocation of all the operations at the Service Park except for the Depot. To date, the county has been unable to secure a new location for the Depot, and with a deadline to vacate of January 2017, it is imperative that an immediate solution for the relocation of the Depot be solidified. Various options were considered, with one option being the most viable. The Blair G. Ewing Center site would accommodate most of the needs and functions of the Depot. Therefore, the Board of Education's Amended FY2015-2020 CIP request included $32 million for the redevelopment of the Blair G. Ewing Center site for the Depot. The County Council did not approve the Board's request and removed $31.3 million from this project. The County Council approved $700,000 in planning for this project and approved the following language. "Planning funds appropriated in FY 2016 in this project must be used to study the following: options to relocate some or all of the current Shady Grove Transportation Depot functions to the Oaks Landfill at 6001 Olney-Laytonsville Road, Laytonsville; options to relocate some or all of the current Shady Grove Transportation Depot functions to 14501 Avery Road, Rockville, the Blair G. Ewing Center facility currently located on this property also is the subject of a feasibility study for the MCPS Alternative Education Programs; options to build a parking garage on the front lot of the Carver Educational Services Center, 850 Hungerford Drive, Rockville, these options must include both structured deck parking that would support only cars with buses underneath and an option for structured deck parking that would support buses on upper decks as well as on the ground level, both options must include an assumption that the resulting garage would include space to share parking with Montgomery College; options to build structured parking at the Randolph and Bethesda Transportation Depots to add parking capacity for buses at those depots, these options must include review of the site with and without the facility maintenance functions; options to relocate facility maintenance, bus maintenance and repair, bus parking, or other elements of the facility and transportation depots to 14645 Rothgeb Drive Rockville, the analysis must estimate the number of additional bus parking spaces at transportation depots that are created from the relocation of facility maintenance; and, an analysis of the envronmental and safety constraints of the Woodfield Road parcel at Snouffler School Road and Muncaster Mill Road in Gaithersburg. MCPS also may use planning funds appropriated to study relocation of all or some functions on the Shady Grove Transportation Depot to other locations not specified in this PDF."

Coordination

Mandatory Referral- MNCPPC, Department of Environmental Protection, Building Permits, Code Review, Fire Marshal, Department of Transportation, Inspections, Sediment Control, Stormwater Management, WSSC Permits

Stormwater Discharge & Water Quality Mgmt: MCPS (P956550)

Category	Montgomery County Public Schools	Date Last Modified	11/17/14
Sub Category	Countywide	Required Adequate Public Facility	No
Administering Agency	Public Schools (AAGE18)	Relocation Impact	None
Planning Area	Countywide	Status	Ongoing

	Total	Thru FY14	Rem FY14	Total 6 Years	FY 15	FY 16	FY 17	FY 18	FY 19	FY 20	Beyond 6 Yrs
EXPENDITURE SCHEDULE ($000s)											
Planning, Design and Supervision	5,096	1,064	576	3,456	576	576	576	576	576	576	0
Land	0	0	0	0	0	0	0	0	0	0	0
Site Improvements and Utilities	2,047	2,047	0	0	0	0	0	0	0	0	0
Construction	1,681	1,681	0	0	0	0	0	0	0	0	0
Other	340	60	40	240	40	40	40	40	40	40	0
Total	**9,164**	**4,852**	**616**	**3,696**	**616**	**616**	**616**	**616**	**616**	**616**	**0**
FUNDING SCHEDULE ($000s)											
G.O. Bonds	9,164	4,852	616	3,696	616	616	616	616	616	616	0
Total	**9,164**	**4,852**	**616**	**3,696**	**616**	**616**	**616**	**616**	**616**	**616**	**0**

APPROPRIATION AND EXPENDITURE DATA (000s)

Appropriation Request	FY 16	616
Supplemental Appropriation Request		0
Transfer		0
Cumulative Appropriation		6,287
Expenditure / Encumbrances		4,852
Unencumbered Balance		1,435

Date First Appropriation	FY 07	
First Cost Estimate		
Current Scope	FY07	0
Last FY's Cost Estimate		9,164

Description

This project will provide funds to meet the State of Maryland requirements that all industrial sites be surveyed and a plan developed to mitigate stormwater runoff. Work under this project includes concrete curbing to channel rainwater, oil/grit separators to filter stormwater for quality control, modifications to retention systems, the installation of a surface pond for stormwater management quality control at the Randolph Bus and Maintenance Depot, and other items to improve stormwater management systems at other depot sites. This project is reviewed by the interagency committee for capital programs that affect other county agencies to develop the most cost effective method to comply with state regulation. This project also will address pollution prevention measures that were formally addressed in the County Water Quality PDF. Federal and State laws require MCPS to upgrade and maintain stormwater pollution prevention measures at schools and support facilities. The State of Maryland, Department of the Environment, through the renewal of Montgomery County's National Pollutant Discharge Elimination System (NPDES) Permit, has included MCPS as a co-permitee under its revised current Municipal Separate Storm Sewer System MS4 permit, subject to certain pollution prevention regulations and reporting requirements not required in the past. As a co-permittee, MCPS will be required to develop a system-wide plan for complying with MS4 permit requirements. The plan could include infrastructure improvements that reduce the potential for pollution to enter into the stormwater system and area streams. A portion of the plan also will include surveying and documenting, in a GIS mapping system, the stormwater systems at various facilities. An FY 2011 appropriation was approved to address water quality issues related to stormwater management and continue the assessments and planning for water quality compliance as required by federal and state law. An FY 2012 appropriation was approved to continue this project. An FY 2013 appropriation was approved to continue this level of effort project. An FY 2014 appropriation was approved to continue this project. An FY 2015 appropriation was approved to address water quality issues related to stormwater management. An FY 2016 appropriation was approved to continue this level of effort project.

Fiscal Note

State Reimbursement: Not eligible

Coordination

$000s	FY 15	FY 16-20
Salaries and Wages	68	340
Fringe Benefits	31	155
Workyears	1	5

Technology Modernization (P036510)

Category	Montgomery County Public Schools	Date Last Modified	11/17/14
Sub Category	Countywide	Required Adequate Public Facility	No
Administering Agency	Public Schools (AAGE18)	Relocation Impact	None
Planning Area	Countywide	Status	Ongoing

	Total	Thru FY14	Rem FY14	Total 6 Years	FY 15	FY 16	FY 17	FY 18	FY 19	FY 20	Beyond 6 Yrs
EXPENDITURE SCHEDULE ($000s)											
Planning, Design and Supervision	296,215	138,949	22,088	135,178	24,758	25,538	21,358	21,998	20,728	20,798	0
Land	0	0	0	0	0	0	0	0	0	0	0
Site Improvements and Utilities	0	0	0	0	0	0	0	0	0	0	0
Construction	0	0	0	0	0	0	0	0	0	0	0
Other	0	0	0	0	0	0	0	0	0	0	0
Total	**296,215**	**138,949**	**22,088**	**135,178**	**24,758**	**25,538**	**21,358**	**21,998**	**20,728**	**20,798**	**0**
FUNDING SCHEDULE ($000s)											
Current Revenue: General	158,661	37,004	11,920	109,737	9,664	19,393	20,278	20,918	19,789	19,695	0
Current Revenue: Recordation Tax	126,846	91,237	10,168	25,441	15,094	6,145	1,080	1,080	939	1,103	0
Federal Aid	10,708	10,708	0	0	0	0	0	0	0	0	0
Total	**296,215**	**138,949**	**22,088**	**135,178**	**24,758**	**25,538**	**21,358**	**21,998**	**20,728**	**20,798**	**0**

APPROPRIATION AND EXPENDITURE DATA (000s)

Appropriation Request	FY 16	23,538
Supplemental Appropriation Request		0
Transfer		0
Cumulative Appropriation		185,795
Expenditure / Encumbrances		138,949
Unencumbered Balance		46,846

Date First Appropriation FY 03	
First Cost Estimate	
Current Scope	0
Last FY's Cost Estimate	294,215

Description

The Technology Modernization (Tech Mod) project is a key component of the MCPS strategic technology plan, Educational Technology for 21st Century Learning. This plan builds upon the following four goals: students will use technology to become actively engaged in learning, schools will address the digital divide through equitable access to technology, staff will improve technology skills through professional development, and staff will use technology to improve productivity and results.

The funding source for the initiative is anticipated to be Federal e-rate funds. The Federal e-rate funds programmed in this PDF consist of available unspent e-rate balance: $1.8M in FY 2010, $1.8M in FY 2011, and $327K in FY 2012. In addition, MCPS projects future e-rate funding of $1.6M each year (FY 2010-2012) that may be used to support the payment obligation pending receipt and appropriation. No county funds may be spent for the initiative payment obligation in FY 2010-2012 without prior Council approval.

During the County Council's reconciliation of the amended FY 2011-2016 CIP, the Board of Education's requested FY 2012 appropriation was reduced by $3.023 million due to a shortfall in Recordation Tax revenue. An FY 2012 supplemental appropriation of $1.339 million in federal e-rate funds was approved; however, during the County Council action, $1.339 million in current revenue was removed from this project resulting in no additional dollars for this project in FY 2012. An FY 2013 appropriation was requested to continue the technology modernization project and return to a four-year replacement cycle starting in FY 2013; however, the County Council, in the adopted FY 2013-2018 CIP reduced the request and therefore, the replacement cycle will remain on a five-year schedule. An FY 2013 supplemental appropriation in the amount of $2.042 million was approved in federal e-rate funds to roll out Promethean interactive technology across all elementary schools and to implement wireless networks across all schools.

An FY 2014 appropriation was approved to continue this project. An FY 2015 appropriation was approved to continue the technology modernization program which will enable MCPS to provide mobile (laptop and tablet) devices in the classrooms. The County Council adopted FY 2015-2020 CIP is approximately $21 million less than the Board's request over the six year period. However, e-rate funding anticipated for FY 2015 and FY 2016 will bring expenditures in those two years up to the Board's request to begin the new initiative to provide mobile devices for students and teachers in the classroom. The County Council, during the review of the amended FY 2015-2020 CIP, programmed an additional $2 million in FY 2016 for this project. A supplemental appropriation will be requested to have the $2 milllion appropriated to MCPS. An FY 2016 appropriation was approved to continue the technology modernization program.

Fiscal Note

A FY2014 supplemental appropriation of $3,384 million in federal e-rate funds was approved by Council in June 2014.

Coordination

($000)	FY 15	FYs 16-20
Salaries and Wages:	1893	9465
Fringe Benefits:	807	4035
Workyears:	20.5	102.5

PART III : CAPITAL IMPROVEMENTS PROJECTS TO BE CLOSED OUT

The following capital projects are closed out effective July 1, 2015, and the appropriation for each project is decreased by the amount of that project's unencumbered balance.

Project Title (Project #)
Ridgeview MS - Improvements (P016520)
Seven Locks ES Addition/Modernization (P026503)
Travilah ES Addition (P026504)
Luxmanor ES Addition (P076502)
East Silver Spring ES Addition (P086500)
Sherwood ES Addition (P096507)
Richard Montgomery Cluster ES Solution (P116516)
B-CC Cluster MS Solution (P126501)
Downcounty Cons. (Northwood) ES Solution (P126502)
Northwest Cluster ES Solution (P126503)
Richard Montgomery Cluster MS Solution (P126504)
Bethesda-Chevy Chase HS Cluster Solution (P136522)
Interim Solution for Facilities Improvements (P651642)

PART IV: CAPITAL IMPROVEMENTS PROJECTS:

PARTIAL CLOSE OUT

Partial close out of the following capital projects is effective June 30, 2015

Project Title (Project #)	Amt (In $000)
Roof Replacement: MCPS (P766995)	5,368
HVAC (Mechanical Systems) Replacement: MCPS (P816633)	13,907
School Gymnasiums (P886550)	7,347
Planned Life Cycle Asset Repl: MCPS (P896586)	1,253
Current Revitalizations/Expansions(P926575)	44,100

Appendix A–1

Montgomery County Public Schools
Actual and Projected Enrollment: 2014–2015 to 2020–2021

June 15, 2015

Grade Level & Program	Official Enrollment 2014–15	Projected Enrollment 2015–16	2016–17	2017–18	2018–19	2019–20	2020–21
Prekindergarten	1,912	2,145	2,145	2,145	2,145	2,145	2,145
Head Start	628	628	628	628	628	628	628
Grades K–5	71,082	71,743	72,284	72,267	71,969	71,370	71,218
Grades 6–8	33,430	34,564	35,470	36,314	37,045	38,011	38,229
Grades 9–12	45,594	45,871	46,743	47,986	49,033	50,339	51,595
Total K–12	150,106	152,178	154,497	156,567	158,047	159,720	161,042
Pre-K Special Education	1,206	1,563	1,563	1,563	1,563	1,563	1,563
GRAND TOTAL	153,852	156,514	158,833	160,903	162,383	164,056	165,378

Source: Montgomery County Public Schools, Division of Long-range Planning.

Appendix A–2

Montgomery County Public Schools
Actual and Projected Grade Enrollment: 2014–2015 to 2020–2021

June 15, 2015

Grades	Official Enrollment	Projected Enrollment					
	2014–15	2015–16	2016–17	2017–18	2018–19	2019–20	2020–21
Kindergarten	11,562	11,434	11,380	11,347	11,352	11,355	11,359
Grade 1	12,269	11,901	11,908	11,718	11,676	11,682	11,702
Grade 2	11,985	12,389	11,980	11,983	11,786	11,751	11,763
Grade 3	11,938	12,166	12,527	12,119	12,121	11,931	11,900
Grade 4	11,697	12,093	12,330	12,689	12,285	12,298	12,120
Grade 5	11,631	11,760	12,159	12,411	12,749	12,353	12,374
Grade 6	11,375	11,702	11,832	12,182	12,433	12,796	12,400
Grade 7	11,136	11,536	11,902	12,030	12,382	12,633	12,996
Grade 8	10,919	11,326	11,736	12,102	12,230	12,582	12,833
Grade 9	13,173	12,924	13,326	13,736	14,102	14,230	14,582
Grade 10	11,753	12,305	12,174	12,576	12,986	13,352	13,480
Grade 11	10,491	10,543	11,105	10,974	11,376	11,786	12,152
Grade 12	10,177	10,099	10,138	10,700	10,569	10,971	11,381
K–5 Total	71,082	71,743	72,284	72,267	71,969	71,370	71,218
6–8 Total	33,430	34,564	35,470	36,314	37,045	38,011	38,229
9–12 Total	45,594	45,871	46,743	47,986	49,033	50,339	51,595
K–12 Total	150,106	152,178	154,497	156,567	158,047	159,720	161,042
Prekindergarten	1,912	2,145	2,145	2,145	2,145	2,145	2,145
Head Start	628	628	628	628	628	628	628
Pre-K Special Education	1,206	1,563	1,563	1,563	1,563	1,563	1,563
GRAND TOTAL	153,852	156,514	158,833	160,903	162,383	164,056	165,378

Source: Montgomery County Public Schools, Division of Long-range Planning.

Appendix A–3

Montgomery County Public Schools Enrollment by Race/Ethnic Groups: 1968–2014

June 15, 2015

School Year	Native Hawaiian/ Pacific Islander		American Indian/ Alaskan Native		Two or more races		Asian		Black or African American		Hispanic		White		Total Enrollment
	Number	Percent	Number	Percent	Number	Percent	Number	Percent	Number	Percent	Number	Percent	Number	Percent	
1968–69			75	≤5%			1,208	≤5%	4,872	≤5%	1,673	≤5%	113,621	93.6%	121,449
1969–70			123	≤5%			1,401	≤5%	5,716	≤5%	1,832	≤5%	115,899	92.7%	124,971
1970–71			2,145	≤5%			2,145	≤5%	6,454	5.0%	2,438	≤5%	114,845	89.7%	128,027
1971–72			113	≤5%			1,640	≤5%	7,292	5.8%	2,475	≤5%	114,687	90.9%	126,207
1972–73			194	≤5%			1,904	≤5%	8,013	6.3%	2,688	≤5%	114,113	89.9%	126,912
1973–74			77	≤5%			1,849	≤5%	9,264	7.3%	1,996	≤5%	112,990	89.5%	126,176
1974–75			113	≤5%			1,929	≤5%	9,928	8.0%	2,050	≤5%	110,299	88.7%	124,319
1975–76			122	≤5%			2,438	≤5%	10,578	8.7%	2,234	≤5%	106,900	87.4%	122,272
1976–77			822	≤5%			3,758	≤5%	11,012	9.4%	3,668	≤5%	98,370	83.6%	117,630
1977–78			545	≤5%			4,084	≤5%	11,201	9.9%	3,517	≤5%	93,278	82.8%	112,625
1978–79			334	≤5%			4,360	≤5%	11,192	10.4%	3,486	≤5%	88,058	82.0%	107,430
1979–80			209	≤5%			4,774	≤5%	11,648	11.4%	3,442	≤5%	82,446	80.4%	102,519
1980–81			187	≤5%			5,598	5.7%	11,912	12.1%	3,760	≤5%	77,386	78.3%	98,843
1981–82			161	≤5%			6,291	6.6%	12,175	12.7%	4,122	≤5%	72,838	76.2%	95,587
1982–83			156	≤5%			6,791	7.3%	12,345	13.3%	4,231	≤5%	68,994	74.6%	92,517
1983–84			166	≤5%			7,266	8.0%	12,714	14.0%	4,388	≤5%	66,496	73.0%	91,030
1984–85			136	≤5%			8,024	8.7%	13,327	14.5%	4,807	5.2%	65,410	71.3%	91,704
1985–86			140	≤5%			8,759	9.4%	13,765	14.8%	5,273	5.7%	64,934	69.9%	92,871
1986–87			142	≤5%			9,471	10.0%	14,342	15.2%	5,845	6.2%	64,660	68.5%	94,460
1987–88			194	≤5%			10,229	10.6%	14,984	15.6%	6,376	6.6%	64,488	67.0%	96,271
1988–89			223	≤5%			10,960	11.1%	15,900	16.1%	7,208	7.3%	64,228	65.2%	98,519
1989–90			294	≤5%			11,565	11.5%	16,612	16.6%	8,199	8.2%	63,589	63.4%	100,259
1990–91			268	≤5%			12,352	11.9%	17,721	17.1%	9,202	8.9%	64,189	61.9%	103,732
1991–92			293	≤5%			12,983	12.1%	18,867	17.6%	10,189	9.5%	65,067	60.6%	107,399
1992–93			323	≤5%			13,521	12.3%	19,938	18.1%	11,071	10.1%	65,184	59.2%	110,037
1993–94			397	≤5%			14,014	12.4%	21,009	18.5%	12,260	10.8%	65,749	58.0%	113,429
1994–95			464	≤5%			14,440	12.3%	22,170	18.9%	13,439	11.5%	66,569	56.9%	117,082
1995–96			400	≤5%			15,016	12.5%	23,265	19.3%	14,437	12.0%	67,173	55.8%	120,291
1996–97			440	≤5%			15,384	12.6%	24,281	19.8%	15,348	12.5%	67,052	54.7%	122,505
1997–98			442	≤5%			15,904	12.7%	25,420	20.3%	16,502	13.2%	66,767	53.4%	125,035
1998–99			428	≤5%			16,380	12.8%	26,820	21.0%	17,815	13.9%	66,409	51.9%	127,852
1999–00			385	≤5%			17,093	13.1%	27,490	21.0%	19,485	14.9%	66,236	50.7%	130,689
2000–01			407	≤5%			17,895	13.3%	28,426	21.2%	21,731	16.2%	65,849	49.0%	134,308
2001–02			414	≤5%			19,042	13.9%	28,928	21.1%	23,517	17.2%	64,931	47.5%	136,832
2002–03			428	≤5%			19,765	14.2%	29,755	21.4%	24,915	17.9%	64,028	46.1%	138,891
2003–04			429	≤5%			19,908	14.3%	30,736	22.1%	26,058	18.7%	62,072	44.6%	139,203
2004–05			396	≤5%			20,118	14.4%	31,446	22.6%	27,011	19.4%	60,366	43.3%	139,337
2005–06			402	≤5%			20,458	14.7%	31,816	22.8%	27,931	20.0%	58,780	42.2%	139,387
2006–07			418	≤5%			20,452	14.8%	31,620	22.9%	28,582	20.7%	56,726	41.2%	137,798
2007–08			403	≤5%			20,931	15.2%	31,597	22.9%	29,602	21.5%	55,212	40.1%	137,745
2008–09			399	≤5%			21,551	15.5%	32,173	23.1%	30,738	22.1%	54,415	39.1%	139,276
2009–10			433	≤5%			22,177	15.6%	32,883	23.2%	32,236	22.7%	54,048	38.1%	141,777
2010–11	82	≤5%	233	≤5%	6,228	≤5%	20,573	14.3%	30,720	21.3%	36,433	25.3%	49,795	34.6%	144,064
2011–12	95	≤5%	256	≤5%	6,519	≤5%	20,984	14.3%	31,106	21.2%	38,102	26.0%	49,435	33.7%	146,497
2012–13	88	≤5%	274	≤5%	6,770	≤5%	21,240	14.3%	31,714	21.3%	39,651	26.7%	49,042	33.0%	148,779
2013–14	86	≤5%	272	≤5%	6,969	≤5%	21,742	14.4%	32,336	21.4%	41,445	27.4%	48,439	32.0%	151,289
2014–15	82	≤5%	280	≤5%	7,202	≤5%	21,832	14.2%	33,031	21.5%	43,761	28.4%	47,664	31.0%	153,852

Source: Montgomery County Public Schools, Department of Reporting and Regulatory Accountability, November 11, 2014.

Notes: All Hispanic students, regardless of their race, are included under Hispanic enrollment.

Due to federal and state guidelines demographic characteristics of schools of less than or equal to 5.0% are not reported.

Beginning in 2010–11 changes in the reporting of race/ethnicity were made. These changes are reflected in the table, where "Two of more races" and "Native Hawaiian/Pacific Islander" are new categories, and "American Indian/Alaskan Native" is an expanded category.

Appendix A–4

Montgomery County Public Schools Annual Enrollment Change
By Race/Ethnic Groups: 1968 to 2014

June 15, 2015

School Year	Native Hawaiian/ Pacific Islander		American Indian/ Alaskan Native		Two or more races		Asian		Black or African American		Hispanic		White		Total	
	Number	Change	Number	Change	Number	Change	Number	Change	Number	Change	Number	Change	Number	Change	Enrollment	Change
1968–69			75				1,208		4,872		1,673		113,621		121,449	
1969–70			2,145	2,145			2,145	937	5,716	844	1,832	159	115,899	2,278	127,737	6,288
1970–71			131	(2,014)			1,476	(669)	6,454	738	2,438	606	114,845	(1,054)	125,344	(2,393)
1971–72			113	(18)			1,640	164	7,292	838	2,475	37	114,687	(158)	126,207	863
1972–73			194	81			1,904	264	8,013	721	2,688	213	114,113	(574)	126,912	705
1973–74			77	(117)			1,849	(55)	9,264	1,251	1,996	(692)	112,990	(1,123)	126,176	(736)
1974–75			113	36			1,929	80	9,928	664	2,050	54	110,299	(2,691)	124,319	(1,857)
1975–76			122	9			2,438	509	10,578	650	2,234	184	106,900	(3,399)	122,272	(2,047)
1976–77			822	700			3,758	1,320	11,012	434	3,668	1,434	98,370	(8,530)	117,630	(4,642)
1977–78			545	(277)			4,084	326	11,201	189	3,517	(151)	93,278	(5,092)	112,625	(5,005)
1978–79			334	(211)			4,360	276	11,192	(9)	3,486	(31)	88,058	(5,220)	107,430	(5,195)
1979–80			209	(125)			4,774	414	11,648	456	3,442	(44)	82,446	(5,612)	102,519	(4,911)
1980–81			187	(22)			5,598	824	11,912	264	3,760	318	77,386	(5,060)	98,843	(3,676)
1981–82			161	(26)			6,291	693	12,175	263	4,122	362	72,838	(4,548)	95,587	(3,256)
1982–83			156	(5)			6,791	500	12,345	170	4,231	109	68,994	(3,844)	92,517	(3,070)
1983–84			166	10			7,266	475	12,714	369	4,388	157	66,496	(2,498)	91,030	(1,487)
1984–85			136	(30)			8,024	758	13,327	613	4,807	419	65,410	(1,086)	91,704	674
1985–86			140	4			8,759	735	13,765	438	5,273	466	64,934	(476)	92,871	1,167
1986–87			142	2			9,471	712	14,342	577	5,845	572	64,660	(274)	94,460	1,589
1987–88			194	52			10,229	758	14,984	642	6,376	531	64,488	(172)	96,271	1,811
1988–89			223	29			10,960	731	15,900	916	7,208	832	64,228	(260)	98,519	2,248
1989–90			294	71			11,565	605	16,612	712	8,199	991	63,589	(639)	100,259	1,740
1990–91			268	(26)			12,352	787	17,721	1,109	9,202	1,003	64,189	600	103,732	3,473
1991–92			293	25			12,983	631	18,867	1,146	10,189	987	65,067	878	107,399	3,667
1992–93			323	30			13,521	538	19,938	1,071	11,071	882	65,184	117	110,037	2,638
1993–94			397	74			14,014	493	21,009	1,071	12,260	1,189	65,749	565	113,429	3,392
1994–95			464	67			14,440	426	22,170	1,161	13,439	1,179	66,569	820	117,082	3,653
1995–96			400	(64)			15,016	576	23,265	1,095	14,437	998	67,173	604	120,291	3,209
1996–97			440	40			15,384	368	24,281	1,016	15,348	911	67,052	(121)	122,505	2,214
1997–98			442	2			15,904	520	25,420	1,139	16,502	1,154	66,767	(285)	125,035	2,530
1998–99			428	(14)			16,380	476	26,820	1,400	17,815	1,313	66,409	(358)	127,852	2,817
1999–00			385	(43)			17,093	713	27,490	670	19,485	1,670	66,236	(173)	130,689	2,837
2000–01			407	22			17,895	802	28,426	936	21,731	2,246	65,849	(387)	134,308	3,619
2001–02			414	7			19,042	1,147	28,928	502	23,517	1,786	64,931	(918)	136,832	2,524
2002–03			428	14			19,765	723	29,755	827	24,915	1,398	64,028	(903)	138,891	2,059
2003–04			429	1			19,908	143	30,736	981	26,058	1,143	62,072	(1,956)	139,203	312
2004–05			396	(33)			20,118	210	31,446	710	27,011	953	60,366	(1,706)	139,337	134
2005–06			402	6			20,458	340	31,816	370	27,931	920	58,780	(1,586)	139,387	50
2006–07			418	16			20,452	(6)	31,620	(196)	28,582	651	56,726	(2,054)	137,798	(1,589)
2007–08			403	(15)			20,931	479	31,597	(23)	29,602	1,020	55,212	(1,514)	137,745	(53)
2008–09			399	(4)			21,551	620	32,173	576	30,738	1,136	54,415	(797)	139,276	1,531
2009–10			433	34			22,177	626	32,883	710	32,236	1,498	54,048	(367)	141,777	2,501
2010–11	82	82	233	(200)	6,228	6,228	20,573	(1,604)	30,720	(2,163)	36,433	4,197	49,795	(4,253)	144,064	2,287
2011–12	95	13	256	23	6,519	291	20,984	411	31,106	386	38,102	1,669	49,435	-360	146,497	2,433
2012–13	88	-7	274	18	6,770	251	21,240	256	31,714	608	39,651	1,549	49,042	-393	148,779	2,282
2013–14	86	-2	272	-2	6,969	199	21,742	502	32,336	622	41,445	1,794	48,439	-603	151,289	2,510
2014–15	82	-4	280	8	7,202	233	21,832	90	33,031	695	43,761	2,316	47,664	-775	153,852	2,563

Source: Montgomery County Public Schools, Department of Reporting and Regulatory Accountability, November 11, 2014

Notes: All Hispanic students, regardless of their race, are included under Hispanic enrollment.
Beginning in 2010–11 changes in the reporting of race/ethnicity were made. These changes are reflected in the table, where "Two of more races" and "Native Hawaiian/Pacific Islander" are new categories, and "American Indian/Alaskan Native" is an expanded category.

Appendix B–1

Actual and Projected ESOL Enrollment

June 15, 2015

Program	Actual Official 2012–13	Actual FY14 2013–14	Budgeted FY15 2014–15	Projected Enrollment FY16 2015–16	FY17 2016–17	FY18 2017–18	FY19 2018–19	FY20 2019–20	FY21 2020–21
Elementary School	15,986	16,027	16,000	16,050	16,000	16,000	16,000	16,000	16,000
Middle School	1,912	2,145	2,145	2,145	2,145	2,145	2,145	1,900	1,900
High School	2,312	2,456	2,350	2,350	2,350	2,350	2,350	2,350	2,350
Special Centers	71082	40	50	50	50	50	50	50	50
Total Enrollment	33,430	20,668	20,545	20,595	20,545	20,545	20,545	20,300	20,300
	45,594								
METS:									
Elementary	43	42	45	45	45	45	45	45	45
Middle	90	101	90	90	90	90	90	90	90
High	1206	214	170	170	170	170	170	170	170

* Actual ESOL enrollment is based on the average monthly enrollment reported by the Division of ESOL/Bilingual programs from October to May.
METS enrollment is broken out for information purposes. METS enrollment is included in the elementary, middle and high school numbers.
Forecasts are developed cooperatively by the Division of Long-range Planning and Division of ESOL/ Bilingual Programs.

Actual and Projected Head Start and Prekindergarten Enrollment

June 15, 2015

Program	Actual FY13 2012–13	Actual FY14 2013–14	Budgeted FY15 2014–15	Projected Enrollment FY16 2015–16	FY17 2016–17	FY18 2017–18	FY19 2018–19	FY20 2019–20	FY21 2020–21
Head Start	618	628	628	628	628	628	628	628	628
Prekindergarten	2,057	2,206	2,125	2,125	2,125	2,125	2,125	2,125	2,125

* Actual Head Start and Prekindergarten enrollment is as of official September 30th each year.
Forecasts developed cooperatively by the Division of Long-range Planning and Div. of Early Childhood Services and Head Start Unit.

Actual and Projected Alternative Program Enrollment

June 15, 2015

Program	Actual FY13 2012–13	Actual FY14 2013–14	Budgeted FY15 2014–15	Projected Enrollment FY16 2015–16	FY17 2016–17	FY18 2017–18	FY19 2018–19	FY20 2019–20	FY21 2020–21
Alternative Programs	137	145	225	225	225	225	225	225	225

* Actual Alternative Programs is as of official September 30th each year.
Forecasts developed cooperatively by the Division of Long-range Planning and the Department of Alternative Programs.

Appendix C

School Enrollment and Capacity

(2014–2015 and 2020–2021 School Years)

School	2014–2015 School Year			2020–2021 School Year		
	Enrollment	Capacity	Utilization	Enrollment	Capacity*	Utilization
Elementary Schools						
Arcola	719	496	(223)	750	659	(91)
Ashburton	892	629	(263)	835	881	46
Bannockburn	407	365	(42)	373	365	(8)
Lucy V. Barnsley	691	404	(287)	619	673	54
Beall	801	638	(163)	783	638	(145)
Bel Pre	541	638	97	537	640	103
Bells Mill	611	626	15	634	609	(25)
Belmont	310	424	114	360	424	64
Bethesda	517	384	(133)	556	568	12
Beverly Farms	621	690	69	560	690	130
Bradley Hills	632	663	31	565	663	98
Brooke Grove	398	531	133	369	531	162
Brookhaven	458	486	28	454	706	252
Brown Station	513	436	(77)	633	709	76
Burning Tree	492	379	(113)	432	379	(53)
Burnt Mills	538	402	(136)	521	425	(96)
Burtonsville	660	485	(175)	675	735	60
Candlewood	329	550	221	390	476	86
Cannon Road	432	521	89	426	521	95
Carderock Springs	418	407	(11)	364	407	43
Rachel Carson	1013	667	(346)	968	667	(301)
Cashell	337	341	4	367	341	(26)
Cedar Grove	641	405	(236)	690	405	(285)
Chevy Chase	541	473	(68)	406	473	67
Clarksburg	305	312	7	506	312	(194)
Clearspring	624	642	18	601	639	38
Clopper Mill	457	417	(40)	546	457	(89)
Cloverly	462	454	(8)	426	454	28
Cold Spring	335	458	123	340	458	118
College Gardens	873	694	(179)	834	694	(140)
Cresthaven	503	467	(36)	486	467	(19)
Captain James Daly	593	518	(75)	600	518	(82)
Damascus	297	328	31	300	328	28
Darnestown	310	471	161	350	471	121
Diamond	648	463	(185)	615	670	55
Dr. Charles R. Drew	444	456	12	448	456	8
DuFief	328	428	100	348	428	80
East Silver Spring	525	582	57	556	582	26
Fairland	623	648	25	577	648	71
Fallsmead	566	598	32	505	598	93
Farmland	655	728	73	700	728	28
Fields Road	484	419	(65)	529	419	(110)
Flower Hill	505	483	(22)	438	483	45
Flower Valley	480	429	(51)	437	429	(8)
Forest Knolls	737	560	(177)	750	560	(190)
Fox Chapel	601	683	82	606	683	77
Gaithersburg	795	771	(24)	868	771	(97)
Galway	808	790	(18)	740	790	50
Garrett Park	749	753	4	769	753	(16)
Georgian Forest	571	649	78	551	649	98
Germantown	316	333	17	343	328	(15)
William B. Gibbs Jr.	778	740	(38)	733	740	7
Glen Haven	547	576	29	632	705	73
Glenallan	650	762	112	716	762	46
Goshen	577	533	(44)	592	533	(59)
Great Seneca Creek	732	566	(166)	675	589	(86)
Greencastle	817	582	(235)	756	582	(174)
Greenwood	505	585	80	450	585	135
Harmony Hills	736	709	(27)	775	709	(66)
Highland	541	522	(19)	586	714	128
Highland View	426	298	(128)	408	298	(110)
Jackson Road	727	709	(18)	696	709	13
Jones Lane	470	441	(29)	408	441	33
Kemp Mill	531	453	(78)	566	696	130

*Includes capacity from approved capital projects.

School	2014–2015 School Year			2020–2021 School Year		
	Enrollment	Capacity	Utilization	Enrollment	Capacity*	Utilization
Kensington-Parkwood	654	472	(182)	645	746	101
Lake Seneca	536	410	(126)	510	410	(100)
Lakewood	549	569	20	475	569	94
Laytonsville	428	448	20	383	448	65
JoAnn Leleck	756	672	(84)	745	715	(30)
Little Bennett	691	676	(15)	615	676	61
Luxmanor	466	428	(38)	578	745	167
Thurgood Marshall	624	534	(90)	656	534	(122)
Maryvale	613	626	13	657	778	121
Spark M. Matsunaga	926	652	(274)	843	652	(191)
S. Christa McAuliffe	629	526	(103)	665	785	120
Ronald McNair	851	623	(228)	794	623	(171)
Meadow Hall	428	370	(58)	413	370	(43)
Mill Creek Towne	412	326	(86)	386	326	(60)
Monocacy	161	219	58	150	219	69
Montgomery Knolls	510	540	30	479	540	61
New Hampshire Estates	516	480	(36)	502	480	(22)
Roscoe R. Nix	518	521	3	509	521	12
North Chevy Chase	355	266	(89)	300	358	58
Oak View	379	358	(21)	446	358	(88)
Oakland Terrace	491	513	22	476	513	37
Olney	629	585	(44)	566	585	19
William T. Page	410	379	(31)	364	379	15
Pine Crest	473	381	(92)	441	381	(60)
Piney Branch	527	611	84	591	611	20
Poolesville	441	539	98	433	539	106
Potomac	474	424	(50)	437	548	111
Judith A. Resnik	615	493	(122)	599	751	152
Dr. Sally K. Ride	527	523	(4)	494	523	29
Ritchie Park	551	387	(164)	551	387	(164)
Rock Creek Forest	628	770	142	661	754	93
Rock Creek Valley	437	393	(44)	428	393	(35)
Rock View	657	687	30	660	687	27
Lois P. Rockwell	456	523	67	444	523	79
Rolling Terrace	905	724	(181)	888	747	(141)
Rosemary Hills	633	478	(155)	624	644	20
Rosemont	569	590	21	855	613	(242)
Sequoyah	433	470	37	481	470	(11)
Seven Locks	398	425	27	427	425	(2)
Sherwood	499	569	70	482	569	87
Sargent Shriver	756	673	(83)	774	814	40
Flora M. Singer	677	680	3	705	680	(25)
Sligo Creek	639	664	25	672	664	(8)
Somerset	567	515	(52)	511	515	4
South Lake	862	716	(146)	845	716	(129)
Stedwick	573	639	66	591	639	48
Stone Mill	619	654	35	606	654	48
Stonegate	492	395	(97)	442	395	(47)
Strathmore	455	439	(16)	456	439	(17)
Strawberry Knoll	599	453	(146)	626	476	(150)
Summit Hall	634	443	(191)	650	466	(184)
Takoma Park	654	636	(18)	602	636	34
Travilah	413	517	104	412	517	105
Twinbrook	531	563	32	556	563	7
Viers Mill	714	760	46	714	743	29
Washington Grove	414	603	189	575	623	48
Waters Landing	691	776	85	675	776	101
Watkins Mill	635	746	111	630	733	103
Wayside	533	671	138	513	641	128
Weller Road	652	752	100	683	772	89
Westbrook	452	554	102	468	549	81
Westover	304	293	(11)	345	293	(52)
Wheaton Woods	537	358	(179)	556	770	214
Whetstone	758	783	25	733	783	50
Wilson Wims	660	759	99	972	754	(218)
Wood Acres	718	527	(191)	705	757	52
Woodfield	302	471	169	306	471	165
Woodlin	623	462	(161)	635	462	(173)
Wyngate	770	777	7	750	777	27

*Includes capacity from approved capital projects.

School	2014–2015 School Year			2020–2021 School Year		
	Enrollment	Capacity	Utilization	Enrollment	Capacity*	Utilization
High Schools						
Bethesda-Chevy Chase	1992	1683	(309)	2367	2398	31
Montgomery Blair	2900	2920	20	3212	2920	(292)
James Blake	1607	1743	136	1781	1743	(38)
Winston Churchill	1996	2013	17	2142	2013	(129)
Clarksburg	1974	1638	(336)	2458	1980	(478)
Damascus	1246	1551	305	1467	1551	84
Albert Einstein	1699	1621	(78)	1978	1604	(374)
Gaithersburg	2245	2407	162	2451	2407	(44)
Walter Johnson	2264	2335	71	2798	2335	(463)
John F. Kennedy	1570	1847	277	1975	1833	(142)
Col. Zadok Magruder	1520	1995	475	1686	1941	255
Richard Montgomery	2199	2236	37	2479	2236	(243)
Northwest	2116	2241	125	2540	2241	(299)
Northwood	1586	1519	(67)	1963	1519	(444)
Paint Branch	1996	2034	38	2158	2034	(124)
Poolesville	1222	1170	(52)	1208	1170	(38)
Quince Orchard	1899	1857	(42)	2019	1857	(162)
Rockville	1339	1570	231	1536	1570	34
Seneca Valley	1284	1374	90	1395	2400	1005
Sherwood	1891	2166	275	1772	2166	394
Springbrook	1750	2145	395	1976	2162	186
Watkins Mill	1499	1906	407	1779	1906	127
Wheaton	1467	1356	(111)	1737	1596	(141)
Walt Whitman	1912	1891	(21)	2155	1891	(264)
Thomas S. Wootton	2195	2184	(11)	2188	2167	(21)
Middle Schools						
Argyle	920	897	(23)	958	897	(61)
John T Baker	772	741	(31)	754	741	(13)
Benjamin Banneker	884	803	(81)	859	803	(56)
Briggs Chaney	891	969	78	902	969	67
Cabin John	943	1129	186	1029	1113	84
Roberto Clemente	1208	1231	23	1286	1231	(55)
Eastern	868	1024	156	1095	1024	(71)
William H. Farquhar	586	906	320	580	752	172
Forest Oak	834	949	115	1019	949	(70)
Robert Frost	1139	1075	(64)	928	1075	147
Gaithersburg	749	933	184	975	933	(42)
Herbert Hoover	1058	1139	81	907	1139	232
Francis Scott Key	942	961	19	1013	961	(52)
Martin Luther King, Jr	612	905	293	728	905	177
Kingsview	1002	1041	39	974	1041	67
Lakelands Park	1011	1122	111	1184	1122	(62)
Col. E. Brooke Lee	719	743	24	1046	743	(303)
A. Mario Loiederman	909	897	(12)	1094	897	(197)
Montgomery Village	658	894	236	782	878	96
Neelsville	914	922	8	1128	922	(206)
Newport Mill	599	825	226	672	825	153
North Bethesda	951	864	(87)	1162	1208	46
Parkland	941	948	7	1128	948	(180)
Rosa Parks	904	978	74	770	978	208
John Poole	327	468	141	300	468	168
Thomas W. Pyle	1483	1289	(194)	1443	1289	(154)
Redland	540	757	217	697	757	60
Ridgeview	702	995	293	793	963	170
Rocky Hill	1133	995	(138)	1778	995	(783)
Shady Grove	592	867	275	581	867	286
Silver Spring International	979	1118	139	1311	1118	(193)
Sligo	523	915	392	919	915	(4)
Takoma Park	996	939	(57)	1202	939	(263)
Tilden	798	972	174	1050	1200	150
Julius West	1201	1054	(147)	1351	1445	94
Westland	1254	1097	(157)	1765	1097	(668)
White Oak	750	962	212	912	962	50
Earle B. Wood	927	961	34	1053	961	(92)

*Includes capacity from approved capital projects.

Appendix D

Montgomery County Public Schools
Relocatable Classrooms: 2014–2015 School Year

Cluster/ School	Relocatables on site for 2014–2015 to Address:		
	Overutilization	DC	Total
Bethesda-Chevy Chase			
Bethesda-Chevy Chase HS	8		8
Westland MS	6		6
Bethesda	5		5
Chevy Chase ES	1		1
North Chevy Chase	5		5
Rosemary Hills	6		6
Total	31	0	**31**
Winston Churchill			
Potomac	5		5
Total	5	0	**5**
Clarksburg			
Clarksburg HS	11		11
Rocky Hill MS	11		11
Clarksburg ES	4		4
Daly	4		4
Little Bennett	4		4
Total	34	0	**34**
Damascus			
Cedar Grove	7		7
Total	7	0	**7**
Downcounty Consortium*			
Wheaton HS	2		2
Takoma Park MS	1		1
Arcola	6		6
Forest Knolls	4		4
Harmony Hills	5		5
Highland View	6		6
Oak View ES	1		1
Kemp Mill ES	3		3
Oakland Terrace	2		2
Pine Crest	5		5
Rolling Terrace	8		8
Sargent Shriver	9		9
Wheaton Woods	9		9
Woodlin	9		9
Total	70	0	**70**
Gaithersburg			
Gaithersburg ES	7		7
Goshen	5		5
Laytonsville	0	1	1
Rosemont	2	0	2
Strawberry Knoll	6		6
Summit Hall	10		10
Total	30	1	**31**
Walter Johnson			
North Bethesda	2		2
Ashburton	8		8
Kensington-Parkwood	7		7
Luxmanor	3		3
Total	20	0	**20**

Cluster/ School	Relocatables on site for 2014–2015 to Address:		
	Overutilization	DC	Total
Col. Zadok Magruder			
Flower Hill	4		4
Mill Creek Towne	3		3
Judith A. Resnik	6		6
Total	13	0	**13**
Richard Montgomery			
Julius West MS	6		6
Beall	8		8
College Gardens	6		6
Ritchie Park	6		6
Twinbrook	4		4
Total	30	0	**30**
Northeast Consortium*			
Burnt Mills	4		4
Burtonsville	6		6
Cloverly	2		2
Galway	2		2
Greencastle	6		6
JoAnn Leleck ES at Broad Acres	6		6
Page	2		2
Stonegate	3	1	4
Westover	2		2
Total	33	1	**34**
Northwest			
Clopper Mill	4		4
Diamond	4	1	5
Great Seneca Creek	3		3
Spark M. Matsunaga	14	1	15
Ronald McNair	7		7
Total	32	2	**34**
Quince Orchard			
Brown Station	6		6
Rachel Carson	10	1	11
Fields Road	4		4
Jones Lane	4		4
Marshall	5		5
Total	29	1	**30**
Rockville			
Lucy V. Barnsley	10		10
Flower Valley	1		1
Maryvale	1		1
Meadow Hall	5		5
Rock Creek Valley	4		4
Carl Sandburg Center	2		2
Total	23	0	**23**
Seneca Valley			
Lake Seneca	9		9
S. Christa McAuliffe	8		8
Sally K. Ride	4		4
Total	21	0	**21**
Sherwood			
Belmont	0	1	1
Total	0	1	**1**

Cluster/ School	Relocatables on site for 2014–2015 to Address:		
	Overutilization	DC	Total
Watkins Mill			
South Lake	3		3
Total	3	0	**3**
Walt Whitman			
Bannockburn	2		2
Burning Tree	4		4
Wood Acres	7		7
Total	13	0	**13**
Thomas S. Wootton			
Thomas S. Wootton HS	8		8
Cold Spring	1		1
DuFief	1	1	2
Total	10	1	**11**
Grand Total by Use	**404**	**7**	**411**

SCHOOL TOTAL: 411

Other Relocatable Uses		
	# Units	Comment
Construction		
Rosemary Hills ES	1	Class displacement
Total	1	
Holding Schools		
Emory Grove Center	7	Candlewood
Fairland Center	9	
Grosvenor Center	21	
North Lake Center	16	
Radnor Center	23	RCF/Wood Acres
Total	76	
Other Uses at Schools		
Gaithersburg ES	1	Parent Resource Ctr.
Monocacy ES	1	
Rosemary Hills ES	1	Benchmarks Program
Seneca Valley HS	1	Transitions (CCC)
Sherwood ES	1	Baldrige Lab
Summit Hall ES	1	Judy Center
Total	6	
Non-school Locations		
Bethesda Depot	3	Offices
Children's Res. Ctr.	1	Infants & Todd. offices
Clarksburg Depot	1	Maintenance
Clarksburg Depot	2	Transportation
Kingsley	5	Transitions
Lincoln Warehouse	1	Copy Plus Program
Montgomery College	2	Germantown
Randolph Depot	3	Offices
Rockinghorse	2	ESOL Offices
Shady Grove Depot	10	
Smith Center	2	Outdoor Education
Total	32	

OTHER TOTAL: 115

DC = Paid for by day-care provider to enable a day-care center to operate inside school.

* In terms of the number of schools, the Downcounty Consortium is the equivalent of 5 clusters, and the NE Consortium is the equivalent of 3 clusters.

Montgomery County Public Schools

Relocatable Classrooms: 2015–2016 School Year

Cluster/ School	Relocatables on site for 2015–2016 to Address: Overutilization	DC	Total
Bethesda-Chevy Chase			
Bethesda-Chevy Chase HS	8		8
Westland MS	6		6
Chevy Chase ES	1		1
Total	15	0	**15**
Winston Churchill			
Potomac	5		5
Total	5	0	**5**
Clarksburg			
Clarksburg HS	11		11
Rocky Hill MS	11		11
Clarksburg ES	4		4
Daly	4		4
Total	30	0	**30**
Damascus			
Cedar Grove	7		7
Total	7	0	**7**
Downcounty Consortium*			
Wheaton HS	2		2
Takoma Park MS	1		1
Arcola	6		6
Forest Knolls	5		5
Harmony Hills	5		5
Highland View	6		6
Oak View	1		1
Kemp Mill	3		3
Oakland Terrace	2		2
Pine Crest	5		5
Rolling Terrace	10		10
Sargent Shriver	9		9
Wheaton Woods	9		9
Woodlin	9		9
Total	73	0	**73**
Gaithersburg			
Gaithersburg ES	7		7
Goshen	5		5
Laytonsville	0	1	1
Rosemont	2	0	2
Strawberry Knoll	6		6
Summit Hall	10		10
Total	30	1	**31**
Walter Johnson			
North Bethesda	3		3
Ashburton	8		8
Kensington-Parkwood	7		7
Luxmanor	3		3
Total	21	0	**21**

Cluster/ School	Relocatables on site for 2015–2016 to Address: Overutilization	DC	Total
Col. Zadok Magruder			
Flower Hill	2		2
Mill Creek Towne	3		3
Judith A. Resnik	6		6
Total	11	0	**11**
Richard Montgomery			
Julius West MS	6		6
Beall	8		8
College Gardens	6		6
Ritchie Park	6		6
Twinbrook	2		2
Total	28	0	**28**
Northeast Consortium*			
Burnt Mills	4		4
Burtonsville	6		6
Cloverly	2		2
Galway	2		2
Greencastle	6		6
JoAnn Leleck ES at Broad Ac	8		8
Page	2		2
Stonegate	3	1	4
Westover	2		2
Total	35	1	**36**
Northwest			
Clopper Mill	4		4
Diamond	4	1	5
Great Seneca Creek	3		3
Spark M. Matsunaga	14	1	15
Ronald McNair	7		7
Total	32	2	**34**
Quince Orchard			
Brown Station	6		6
Rachel Carson	10	1	11
Fields Road	4		4
Jones Lane	4		4
Marshall	5		5
Total	29	1	**30**
Rockville			
Lucy V. Barnsley	10		10
Flower Valley	1		1
Maryvale	1		1
Meadow Hall	5		5
Rock Creek Valley	4		4
Carl Sandburg Center	2		2
Total	23	0	**23**
Seneca Valley			
Lake Seneca	9		9
S. Christa McAuliffe	8		8
Sally K. Ride	4		4
Total	21	0	**21**
Sherwood			
Belmont	0	1	1
Total	0	1	**1**

Cluster/ School	Relocatables on site for 2015–2016 to Address: Overutilization	DC	Total
Watkins Mill			
South Lake	4		4
Total	4	0	**4**
Walt Whitman			
Bannockburn	2		2
Burning Tree	4		4
Total	6	0	**6**
Thomas S. Wootton			
Thomas S. Wootton HS	6		6
Cold Spring	1		1
DuFief	1	1	2
Total	8	1	**9**
Grand Total by Use	**378**	**7**	**385**

SCHOOL TOTAL: 385

Other Relocatable Uses	# Units	Comment
Construction		
Total	0	
Holding Schools		
Emory Grove Center	7	
Fairland Center	0	
Grosvenor Center	17	
North Lake Center	16	
Radnor Center	23	
Total	63	
Other Uses at Schools		
Gaithersburg ES	1	Parent Resource Ctr.
Monocacy	1	
Seneca Valley HS	1	Transitions (CCC)
Sherwood ES	1	Baldrige Lab
South Lake	1	Linkages to Learning
Summit Hall	1	Judy Center
Total	6	
Non-school Locations		
Bethesda Depot	3	Offices
Children's Res. Ctr.	1	Infants & Todd. offices
Clarksburg Depot	1	Maintenance
Clarksburg Depot	2	Transportation
Kingsley	5	Transitions
Lincoln Warehouse	1	Copy Plus Program
Montgomery College	2	Germantown
Randolph Depot	3	Offices
Rocking Horse Road	4	ESOL Offices
Shady Grove Depot	10	
Smith Center	2	Outdoor Education
Total	34	

OTHER TOTAL: 103

DC = Paid for by day-care provider to enable a day-care center to operate inside school.
* In terms of the number of schools, the Downcounty Consortium is the equivalent of 5 clusters, and the NE Consortium is the equivalent of 3 clusters.

Appendix E

Revitalization/Expansion Schedule for Assessed Schools

Schools	Year Built	Year Renovated	FACT Score	Schedule
Elementary				
Candlewood	1968		1489	1/2015
Rock Creek Forest	1950	1971	1492	1/2015
Wayside	1969		1502	8/2017
Brown Station	1969		1516	8/2017
Wheaton Woods	1952	1976	1525	8/2017
Potomac	1949	1976	1550	1/2020
Luxmanor	1966		1578	1/2020
Maryvale/*Sandburg Learning Center*	1969/*1962*		1578/*414.05*	1/2020
Cold Spring	*1972*		*382.04*	*8/2021*
DuFief	*1975*		*357.01*	*8/2021*
Belmont	*1974*		*349.28*	*8/2021*
Stonegate	*1971*		*334.95*	*8/2021*
Damascus	*1934*	*1980*	*331.89*	*1/2023*
Twinbrook	*1952*	*1986*	*330.58*	*1/2023*
Summit Hall	*1971*		*328.90*	*1/2023*
Rosemary Hills	*1956*	*1988*	*327.05*	*1/2023*
Middle				
William H. Farquhar	1968		1434	8/2016
Tilden/*Rock Terrace School*	1966/*1950*		1455/*382.13*	8/2020
Eastern	1951	1976	1472	8/2022
E. Brooke Lee	1966		1479	TBD
High				
Wheaton/ Thomas Edison	1954	1983	1220	1/2016 Building 8/2017 Building 8/2018 Site
Seneca Valley	1974		1254	8/2019 Building 8/2020 Site
Thomas S. Wootton	1970		1301	8/2021 Building 8/2022 Site
Poolesville	1953	1978	1362	8/2023 Building 8/2024 Site
Col. Zadok Magruder	1970		1471	TBD
Damascus	1950	1978	1496	TBD
Northwood	1956	2004	****	TBD

Note: Schools were assessed in 1992, 1996, and 1999. Assessments were completed on the remaining 34 elementary and 11 middle schools during December 2010 and June 2011. (These schools are listed above in italics.) Four holding centers, three Special Education Learning Centers, and one Alternative Program Center also were assessed during December 2010 and June 2011. Schools will be added to the revitalization/expansion list once planning and or construction expenditures are included in the six-year Capital Improvements Program. See Appendix F for a complete list of schools that were assessed in the 2010–2011 school year.

Projects that were assessed prior to December 2010 and do not have planning and/or construction expenditures in the Adopted FY 2016 Capital Budget and Amendments to the FY 2015–2020 CIP have completion dates to be determined (TBD). This TBD status will be revised in a future CIP.

Appendix F

Assessing Schools for Revitalization/Expansion
(Formerly Known as Modernizations)

On December 7, 2010, the Board of Education adopted Policy FKB, *Sustaining and Modernizing Montgomery County Public Schools (MCPS) Facilities*. This policy updated Policy FKB, *Modernization/Renovation* that was adopted in 1992 and had never been updated by the Board of Education. The updated version of Policy FKB provides for a new emphasis on sustaining Montgomery County Public Schools (MCPS) facilities in good condition through systematic life-cycle asset replacement. At the same time, the policy recognizes the need to modernize schools as a facility reaches the end of its useful lifecycle.

As part of the Superintendent's Recommended FY 2015 Capital Budget and the FY 2015–2020 Capital Improvements Program, the name of "modernizations" was changed to "revitalizations/expansions" to accurately reflect the scope of work detailed in the MCPS educational specifications. In order to implement Policy FKB it was necessary to have an updated means of assessing and prioritizing schools for revitalization/expansion projects.

While a primary factor in the need to revitalize a school is the age of the facility, a number of other factors also are considered in assessing the condition of a school. When the MCPS modernization program began in the early 1990s, a methodology known as Facilities Assessment with Criteria and Testing (FACT) was developed. The original FACT methodology was applied to three groups of school assessments—the first group in FY 1993, the second in FY 1996 and the third in FY 2000. Through the 2011–2012 school year, these assessments resulted in the revitalization/expansion of 35 elementary schools, 8 middle schools, and 8 high schools. Another 12 elementary schools, 5 middle schools, and 9 high schools are now either under construction, in design, or are in the queue for revitalization/expansion. The list of these schools is provided in Appendix E. The list of elementary schools from this queue for revitalization/expansion is almost complete, with the last three elementary schools in the queue scheduled for completion in January 2019. As a result, it was necessary to assess additional elementary and secondary schools that are aging and in need of revitalization/expansion. A total of 53 facilities were identified for FACT assessments. The new list includes facilities that were built prior to the mid-1980s and had never been revitalized, although some of these schools may have had some renovation work performed.

Beginning in spring 2010, a process to update the FACT methodology was undertaken. A multi-stakeholder committee reviewed and prepared recommendations to update the methodology. The Board of Education supported the recommendations of the committee by adopting the updated FACT methodology on July 8, 2010. The updated FACT methodology describes the criteria to assess the condition of schools, the measures for each criterion, and the relative weights to apply to various criteria to obtain an overall score for each facility. Consultants EMG, Inc. provided technical expertise in the development of the detailed revised FACT methodology and the firm was responsible for conducting the assessments.

The old FACT methodology scoring system used a 2,000 point scale and schools in worse condition scored lower while schools in better condition received a higher score. In contrast, the new FACT methodology uses a 600 points scale in which the buildings in worse condition received higher scores and the buildings in better condition received lower scores. "Educational Program" parameters such as educational specifications, open plan schools, and controlled access were assigned 300 points and "Physical Infrastructure" parameters, such as facility design guidelines, utility and energy efficiency, maintenance cost, and community use of public facilities, were assigned 300 points. The final report of the assessments, including the facility scores, was presented to the Board of Education on October 11, 2011.

The table on the following page presents the scores for each school in rank order for elementary schools and secondary schools. As the current queue of schools scheduled for revitalization/expansion projects is completed (see Appendix E), schools on the following page will be placed in the revitalization/expansion queue according to their score. The movement of the newly assessed schools to the revitalization/expansion queue will occur as planning and construction funds are programmed in the six year CIP period. At that time a completion date for the revitalization/expansion project also will be provided. The purpose of the following list is to show the rank order and scores of all the schools that were recently assessed.

In addition to 34 elementary schools and 11 middle schools, the recent FACT assessments included three special education program centers—Stephen Knolls, Rock Terrace, and Carl Sandburg—the Blair G. Ewing Center, and the four elementary school holding centers. Stephen Knolls is placed in the

list of elementary schools on the following page and Rock Terrace and the Blair G. Ewing Center are placed in the list of secondary schools. The Carl Sandburg Learning Center is not included on the following table because of the adopted plan to collocate this school at Maryvale Elementary School as part of the revitalization/expansion project. Finally, the elementary school holding centers are not included on the following table because improvements to these facilities will be addressed through a separate capital project.

FACT* Scores

Rank	Elementary Schools	Total FACT Score Maximum Score = 600
1	Cold Spring Elementary School	382.04
2	DuFief Elementary School	357.01
3	Belmont Elementary School	349.28
4	Stonegate Elementary School	334.95
5	Damascus Elementary School	331.89
6	Twinbrook Elementary School	330.58
7	Summit Hall Elementary School	328.90
8	Rosemary Hills Elementary School	327.05
9	Burnt Mills Elementary School	318.29
10	Poolesville Elementary School	314.42
11	Woodfield Elementary School	314.09
12	South Lake Elementary School	302.69
13	Cedar Grove Elementary School	302.46
14	Greenwood Elementary School	300.47
15	Piney Branch Elementary School	294.73
16	Whetstone Elementary School	293.22
17	Takoma Park Elementary School	292.86
18	Gaithersburg Elementary School	290.88
19	Strathmore Elementary School	289.46
20	Diamond Elementary School	286.57
21	Fox Chapel Elementary School	278.71
22	Stephen Knolls School	276.56
23	East Silver Spring Elementary School	276.41
24	JoAnn Leleck Elementary School at Broad Acres	275.88
25	Woodlin Elementary School	273.72
26	Germantown Elementary School	272.61
27	Fallsmead Elementary School	267.41
28	Watkins Mill Elementary School	266.33
29	Fields Road Elementary School	257.61
30	Stedwick Elementary School	249.55
31	Cloverly Elementary School	244.31
32	Darnestown Elementary School	241.67
33	Washington Grove Elementary School	227.68
34	Bradley Hills Elementary School	212.04
35	Sherwood Elementary School	210.92

Rank	Secondary Schools	Total FACT Score Maximum Score = 600
1	Rock Terrace School	382.13
2	Blair G. Ewing Center	380.99
3	Banneker Middle School	341.88
4	Argyle Middle School	322.24
5	Newport Mill Middle School	315.72
6	Ridgeview Middle School	309.03
7	Silver Spring Intl. Middle School	301.37
8	Neelsville Middle School	291.74
9	Baker Middle School	279.58
10	Frost Middle School	255.22
11	Loiederman Middle School	254.66
12	Redland Middle School	245.35
13	North Bethesda Middle School	240.74

* FACT refers to the Facilities Assessment with Criteria and Testing methodology for evaluating and scoring the condition of schools. The higher the FACT score the worse the condition of a facility. These assessments were completed during the 2010-11 school year.

Appendix G

Restroom Renovations Schedule

School Rank	Name of School	Raw Rating*
	FY 2013	
1	Albert Einstein High School	1574
2	Watkins Mill High School	1567
3	Watkins Mill Elementary School	1566
4	Jones Lane Elementary School	1565
5	Highland View Elementary School	1547
6	Radnor Center	1544
7	Woodfield Elementary School	1541
8	Roberto Clemente Middle School	1525
9	Fairland Center	1513
10	Rock Terrace School	1509
	FY 2014	
11	Cold Spring Elementary School	1492
12	Sherwood High School	1475
13	Carl Sandburg Center	1456
14	Cedar Grove Elementary School	1455
15	Fields Road Elementary School	1439
16	Rachel Carson Elementary School	1413
17	Silver Spring International Middle School	1412
18	White Oak Middle School	1408
19	Beall Elementary School	1394
20	Rosa M. Parks Middle School	1380
21	Dr. Martin Luther King, Jr. Middle School	1357
	FY 2015	
22	Sligo Middle School	1352
23	Briggs Chaney Middle School	1348
24	Cloverly Elementary School	1335
25	Thurgood Marshall Elementary School	1333
26	Stephen Knolls Center	1328
27	Wyngate Elementary School	1325
28	Montgomery Knolls Elementary School	1315
29	Pine Crest Elementary School	1314
30	Meadow Hall Elementary School	1299
31	Twinbrook Elementary School	1295
32	Greencastle Elementary School	1265
33	Waters Landing Elementary School	1260
34	Sligo Creek Elementary School	1252
35	Westbrook Elementary School	1244
	FY 2016	
36	S. Christa McAuliffe Elementary School	1235
37	Northwood High School	1234
38	Ritchie Park Elementary School	1234
39	Brookhaven Elementary School	1228
40	Travilah Elementary School	1225
41	Georgian Forest Elementary School	1221
42	Clopper Mill Elementary School	1219
43	Takoma Park Middle School	1214
44	John Poole Middle School	1211
45	Laytonsville Elementary School	1207
46	Montgomery Blair High School	1204
47	Jackson Road Elementary School	1201
48	Bethesda Elementary School	1201
49	Oakland Terrace Elementary School	1195
50	Dr. Sally K. Ride Elementary School	1191
51	North Chevy Chase Elementary School	1188
52	Highland Elementary School	1181
53	Ashburton Elementary School	1180
54	Lucy V. Barnsley Elementary School	1178
55	Flower Hill Elementary School	1177
56	Northwest High School	1172
57	Viers Mills Elementary School	1163
58	Lois P. Rockwell Elementary School	1161
59	Monocacy Elementary School	1159
60	Oak View Elementary School	1158
61	Rock View Elementary School	1153
62	Harmony Hills Elementary School	1152
63	Ronald McNair Elementary School	1150
64	Olney Elementary School	1147
	FY 2017	
65	Shady Grove Middle School	1132
66	Capt. James E. Daly Elementary School	1130
67	Goshen Elementary School	1130
68	Forest Knolls Elementary School	1121
69	Rosemary Hills Elementary School	1119
70	North Bethesda Middle School	1116
71	Walt Whitman High School	1108
72	Bethesda Chevy-Chase High School	1106
73	Burning Tree Elementary School	1105
74	Kemp Mill Elementary School	1102
75	James Hubert Blake High School	1102
76	Gaithersburg Elementary School	1094
77	Westland Middle School	1087
78	Flower Valley Elementary School	1084
79	Kingsview Middle School	1083
80	Fairland Elementary School	1080
81	Westover Elementary School	1079
82	Rosemont Elementary School	1076
83	Brooke Grove Elementary School	1075
84	Springbrook High School	1063
85	New Hampshire Est. Elementary School	1062
86	John F. Kennedy High School	1061
87	Greenwood Elementary School	1061
88	Burtonsville Elementary School	1045
89	Dr. Charles R. Drew Elementary School	1039
90	Forest Oak Middle School	1039
91	Sequoyah Elementary School	1030
	FY 2018	
92	Argyle Middle School	1029
93	Clarksburg Elementary School	1022
94	Judith Resnik Elementary School	1020
95	Thomas W. Pyle Middle School	1013
96	Strawberry Knoll Elementary School	1010

* The raw rating was determined based on an evaluation method using a preset number scale for the assessment of the existing plumbing fixtures, accessories, and room finish materials. The ratings also were based upon visual inspections of the existing materials and fixtures as of August 1, 2009 and conversations with the principal, building services manager, assistant principal, and staff about the existing conditions of the restroom facilities. A total of 110 facilities were assessed and, based on funding, 96 facilities are proposed for renovation in the six year CIP.

Appendix H

Head Start and Prekindergarten Locations: 2015–2016

School	Head Start Sessions	# Head Start Students	Pre-K Sessions	# Pre-K Students	Total Head Start and Pre-K Enrollment
Montgomery College Rockville	1	20			20
Beall Elementary School	1[a]	15	1	20	35
Bel Pre Elementary School			5	100	100
Bells Mill Elementary School	1	20			20
Brooke Grove Elementary School			1	20	20
Brookhaven Elementary School			2	40	40
Brown Station Elementary School	1	20	2	40	60
Burnt Mills Elementary School			2	40	40
Rachel Carson Elementary School			2	40	40
Cashell Elementary School			1	20	20
Clearspring Elementary School	1	20	1	20	40
Clopper Mill Elementary School	1	20	3	60	80
College Gardens Elementary School	1[c]	17			17
Capt. James E. Daly Elementary School			2	40	40
Dr. Charles R. Drew Elementary School			3	60	60
East Silver Spring Elementary School	1[c]	17	2	40	57
Fairland Elementary School	1	20	1	20	40
Fields Road Elementary School			1	20	20
Flora M. Singer Elementary School			1	20	20
Flower Hill Elementary School			2	40	40
Forest Knolls Elementary School			2	40	40
Fox Chapel Elementary School			2	40	40
Gaithersburg Elementary School			2	40	40
Galway Elementary School			2	40	40
Georgian Forest Elementary School	1	20	2	40	60
William B. Gibbs, Jr. Elementary School			2	40	40
Glen Haven Elementary School			2	40	40
Glenallan Elementary School	1	20			20
Greencastle Elementary School			2	40	40
Harmony Hills Elementary School	1	20	2	40	60
Highland Elementary School	1	20	2	40	60
Jackson Road Elementary School			2	40	40
Kemp Mill Elementary School	1	20	2	40	60
Lake Seneca Elementary School			2	40	40

School	Head Start Sessions	# Head Start Students	Pre-K Sessions	# Pre-K Students	Total Head Start and Pre-K Enrollment
JoAnn Leleck ES at Broad Acres	1	20	4	80	100
Maryvale Elementary School	2[a]	35	2	40	75
S. Christa McAuliffe Elementary School	1	20			20
Ronald McNair Elementary School			1	20	20
Mill Creek Towne Elementary School			1	20	20
Mont. Knolls Elementary School	1	20	2	40	60
New Hamp. Est. Elementary School	4[a]	75	2	45	120
Rock Creek Forest Elementary School			1	20	20
Roscoe Nix Elementary School			2	40	40
Oakland Terrace Elementary School			1	20	20
William T. Page Elementary School			2	40	40
Judith A. Resnik Elementary School			2	40	40
Sally K. Ride Elementary School	1[a]	15	2	40	55
Rock View Elementary School			2	40	40
Rolling Terrace Elementary School	1	20	2	40	60
Rosemary Hills Elementary School			2	40	40
Rosemont Elementary School			2	40	40
Sargent Shriver Elementary School			2	40	40
South Lake Elementary School	1	20	2	40	60
Stedwick Elementary School			2	40	40
Strawberry Knoll Elementary School	1[b]	14	1	20	34
Summit Hall Elementary School	1	20	2	40	60
Takoma Park Elementary School			1	20	40
Twinbrook Elementary School	1	20	2	40	60
Viers Mill Elementary School	1	20	2	40	60
Wash. Grove Elementary School	1	20	4	80	100
Watkins Mill Elementary School	1	20	1	20	40
Weller Road Elementary School	1	20	3	60	80
Wheaton Woods Elementary School	1	20	2	40	60
Whetstone Elementary School			2	40	40
Total Sessions Served by MCPS	32		114		
Total Enrollment Served by MCPS		628		2,285	2,913

[a] One session is for 15 three-year-olds

[b] One session is a four-hour session for 14 students

[c] One session is a mixed-age class of 3s & 4s

Appendix I

Subdivision Staging Policy FY 2015 School Test: Cluster Utilizations in 2019–2020

Reflects County Council Approved FY 2015 Capital Budget and FY 2015–2020 Capital Improvements Program (CIP)

Effective July 1, 2014

Elementary School Test: Percent Utilization >105% School Facility Payment and >120% Moratorium

Cluster Area	Projected August 2019 Enrollment	100% MCPS Program Capacity With BOE Requested FY15–20 CIP	Cluster Percent Utilization in 2019	School Test Result Capacity is:	Cluster is?
Bethesda-Chevy Chase	3,449	3,813	90.5%	Adequate	Open
Montgomery Blair	**4,471**	**4,148**	**107.8%**	**Inadequate**	**School Payment**
James Hubert Blake	2,296	2,201	104.3%	Adequate	Open
Winston Churchill	2,645	2,928	90.3%	Adequate	Open
Clarksburg	**4,461**	**3,872**	**115.2%**	**Inadequate**	**School Payment**
Damascus	1,847	2,133	86.6%	Adequate	Open
Albert Einstein	3,074	2,963	103.7%	Adequate	Open
Gaithersburg	**4,385**	**3,838**	**114.3%**	**Inadequate**	**School Payment**
Walter Johnson	4,141	4,353	95.1%	Adequate	Open
John F. Kennedy	2,875	3,046	94.4%	Adequate	Open
Col. Zadok Magruder	**2,768**	**2,590**	**106.9%**	**Inadequate**	**School Payment**
Richard Montgomery	2,762	2,882	95.8%	Adequate	Open
Northwest	4,234	4,519	93.7%	Adequate	Open
Northwood	**3,666**	**3,435**	**106.7%**	**Inadequate**	**School Payment**
Paint Branch	**2,561**	**2,242**	**114.2%**	**Inadequate**	**School Payment**
Poolesville	560	758	73.9%	Adequate	Open
Quince Orchard	**3,135**	**2,791**	**112.3%**	**Inadequate**	**School Payment**
Rockville	2,639	2,580	102.3%	Adequate	Open
Seneca Valley	**2,471**	**2,183**	**113.2%**	**Inadequate**	**School Payment**
Sherwood	1,912	2,422	78.9%	Adequate	Open
Springbrook	3,266	3,178	102.8%	Adequate	Open
Watkins Mill	2,714	2,790	97.3%	Adequate	Open
Wheaton	3,212	3,631	88.5%	Adequate	Open
Walt Whitman	2,605	2,561	101.7%	Adequate	Open
Thomas S. Wootton	2,710	3,222	84.1%	Adequate	Open

Middle School Test: Percent Utilization >105% School Facility Payment and >120% Moratorium

Cluster Area	Projected August 2019 Enrollment	100% MCPS Program Capacity With BOE Requested FY15–20 CIP	Cluster Percent Utilization in 2019	School Test Result Capacity is:	Cluster is?
Bethesda-Chevy Chase	1,694	2,041	83.0%	Adequate	Open
Montgomery Blair	**2,672**	**2,354**	**113.5%**	**Inadequate**	**School Payment**
James Hubert Blake	1,263	1,354	93.3%	Adequate	Open
Winston Churchill	1,439	1,716	83.9%	Adequate	Open
Clarksburg	2,113	2,380	88.8%	Adequate	Open
Damascus	785	791	99.2%	Adequate	Open
Albert Einstein	1,304	1,434	90.9%	Adequate	Open
Gaithersburg	1,872	1,866	100.3%	Adequate	Open
Walter Johnson	2,126	2,188	97.2%	Adequate	Open
John F. Kennedy	**1,658**	**1,550**	**107.0%**	**Inadequate**	**School Payment**
Col. Zadok Magruder	1,277	1,602	79.7%	Adequate	Open
Richard Montgomery	1,341	1,445	92.8%	Adequate	Open
Northwest	2,258	2,225	101.5%	Adequate	Open
Northwood	**1,760**	**1,560**	**112.8%**	**Inadequate**	**School Payment**
Paint Branch	1,380	1,384	99.7%	Adequate	Open
Poolesville	288	468	61.5%	Adequate	Open
Quince Orchard	1,496	1,695	88.3%	Adequate	Open
Rockville	**1,064**	**961**	**110.7%**	**Inadequate**	**School Payment**
Seneca Valley	1,271	1,391	91.4%	Adequate	Open
Sherwood	1,098	1,456	75.4%	Adequate	Open
Springbrook	1,288	1,250	103.0%	Adequate	Open
Watkins Mill	1,298	1,379	94.1%	Adequate	Open
Wheaton	**1,773**	**1,488**	**119.2%**	**Inadequate**	**School Payment**
Walt Whitman	**1,455**	**1,326**	**109.7%**	**Inadequate**	**School Payment**
Thomas S. Wootton	1,455	1,640	88.7%	Adequate	Open

High School Test: Percent Utilization >105% School Facility Payment and >120% Moratorium

Cluster Area	Projected August 2019 Enrollment	100% MCPS Program Capacity With BOE Requested FY15–20 CIP	Cluster Percent Utilization in 2019	School Test Result Capacity is:	Cluster is?
Bethesda-Chevy Chase*	2,286	2,399	95.3%	Adequate	Open
Montgomery Blair	3,053	2,938	103.9%	Adequate	Open
James Hubert Blake	1,749	1,743	100.3%	Adequate	Open
Winston Churchill	2,091	2,013	103.9%	Adequate	Open
Clarksburg	**2,297**	**1,980**	**116.0%**	**Inadequate**	**School Payment**
Damascus	1,433	1,551	92.4%	Adequate	Open
Albert Einstein	**1,760**	**1,621**	**108.6%**	**Inadequate**	**School Payment**
Gaithersburg	2,240	2,317	96.7%	Adequate	Open
Walter Johnson	**2,630**	**2,336**	**112.6%**	**Inadequate**	**School Payment**
John F. Kennedy	1,801	1,847	97.5%	Adequate	Open
Col. Zadok Magruder	1,663	1,995	83.4%	Adequate	Open
Richard Montgomery	**2,416**	**2,236**	**108.1%**	**Inadequate**	**School Payment**
Northwest	**2,430**	**2,241**	**108.4%**	**Inadequate**	**School Payment**
Northwood	**1,762**	**1,575**	**111.9%**	**Inadequate**	**School Payment**
Paint Branch	2,059	2,047	100.6%	Adequate	Open
Poolesville	1,146	1,170	97.9%	Adequate	Open
Quince Orchard	**2,012**	**1,857**	**108.3%**	**Inadequate**	**School Payment**
Rockville	1,504	1,570	95.8%	Adequate	Open
Seneca Valley	1,282	1,994	64.3%	Adequate	Open
Sherwood	1,748	2,136	81.8%	Adequate	Open
Springbrook	1,921	2,167	88.6%	Adequate	Open
Watkins Mill	1,672	1,917	87.2%	Adequate	Open
Wheaton	1,610	1,596	100.9%	Adequate	Open
Walt Whitman	**2,121**	**1,882**	**112.7%**	**Inadequate**	**School Payment**
Wootton	2,158	2,154	100.2%	Adequate	Open

Appendix J

Facilities Data and State Rated Capacity
School Year 2014–2015

	Elementary Schools	Sm. Gr.	Year Built	Year Renov./ Reopen/ Revital.*	Exist. Sq. Ft.	Site Size	Park	State-Rated Capacity Number of Rooms				State-Rated Capacity	MCPS Program Capacity
								Pre-K @20	Kind. @22	Reg. @23	Sp. Ed. @10		
	Elementary Schools												
1	Arcola	S	1956	2007	85,469	5	Yes	0	8	18	1	600	496
2	Ashburton	S	1957	1993	81,438	8.32		0	5	18	7	594	629
3	Bannockburn	S	1957	1988	54,234	8.34		0	3	13	0	365	365
4	Lucy V. Barnsley	S	1965	1998	72,024	10		0	5	13	6	469	404
5	Beall	S	1954	1991	79,477	8.44	Yes	2	5	19	3	617	638
6	Bel Pre	S	1968	2014	102,198	8.91	Yes	2	9	22	0	744	638
7	Bells Mill	S	1968	2009	77,244	9.6		1	4	22	2	634	626
8	Belmont	S	1974		49,279	10.52		0	3	15	1	421	424
9	Bethesda	R	1952	1999	62,557	8.42		0	3	13	2	385	384
10	Beverly Farms	S	1965	2012	98,916	5	Yes	0	3	26	2	684	690
11	Bradley Hills	S	1951	1984	76,745	6.71	Yes	0	4	25	0	663	663
12	Brooke Grove	S	1990		72,582	10.96		1	2	18	5	528	531
13	Brookhaven	S	1961	1995	81,320	8.57		1	4	14	6	490	486
14	Brown Station	G	1969		58,338	9	Yes	2	5	12	4	466	436
15	Burning Tree	S	1958	1991	68,119	6.78	Yes	0	3	11	6	379	379
16	Burnt Mills	S	1964	1990	57,318	15.14		1	4	14	1	440	402
17	Burtonsville	G	1952	1993	71,349	11.92		0	6	19	0	569	485
18	Candlewood	S	1968	2015	92,222	11.78		0	2	22	0	550	550
19	Cannon Road	S	1967	2012	83,377	4.4	Yes	0	4	19	5	575	521
20	Carderock Springs	S	1966	2010	75,351	9		0	2	15	3	419	407
21	Rachel Carson	G	1990		78,547	12.4		1	7	20	1	644	667
22	Cashell	S	1969	2009	71,171	10.24		1	2	11	4	357	341
23	Cedar Grove	G	1960	1987	57,037	10.12		0	4	13	3	417	405
24	Chevy Chase	S	1936	2000	70,976	3.78		0	0	20	1	470	473
25	Clarksburg	G	1952	1993	54,983	9.97		0	3	9	3	303	312
26	Clearspring	S	1988		77,535	10	Yes	1	3	22	5	642	642
27	Clopper Mill	S	1986		64,851	9	Yes	2	4	13	4	467	417
28	Cloverly	S	1961	1989	61,991	10	Yes	0	3	14	6	448	454
29	Cold Spring	S	1972		55,158	12.38		0	2	18	0	458	458
30	College Gardens	G	1967	2008	96,986	7.94	Yes	1	5	24	2	702	694
31	Cresthaven	G	1962	2010	76,862	9.81		0	0	18	5	464	467
32	Capt. James E. Daly	S	1989		78,210	10	Yes	1	6	17	3	573	518
33	Damascus	S	1934	1980	53,239	9.42		0	2	11	4	337	328
34	Darnestown	S	1954	1980	64,840	7.21		0	2	18	1	468	471
35	Diamond	G	1975		64,950	10	Yes	0	5	14	4	472	463
36	Dr. Charles R. Drew	S	1991		73,975	12		2	3	14	6	488	456
37	DuFief	S	1975		59,013	10		0	2	14	6	426	428
38	East Silver Spring	R	1929	1975	88,895	8.43		2	5	18	5	614	582
39	Fairland	S	1992		92,227	11.79		2	6	23	3	731	648
40	Fallsmead	S	1974		67,472	8.98	Yes	0	4	21	2	591	598
41	Farmland	S	1963	2011	89,988	4.75	Yes	0	5	26	2	728	728
42	Fields Road	G	1973		72,302	10		1	5	14	5	502	419
43	Flower Hill	S	1985		58,770	10	Yes	1	4	17	2	519	483
44	Flower Valley	S	1967	1996	61,567	9.28		0	3	14	5	438	429
45	Forest Knolls	S	1960	1993	89,564	7.77		1	8	18	3	640	560
46	Fox Chapel	S	1974		85,182	10.34	Yes	1	5	26	0	728	683
47	Gaithersburg	S	1947	1983	94,468	8.39		1	9	26	4	856	771
48	Galway	S	1967	2009	103,170	9	Yes	1	6	29	3	849	790
49	Garrett Park	S	1948	2012	96,348	4.4	Yes	0	6	27	0	753	753
50	Georgian Forest	S	1961	1995	88,111	10.94	Yes	2	6	22	2	698	649
51	Germantown	G	1935	1978	57,668	7.75		0	3	10	5	346	333
52	William B. Gibbs, Jr.	G	2009		88,042	10.75		1	5	23	4	699	740
53	Glen Haven	R	1950	2004	85,845	10	Yes	1	5	20	4	630	576
54	Glenallan	S	1966	2013	98,700	12.1		1	7	28	3	848	762
55	Goshen	S	1988		76,740	10.47		0	6	20	2	612	533
56	Great Seneca Creek	G	2006		82,511	13.71		0	5	21	4	633	566
57	Greencastle	S	1988		78,275	18.88		1	7	19	3	641	582
58	Greenwood	G	1970		64,609	10	Yes	0	3	22	1	582	585
59	Harmony Hills	S	1957	1999	85,648	10.19	Yes	2	8	25	0	791	709
60	Highland	S	1950	1989	84,138	11	Yes	2	5	18	1	574	522
61	Highland View	S	1953	1994	59,213	6.61		0	4	11	1	351	298
62	Jackson Road	S	1959	1995	91,465	8.76		1	4	26	4	746	709
63	Jones Lane	S	1987		60,679	12.06		0	3	14	5	438	441
64	Kemp Mill	S	1960	1996	68,222	10		2	6	14	1	504	453
65	Kensington-Parkwood	S	1952	2006	77,136	9.86		0	4	15	3	463	472
66	Lake Seneca	G	1985		58,770	9.35		1	5	12	4	446	410
67	Lakewood	G	1968	2003	77,526	13.07		0	3	21	2	569	569

Note: State-rated capacity and MCPS capacity may differ due to the method of calculating capacity for special education classes. For MCPS calculations, please refer to the individual school calculations.

Smart Growth (Sm. Gr.): S=Stabilized; R=Revitalization; G=Growth; N=Non Growth

* Schools with a date before 1986 underwent a renovation, not a full revitalization of the facility. Schools that were reopened but not fully revitalized or completely rebuilt will be included in the assessments for future revitalization based on the year the school was originally opened. See Appendix K for more information.

	Elementary Schools	Sm. Gr.	Year Built	Year Renov./ Reopen/ Revital.*	Exist. Sq. Ft.	Site Size	Park	State-Rated Capacity Number of Rooms				State-Rated Capacity	MCPS Program Capacity
								Pre-K @20	Kind. @22	Reg. @23	Sp. Ed. @10		
68	Laytonsville	S	1951	1989	64,160	10.43		0	3	15	5	461	448
69	JoAnn Leleck at Broad Acres	R	1952	1974	88,922	6.25	Yes	3	6	24	0	744	672
70	Little Bennett	G	2006		82,511	4.81	Yes	0	4	25	1	673	676
71	Luxmanor	S	1966		61,694	6.5	Yes	0	4	14	2	430	428
72	Thurgood Marshall	S	1993		77,798	12		0	5	15	5	505	534
73	Maryvale	S	1969		92,050	17.67		3	5	21	3	683	626
74	Spark M. Matsunaga	G	2001		90,718	11.8		0	5	23	1	649	652
75	S. Christa McAuliffe	S	1987		77,240	10.59	Yes	1	6	19	2	609	526
76	Ronald McNair	S	1990		78,275	10	Yes	1	5	20	1	600	623
77	Meadow Hall	S	1956	1994	61,964	8.37	Yes	0	5	12	5	436	370
78	Mill Creek Towne	S	1966	2000	67,465	8.38		1	3	10	6	376	326
79	Monocacy	S	1961	1989	42,482	27		0	1	8	1	216	219
80	Montgomery Knolls	S	1952	1989	97,213	10.33		2	8	15	4	601	540
81	New Hampshire Estates	S	1954	1988	73,306	5.42		6	8	12	0	572	480
82	Roscoe R. Nix	G	2006		88,351	7.8	Yes	1	9	16	4	626	521
83	North Chevy Chase	S	1953	1995	48,350	7.94		0	0	11	1	263	266
84	Oak View	S	1949	1985	57,560	11.25		0	0	15	1	355	358
85	Oakland Terrace	S	1950	1993	79,145	9.54	Yes	1	5	17	4	561	513
86	Olney	G	1954	1990	68,755	9.88		0	3	22	1	582	585
87	William T. Page	S	1965	2003	58,726	9.76		1	4	13	1	417	379
88	Pine Crest	S	1941	1992	53,778	5.64	Yes	0	0	16	1	378	381
89	Piney Branch	R	1973		99,706	1.97	Yes	0	0	26	1	608	611
90	Poolesville	S	1960	1978	64,803	12.28		0	3	20	1	536	539
91	Potomac	G	1949	1976	57,713	9.61		0	3	15	1	421	424
92	Judith A. Resnik	S	1991		78,547	12.98		1	5	18	2	564	493
93	Sally K. Ride	S	1994		78,686	13.48		2	4	16	6	556	523
94	Ritchie Park	S	1966	1997	58,500	9.22		0	4	13	0	387	387
95	Rock Creek Forest	S	1950	2015	98,140	7.95		1	5	30	0	820	770
96	Rock Creek Valley	S	1964	2001	76,692	10.44		0	5	13	7	479	393
97	Rock View	S	1955	1999	91,977	7.44		1	5	25	4	745	687
98	Lois P. Rockwell	S	1992		75,520	10.56		0	3	17	4	497	523
99	Rolling Terrace	S	1988		88,835	4.33		2	6	26	1	780	724
100	Rosemary Hills	S	1956	1988	70,541	6.07		1	11	7	4	463	478
101	Rosemont	G	1965	1995	88,764	8.91		1	6	20	5	662	590
102	Sequoyah	S	1990		72,582	10	Yes	0	5	17	3	531	470
103	Seven Locks	S	1964	2012	66,915	9.98		0	2	16	1	422	425
104	Sherwood	S	1977		81,727	10.85		0	3	20	5	576	569
105	Sargent Shriver	S	1954	2006	91,628	9.17		1	7	25	0	749	673
106	Flora M. Singer	S	1950	2012	95,831	12		1	6	24	3	734	680
107	Sligo Creek	S	1934	1999	98,799	5	Yes	0	5	23	3	669	664
108	Somerset	R	1949	2005	80,122	3.71		0	4	18	1	512	515
109	South Lake	S	1972		83,038	10.2		2	6	26	0	770	716
110	Stedwick	S	1974		109,677	10		1	5	23	3	689	639
111	Stone Mill	S	1988		78,617	11.76		0	4	22	5	644	654
112	Stonegate	S	1971		52,468	10.26		0	3	13	3	395	395
113	Strathmore	S	1970		59,497	10.8	Yes	0	0	18	3	444	439
114	Strawberry Knoll	G	1988		78,723	10.82		2	5	13	7	519	453
115	Summit Hall	S	1971		68,059	10.16	Yes	2	6	14	1	504	443
116	Takoma Park	R	1979		85,553	4.7		2	10	22	0	766	636
117	Travilah	G	1960	1992	65,378	9.3		0	2	19	2	501	517
118	Twinbrook	S	1952	1986	79,818	10.45		2	4	20	2	608	563
119	Viers Mill	S	1950	1991	120,572	10.52		2	7	25	4	809	760
120	Washington Grove	G	1956	1984	86,266	10.67		3	3	19	5	613	603
121	Waters Landing	S	1988		101,352	9.99		0	7	30	3	874	776
122	Watkins Mill	S	1970		80,923	10	Yes	2	5	28	3	824	759
123	Wayside	S	1969		77,507	9.26		0	3	25	4	681	671
124	Weller Road	S	1953	2013	121,346	11.1		2	6	28	1	826	775
125	Westbrook	S	1939	1990	91,359	12.46	Yes	0	3	19	4	543	554
126	Westover	S	1964	1998	54,645	7.56		0	2	9	5	301	293
127	Wheaton Woods	S	1952	1976	66,763	8		2	5	11	0	403	358
128	Whetstone	S	1968		96,946	8.82		1	6	27	5	823	783
129	Wilson Wims	S	2014		91,931	9.29		0	6	27	1	763	759
130	Wood Acres	S	1952	2002	73,138	4.78	Yes	0	5	17	2	521	527
131	Woodfield	S	1962	1985	53,212	10		0	2	17	2	455	471
132	Woodlin	R	1944	1974	60,725	11		0	5	13	5	459	462
133	Wyngate	S	1952	1997	89,104	9.45		0	5	29	0	777	777
	Total Elementary Schools				10,196,240	1,268		97	588	2,464	366	75,208	71,545

Note: State-rated capacity and MCPS capacity may differ due to the method of calculating capacity for special education classes. For MCPS calculations, please refer to the individual school calculations.

Smart Growth (Sm. Gr.): S=Stabilized; R=Revitalization; G=Growth; N=Non Growth

* Schools with a date before 1986 underwent a renovation, not a full revitalization of the facility. Schools that were reopened but not fully revitalized or completely rebuilt will be included in the assessments for future revitalization based on the year the school was originally opened. See Appendix K for more information.

Facilities Data and State Rated Capacity
School Year 2014–2015

	Schools	Sm. Gr.	Year Built	Year Renov./ Reopen/ Revital. *	Existing Sq. Ft.	Site Size	Park	Capacity Reg. @25	Capacity Sp. Ed. @10	State Rated Capacity (85% Reg. + Sp .Ed.)	MCPS Capacity (Tot. Cap.)
	Middle Schools									(85% + Sp. Ed.)	(X 85%)
1	Argyle	S	1971	1993	120,205	19.9		43	0	914	897
2	John T. Baker	G	1971		120,532	22	Yes	34	3	753	741
3	Benjamin Banneker	G	1974		117,035	20		37	3	816	803
4	Briggs Chaney	S	1991		115,000	29.37		46	0	978	969
5	Cabin John	S	1967	2011	159,514	18.24		52	5	1,155	1,129
6	Roberto Clemente	G	1992		148,246	19.87		57	3	1,241	1,231
7	Eastern	S	1951	1976	152,030	14.51		49	2	1,061	1,024
8	William H. Farquhar	G	1968		116,300	20		42	2	913	906
9	Forest Oak	G	1999		132,259	41.19		45	2	976	949
10	Robert Frost	G	1971		143,757	24.79		51	0	1,084	1,075
11	Gaithersburg	S	1960	1988	157,694	22.82		42	7	963	933
12	Herbert Hoover	S	1966	2013	165,367	19.14		52	4	1,145	1,139
13	Francis Scott Key	S	1966	2009	147,424	20.58		46	0	978	961
14	Martin Luther King	G	1996		135,867	18.61		43	0	914	905
15	Kingsview	G	1997		140,398	18.45	Yes	49	0	1,041	1,041
16	Lakelands Park	G	2005		153,588	8.11	Yes	52	5	1,155	1,122
17	Col. E. Brooke Lee	S	1966		123,199	16.45	Yes	36	3	795	775
18	A. Mario Loiederman	G	1956	2005	131,746	17.08		43	0	914	897
19	Montgomery Village	S	1968	2003	141,615	15.14		42	4	933	894
20	Neelsville	S	1981		131,432	29.2		45	0	956	922
21	Newport Mill	S	1958	2002	108,240	8.4	Yes	38	3	838	825
22	North Bethesda	G	1955	1999	130,461	19.99		40	2	870	864
23	Parkland	G	1963	2007	151,169	9.18	Yes	45	0	956	948
24	Rosa M. Parks	S	1992		137,469	24.05	Yes	46	0	978	978
25	John Poole	S	1997		85,669	20.51		22	0	468	468
26	Thomas W. Pyle	S	1962	1993	153,824	14.32		60	3	1,305	1,289
27	Redland	S	1971		112,297	20.64	Yes	36	0	765	757
28	Ridgeview	G	1975		139,742	20		47	1	1,009	995
29	Rocky Hill	G	2004		148,065	23.29		46	2	998	995
30	Shady Grove	S	1995	1999	129,206	20		40	2	870	867
31	Silver Spring International	G	1934	1999	152,731	10.64	Yes	53	0	1,126	1,118
32	Sligo	G	1959	1991	149,527	21.74	Yes	43	2	934	915
33	Takoma Park	S	1939	1999	137,348	18.83	Yes	45	0	956	939
34	Tilden	G	1967	1991	135,150	29.8		45	5	1,006	972
35	Julius West	G	1961	1995	147,223	21.31		50	2	1,083	1,054
36	Westland	G	1951	1997	146,006	25.09		52	0	1,105	1,097
37	White Oak	S	1962	1993	140,990	17.34		46	2	998	962
38	Earle B. Wood	S	1965	2001	152,588	8.5	Yes	44	6	995	961
	Total Middle Schools				5,210,913	749.08		1704	73	36,940	36,315
	High Schools									(85% + Sp. Ed.)	(X 90%)
1	Bethesda-Chevy Chase	G	1934	2001	308,215	16.36		76	0	1615	1683
2	Montgomery Blair	G	1998		386,567	30.15	Yes	133	0	2826	2921
3	James H. Blake	G	1998		297,125	91.09		77	2	1656	1743
4	Winston Churchill	G	1964	2001	322,078	30.28		87	7	1919	2013
5	Clarksburg	G	1995	2006	309,216	62.73		72	3	1560	1638
6	Damascus	G	1950	1978	235,986	32.65		67	6	1484	1551
7	Albert Einstein	G	1962	1997	276,462	26.67	Yes	71	9	1599	1621
8	Gaithersburg	G	1951	2013	427,048	40.48		104	18	2390	2407
9	Walter Johnson	G	1956	2009	365,138	30.86		104	3	2240	2345
10	John F. Kennedy	G	1964	1999	280,048	29.14		82	4	1783	1847
11	Col. Zadok Magruder	G	1970		295,478	30		89	2	1911	1995
12	Richard Montgomery	G	1942	2007	311,500	29.05		99	3	2134	2237
13	Northwest	G	1998		340,867	34.56	Yes	98	4	2123	2241
14	Northwood	G	1956	2004	253,488	29.56		70	3	1518	1530
15	Paint Branch	G	1969	2012	347,169	45.96		88	6	1930	2034
16	Poolesville	S	1953	1978	165,056	37.2		52	0	1105	1170
17	Quince Orchard	G	1988		284,912	30.11		83	3	1794	1857
18	Rockville	G	1968	2004	316,973	30.32		67	9	1514	1571
19	Seneca Valley	G	1974		251,278	29.37		61	5	1346	1374
20	Sherwood	G	1950	1991	333,154	49.33		97	3	2091	2166
21	Springbrook	S	1960	1994	305,006	25.13	Yes	95	5	2069	2145
22	Watkins Mill	G	1989		301,579	50.99	Yes	86	3	1858	1917
23	Wheaton	G	1954	1983	258,117	28.23		61	4	1336	1356
24	Walt Whitman	S	1962	1992	261,295	30.67	Yes	83	5	1814	1891
25	Thomas S. Wootton	G	1970		295,620	27.37		97	2	2081	2184
	Total High Schools				7,529,375	898.26		2099	109	45,694	47,436
	Total Secondary Schools				12,740,288	1647.3		3803	182	82,634	83,752

Note: State-rated capacity and MCPS capacity may differ due to the method of calculating capacity for special education classes.
For MCPS calculations, please refer to the individual school calculations.
Smart Growth (Sm. Gr.): S = Stabilized; R= Revitalization; G= Growth; N= Non Growth

* Schools with a date before 1986 underwent a renovation, not a full revitalization of the facility. Schools that were reopened but not fully revitalized or completely rebuilt, will be included in the assessments for future revitalization/expansion based on the year the school was originally opened. See Appendix K for more information.

Appendix K

Schools Reopened and Extent of Improvements Made When Reopened

School	Year Facility Originally Opened	Year Facility Closed	Year Facility Improvement	Year Fully Revitalized/Expanded* or Completely Rebuilt
Elementary Schools				
Arcola (on site of former Arcola ES)	1956	1982		2007
Burnt Mills	1964	1977	1990	
Cloverly	1961	1983	1989	
Roscoe Nix (on site of former Brookview ES)	1955	1982		2006
Sargent Shriver (former Connecticut Park ES)	1954	1983		2006
Sligo Creek (part of former Blair HS)	1935	1998		1999
Middle Schools				
Argyle	1971	1981	1993	
Cabin John	1968	1987	1989	2011
Francis Scott Key	1966	1983	1990	2009
A. Mario Loiederman (former Belt JHS)	1956	1983	2005	
Newport Mill	1958	1982	2002	
North Bethesda	1955	1981	1999	
Silver Spring International (part of former Blair HS)	1935	1998	1999	
Tilden (Tilden MS relocated to former Woodward HS)	1967	1986	1991	2019 scheduled @ Tilden Lane
High Schools				
Clarksburg (originally opened as Rocky Hill MS)	1995	2004		2006 expanded to HS
Northwood	1956	1985	2004	


Notes: Revitalization/Expansion projects were formerly known as Modernizations. Schools that were reopened, but were not fully revitalized/expanded were included in the FY 2011 FACT assessment of schools. Northwood HS is the only high school that has not been revitalize/expanded. It is in the queue for high school revitalizations/expansions. See Appendix E and F for a list of schools on the revitalization/expansion schedule.

Appendix L

Former Operating Schools and Current Status

June 2015

NAME	ADDRESS	CLUSTER	CURRENT USE	SITE	ROOMS	SF
BOARD OF EDUCATION OWNED FACILITIES						
Concord School	7210 Hidden Creek Road	Whitman	Central Records	3.45	12	26,444
Emory Grove Center	18100 Washington Grove Lane	Magruder	Holding School	10.17	19	49,858
Fairland Center	13313 Old Columbia Pike	Paint Branch	Holding School	9.21	26	45,082
Grosvenor Center	5701 Grosvenor Lane	W. Johnson	Holding School	10.21	18	36,770
Lynnbrook Center	8001 Lynnbrook Drive	B-CC	MCPS program offices	4.21	15	35,000
Montrose ES	12301 Academy Way	W. Johnson	Leased to two private schools	7.50	16	34,243
North Lake Center	15101 Bauer Drive	Rockville	Holding School	9.66	22	40,378
Radnor Center	7000 Radnor Road	Whitman	Holding School	9.03	20	36,663
Rocking Horse Road ES	4910 Macon Road	Wheaton	ESOL; Head Start; Title 1; International Student Admiss.	18.70	28	57,639
Rollingwood ES	3200 Woodbine Street	B-CC	Leased to private school	4.07	12	26,624
Spring Mill Center	11721 Kemp Mill Road	Kennedy	Consortia offices; Special Education offices	7.69	14	29,300
Taylor ES	19501 White Ground Road	Poolesville	Science Materials Center	11.47	8	20,827
Tilden Center	6300 Tilden Lane	W. Johnson	Holding School	19.70	39	119,516
Tuckerman ES	8224 Lochinver Lane	Churchill	Leased to private school	9.13	24	47,965
MONTGOMERY COUNTY OWNED FACILITIES						
Alta Vista ES	5615 Beech Avenue	W. Johnson	Leased to private school	3.53	12	15,000
Aspen Hill ES	4915 Aspen Hill Road	Rockville	Leased to private school	6.00	24	50,000
Ayrlawn ES	5650 Oakmont Avenue	W. Johnson	Leased to YMCA	3.08	11	28,000
Clara Barton ES	7425 MacArthur Boulevard	Whitman	Child Care; County Recreation	4.00	12	26,084
Brookmont ES	4800 Sangamore Road	Whitman	Leased to private school	5.65	22	36,000
Broome JHS	751 Twinbrook Parkway	Rockville	Various county users	19.49	45	135,210
Bushey Drive ES	12210 Bushey Drive	Wheaton	County Recreation Office	6.07	NA	32,675
Colesville ES	14015 New Hampshire Avenue	Springbrook	Community services	11.11	14	25,174
Congressional ES	1801 E. Jefferson Street	W. Johnson	Elderly services	9.91	12	26,206
Dennis Avenue ES	2000 Dennis Avenue	Einstein	MC Health Services	6.97	12	26,790
English Manor ES	4511 Bestor Drive	Rockville	Leased to private school	8.25	28	50,000
Fernwood ES	6801 Greentree Road	Whitman	Leased to private school	6.15	18	32,000
Forest Grove ES	9805 Dameron Drive	Einstein	Leased to Holy Cross Hospital	6.17	24	38,000
Four Corners ES	325 W. University Boulevard	Blair	Elderly services	5.66	9	18,600
Georgetown Hill ES	11614 Seven Locks Road	Churchill	Leased to private school	10.35	28	50,000
Hillandale ES	10501 New Hampshire Avenue	Springbrook	Handicapped services	6.81	17	36,000
Holiday Park ES	3930 Ferrara Drive	Wheaton	Elderly services	5.62	25	48,595
Hungerford Park ES	322 W. Edmonston Drive	Richard Montgomery	Family Resources; child servies	11.06	26	34,511
Kensington ES	10400 Detrick Avenue	W. Johnson	HOC Offices	4.54	19	45,206
Lake Normandy ES	11315 Falls Road	Churchill	Recreation Center	10.59	22	40,203
Lone Oak ES	1010 Grandin Avenue	Rockville	CHI Centers, Inc./Elderly day care	7.09	28	40,000
Macdonald Knolls ES	10611 Tenbrook Drive	Einstein	Handicapped services; child care	8.06	15	28,000
Montgomery Hills JHS	2010 Linden Lane	Einstein	Leased to private school	8.67	44	130,000
Parkside ES	9500 Brunett Avenue	Blair	M-NCCPC Parks Offices	11.61	NA	26,369
Pleasant View ES	3015 Upton Drive	Einstein	Single-parent housing; charter school	6.22	0	NA
Randolph JHS	11710 Hunters Lane	Wheaton	Leased to private school	8.07	40	110,000
Saddlebrook ES	12751 Layhill Road	Kennedy	Park Police Headquarters	10.59	29	42,274
Sandy Spring ES	13025 Brooke Road	Sherwood	Community Center	8.39	NA	NA
Woodside ES	8818 Georgia Avenue	Einstein	Silver Spring Health Center	2.70	23	36,614
MARYLAND-NATIONAL CAPITAL PARK AND PLANNING COMMISSION OWNED FACILITIES						
Concord School	7210 Hidden Creek Road	Whitman	Recreation fields	5.40	NA	NA
Kensington JHS	3701 Saul Road	B-CC	Bldg. razed; local park	8.21	NA	NA
Leland JHS	4300 Elm Street	B-CC	Bldg. razed; Community Center, park	3.71	NA	NA
Lynnbrook Center	8001 Lynnbrook Drive	B-CC	Park	5.83	NA	NA
CITY OF ROCKVILLE OWNED FACILITIES						
Woodley Gardens ES	1150 Carnation Drive	Richard Montgomery	Senior Center	9.64	16	31,767

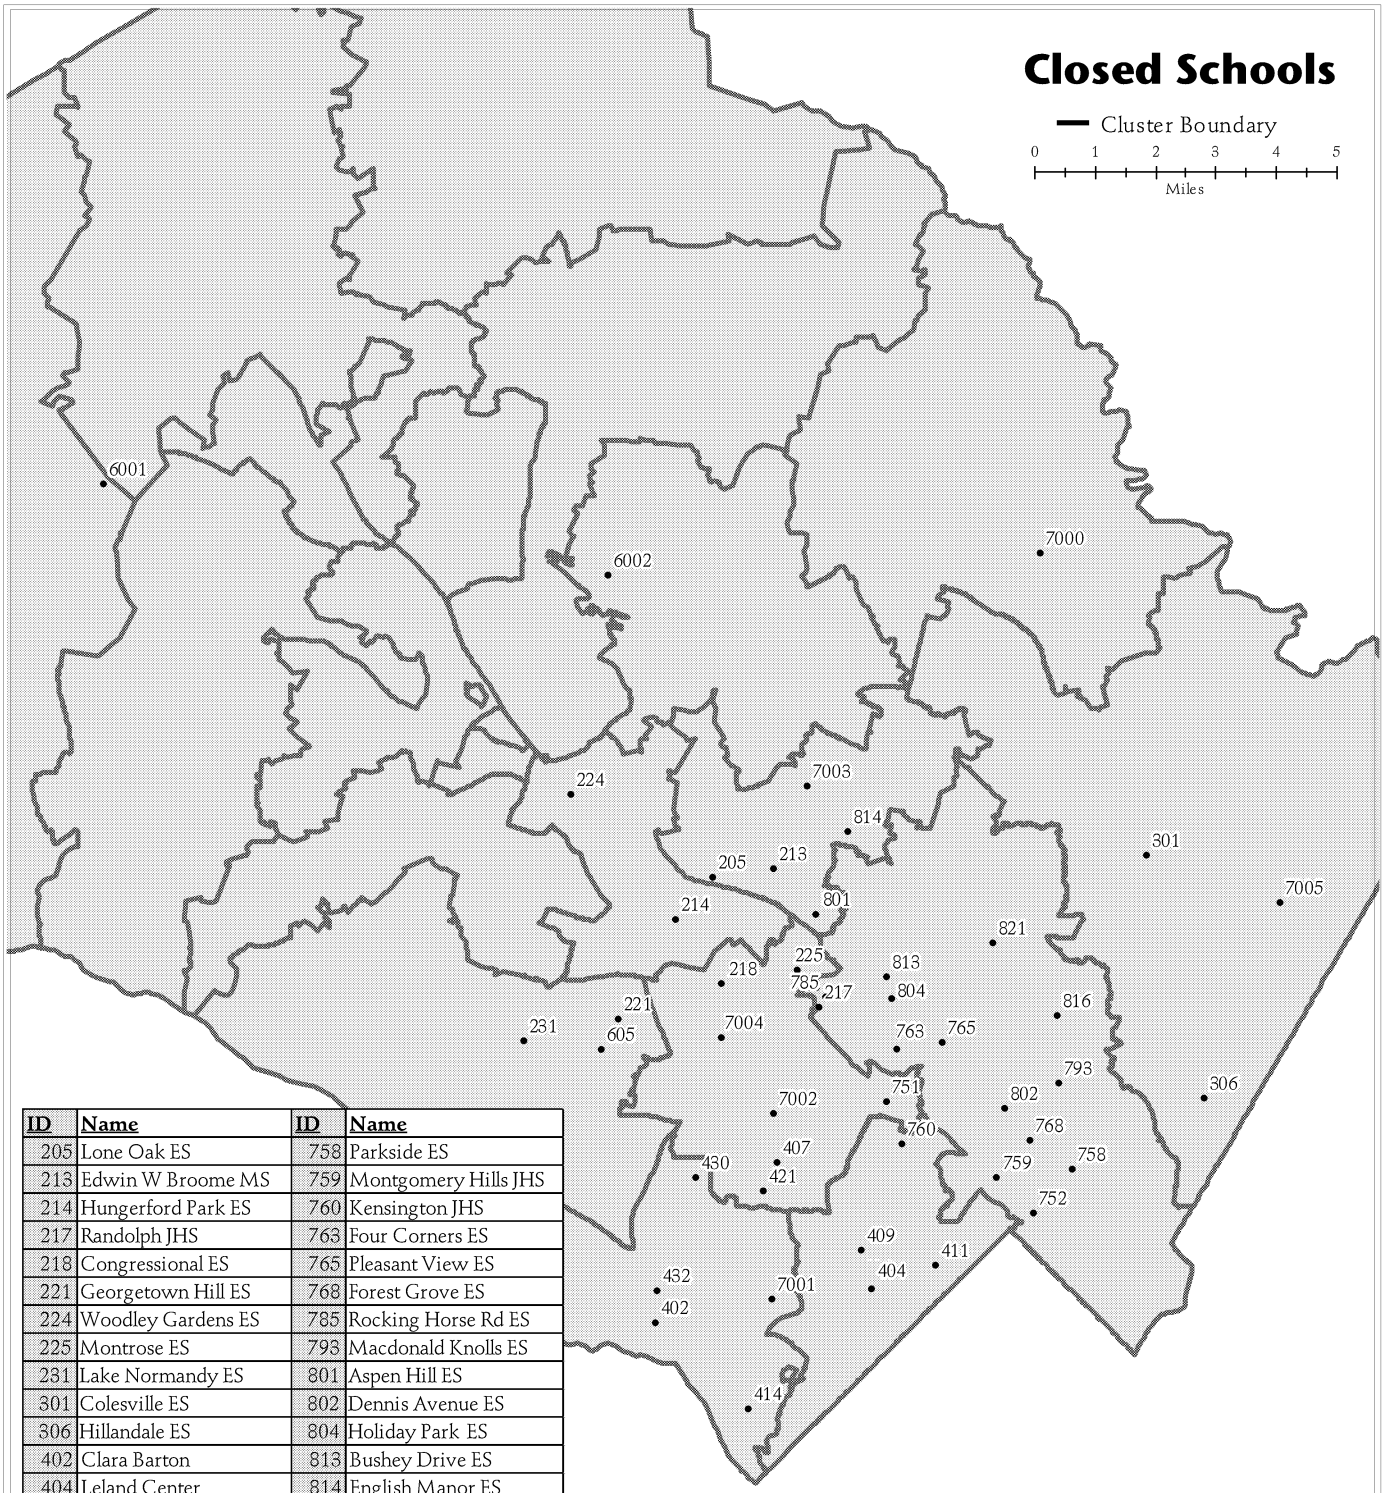

ID	Name	ID	Name
205	Lone Oak ES	758	Parkside ES
213	Edwin W Broome MS	759	Montgomery Hills JHS
214	Hungerford Park ES	760	Kensington JHS
217	Randolph JHS	763	Four Corners ES
218	Congressional ES	765	Pleasant View ES
221	Georgetown Hill ES	768	Forest Grove ES
224	Woodley Gardens ES	785	Rocking Horse Rd ES
225	Montrose ES	793	Macdonald Knolls ES
231	Lake Normandy ES	801	Aspen Hill ES
301	Colesville ES	802	Dennis Avenue ES
306	Hillandale ES	804	Holiday Park ES
402	Clara Barton	813	Bushey Drive ES
404	Leland Center	814	English Manor ES
407	Alta Vista ES	816	Spring Mill Center
409	Lynnbrook Center	821	Saddlebrook ES
411	Rollingwood ES	6001	Taylor ES
414	Brookmont ES	7000	Sandy Spring ES
421	Ayrlawn ES	7001	Radnor Center
430	Fernwood ES	7002	Grosvenor Center
432	Concord School	7003	North Lake Center
605	Tuckerman ES	7004	Tilden Center
751	Kensington ES	7005	Fairland Center
752	Woodside ES	7006	Emory Grove Center

Montgomery County Public Schools - Division of Long-range Planning - June 2015

Reopened Closed Schools*

June 2015

Name	School Year Reopened	Address	Cluster	Acreage
Cloverly ES	1989–90	800 Briggs Chaney Road, Silver Spring	Northeast Consortium	10.0
Cabin John MS	1989–90	10701 Gainsborough Road, Potomac	Churchill	18.2
Burnt Mills ES	1990–91	11211 Childs Street, Silver Spring	Northeast Consortium	15.1
Francis Scott Key MS	1990–91	910 Schindler Drive, Silver Spring	Northeast Consortium	20.6
Argyle MS	1993–94	2400 Bel Pre Road, Silver Spring	Downcounty Consortium	19.9
Sligo Creek ES	1999–00	500 Schuyler Road, Silver Spring	Downcounty Consortium	15.6
North Bethesda MS	1999–00	8935 Bradmoor Drive, Bethesda	Walter Johnson	20.0
Silver Spring International MS	1999–00	313 Wayne Avenue, Silver Spring	Downcounty Consortium	10.6
Newport Mill MS	2002–03	11311 Newport Mill Road, Silver Spring	Downcounty Consortium	8.4
Northwood HS	2004–05	919 University Boulevard, Silver Spring	Downcounty Consortium	29.6
A. Mario Loiederman MS	2005–06	12701 Goodhill Road, Silver Spring	Downcounty Consortium	17.1
Roscoe R. Nix ES	2006–07	1100 Corliss Street, Silver Spring	Northeast Consortium	9.0
Sargent Shriver ES	2006–07	12518 Greenly Drive, Silver Spring	Downcounty Consortium	9.2
Arcola ES	2007–08	1820 Franwall Avenue, Silver Spring	Downcounty Consortium	5.0
Flora M. Singer ES	2012–13	2600 Hayden Drive, Silver Spring	Downcounty Consortium	12.7

* Schools listed include schools repurposed for use by another school, reopened, or built new on the site of a former school. In some cases the school was renamed.


Future School Sites

June 2015


Name	Tax Grid	Address	Cluster	Acreage
Board of Education Owned Sites				
Brickyard MS	FN33	Brickyard Road	Churchill	20.00
Clarksburg/Damascus MS	FW21	Route 27 & Skylark Road	Damascus	22.00
Hawkins Creamery Road ES	FX51	Hawkins Creamery Road	Damascus	13.51
Kendale ES	GP12	Kendale Road	Churchill	10.54
Kings Bridge MS	FW32	Founders Way	Damascus	30.33
Laytonsville MS	GU33	Warfield Road	Gaithersburg	22.74
Northwest ES #8	ET23	Schaeffer Road	Northwest	12.70
Northwest Branch ES	JS12	Layhill Road	Northeast Consortium	11.41
Oak Drive ES	FX31	Oak Drive	Damascus	12.99
Oakdale MS	HT31	Cashell Road	Magruder	18.49
Sherwood ES #6	HT23	Wickham Road	Sherwood	17.00
Waring Station ES	EU61	Waring Station Road	Seneca Valley	9.99
Woodwards Road ES	FT63	Emory Grove Road	Magruder	11.05
Wootton ES # 7	FR32	Cavanaugh Drive	Wootton	12.10
Master Planned School Sites Titled to Others as Shown in County Master Plan				
Cabin Branch ES	EV23	Clarksburg Road	Clarksburg	TBD
Central Area HS (Crown Farm)	FS-52	Fields Road	Gaithersburg	32.1
Clarksburg Village ES #2	EV63	Newcut Road	Clarksburg	9.76
Fallsgrove ES	FR53	Fallsgrove Road	Richard Montgomery	TBD
Great Seneca Science Corridor ES	FR43	Great Seneca Hwy. and Key West Ave.	Wootton	TBD
Jeremiah Park ES	GS23	SE Shady Grove Road and Crabbs Branch Way	Gaithersburg	TBD
King Farm ES	GS11	Watkins Pond Road	Richard Montgomery	TBD
King Farm MS	GS12	Piccard Drive	Gaithersburg	TBD
Northeast Consotrium ES #17	LS21	Saddle Creek Drive	Northeast Consortium	TBD
West Old Baltimore Road ES	EV42	West Old Baltimore Road	Clarksburg	9.30
White Flint ES	HQ11	South side of current White Flint Mall property	Walter Johnson	TBD


Future School Sites
Titled to BOE
Titled to Others in County Master Plan
Cluster Boundary
0
1.5
3
6
Miles
Oak Drive ES
Hawkins Creamery Road MS
Kings Bridge MS
Clarksburg Damascus MS
Clarksburg Village ES #2
Cabin Branch ES
West Old Baltimore Rd ES
Laytonsville MS
Waring Station ES
Northwest ES #8
Woodwards Road ES
Sherwood ES #6
Oakdale MS
Jeremiah Park ES
King Farm MS
Central Area HS
King Farm ES
Northwest Branch ES
Great Seneca Science Corridor ES
Fallsgrove ES
Northeast Consortium ES #17
Wootton ES #7
White Flint ES
Kendale ES
Brickyard MS
MCPS
Long-range Planning
Montgomery County Public Schools - Division of Long-range Planning - June 2015

Appendix M

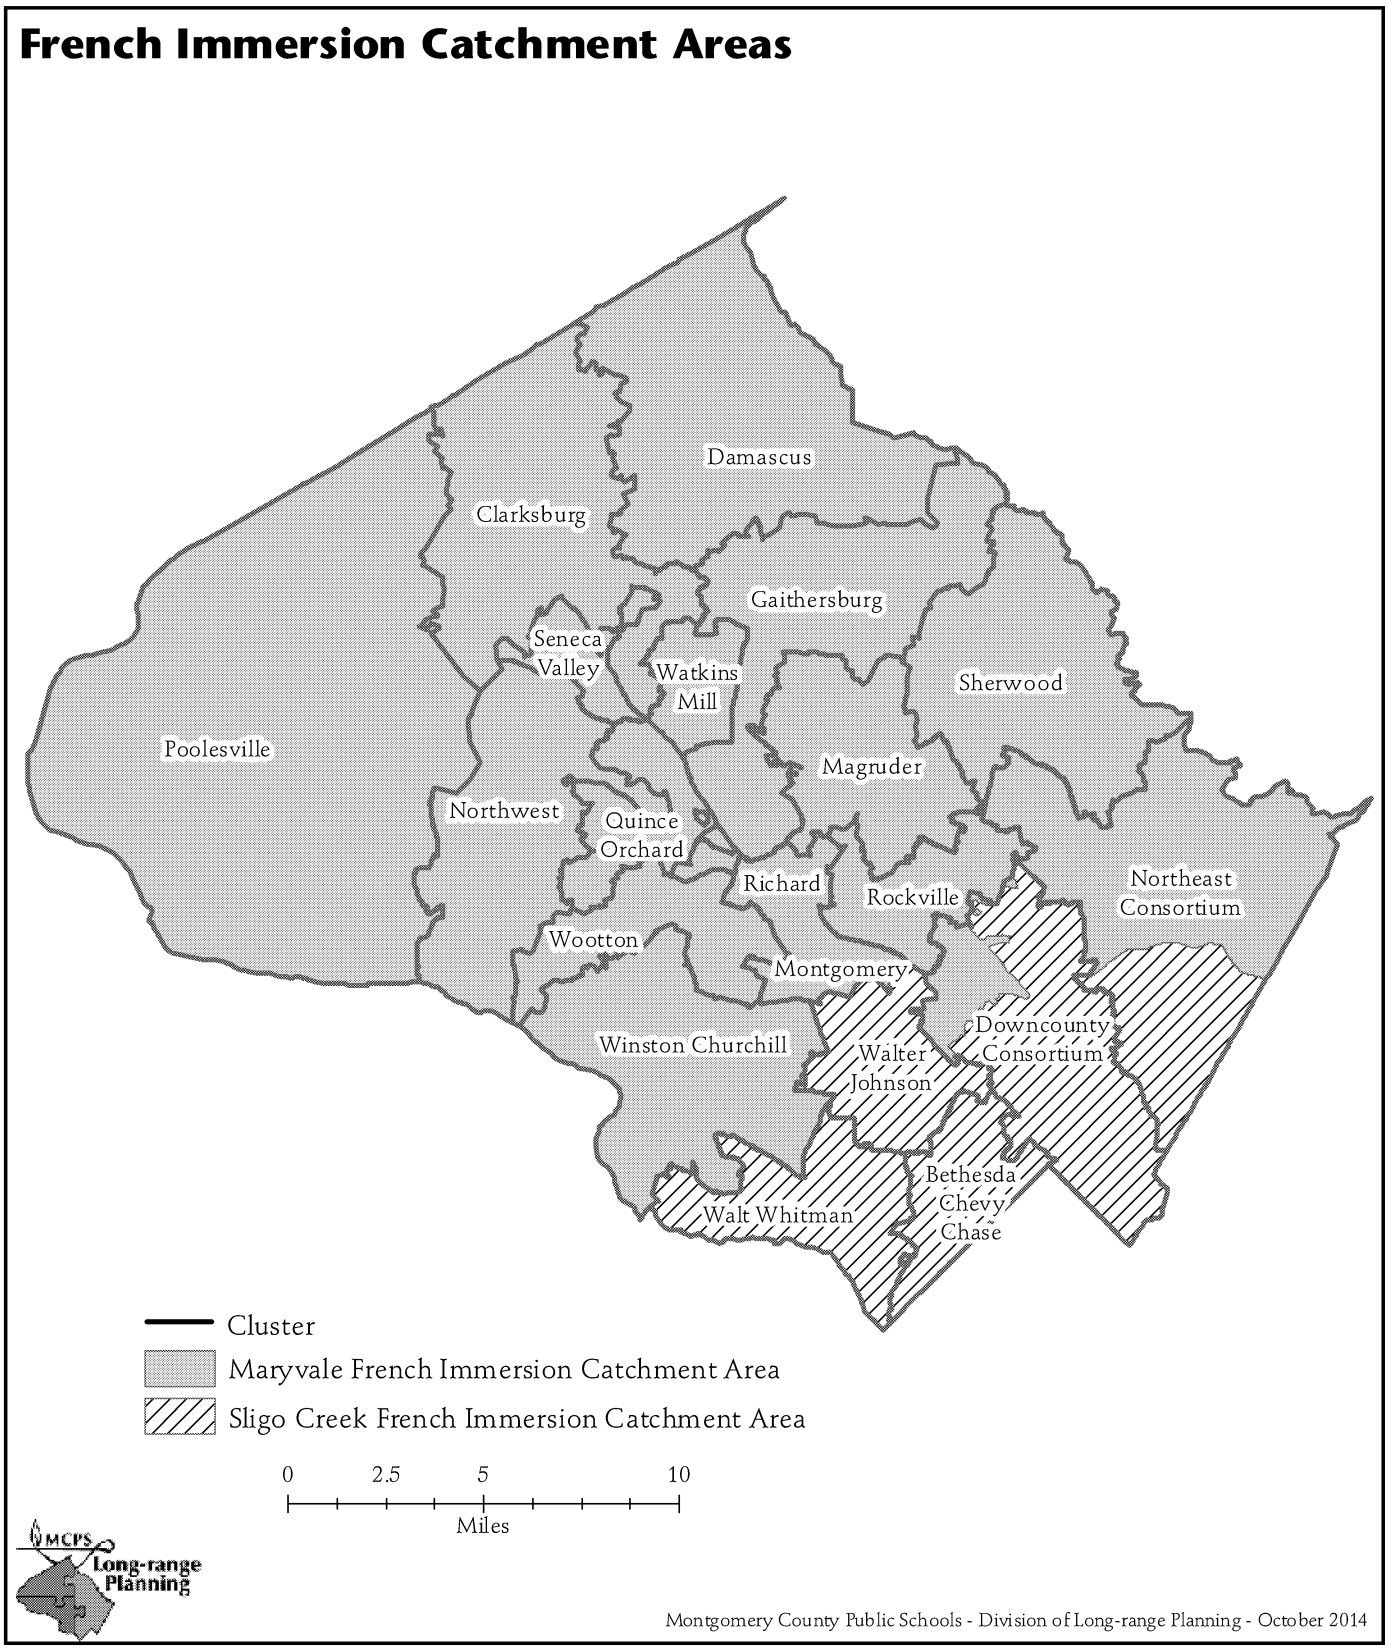

French Immersion Catchment Areas
Damascus
Clarksburg
Gaithersburg
Seneca Valley
Watkins Mill
Sherwood
Poolesville
Magruder
Northwest
Quince Orchard
Richard
Rockville
Northeast Consortium
Wootton
Montgomery
Downcounty Consortium
Winston Churchill
Walter Johnson
Bethesda Chevy Chase
Walt Whitman
Cluster
Maryvale French Immersion Catchment Area
Sligo Creek French Immersion Catchment Area
0
2.5
5
10
Miles
MCPS
Long-range Planning
Montgomery County Public Schools - Division of Long-range Planning - October 2014

Highly Gifted Catchment Areas

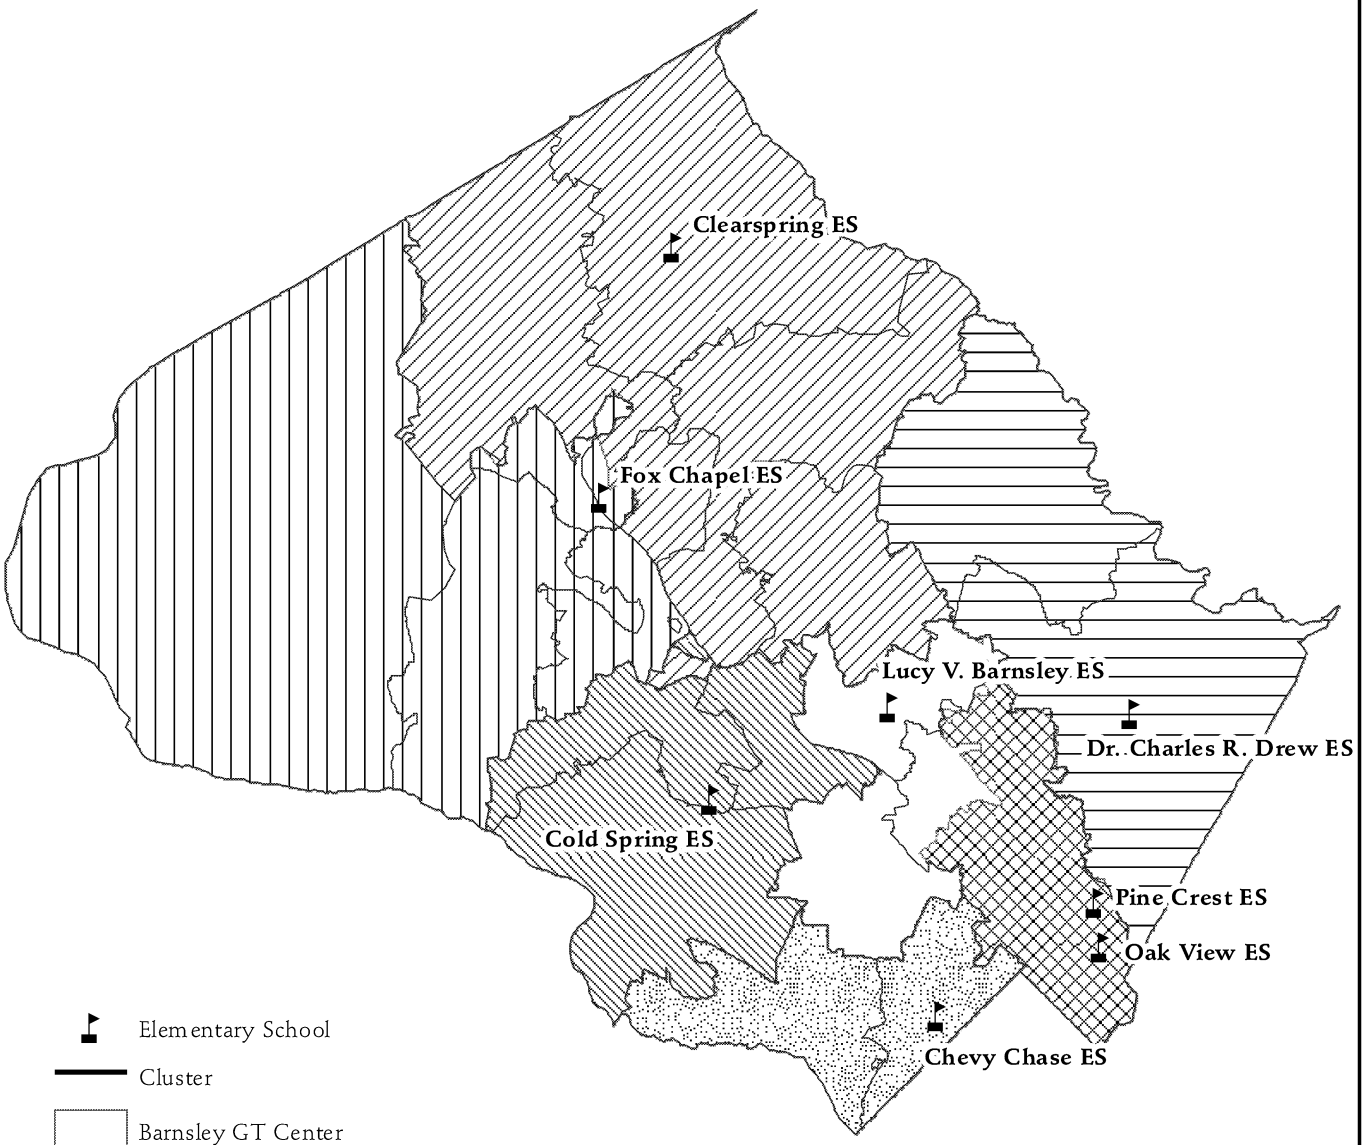

Montgomery County Public Schools - Division of Long-range Planning - October 2014

Secondary Magnet School Catchment Areas

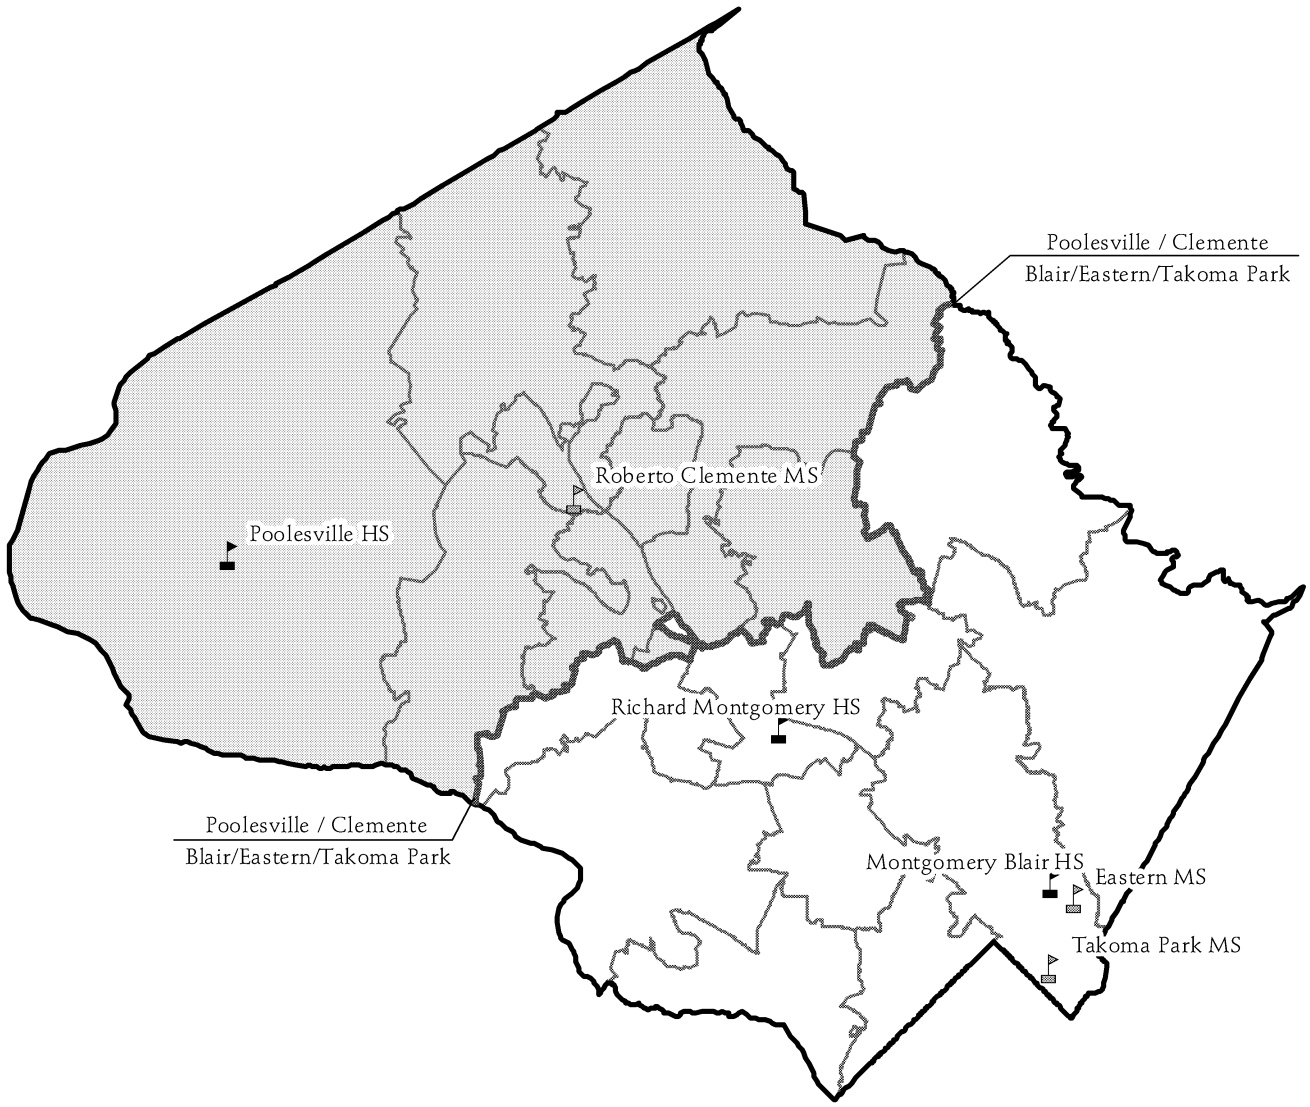

Middle School

High School

Secondary Magnet School Catchment Boundary

0 2.5 5 10 Miles

MCPS Long-range Planning

Montgomery County Public Schools - Division of Long-range Planning - October 2014

Appendix N

School/Program Sites and Political Districts

School	Board of Education District	Councilmanic District	Legislative District
Elementary Schools			
Arcola	4	4	18
Ashburton	3	1	16
Bannockburn	3	1	16
Lucy V. Barnsley	5	3	19
Beall	2	3	17
Bel Pre	4	4	19
Bells Mill	3	1	15
Belmont	5	4	14
Bethesda	3	1	16
Beverly Farms	3	1	15
Bradley Hills	3	1	16
Brooke Grove	5	4	14
Brookhaven	4	3	19
Brown Station	2	3	17
Burning Tree	3	1	16
Burnt Mills	5	5	20
Burtonsville	5	5	14
Candlewood	5	3	19
Cannon Road	5	5	20
Carderock Springs	3	1	16
Rachel Carson	2	3	17
Cashell	5	4	14
Cedar Grove	1	2	14
Chevy Chase	3	1	18
Clarksburg	1	2	15
Clearspring	1	2	14
Clopper Mill	2	2	39
Cloverly	5	5	14
Cold Spring	2	3	15
College Gardens	2	3	17
Cresthaven	5	5	20
Captain James Daly	1	2	39
Damascus	1	2	14
Darnestown	2	1	15
Diamond	2	3	17
Dr. Charles R. Drew	5	5	14
DuFief	2	2	15
East Silver Spring	4	5	20
Fairland	5	5	14
Fallsmead	2	3	17
Farmland	3	1	16
Fields Road	2	3	17
Flower Hill	1	4	39
Flower Valley	5	3	19
Forest Knolls	4	5	19
Fox Chapel	1	2	39
Gaithersburg	1	3	17
Galway	5	5	14
Garrett Park	3	1	18
Georgian Forest	4	4	19
Germantown	2	2	15
William B. Gibbs Jr.	1	2	39
Glen Haven	4	4	18
Glenallan	4	4	19
Goshen	1	2	14
Great Seneca Creek	2	2	39
Greencastle	5	5	14
Greenwood	5	4	14
Harmony Hills	4	4	19
Highland	4	4	18
Highland View	4	5	20
Jackson Road	5	5	20
Jones Lane	2	2	15
Kemp Mill	4	4	19
Kensington-Parkwood	3	1	18
Lake Seneca	1	2	15
Lakewood	2	3	17

School	Board of Education District	Councilmanic District	Legislative District
Elementary Schools			
Laytonsville	1	4	14
JoAnn Leleck at Broad Acres	5	5	20
Little Bennett	1	2	15
Luxmanor	3	1	16
Thurgood Marshall	2	3	39
Maryvale	5	3	17
Spark M. Matsunaga	2	2	39
S. Christa McAuliffe	1	2	39
Ronald McNair	2	2	15
Meadow Hall	5	3	17
Mill Creek Towne	1	4	19
Monocacy	1	2	15
Montgomery Knolls	4	5	20
New Hampshire Estates	4	5	20
Roscoe R. Nix	5	5	20
North Chevy Chase	3	1	18
Oak View	4	5	20
Oakland Terrace	4	5	18
Olney	5	4	14
William T. Page	5	5	14
Pine Crest	4	5	20
Piney Branch	4	5	20
Poolesville	1	1	15
Potomac	3	1	15
Judith A. Resnik	1	4	39
Dr. Sally K. Ride	1	2	39
Ritchie Park	2	3	17
Rock Creek Forest	3	1	18
Rock Creek Valley	5	3	19
Rock View	4	4	18
Lois P. Rockwell	1	2	14
Rolling Terrace	4	5	20
Rosemary Hills	3	5	18
Rosemont	2	3	17
Sequoyah	5	4	19
Seven Locks	3	1	16
Sherwood	5	4	14
Sargent Shriver	4	4	18
Flora M. Singer	4	5	18
Sligo Creek	4	5	20
Somerset	3	1	16
South Lake	1	2	39
Stedwick	1	2	39
Stone Mill	2	3	15
Stonegate	5	4	14
Strathmore	4	4	19
Strawberry Knoll	1	2	39
Summit Hall	2	3	17
Takoma Park	4	5	20
Travilah	2	2	15
Twinbrook	2	3	17
Viers Mill	4	4	18
Washington Grove	2	3	19
Waters Landing	1	2	15
Watkins Mill	1	2	39
Wayside	3	1	15
Weller Road	4	4	19
Westbrook	3	1	16
Westover	5	4	14
Wheaton Woods	4	4	19
Whetstone	1	2	39
Wilson Wims	1	2	15
Wood Acres	3	1	16
Woodfield	1	2	14
Woodlin	4	5	18
Wyngate	3	1	16

School	Board of Education District	Councilmanic District	Legislative District
Middle Schools			
Argyle	4	4	19
John T Baker	1	2	14
Benjamin Banneker	5	5	14
Briggs Chaney	5	5	14
Cabin John	3	1	15
Clarksburg/Damascus MS	1	2	39
Roberto Clemente	1	2	39
Eastern	4	5	20
William H. Farquhar	5	4	14
Forest Oak	1	3	17
Robert Frost	2	3	17
Gaithersburg	1	3	17
Herbert Hoover	3	1	15
Francis Scott Key	5	5	20
Martin Luther King, Jr	1	2	15
Kingsview	2	2	15
Lakelands Park	2	3	17
Col. E. Brooke Lee	4	4	19
A. Mario Loiederman	4	4	19
Montgomery Village	1	2	39
Neelsville	1	2	39
Newport Mill	4	4	18
North Bethesda	3	1	16
Parkland	4	3	19
Rosa Parks	5	4	14
John Poole	1	1	15
Thomas W. Pyle	3	1	16
Redland	5	4	19
Ridgeview	2	3	39
Rocky Hill	1	2	15
Shady Grove	2	3	19
Silver Spring International	4	5	20
Sligo	4	4	18
Takoma Park	4	5	20
Tilden	3	1	16
Julius West	2	3	17
Westland	3	1	16
White Oak	5	5	20
Earle B. Wood	5	3	19

School	Board of Education District	Councilmanic District	Legislative District
High Schools			
Bethesda-Chevy Chase	3	1	18
Montgomery Blair	4	5	20
James Blake	5	4	14
Winston Churchill	3	1	15
Clarksburg	1	2	15
Damascus	1	2	14
Albert Einstein	4	4	18
Gaithersburg	2	3	17
Walter Johnson	3	1	16
John F. Kennedy	4	4	19
Col. Zadok Magruder	5	4	19
Richard Montgomery	2	3	17
Northwest	2	2	39
Northwood	4	5	19
Paint Branch	5	5	14
Poolesville	1	1	15
Quince Orchard	2	2	15
Rockville	5	3	17
Seneca Valley	1	2	39
Sherwood	5	4	14
Springbrook	5	4	20
Watkins Mill	1	2	39
Wheaton	4	4	18
Walt Whitman	3	1	16
Thomas S. Wootton	2	3	17
Special Education Centers			
Carl Sandburg Learning Center	5	3	17
Longview School	2	2	39
RICA	2	3	15
Rock Terrace School	2	3	17
Stephen Knolls School	4	4	18
Other Educational Facilities			
Blair G. Ewing Center	5	3	17
Lathrop E. Smith Center	5	3	19
Thomas Edison HS of Tech.	4	4	18

Political Districts

Board of Education

District	Name
1	Judith Docca
2	Rebecca Smondrowski
3	Patricia O'Neill
4	Christopher S. Barclay
5	Michael A. Durso
At-large	Philip Kauffman
At-large	Jill Ortman-Fouse
Student	Dahlia Hue

County Council

District	Name
1	Roger Berliner
2	Craig Rice
3	Sidney Katz
4	Nancy Navarro
5	Tom Hucker
At-large	Marc Elrich
At-large	Nancy Floreen
At-large	George Leventhal
At-large	Hans Riemer

General Assembly

Legislative District 14	
Senator	Karen S. Montgomery
Delegate	Anne R. Kaiser
Delegate	Eric G. Luedtke
Delegate	Craig J. Zucker

Legislative District 15	
Senator	Brian J. Feldman
Delegate	Kathleen M. Dumais
Delegate	David Fraser-Hidalgo
Delegate	Aruna Miller

Legislative District 16	
Senator	Susan C. Lee
Delegate	C. William Frick
Delegate	Ariana B. Kelly
Delegate	Marc Korman

Legislative District 17	
Senator	Cheryl C. Kagan
Delegate	Kumar P. Barve
Delegate	Jim Gilchrist
Delegate	Andrew Platt


Legislative District 18	
Senator	Richard S. Madaleno, Jr.
Delegate	Alfred C. Carr, Jr.
Delegate	Ana Sol Gutierrez
Delegate	Jeff Waldstreicher

Legislative District 19	
Senator	Roger P. Manno
Delegate	Bonnie L. Cullison
Delegate	Benjamin F. Kramer
Delegate	Marice Morales

Legislative District 20	
Senator	Jamie Raskin
Delegate	Sheila E. Hixson
Delegate	David Moon
Delegate	William C. Smith Jr.

Legislative District 39	
Senator	Nancy J. King
Delegate	Charles Barkley
Delegate	Kirill Reznik
Delegate	Shane Robinson

Board of Education Districts

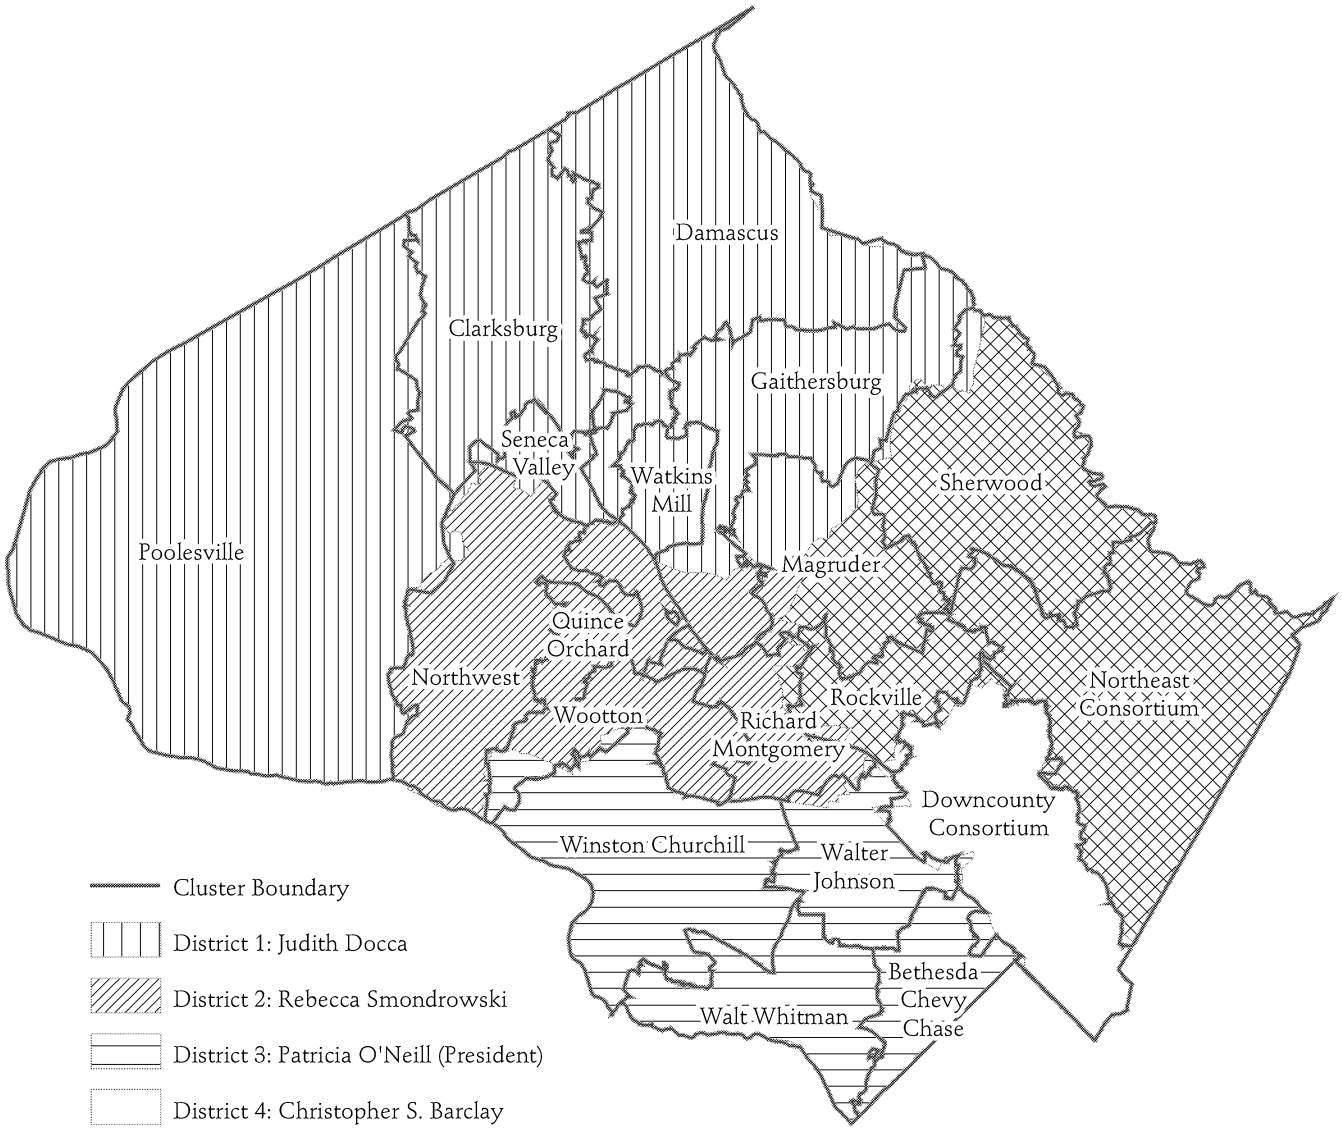

BOE Members at Large:
Jill Ortman-Fouse
Philip Kauffman


BOE Student Member:
Dahlia Huh

0 2.5 5 10 Miles

MCPS Long-range Planning

Montgomery County Public Schools - Division of Long-range Planning - June 2015

Councilmanic Districts

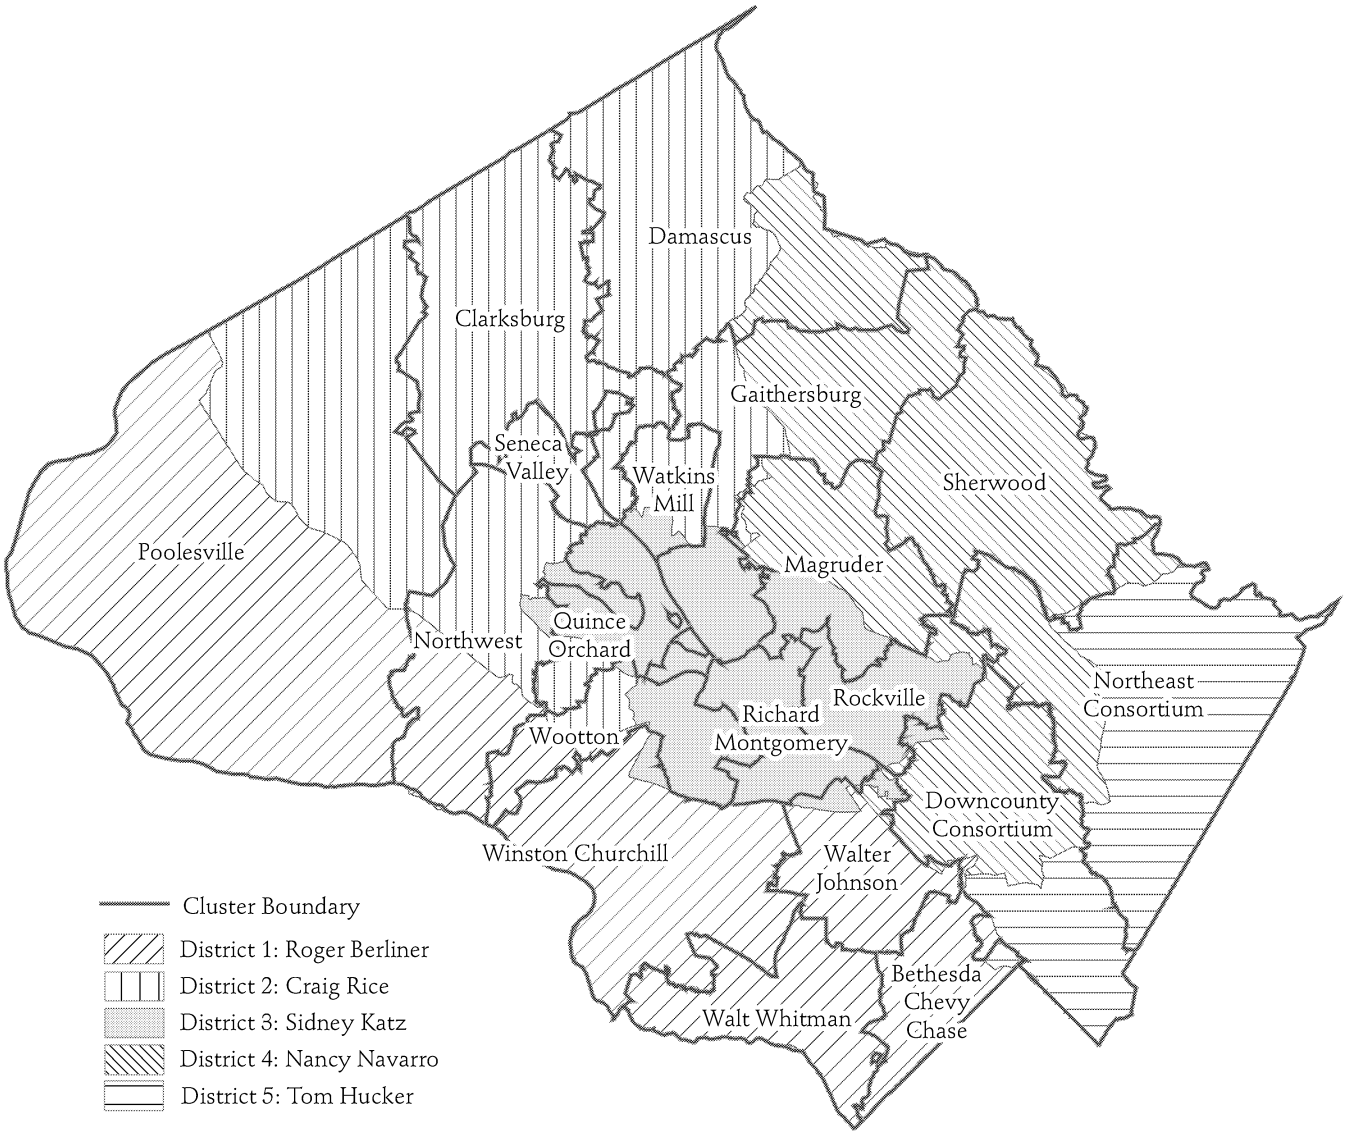


Councilmanic Members at Large:
Marc Elrich
Nancy Floreen (Vice President)
George Leventhal (President)
Hans Riemer

0 2.5 5 10 Miles

MCPS Long-range Planning

Montgomery County Public Schools - Division of Long-range Planning - June 2015

Legislative Districts

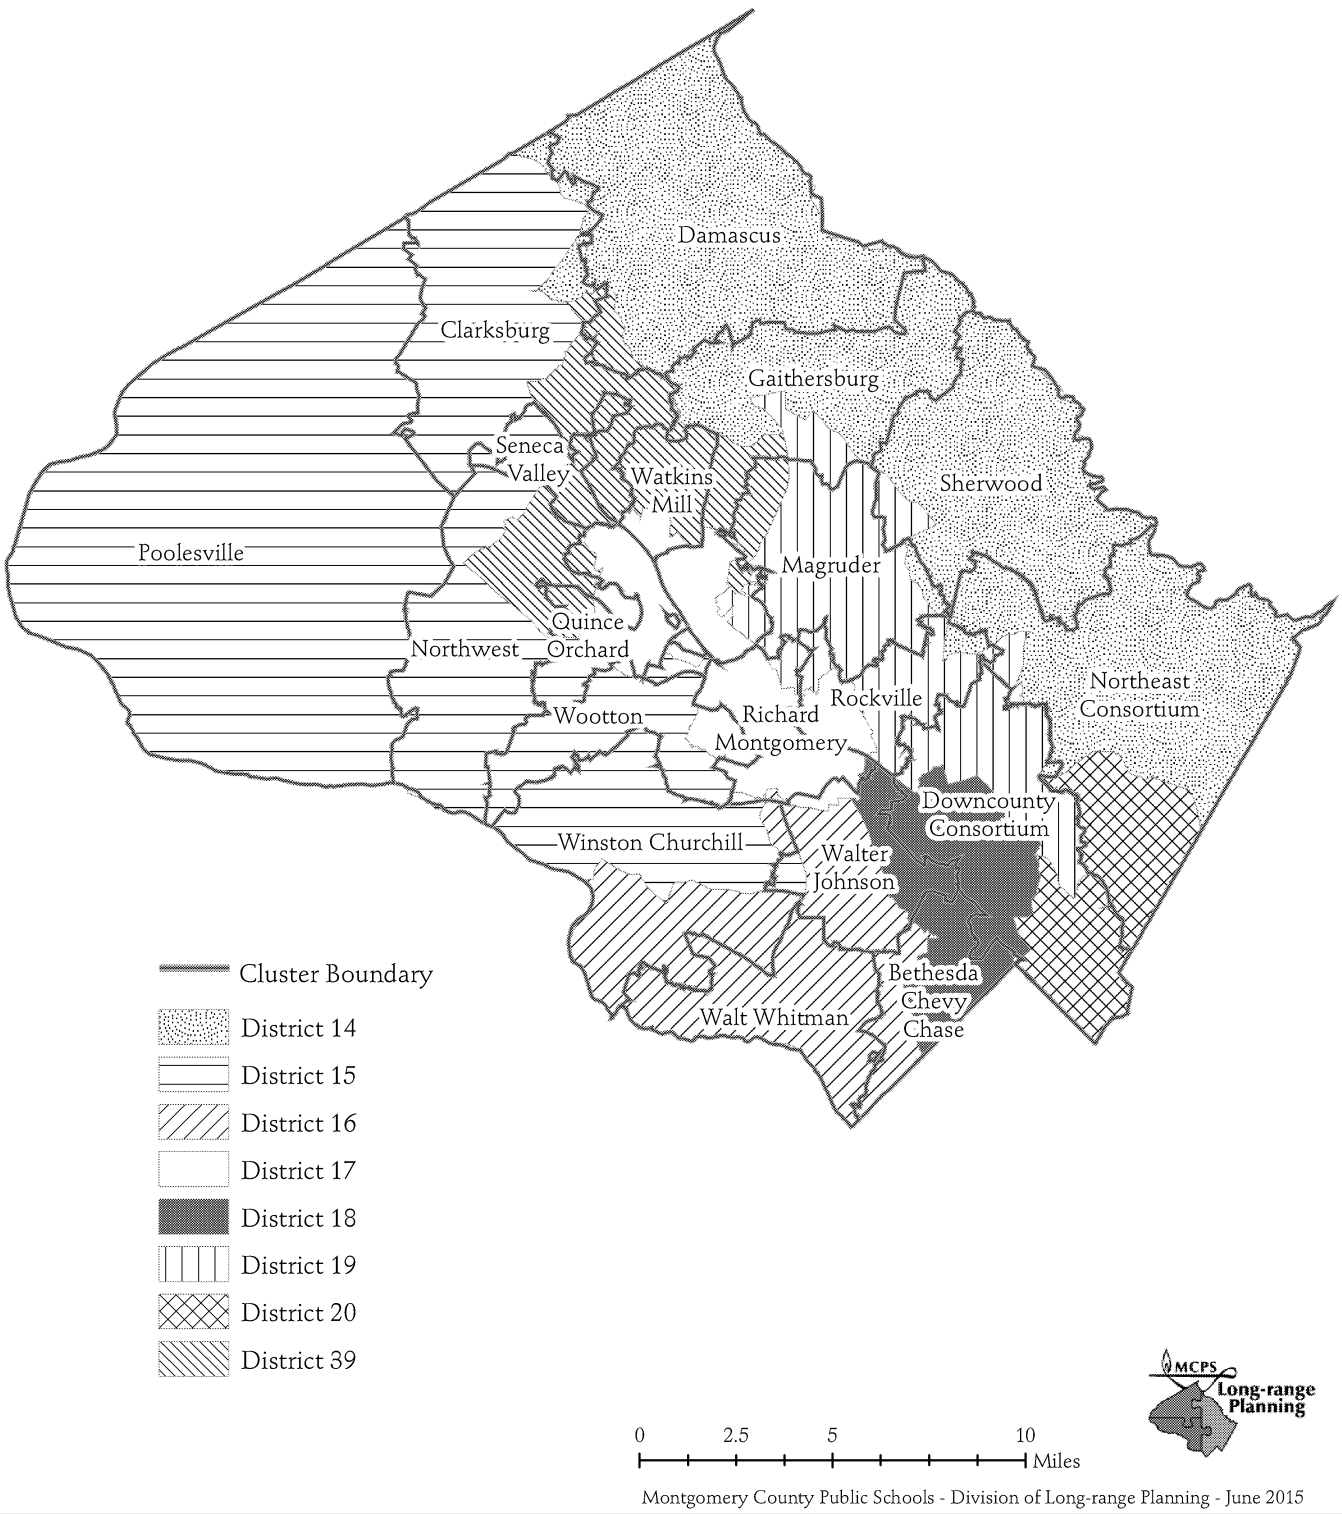


Montgomery County Public Schools - Division of Long-range Planning - June 2015

Appendix O

Priority Funding Areas

Priority Funding Areas are locations where the state and local governments want to target their efforts to encourage and support economic development and new growth. The following areas qualify as Priority Funding Areas: every municipality, as they existed in 1997; areas inside the Washington Beltway; areas already designated as enterprise zones, neighborhood revitalization areas, heritage areas and existing industrial land.

Priority Funding Areas in MCPS
- All MCPS Schools serve students from Priority Funding Areas
- High Schools NOT in a Priority Funding Area: Blake, Magruder, Sherwood
- Middle Schools NOT in a Priority Funding Area: Briggs Chaney, Farquhar, Redland, Rosa Parks
- Elementary Schools NOT in a Priority Funding Area: Burtonsville, Darnestown, Drew, Goshen, Marshall, Monocacy, Potomac, Sequoyah, Sherwood

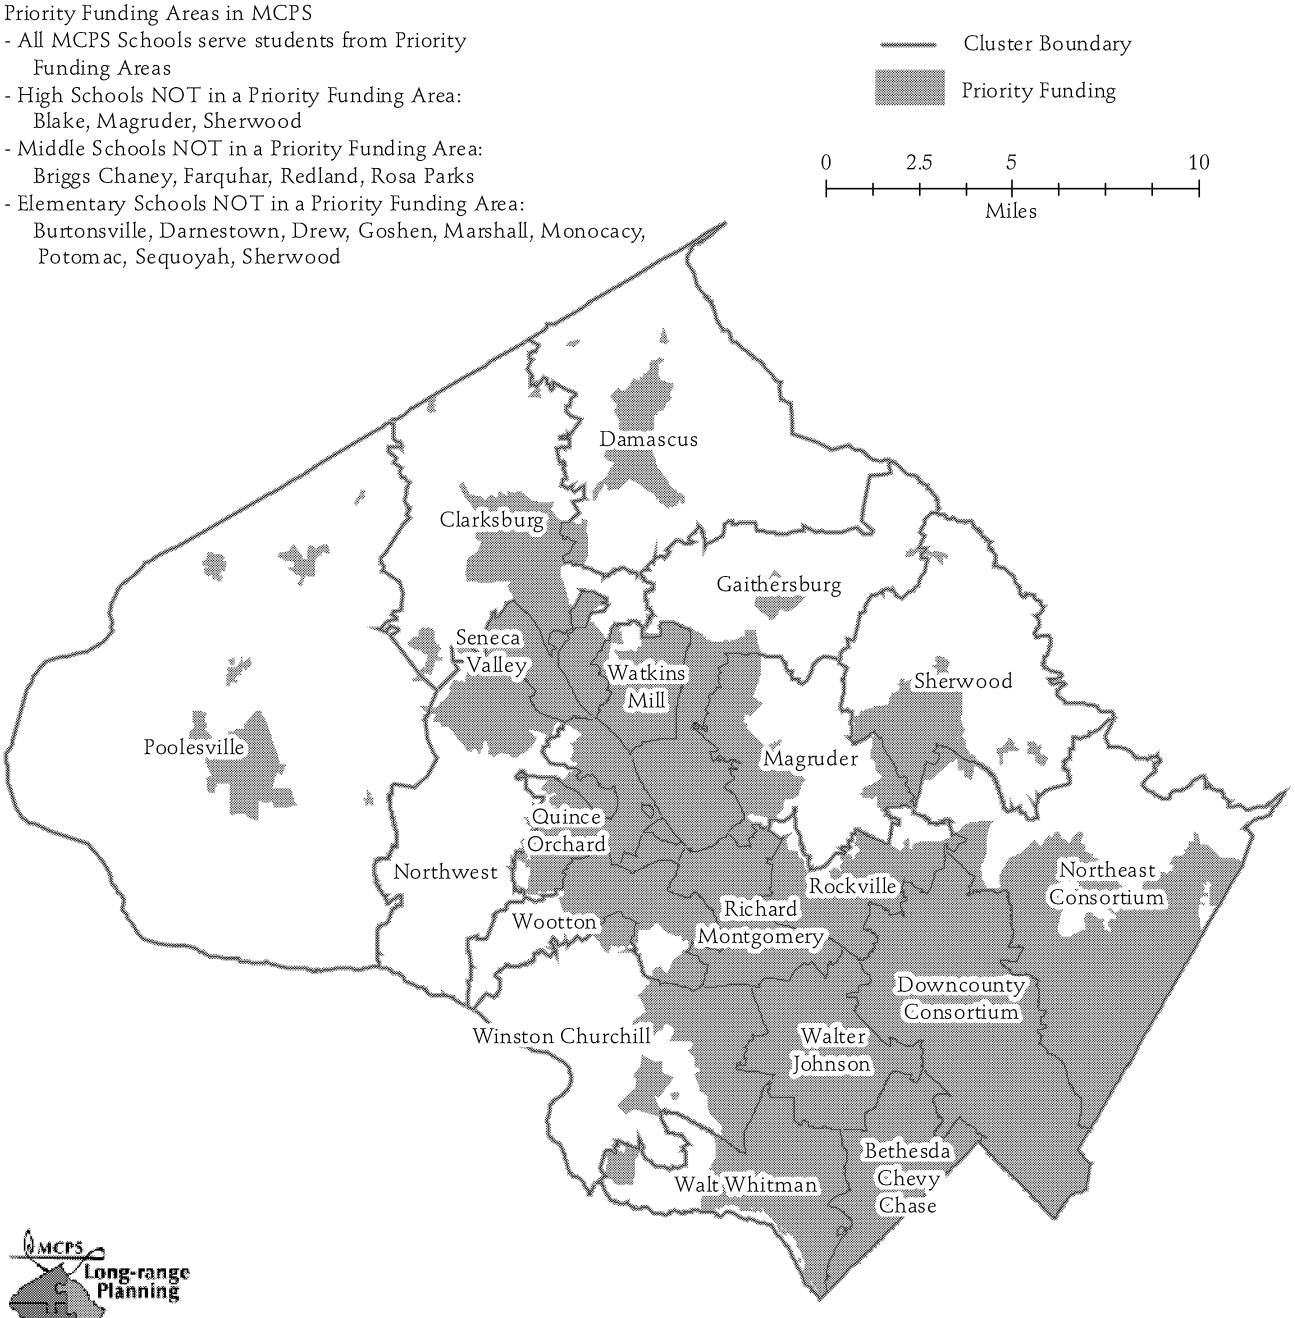

Montgomery County Public Schools - Division of Long-range Planning - October 2014

Appendix P-1

MCPS Role in County Land Use Planning, Zoning, Subdivision Review, and Growth Policy

Montgomery County Public Schools (MCPS) collaborates with the Montgomery County Planning Department (MCPD), the Montgomery County Planning Board (Planning Board), the Montgomery County Hearing Examiner, and the Montgomery County Council (County Council) in a range of planning activities that impact school enrollment and facility needs. These activities are discussed below, from the more general and long-range activities to the more specific and short term activities.

County Land Use Planning

The Planning Board, working with MCPD staff, creates local master plans and sector plans to set forth the land use vision for those areas. The sequence of steps in the development of master plans begins with the MCPD staff development of plan scenarios and collection of community input. At this early stage, and throughout the plan development process, MCPS staff provides MCPD staff with estimates of the number of students that will be generated under various housing scenarios. If housing scenarios generate enough students to require one or more school sites, then these sites are included within the plan area. The MCPD staff recommended plan works its way through Planning Board review and recommendation. Finally, the County Council reviews the Planning Board recommended plan, making any changes it deems appropriate. Ultimately, the County Council takes action to approve the plan.

The identification of school sites is the primary form of input MCPS provides on land use plans. MCPS monitors the implementation of land use plans once they are approved, and works in close coordination with the Montgomery County Planning Department staff and developers to ensure changes in land use are incorporated in facility plans.

Zoning

The implementation of master plans does not occur until the County Council approves a Sectional Map Amendment (SMA). An SMA is a comprehensive action that identifies various zones to be applied to individual tracts of land, as recommended in the master plan. Once the SMA is adopted, property owners have the right to subdivide their properties according to the zoning. On occasion, property owners may request rezoning of their land to allow projects that they believe are consistent with the intent of the master plan. MCPS provides comments on rezoning applications that include housing. These comments include estimates of the number of students that would be generated under the proposed rezoning and the projected utilization levels of schools that serve the property in question. These comments are submitted to MCPD staff during the review of the rezoning, and as requested, to the County Hearing Examiner during review of the rezoning request.

Subdivision

Subdivision plans are submitted by property owners when they are ready to develop their land. Subdivisions are reviewed by MCPD staff and modifications to the plans may be worked out between staff and property owners prior to the plan going to the Planning Board for approval. Once a preliminary plan is complete, a public hearing is held before the Planning Board and action is taken. The Planning Board has the sole authority for review and approval of subdivision applications.

There are numerous considerations that come into play in reviewing a subdivision plan. The Planning Board must determine if a proposed subdivision is consistent with the area master plan and zoning of the property. The Planning Board also must determine if the area of development is "open" to subdivision approval given the results of the Adequate Public Facilities Ordinance (APFO) and County Growth Policy. In regard to the school test of the Growth Policy, one of three conditions may exist when reviewing residential subdivisions:

- First, there may be adequate capacity in the school cluster serving the property. In this case there are no conditions on subdivision approval related to schools.
- Second, schools in the cluster serving the property may be overutilized and require that a school facility payment be collected as a condition of subdivision approval. This payment is collected when building permits are issued for the subdivision. These payments are reserved for school capacity projects in the cluster where they are collected.
- Third, schools serving the property may be so overutilized that residential subdivisions may not be approved until capacity is adequate (through a future capital project or a decline in enrollment).

The thresholds for the second and third conditions are outlined below in the discussion of the County Subdivision Staging Policy. MCPS staff also provides comments on the impact of subdivisions that abut school system property. Once a preliminary plan of subdivision is approved by the Planning Board, an estimate of the number of students the plan will generate is incorporated in enrollment projections for schools that serve

the property. Appendix P-2 describes how enrollment projections are developed.

County Subdivision Staging Policy

Since 1973 the Montgomery County subdivision regulations have included the APFO, with the goal of synchronizing development with the availability of public facilities. (County Code, Section 50-35 (k).) In response to strong growth pressures in the mid-1980s, the County Council enacted legislation to direct the Planning Board's administration of the APFO. This legislation originally was known as the County Growth Policy. More recently the name of the policy was changed to better reflect its purpose. The policy is now called the Subdivision Staging Policy. The APFO and Subdivision Staging Policy have nothing to do with the location, amount, type, or mix of development. These determinations occur in the master planning and zoning processes. The role of the Subdivision Staging Policy is the staging of subdivision approvals commensurate with adequate facility capacity. The two main areas of public facility capacity considered in the policy are schools and transportation facilities.

The County Subdivision Staging Policy, which prescribes the school test of facility adequacy, is reviewed on a four year cycle. The school test of facility adequacy is conducted annually based on the latest enrollment forecast and adopted capital improvements program. The three tiered school test evaluates school utilization levels in the 25 cluster areas at the elementary, middle, and high school levels. If school utilizations exceed certain thresholds, action on subdivision applications are prescribed. Each year, MCPS prepares the data on cluster school utilizations for the school test, and the Planning Board adopts the results of the school test prior to July 1st. The test results are in place for the following fiscal year. The Subdivision Staging Policy school test thresholds are:

- Subdivision applications in clusters with enrollment levels between 105 and 120 percent of MCPS program are required to make a facility payment to obtain approval. This payment is calculated at 60 percent of the marginal cost of the students generated by the subdivision on school construction costs.
- Subdivision applications in clusters with enrollment levels above 120 percent may not be approved until the utilization level falls below 120 percent. The results of the school test for FY 2013 are shown in Appendix I. This test reflects enrollment projections developed in the fall 2011 and approved school capacity projects in the County Council adopted FY 2013 Capital Budget and FY 2013–2018 Capital Improvements Program.
- In the case of clusters that exceed the 120 percent threshold, the County Council may include a "placeholder" capital project in the adopted CIP to avoid moratorium. The placeholder includes funds that will bring the cluster just below the 120 percent threshold. In the following CIP cycle, the Board of Education supersedes the "placeholder" capital project with a request that will bring the utilization of the cluster below 100 percent.

Appendix P-2

MCPS Enrollment Forecasting

The prediction of school enrollment involves the consideration of a wide range of factors. The demographic makeup of communities is the foremost consideration. In addition, characteristics of schools, such as the programs offered and changes within school service areas (such as new housing), can influence enrollment. Economic activity at the local, regional, and national levels also influences the accuracy of enrollment forecasts. Developing a forecast that extends from 1 to 15 years requires assessment of current local events in light of broader, long-term trends. Forecast accuracy varies depending on the projection's geographic scope as well as its time span. Accuracy is greatest when enrollment is projected for large areas for the short-term (one or two years in the future). Accuracy in forecasts diminishes as the geographic area projected becomes smaller and as the forecast is made for more distant points in the future. Therefore, a one-year countywide forecast for total enrollment for all schools will have less error than forecasts that extend further into the future for individual schools.

The MCPS enrollment forecast is developed after an annual study of trends at the county and individual school levels. The grade enrollment history of each school is compiled and updated annually. Analysis of this history uncovers patterns in the aging of students from one grade to the next. Extrapolating these patterns enables the forecast for each school to be developed. This approach, termed the cohort-survivorship method, is the most widely accepted and applied school enrollment forecasting method.

MCPS projections, prepared in the fall of every year, extend through the upcoming six years for all schools, and for the tenth and fifteenth years in the future for secondary schools. The actual September enrollment at each school is used as the basis from which projections are developed. The cohort-survivorship method "ages" the student population ahead through the grade levels at each school to the desired forecast years. For each school in the system and for the entire system, calculations of the net change in grade level enrollments as students transition from one grade to the next are developed. These enrollment change amounts are applied to current grade enrollments in order to project future enrollment in the grades system wide and at individual schools. For example, system wide, and at many schools, the number of Grade 1 students typically exceeds the number of kindergarteners the previous year. This example is usually the result of parents choosing private kindergarten for their children, and then enrolling them in public schools beginning in Grade 1. (This is less of a factor now that MCPS offers full-day kindergarten at all elementary schools and the share of county students in public schools, compared to nonpublic schools, increases.) Similar trends in the amount of "grade change" are discernible for each grade system wide, and at individual schools. Each school is unique, and projections must be sensitive to population dynamics in the communities served by the school, and the specific trends in the cohort movements through the grades.

Migration to Montgomery County by families with preschool and school-age children has yielded substantial numbers of new students. This source of enrollment growth was especially significant in the 1980s and 1990s, when a large number of new subdivisions were being built and turnover of homes in older communities hit record levels. Though the county's draw of migrating households is now more moderate, migration continues to be a key factor that is incorporated into enrollment forecasts. Forecasters add these new students by tracking enrollment changes in schools and by tracking residential building plans, construction, and sales activity in developing areas of the county. Estimates of student yield from subdivisions are applied to the forecast for the school serving the development after the projected building schedule is considered. Recently, MCPS has received more students from county private schools and fewer students have left the county to attend school in other jurisdictions. These trends have led to marked increases in enrollment despite the poor economy.

Because of the uncertainty that surrounds both short- and long-range forecasts, MCPS forecasts are revised each fall. In addition, the one-year forecast is revised each spring. The primary purpose of evaluating the upcoming school year forecast is to increase accuracy in making staffing decisions and to place relocatable classrooms where needed. The evaluation assesses the enrollment change in each school from September, when the original forecast is made, to the time of spring revision. In areas of the county that are developing, an assessment of the rate of housing construction is made. Also, in some cases administrative or Board of Education actions, such as a change in a school service area, may affect enrollment.

The most difficult component of the enrollment forecast is predicting kindergarten enrollment. To develop forecasts for kindergarten, an annual review of resident birth records compiled by the Maryland Center for Health Statistics is undertaken. Births in nearby jurisdictions to mothers who reside in Montgomery County are included in the records that are reported at the county level. These records provide a general measure of potential kindergarten enrollment five years in the future.

Analyzing the relationship between actual and projected county births—kindergarten enrollment five years after the birth year—enables ratios of kindergarten enrollment to births five years previously, to be developed. These ratios are then applied to more recent birth numbers, and projected births, to develop the total kindergarten enrollment forecast for MCPS. Kindergarten enrollment forecasts are then developed for each school, using recent trends in kindergarten enrollment at the school to guide the forecast. Individual school kindergarten projections are then reconciled to the countywide kindergarten forecast at the end

of the process. Kindergarten trends are reevaluated each year through close coordination with school principals.

Continuous efforts are underway to increase the accuracy of forecasting techniques. Advances continue to be made in the use of computers for the retrieval and analysis of demographic and facility planning data. For this reason MCPS is increasingly using the county Geographic Information System (GIS). This GIS system contains extensive demographic and land-use data that is used in the forecasting and facility planning processes. Ties between MCPS planners, county planning agencies, the real estate and development communities, and community representatives enable an ongoing exchange of information relevant to forecasting. This pooled knowledge is a valuable resource in the inherently difficult job of predicting the future.

Appendix Q

Capacity Calculations

School capacity is defined by the State of Maryland as the maximum number of students that can reasonably be accommodated in a facility without significantly hampering delivery of the given educational program. School capacity is the product of the number of teaching stations at a school and the average class size for each program (based generally on the student-to-teacher ratio). The state of Maryland and MCPS rate capacities using slightly different student-to-teacher ratios.

MCPS Program Capacity

Class size for regular and supplemental programs, such as English for Speakers of Other Languages (ESOL), is based on MCPS policy, regulation, and budget guidelines. Many jurisdictions in Maryland, including Montgomery County, strive to reduce class sizes. State and federal regulations mandate a maximum class size limit for preschool programs.

The current standard student-to-classroom ratios used to calculate school capacities as stated in the Board of Education Long-range Educational Facilities Regulation (FAA-RA) are as follows:

Head Start and prekindergarten—2 sessions	40:1
Head Start and prekindergarten—1 session	20:1
Grade K—full-day	22:1
Grade K—reduced class size full-day	18:1
Grades 1–2—reduced class size	18:1
Grades 1–5/6 Elementary	23:1
Grades 6–8 Middle	25:1*
Grades 9–12 High	25:1**
ESOL (secondary)	15:1

*Program capacity is adjusted at the middle school level to account for scheduling constraints. The regular classroom capacity of 25 is multiplied by .85 to reflect the optimal utilization of a middle school facility (equivalent to 21.25 students per classroom.)

**Program capacity is adjusted at the high school to account for scheduling constraints. The regular classroom capacity of 25 is multiplied by .9 to reflect the optimal utilization of a high school facility (equivalent to 22.5 students per classroom.)

Many schools that appear to have space based on the calculated program capacity often need relocatable classrooms to accommodate the programs operating in the school. There are several explanations for this situation.

- ***Staffing Ratio:*** Capacity calculations for elementary schools are based on a student-to-classroom ratio of 23:1; however, staffing (student-to-teacher ratio) is not always provided at the same ratio. When the student-to-teacher ratio is less than the student-to-room ratio, the calculated capacity will not support the number of teachers provided by the staffing ratio in the facility. For example, if staffing is provided at 22:1, and capacity is calculated at 23:1, then for a building with 20 classrooms the capacity would be 460 (20 x 23) students but there would be 21 teachers based on the staffing ratio (460/22 = 20.9), therefore one additional classroom would be needed to accommodate a 22:1 staffing ratio.
- ***Combined Staffing:*** Some schools are provided additional staffing to meet the needs of students in the school. For example, a school that has a large number of students impacted by poverty may be allocated an additional .5 teaching position to assist students and an additional .5 teaching position for Title 1 services. The school may decide to combine the allocated staff to create an additional classroom teaching position, thereby creating the need for an additional classroom. In this case, the enrollment has not increased and the calculated capacity has not changed, but the need for classrooms has increased.
- ***Capping Class Size:*** In schools that may have very large class sizes in certain grades, additional staff may be provided to reduce the oversized classes to keep them within Board of Education guidelines. For example, if a school has two second-grade classes each with 28 students and four more students enroll in second grade, adding the additional students to the two large classes would cause the two classes to exceed the maximum class size cap of 28 students. If there was no opportunity to create combination classes with other grades, an additional teacher would be provided, and the school would reorganize with three second-grade classes of 20 students each. The additional teacher could create the need for a relocatable classroom.

Small instructional spaces and specialized classrooms are provided for all schools and are allocated on the basis of enrollment size and the need for supplementary instructional activities, such as remedial reading, special education resource, speech, art, and music.

In situations where the educational program will not be adversely affected, MCPS leases space on an annual basis to appropriate outside organizations. In most cases, these organizations are referred to as "joint occupants" and are usually day-care providers. Before and after school programs also are provided in many MCPS schools. Spaces used by day-care providers on MCPS sites range from shared use of multipurpose rooms before and after school, to relocatable classrooms on a school site that are financed by the provider and operated for the school community. If space is available, one or more classrooms can be leased for full-day programs.

State-rated Capacity

State-rated capacity, used to determine state funding, is calculated using the following calculations. These calculations make MCPS and state capacity ratings differ. See appendix J for a comparison of capacity ratings for all schools.

Head Start and prekindergarten—1 session	20:1
Grade K—full-day	22:1
Grades 1–5/6 Elementary	23:1
Grades 6–12 Secondary	25:1*
Special Education	10:1

*Program capacity differs at the secondary level in that regular classroom capacity in the regular classroom capacity of 25 is multiplied by .85 to reflect the optimal utilization of a secondary school (equivalent to 21.25 students per classroom).

Appendix R

Planned Life-cycle Asset Replacement (PLAR) Projects
Completed Summer 2014

	School/Facility	Project Scope
1	Arcola ES	Fire Extinguishers
2	Argyle MS	Fire Door Replacement
3	Argyle MS	Sprinkler (Locker Rooms)
4	John T. Baker MS	Oven
5	Benjamin Banneker MS	Tennis Court Refurbishment
6	Bannockburn ES	Fire Alarm Replacement
7	Lucy V. Barnsley ES	Enclosure Fence
8	Beall ES	Cooling Tower Platforms
9	Beall ES	Fence
10	Beall ES	Security Cable Replacement
11	Bells Mill ES	Ladder Modifications/Safety Rails
12	Bethesda ES	Fence
13	Bethesda ES	Ladder Repairs
14	Bethesda-Chevy Chase HS	Combi Oven
15	Bethesda-Chevy Chase HS	Dormers (Paint Exterior)
16	Bethesda-Chevy Chase HS	Oven (Hydrovection)
17	Bethesda-Chevy Chase HS	Running Track Repairs
18	Bethesda-Chevy Chase HS	Skylight Repairs
19	Montgomery Blair HS	Exterior Waterproofing Fascia
20	Montgomery Blair HS	Library Security Gate
21	Montgomery Blair HS	Parking Lot Restriping
22	Montgomery Blair HS	Running Track Refurbishment
23	James Hubert Blake HS	Combi Oven (Remove Fryers)
24	James Hubert Blake HS	Dance Floor
25	James Hubert Blake HS	Fire Alarm Replacement
26	James Hubert Blake HS	Grandstand (weed block and gravel)
27	James Hubert Blake HS	Oven (Hydrovection)
28	James Hubert Blake HS	Running Track Refurbishment
29	Briggs Chaney MS	Oven (Hydrovection)
30	Brook Grove ES	Window Replacement
31	Brook Grove ES	Full Roof Replacement
32	Burning Tree ES	Ceiling & Lights
33	Burning Tree ES	Fascia and Soffit
34	Burning Tree ES	Paint (Exterior & Interior)
35	Burtonsville ES	Boiler Chimney Refurbishing
36	Burtonsville ES	Full Roof Replacement
37	Cabin John MS	Hatch Rail & Barrier Protection
38	Rachel Carson ES	Lock Box
39	Rachel Carson ES	Stair Treads
40	Cedar Grove ES	Flooring
41	Winston Churchill HS	Tennis Court Repairs
42	Winston Churchill HS	Track Repairs
43	Clarksburg ES	Boiler Chimney Replacement
44	Clarksburg ES	Canopy & Railing Repl (4)
45	Clarksburg ES	Concrete (Back of School by Portables)
46	Clarksburg ES	Roof Replacement
47	Clarksburg HS	Gym Floor Refinishing
48	Clarksburg HS	Gym Restriping
49	Clearspring ES	Blinds
50	Clearspring ES	Convection Oven
51	Clearspring ES	Solar Window Film
52	Clearspring ES	Windows and Doors
53	Roberto Clemente MS	Elevator Repair
54	Clopper Mill ES	Asphalt (Play Area)
55	Cloverly ES	Concrete
56	Cloverly ES	PA System
57	Cloverly ES	Restroom Renovation
58	Cold Spring ES	Concrete
59	Cold Spring ES	PA System
60	Cold Spring ES	Replace Toilet Seats
61	Cold Spring ES	Skirting Replacement
62	Capt. James E. Daly ES	Canopy & Railing Repl (3)
63	Capt. James E. Daly ES	Doors
64	Capt. James E. Daly ES	Fire Alarm Replacement
65	Capt. James E. Daly ES	Flashing
66	Capt. James E. Daly ES	Oven (Stacking)
67	Capt. James E. Daly ES	Windows Replacement
68	Damascus ES	Fall Protection Repairs
69	Damascus HS	Hydrovection Oven
70	Damascus HS	Oven (Hydrovection)
71	Damascus HS	Strata Pit Filler
72	Damascus HS	Striping
73	Damascus HS	Tennis Court Refurbishment
74	Damascus HS	Window Replacement
75	Darnestown ES	Concrete Loading Dock
76	Darnestown ES	Windows (Phase 1 of 2)
77	Diamond ES	Gym Floor
78	Diamond ES	Lights (Poles)
79	Dr. Charles R. Drew ES	Concrete
80	Dr. Charles R. Drew ES	Cove Base
81	East Silver Spring ES	Field Renovation
82	East Silver Spring ES	Serving Line Replacement
83	Albert Einstein HS	Catwalk Safety Rail
84	Albert Einstein HS	Engineering Work
85	Albert Einstein HS	Running Track Repairs
86	Emory Grove Center	Emergency Generator
87	Blair G. Ewing Center	Exterior Walls
88	Blair G. Ewing Center	Paint (Exterior & Interior)
89	Blair G. Ewing Center	Warmer
90	Blair G. Ewing Center	Windows and Doors
91	Blair G. Ewing Center	Flooring
92	Fallsmead ES	Abatement
93	Farmland ES	Firestopping
94	Flower Hill ES	Fire Alarm System
95	Flower Hill ES	Gym Floor
96	Flower Hill ES	Restroom Renovation
97	Flower Hill ES	Suspended Ceilings and Lights
98	Flower Hill ES	Abatement
99	Forest Oak MS	Oven (Hydrovection)
100	Fox Chapel ES	White Board Installation
101	Robert Frost MS	Winches for Basketball
102	Robert Frost MS	Partial Roof Replacement
103	Gaithersburg ES	Flooring Replacement
104	Gaithersburg ES	Windows (Back of School)
105	Gaithersburg MS	Gym Floor Refinishing
106	Gaithersburg MS	Masonry Wall (Green Houses)
107	Gaithersburg MS	Windows and Doors (Phase 1 of 3)
108	Georgian Forest ES	Concrete Steps/Sidewalks
109	William B. Gibbs Jr. ES	Gym Line Painting
110	Greencastle ES	Restroom Renovation
111	Harmony Hills ES	Convection Oven
112	Harmony Hills ES	Firestopping
113	Harmony Hills ES	Freezers
114	Harmony Hills ES	Ladder Modifications/Safety Rails
115	Highland View ES	Masonry Wall Repairs
116	Jackson Road ES	Ladder Modifications/Safety Rails
117	Walter Johnson HS	Sprinkler System Access Panels
118	Jones Lane ES	Fire Alarm System
119	John F. Kennedy HS	Lighting Retrofit
120	John F. Kennedy HS	Long Jump Reconstruction
121	John F. Kennedy HS	Oven (Hydrovection)
122	John F. Kennedy HS	Running Track Refurbishment
123	Kingsview MS	Gym Floor (Refinishing)
124	Kingsview MS	Oven (Hydrovection)
125	Kingsview MS	Roof Repairs
126	Lake Seneca ES	Abatement

	School/Facility	Project Scope
127	Lakewood ES	Field Renovation
128	Laytonsville ES	Gym Floor
129	Col. E. Brooke Lee MS	Library Security Gate
130	JoAnn Leleck ES at Broad Acres	Walk Platforms
131	Luxmanor ES	Ladder Repairs
132	Col. Zadok Magruder HS	Gym Floor Refinishing
133	Col. Zadok Magruder HS	Running Track Repairs
134	Col. Zadok Magruder HS	Strata Pit Filler
135	S. Christa McAuliffe ES	Fence
136	S. Christa McAuliffe ES	Restroom Renovation
137	Ronald McNair ES	Asphalt
138	Ronald McNair ES	Paint
139	Ronald McNair ES	Restroom Renovation
140	Meadow Hall ES	Restroom Renovation
141	Mill Creek Towne ES	Firestopping
142	Monocacy ES	Asphalt
143	Richard Montgomery HS	Field Renovation
144	Richard Montgomery HS	Ladder and Platform
145	Richard Montgomery HS	Ladder Modifications/Safety Rails
146	Richard Montgomery HS	Water Heater Replacement
147	Montgomery Knolls ES	Mag Lock
148	Neelsville MS	Ext Doors and Windows
149	Neelsville MS	Sidewalk Repairs
150	Newport Mill MS	Electric Hoist for Gym
151	Newport Mill MS	Library Security Gate
152	North Bethesda MS	Additional Lockers Phase 1
153	North Bethesda MS	Additional Lockers Phase 2
154	North Bethesda MS	Milk Cooler
155	North Bethesda MS	Oven (Hydrovection)
156	North Bethesda MS	Roof Safety Rail
157	North Lake Center	Emergency Generator
158	North Lake Center	Light Fixtures
159	North Lake Center	Security Cable Repl
160	North Lake Center	Water Main
161	Northwest HS	Running Track Refurbishment
162	Northwood HS	Restroom Renovation
163	Northwood HS	Running Track Repairs
164	Northwood HS	Striping
165	Northwood HS	Water Booster Pump System
166	Oak View ES	Ladder Modifications/Safety Rails
167	Olney ES	Fall Protection Repairs
168	Olney ES	Gutter Guard
169	Rosa Parks MS	Ramp Repairs
170	Pine Crest ES	Paint
171	Pine Crest ES	Restroom Renovation
172	Piney Branch ES	Suspended Ceilings and Lights
173	John Poole MS	Oven (Hydrovection)
174	John Poole MS	Restroom Renovation
175	Poolesville ES	Doors and Frames
176	Poolesville ES	Lock Box
177	Poolesville ES	Paint
178	Poolesville HS	Library Security Gate
179	Poolesville HS	Flooring
180	Thomas W. Pyle MS	Tennis Court Replacement
181	Quince Orchard HS	Asphalt
182	Quince Orchard HS	Basketball Winches
183	Quince Orchard HS	Lighting Replacement
184	Quince Orchard HS	Locker Keys
185	Radnor Center	Ladder Modifications/Safety Rails
186	Radnor Center	Screen Wall
187	Judith A. Resnik ES	Asphalt
188	Judith A. Resnik ES	Fire Alarm System
189	Judith A. Resnik ES	Storage Room Ladder
190	Dr. Sally K. Ride ES	Canopy & Railing Repl (4)
191	Ridgeview MS	Electrical Shed Replacement
192	Ridgeview MS	Music Room windows and stucco
193	Rock Terrace School	Audio System
194	Rock Terrace School	Ladder Modifications/Safety Rails
195	Rock View ES	Concrete
196	Rockville HS	Fall Protection Repairs
197	Rockville HS	Ladder Modifications
198	Rockville HS	Masonry Walls
199	Rockville HS	Partial Re-roofing
200	Rockville HS	Rigging Modifications
201	Rockville HS	Water Heater Replacement
202	Lois P. Rockwell ES	Paint
203	Lois P. Rockwell ES	Restroom Renovation
204	Lois P. Rockwell ES	Sprinkler System
205	Lois P. Rockwell ES	Partial Roof Replacement
206	Rocky Hill MS	Door Mag
207	Rocky Hill MS	Floor Covering
208	Rolling Terrace ES	Air Diffusers
209	Rolling Terrace ES	Paint (Exterior & Interior)
210	Rolling Terrace ES	Site Improvements
211	Rosemary Hills ES	Ceiling Tile Replacement
212	Rosemary Hills ES	Fall Protection Repairs
213	Rosemary Hills ES	Ladder Modifications/Safety Rails
214	Rosemary Hills ES	Repairs and Painting (2)
215	Rosemary Hills ES	Screen Wall
216	Rosemont ES	Improvements
217	Rosemont ES	Lock Box
218	Carl Sandburg Learning Center	Painting
219	Carl Sandburg Learning Center	Skirting Replacement
220	Sequoyah ES	Aluminum Walkways
221	Sequoyah ES	Blinds
222	Sequoyah ES	Solar Window Film
223	Seven Locks ES	Fall Protection Repairs
224	Sherwood HS	Concrete
225	Sherwood HS	Downspout Modifications
226	Sherwood HS	Drainage (Phase II)
227	Flora M. Singer ES	Elevator Repair
228	Silver Spring International MS	Field
229	Silver Spring International MS	Fire Stops
230	Silver Spring International MS	Gym Floor Refinishing
231	Silver Spring International MS	Lavatory Reinstallation
232	Sligo MS	Restroom Renovation
233	Sligo Creek ES	Lavatory Reinstallation
234	South Lake ES	Fall Protection Repairs
235	South Lake ES	Lock Box
236	South Lake ES	Oven (Double Stack Convection)
237	South Lake ES	Serving Line Replacement
238	South Lake ES	Windows and Doors (Phase 2 of 2)
239	Springbrook HS	Stadium Grandstands Repairs
240	Stedwick ES	Lock Box
241	Stephen Knolls School	Asphalt (Driveway, Parking, Play Areas)
242	Stephen Knolls School	Restroom Renovation
243	Stonegate ES	Ladder Modifications/Safety Rails
244	Strathmore ES	Doors
245	Strathmore ES	Serving Line Replacement
246	Strathmore ES	Walk-In Freezer
247	Strathmore ES	Partial Roof Replacement
248	Strawberry Knoll ES	Asphalt
249	Strawberry Knoll ES	Fire Alarm System
250	Strawberry Knoll ES	Gym Floor
251	Strawberry Knoll ES	Lock Box
252	Summit Hall ES	Canopy & Railing Repl (3)
253	Summit Hall ES	Security Cable Replacement
254	Takoma Park ES	Exterior Wall Repairs
255	Takoma Park ES	Waterproofing (Phase 2)
256	Takoma Park ES	Windows and Doors
257	Tilden MS	Exterior Wall Repairs
258	Tilden MS	Water Heater
259	Twinbrook ES	Improvements
260	Twinbrook ES	Restroom Renovation

	School/Facility	Project Scope
261	Twinbrook ES	Skirting Replacement (2)
262	Twinbrook ES	Suspended Ceilings and Lights
263	Viers Mill ES	Restroom Renovation
264	Viers Mill ES	Partial Roof Replacement
265	Washington Grove ES	Gym Floor
266	Waters Landing ES	Lock Box
267	Waters Landing ES	Restroom Renovation
268	Waters Landing ES	Suspended Ceilings and Lights
269	Watkins Mill ES	Lock Box
270	Watkins Mill HS	Dance Floor
271	Watkins Mill HS	Running Track Repairs
272	Julius West MS	Fire Alarm Replacement
273	Julius West MS	Floor Covering
274	Julius West MS	Sprinkler System
275	Julius West MS	Water Heater

	School/Facility	Project Scope
276	Westbrook ES	Blinds and Shades
277	Westbrook ES	Ladder Modifications/Safety Rails
278	Westbrook ES	Restroom Renovation
279	Westland MS	Field Renovation
280	Whetstone ES	Interior Door Replacement
281	Whetstone ES	Ladder Repairs
282	White Oak MS	Fire Alarm Replacement
283	Walt Whitman HS	Stage Floor
284	Walt Whitman HS	Water Heater
285	Woodfield ES	Suspended Ceilings and Lights
286	Woodlin ES	Doors (1 set)
287	Woodlin ES	Gym Wood Flooring Installation
288	Thomas S. Wootton HS	Skirting Replacement
289	Wyngate ES	Restroom Renovation

Appendix S

Special Education Services Descriptions

School-based Service Delivery Model

Resource Room Services

Resource Room Services, available in all MCPS schools, provide students with disabilities with the support they need to be academically successful in the general education environment. Resource teachers provide an array of services to students with disabilities including strategy-based instruction, direct instruction aligned with the Common Core State Standards in reading/language arts, writing, mathematics, and organizational skills, in preparation for the Partnership for Assessment of Readiness for College and Careers (PARCC) assessments.

Speech and Language Services

The goals of Speech and Language Services are to diagnose communication disorders, improve spoken language skills, facilitate compensatory skills, and enhance the development of language, vocabulary, and expressive communication skills to support student access to the general education curriculum. The type and frequency of services provided are determined by individual student needs. For students with less intensive needs, educational strategies are provided to the student's general education teachers and parents for implementation within the classroom and home environments. Students may receive services in their classroom program in small groups, or individually.

Elementary Home School Model

Elementary Home School Model supports students in Grades K–5 as a result of a disability that impacts academic achievement in one or more content areas, organization, and/or behavior. Students served by this model are assigned to age-appropriate heterogeneous classes in their neighborhood schools. Student access to the general education curriculum during the course of the day is based on individual student needs and encompasses a variety of instructional models that may include instruction in a general education environment and/or a self-contained setting.

Secondary Learning and Academic Disabilities (LAD) Services

Secondary Learning and Academic Disabilities services, available in all secondary schools in MCPS, provide services to students as a result of a disability that impacts academic achievement. Students served by this model receive special education support to demonstrate progress towards the Individualized Education Program (IEP) goals and objectives. These services are provided in a continuum of settings that may include components of self-contained classes, cotaught general education classes, and other opportunities for participation with nondisabled peers.

Transition Services

Transition Services are provided to students receiving special education services, age 14 or older, to prepare for college, career and community readiness. These activities include, but are not limited to, postsecondary education, workforce experiences, continuing and adult education, adult services, independent living, and/or community participation. Services are based on the individual student's needs, considering the student's strengths, preferences, and interests. Transition services are delivered through direct and/or indirect support coordinated by a transition support teacher.

Cluster-based Service Delivery Model

Elementary Learning and Academic Disabilities (LAD) Services

Elementary Learning and Academic Disabilities classes provide services to students as a result of a disability that impacts academic achievement. Students served by this model previously received considerable amounts of special education support in the general education environment, but require additional services in order to demonstrate progress toward the IEP goals and objectives. Selected elementary schools provide this service within each quad-cluster.

Quad-cluster/Regionally-based Service Delivery Model

Elementary Learning Center (ELC)

The Elementary Learning Centers provide comprehensive special education and related services. The program offers a continuum of services for Grades K–5 in self-contained classes with opportunities to be included with nondisabled peers in the general education environment. These services address the goals and objectives in the student's IEP while ensuring access to the general curriculum through strategies such as assistive technology, reduced class size, and differentiated instruction.

Learning for Independence (LFI) Program

Learning for Independence (LFI) services are designed for students with complex learning and cognitive needs, including mild to moderate intellectual disabilities. Services support the

implementation of Alternate Academic Learning Outcomes aligned with Curriculum 2.0. Students are provided with many opportunities for interaction with general education peers, including inclusion in general education classes as appropriate, peer tutoring, and extracurricular activities. The students learn functional life skills in the context of the general school environment and in community settings. Community-based instruction and vocational training are emphasized at the secondary level so that students are prepared for the transition to post-secondary opportunities upon graduating with a certificate from the school system.

School/Community-based (SCB) Program

School/Community-based Program (SCB) services are designed for students with severe or profound intellectual disabilities and/or multiple disabilities. Students typically have significant needs in the areas of communication, personal management, behavior management, and socialization. The program emphasizes individualized instruction, utilizing Alternate Academic Learning Outcomes aligned with Curriculum 2.0, in comprehensive schools and related community and work environments. The SCB model includes the following components—age-appropriate classes, heterogeneous groupings, peer interactions, individualized instruction, and transition—which are available in all quad-clusters. The goal of the program is to prepare students to transition to post-secondary opportunities upon graduating with a certificate from the school system.

Infants and Toddlers Program

Infants and Toddlers early intervention services are provided to families and children with developmental delays from birth to age three, or until the start of the school year following the child's fourth birthday, under the Extended Individualized Family Service Plan option. Services are provided in the Natural Environment and may include specialized instruction, auditory and vision instruction, physical and occupational therapy, and speech/language services. Parental involvement and coaching is a major service component based on the philosophy that a parent can be a child's most effective teacher in the natural setting.

Preschool Education Program (PEP)

The Preschool Education Program (PEP) offers a continuum of prekindergarten classes and services for students with disabilities ages 3 through 5. PEP serves students with delays in multiple developmental domains that impact learning of age-appropriate skills. Services range from consultative and itinerant services for children in community-based child care settings and preschools to itinerant instruction at home for medically fragile children. Classes are provided for children who need a comprehensive approach to learning. PEP PILOT provides a two-day per week early childhood setting; PEP collaboration classes offer inclusive opportunities for prekindergarten students utilizing a coteaching model. PEP Classic and PEP Intensive Needs classes serve children with developmental delays in a structured special education setting. PEP Comprehensive and Beginnings serve students with moderate to severe delays and/or multiple disabilities. Programs are offered at selected elementary schools in one or more quad-cluster administrative area(s).

Prekindergarten Language Classes

Prekindergarten Language classes serve students ages 3 through 5, with delays in receptive and/or expressive language that impact their ability to communicate and learn in typical preschool environments. Speech and language supports and related services are provided in a two days per week developmentally appropriate class, or five days per week in an early childhood classroom setting with opportunities for learning with nondisabled peers. The purpose of this program is to use oral language for successful communication and to develop pre-academic skills in preparation for kindergarten. Selected elementary schools offer this program to support one or more quad-cluster administrative areas.

Autism Spectrum Disorders Services

The Comprehensive Autism Preschool Program (CAPP) provides highly intensive and individualized services for students ages 3 through 5. Evidence-based instructional practices are utilized to increase academic, language, social, and adaptive skills to ultimately provide access to a variety of school-aged services and to maximize independence in all domains. Autism services for students, elementary through age 21, provide access to Alternate Academic Learning Outcomes aligned with Curriculum 2.0. Students receive Applied Behavior Analysis (ABA) intensive instruction in a highly structured setting to improve learning and communication and access inclusive opportunities with nondisabled peers. At the secondary level, students also receive vocational and community support.

Secondary Autism Resource Services

Secondary Autism Resource Services, located in three middle schools and three high schools, are designed for students with autism spectrum disorders who are diploma bound and have difficulty mastering grade-level curriculum. The students require a modified pace and individual accommodations representative of the needs and characteristics of students with autism spectrum disorders. Students receive instruction in the general education curriculum with the supports indicated on their IEPs. Access to the general education curriculum with enrichment is reinforced.

Augmentative and Alternative Communication

The Augmentative and Alternative Communication (AAC) classrooms provide intensive support for students who are not verbal or have limited speech with severe intelligibility issues. Students learn to use and expand their knowledge of augmentative communication devices and other forms of aided communication in order to access the general education curriculum. Emphasis is on the use of alternative communication systems to enhance language development, vocabulary development, and expressive communication skills. Services and supports are often provided within the general education environment to the greatest extent possible.

Emotional Disabilities Services

Emotional Disabilities (ED) Services are provided to students who demonstrate significant social, emotional, learning and/or behavioral challenges that adversely impact their success in school. Students access the MCPS general education curriculum, yet may have difficulty achieving academic success due to emotional and behavioral challenges that interfere with their ability to participate successfully in an educational environment. Students are served in a continuum of settings that may include self-contained classes and opportunities for participation in general education classes with nondisabled peers as appropriate.

Bridge Services

Bridge Services are designed to meet the needs of students who demonstrate significant social, emotional, learning, and/or behavioral challenges that make it difficult to succeed in a large school environment. Many students require social and emotional supports in order to access their academic program. Comprehensive behavior management is utilized in the model that includes proactive teaching and rehearsal of social skills, as well as the use of structured and consistent reinforcement systems. Services are provided in a continuum of settings that may include separate classes and opportunities for participation in general education classes with nondisabled peers as appropriate.

Gifted and Talented/Learning Disabled Services

Twice exceptional students receiving gifted and talented/learning disabled (GT/LD) services demonstrate superior cognitive ability in at least one area and typically have production problems, particularly in the area of written expression. GT/LD services provide students with specialized instruction, adaptations, and accommodations that facilitate appropriate access to rigorous instruction in the least restrictive environment, which may include placement in Honors or Advanced Placement classes, and access to the acceleration and enrichment components in the MCPS instructional guidelines. Some students may receive services in specialized classrooms.

Elementary Physical Disabilities Services

Elementary physical disabilities services provide comprehensive supports to students with physical and health-related disabilities that cause a significant impact on educational performance in the general education environment. Students exhibit needs in motor development and information processing. Services include special education instruction, consultation with classroom teachers, and occupational and physical therapy services.

Longview School

The Longview School provides services to students, ages 5–21, with severe to profound intellectual disabilities and multiple disabilities. Alternate Academic Learning Outcomes aligned with Curriculum 2.0 are utilized to provide students with skills in the area of communication, mobility, self-help, functional academics, and transition services.

Stephen Knolls School

The Stephen Knolls School services students, ages 5–21, with severe to profound intellectual disabilities and multiple disabilities. Alternate Academic Learning Outcomes aligned with Curriculum 2.0 are utilized to provide students with skills in the area of communication, mobility, self-help, functional academics, and transition services.

Countywide Service Delivery Model

(Because of low incidence, these programs are based in central locations and serve students from the entire county. In some cases, the programs are provided regionally when the level of incidence increases.)

Services for the Visually Impaired

Vision services are provided to students with significant visual impairments or blindness. Services enable students to develop effective compensatory skills and provide them with access to the general education environment. A prekindergarten class prepares children who are blind or have low vision for entry into kindergarten. Itinerant vision services are provided to school-aged students in their home or assigned school. Skills taught include visual utilization, vision efficiency, reading and writing using Braille, and the use of assistive technology. Students may receive orientation and mobility instruction to help them navigate their environment. Students over the age of 14 receive specialized transition support as appropriate.

Deaf and Hard of Hearing Services

Deaf and Hard of Hearing services provide comprehensive educational supports to students who are deaf or have a significant hearing loss. These services, provided by itinerant teachers, enable students to develop effective language and communication skills necessary to access the general education environment in neighborhood schools. Students with more significant needs receive services in centrally-located classes. Services are provided in three communications options: oral/aural, total communication, and cued speech. Assistive technology and consultation also are provided to students and school staff members.

Occupational/Physical Therapy Services

Related services of occupational and physical therapy provide supports for students with physical and/or health-related disabilities to facilitate access to their school program. Services are provided as direct therapy to students and/or consultation to classroom staff members. Services are provided at elementary, middle, and high schools throughout MCPS.

Extensions

Extensions serves students of middle and high school age with the most significant cognitive disabilities, multiple disabilities, and/or autism. These students have a prolonged history of requiring intensive, systematic behavioral supports and services to reduce self-injurious and/or disruptive behaviors. The goal of the Extensions Program is to provide intensive educational

programming to enable these students to acquire Alternate Academic Learning Outcomes aligned with Curriculum 2.0 and postsecondary opportunities including adult day services and employment.

Carl Sandburg Learning Center

Carl Sandburg Learning Center is a special education school that serves students with multiple disabilities in kindergarten through Grade 5, including intellectual disabilities, autism spectrum disorders, language disabilities, and emotional and other learning disabilities. Services are designed for elementary students who need a highly-structured setting, small student-to-teacher ratio, and access to the MCPS general education curriculum or Alternate Academic Learning Outcomes aligned with Curriculum 2.0. Modification of curriculum materials and instructional strategies, based on students' needs, is the basis of all instruction. Emphasis is placed on the development of language, academic, and social skills provided through an in-class transdisciplinary model of service delivery in which all staff members implement the recommendations of related service providers. Special emphasis is placed on meeting the sensory and motor needs of students in their classroom setting. To address behavioral goals, services may include a behavior management system, psychological consultation, and crisis intervention.

Rock Terrace School

Rock Terrace School is comprised of a middle, high, and upper school program. The instructional focus of the middle school is the implementation of Alternate Academic Learning Outcomes aligned with Curriculum 2.0 to prepare the students for transition to the high school program. The high school program emphasizes the Alternate Academic Learning Outcomes aligned with Curriculum 2.0 and community-based instruction activities that enable students to demonstrate skills that lead to full participation in school-to-work and vocational/community experiences. Authentic jobs help in reinforcing classroom learning. The upper school prepares students for college, career and community readiness.

John L. Gildner Regional Institute for Children and Adolescents (RICA) Program

The John L. Gildner Regional Institute for Children and Adolescents (RICA), in collaboration with the Maryland State Department of Health and Mental Hygiene, provides appropriate educational and treatment services to all students and their families through highly-structured, intensive special education services with therapy integrated in a day and residential treatment facility. An interdisciplinary treatment team, consisting of school, clinical, residential and related service providers, develops the student's total educational plan and monitors progress. Consulting psychiatrists, a full time pediatrician, and a school community health nurse are also on staff.

RICA offers fully accredited special education services which emphasize rigorous academic and vocational/occupational opportunities, day and residential treatment, and individual, group, and family therapy. The RICA program promotes acquisition of grade and age appropriate social and emotional skills and allows students to access the general education curriculum.

Assistive Technology Services

Assistive Technology Services provide support for students from birth–21. Augmentative communication and technology services support students who are severely limited in verbal expression or written communication skills, often due to physical disabilities. Services are provided in the natural environment for children birth to age three, and in the elementary, middle, or high school classroom setting for students prekindergarten through age 21.

Aspergers Services

Aspergers Services provide direct classroom instruction in the areas of coping strategies and pro-social behaviors with supported access to the general education curriculum. Students receive appropriate accommodations and supports for coping, organization, and self-advocacy.

Appendix T

Long-range Educational Facilities Planning Policy (FAA) and Regulation (FAA-RA)

On May 23, 2005, the Board of Education adopted a revision to Policy FAA—Long-range Educational Facilities Planning. This policy was revised in order for Policy FAA to conform to other Board of Education policies that separate policy requirements from regulations. Subsequently, on June 1, 2005, the superintendent issued interim Regulation FAA-RA. The regulation was created from language previously contained in Policy FAA that was regulatory in nature.

In adopting revisions to Policy FAA, the Board of Education directed the superintendent to conduct a public review process for Regulation FAA-RA, prior to a final regulation being issued. A review process was conducted in the fall 2005 with input from MCCPTA and other community representatives. The superintendent incorporated this input in issuing the Regulation FAA-RA on March 21, 2006.

POLICY BOARD OF EDUCATION OF MONTGOMERY COUNTY

Related Entries: ABA, ABC, ABC-RA, ACD, DNA, FAA-RA, FKB, JEE, JEE-RA
Responsible Office: Chief Operating Officer
Department of Facilities Management

Long-range Educational Facilities Planning

A. PURPOSE

The Montgomery County Board of Education (Board) has a primary responsibility to plan for school facilities that address changing enrollment patterns and sustain high-quality educational programs in accordance with the policies of the Board. The Board fulfills this responsibility through the facilities planning process. Long-range educational facilities planning is essential to identify the infrastructure needed to ensure success for every student.

The *Long-range Educational Facilities Planning* (LREFP) policy guides the planning process. The process is designed to promote public understanding of planning for Montgomery County Public Schools (MCPS) and to ensure that there are sufficient opportunities for parents, students, staff, community members and organizations, local government agencies, and municipalities to identify and communicate their priorities and concerns to the superintendent of schools and the Board. LREFP will be in accordance with all federal, state, and local laws and regulations.

B. ISSUE

Enrollment in MCPS is constantly changing. The fundamental goal of facilities planning is to provide a sound educational environment for changing enrollment. The number of students, their geographic distribution, and the demographic characteristics of this population all impact facilities planning. Enrollment changes are driven by factors including birth rates and movement within the school system and into the school system from other parts of the United States and the world.

MCPS is among the largest school systems in the country in terms of enrollment and serves a county of approximately 500 square miles. The full range of population density, from rural to urban, is present in the county. Since 1984, enrollment has increased where new communities have formed, as well as in established areas of the county where turnover of houses has occurred.

MCPS is challenged continually to anticipate and plan for facilities in an efficient and fiscally responsible way to meet the varied educational needs of students. The LREFP policy describes how the school system responds to educational and enrollment change; the rate of change; its geographic distribution; and the racial, ethnic, and socioeconomic diversification of enrollment.

School facilities also change. Aging of the physical plant requires a program of maintenance, renovation, and revitalization/expansion, in accordance with Board Policy FKB, *Sustaining and Modernizing Montgomery County Public Schools (MCPS) Facilities*. Acquiring new sites, designing new facilities, and modifying existing facilities to keep current with program needs is essential. This policy provides the framework to coordinate planning for capital improvements.

C. POSITION

The long-range facilities planning process will continue to:

1. Plan for utilization of schools in ways that are consistent with sound educational practice and consider the impact of facility changes on educational program and related operating budget requirements and on the community.

2. Establish processes designed to obtain input by engaging in a discussion among a broad variety of stakeholders and utilizing opportunities for input from the public and relevant staff members, in accordance with Board Policy ABA, *Community Involvement*, for the capital improvements program and the facilities planning activities listed below:

    a) Selection of school sites

    b) Facility design

    c) Boundary changes

    d) Geographic student choice assignment plans (such as consortia)

    e) General enrollment, demographic, and facility related issues that are explored through roundtables and other community input processes.

    f) School closures and consolidations

3. Provide a six-year capital improvements program and educational facilities master plan which include enrollment projections, educational program needs, and available school capacity countywide, and identify—

a) when new schools and additions will be needed to keep facilities current with enrollment levels and educational program needs;

b) funds for systemic maintenance and replacement projects to sustain schools in good condition and extend their useful life;

c) a schedule to revitalize/expand older school buildings in order to continue their use on a cost-effective basis, and to keep facilities current with educational program needs;

d) when school closures and consolidations are appropriate due to declining enrollment levels; and

e) facility utilization levels, capacity calculations, school enrollment size guidelines, and school site size (adopted as part of the Board review of the superintendent of schools' recommended CIP).

4. Provide for the Board to hold public hearings and solicit written testimony on the recommendations of the superintendent of schools.

5. Provide a process for facility design that—

a) ensures a safe and secure environment;

b) is consistent with educational program needs;

c) includes community input;

d) demonstrates environmental stewardship; and

e) anticipates future needs

6. Provide a process for changing school boundaries and establishing geographic student choice assignment plans that—

a) Solicits input at the outset of the process consistent with Board Policy ABA, *Community Involvement*;

b) Considers four main factors in development of school boundaries, student choice assignment plans, and ways to address other facility issues including—

1) demographic characteristics of student population,

2) geographic proximity of communities to schools,

3) stability of school assignments over time,

4) facility utilization;

c) recognizes that the Board may, by majority vote, identify alternatives to the superintendent of schools' recommendations for school boundaries or geographic student choice assignment plans for review;

d) allows time for the Board to hold public hearings and solicit written testimony on the recommendations of the superintendent of schools and Board identified alternatives for school boundaries or geographic student choice assignment plans; and

e) Recognizes that the Board has the discretion to adopt minor modifications to the superintendent of schools' recommendation or Board identified alternatives if, by a majority vote, the Board has determined that such action will not have a significant impact on an option for school boundaries or geographic student choice assignment plans that has received public review.

7. Provide a process for closing and consolidating schools that meets the requirements of COMAR (Chapter 13A).

8. Provide for articulation in school assignments by:

a) Traditional Student Assignments

Structure high schools for Grades 9-12 and, where possible, creating straight articulation for clusters composed of one high school, and a sufficient number of elementary and middle schools, each of which sends its students, including special education and ESOL students, to the next higher level school in that cluster.

b) Student Choice Assignment Plans

In cases where students participate in a student choice assignment plan (e.g., consortium) to identify the school they wish to attend, articulation patterns may vary from the straight articulation pattern that is desired in traditional student assignment.

9. Provide for a different and/or condensed process and time schedule, developed by the superintendent of schools, for making recommendations to the Board regarding the capital improvements program and the facility planning activities listed above, including but not limited to changing school boundaries and establishing geographic student choice assignment plans in the event that the Board determines that unusual circumstances exist.

D. DESIRED OUTCOMES

1. A LREFP process that identifies the infrastructure necessary to deliver high quality educational facilities to all students and incorporates the input of parents, staff, and community and, as appropriate, students.

2. The superintendent of schools will develop regulations with student, staff, community, and parental input to guide implementation of this policy.

E. REVIEW AND REPORTING

1. The annual June publication of the Educational Facilities Master Plan will constitute the official reporting on facility planning. This document will reflect all facilities actions taken during the year by the Board and approved by the County Council. The Master Plan will project the enrollment and utilization of each school, and identify schools and sites that may be involved in future planning activities.

2. This policy will be reviewed in accordance with the Board policy review process.

Policy History: Adopted by Resolution No. 257-86, April 28, 1986; amended by Resolution No. 271-87, May 12, 1987; amended by Resolution No. 831-93, November 22, 1993; amended by Resolution No. 679-95, October 10, 1995; amended by Resolution No. 581-99 September 14, 1999; updated office titles June 1, 2000; updated November 4, 2003; amended by Resolution No. 268-05, May 23, 2005; amended by Resolution 282-14, June 17, 2014.

REGULATION MONTGOMERY COUNTY PUBLIC SCHOOLS

Related Entries: ABA, ABC, ACD, CFA, DNA, FAA, FKB, JEE, JEE-RA
Responsible Office: Chief Operating Officer
Department of Facilities Management
Related Source: *Code of Maryland Regulations* 13A.02.09.01

Long-range Educational Facilities Planning

I. PURPOSE

To implement the Montgomery County Board of Education (Board) Policy FAA, *Long-range Educational Facilities Planning,* by addressing changing enrollment patterns and supporting high-quality educational programs through the provision of appropriately utilized, functional, and modern facilities

II. BACKGROUND

Montgomery County Public Schools (MCPS) is one of the largest school systems in the country, with an enrollment that is constantly changing. Montgomery County is increasingly diverse, creating a student population with varying educational needs. MCPS' success depends in part on appropriately utilized, functional, and modern facilities, as well as a facility planning process, based on rigorous analyses, that takes into account best educational practices, the changing needs of the community, and fiscal realities, to produce the physical learning environment necessary for an excellent educational system.

The components of long-range educational facilities planning include the following: facilities planning guidelines; the facility planning process; the Capital Improvements Program (CIP), and Educational Facilities Master Plan (Master Plan); community involvement processes; and the calendar for facilities planning activities.

III. DEFINITIONS

A. The *Capital Budget* is the annual budget adopted for capital project appropriations.

B. The *Capital Improvements Program (CIP)* is a comprehensive six-year spending plan for capital improvements. The CIP focuses on the acquisition, construction, revitalization/expansion, and maintenance of public school facilities. The CIP is reviewed and approved through a biennial process that takes effect for the six-year period that begins in each odd-numbered fiscal year. For even-numbered fiscal years, amendments are considered to the adopted CIP for changes needed in the second year of the six-year CIP period.

C. *Civic groups* are civic, homeowner, neighborhood, or citizen associations listed with the Maryland-National Capital Park and Planning Commission (M-NCPPC) or Montgomery Regional Service Centers.

D. *Cluster* is a geographic grouping of schools within a defined attendance area that includes a high school and the elementary and middle schools that send students to that high school.

E. *Community involvement,* for the purposes of Board Policy FAA, *Long-range Educational Facilities Planning,* and this regulation, refers to processes designed to obtain input by engaging a broad variety of stakeholders and to utilize opportunities for input from the public and relevant staff members, in accordance with Board Policy ABA, *Community Involvement*.

F. *Consortium* is a grouping of high schools or middle schools within proximity to one another that provides students the opportunity to express their preference for attending one of the schools based on a specific instructional program or emphasis.

G. *Facility Design* encompasses all the planning and design processes that lead up to construction of a school facility. In order of events, the milestones of facility design are:

1. Educational specifications—a description of spaces needed to support the instructional program and guide the architect in development of the building layout and design.

2. Feasibility study—determines the scope and estimated cost of a project, but does not develop a detailed design of the facility.

3. Schematic design—the initial design phase that evaluates and develops concepts into a preliminary design for the school. When it is complete, it is presented to the Board for approval.

4. Design development—this phase of design refines the architecture and develops the infrastructure of the project including mechanical, electrical, and plumbing systems.

5. Construction documents—provide the details of construction that are incorporated into the drawings and specifications for use as contract documents to construct the facility.

H. *Geographic Student Choice Assignment Plans* identify the geographic area(s) wherein students may express a preference for a school assignment, based on program offerings or emphasis. These geographic areas may include areas known as "base areas," where students may be guaranteed attendance at the school under certain criteria; or, the area may be a single unified area with no base areas for individual schools.

I. *Parent Teacher (Student) Associations (PT(S)As)* are member groups of the Montgomery County Council of Parent Teacher Associations, Inc. (MCCPTA). Also, in the absence of a PT(S)A, an organization of parents, teachers and (students) that operate at a school in lieu of a PT(S)A.

IV. FACILITIES PLANNING GUIDELINES

The following calculations and analyses are developed as part of the facilities planning process.

A. *Enrollment Forecasts* are the basis for evaluating school space needs and initiating planning activities.

1. Enrollment forecasts are developed in coordination with the Montgomery County Department of Planning's county population forecast and other relevant planning sources.

2. Each fall, enrollment forecasts for each school are developed for a six-year period. Long-term forecasts project enrollment to the subsequent 10th and 15th year. The units of analysis for long-term forecasts are secondary school level, and the cluster or consortium level for elementary schools.

3. On or about March 1, revisions to school enrollment forecasts for the next school year are developed to refine the forecast and to reflect any changes in service areas or programs.

4. The enrollment forecast methodology utilized is provided in an appendix to the CIP and Master Plan documents.

B *Preferred Range of Enrollment* for schools includes all students attending a school.

1. The preferred ranges of enrollment for schools are—

a) 450 to 750 students in elementary schools;

b) 750 to 1,200 students in middle schools; and

c) 1,600 to 2,400 students in high schools.

d) Enrollment in special and alternative program centers may differ from the above ranges and generally is lower.

2. The preferred range of enrollment is considered when planning new schools or when changes are made to existing schools. Departures from the preferred ranges may occur if circumstances warrant.

C. *School Demographic Profile* and *Facility Profile*

1. *School Demographic Profile* includes the racial/ethnic composition of a school's student population, the percentage of students participating in the Free and Reduced-price Meals System (FARMS) and English for Speakers of Other Languages (ESOL) programs, and school mobility rates.

2. *Facility Profile* includes room use by program and facility characteristics such as square footage, site size, year of opening, adjacency to parks, and number of relocatable classrooms.

D. *Program Capacity* refers to the number of students that can be accommodated in a facility based on the educational programs at the facility. The MCPS program capacity is calculated as the product of the number of teaching stations in a school and the student-to-classroom ratio for each grade and program in each classroom.

E. *Program Capacity* and *Facility Utilization* are calculated as follows:

1. Unless otherwise specified by Board action, the *program capacity* of a facility is determined by the space requirements of the educational

programs in the facility and student-to-classroom ratios. These ratios should not be confused with staffing ratios that are determined through the annual operating budget process.

Ratio Guidelines

Level	Student-to-Classroom Ratios
Head Start & prekindergarten	40:1 (2 sessions per day)
Head Start & prekindergarten	20:1 (1 session per day)
Grade K	22:1
Grade K-reduced class size	18:1
Grades 1-2—reduced class size	18:1
Grades 1-5 Elementary	23:1
Grades 6-12 Secondary Grades: 6-8 Middle School Grades: 9-12 High School	 25:1[a] 25:1[b]
Special Education, ESOL, Alternative Programs	See "c" below

a) Program capacity is adjusted at the middle school level to account for scheduling constraints. The regular classroom capacity of 25 is multiplied by .85 to reflect the optimal utilization of a middle school facility (equivalent to 21.25 students per classroom).

b) Program capacity is adjusted at the high school level to account for scheduling constraints. The regular classroom capacity of 25 is multiplied by .90 to reflect the optimal utilization of a high school facility (equivalent of 22.5 students per classroom).

c) Special education, ESOL, alternative programs, and other special programs may require classroom ratios different from those listed.

2. Unless otherwise specified by Board action, elementary, middle, and high schools should operate in an efficient facility utilization range of 80 to 100 percent of program capacity. If a school is projected to be underutilized (less than 80 percent) or overutilized (more than 100 percent), then a boundary study, noncapital action, or a capital project may be considered. Whether a school meets the preferred range of enrollment also is considered. In the case of overutilization, an effort to

judge the long-term need for permanent space is made prior to planning for new construction. Underutilization of facilities also is evaluated in the context of long-term enrollment forecasts.

3. Relocatable classrooms may be used on an interim basis to provide program space for enrollment growth until permanent capacity is available. Relocatable classrooms also may be used to enable child care programs to be housed in schools, and may be used to accommodate other complementary uses. Relocatable classrooms should have health and safety standards that are comparable to other MCPS classrooms.

F. *School Site Size* is the minimum acreage desired to accommodate the full instructional program, as follows:

1. Elementary schools——a minimum useable site size of 7.5 acres that is capable of fitting the instructional program, including site requirements. The 7.5 acres is based on an ideal leveled site, and the size may vary depending on site shapes and surrounding site constraints.

2. Middle schools——a minimum useable site size of 15.5 acres that is capable of fitting the instructional program, including site requirements. The 15.5 acres is based on an ideal leveled site, and the size may vary depending on site shapes and surrounding site constraints.

3. High schools——a minimum useable site size of 35 acres that is capable of fitting the instructional program, including site requirements. The 35 acres is based on an ideal leveled site, and the size may vary depending on site shapes and surrounding site constraints.

G. *State-rated Capacity (SRC)* is defined by the state of Maryland as the number of students who can be accommodated in a school, based on the product of state-determined student-to-classroom ratios and the number of teaching stations in a school. SRC is used by the state to determine state budget eligibility for capital projects funded through the Public School Construction Program administered by the Interagency Committee for Public School Construction. SRCs are provided for schools in appendices to the CIP and the Master Plan.

V. GUIDELINES FOR FACILITY PLANNING: EVALUATING UTILIZATION OF FACILITIES

A. By November 1 each year, after new enrollment forecasts are developed, the projected utilization levels of all facilities are evaluated and incorporated into the superintendent of schools' CIP recommendations. The effect of class size changes and other relevant factors, such as proposed educational program

changes, including prekindergarten programs, special education programs, ESOL programs, or grade level reorganizations also is evaluated. For schools that are projected to have insufficient capacity, excess capacity, or other facility issues, the superintendent of schools may recommend—

1. a capital project;

2. a noncapital action such as convening a roundtable discussion group, boundary change, geographic student choice assignment plan, school pairing, facility sharing, closing/consolidation, or any other similar action;

3. no action; or

4. deferral pending further study of enrollment or other factors.

B. Facility recommendations made by the superintendent of schools include consideration of educational program impacts. As part of the process of developing facility plans, MCPS staff members will work closely with appropriate program staff members to identify program requirements for facility plans. Modifications to the facility will adhere to the requirements of the *Americans with Disabilities Act*.

VI. CAPITAL IMPROVEMENTS PROGRAM AND EDUCATIONAL FACILITIES MASTER PLAN

A. CIP

1. On or about November 1 of each year, the superintendent of schools publishes recommendations for an annual Capital Budget and a six-year CIP or amendments to the previously adopted CIP. Boundary change or geographic student choice assignment plan recommendations, and any other facility planning recommendations identified by the superintendent of schools as requiring more time for public review, are released by mid-October.

2. The six-year CIP includes:

a) The following standards for Board review and action:

(1) Preferred range of school enrollments

(2) Program capacity and facility utilization calculations

(3) School site size

b) Background information on the enrollment forecasting methodology.

c) Current enrollment figures, school demographic profiles, and facility profiles.

d) School enrollment forecasts for each of the next six years and long-term forecasts for the 10th and 15th year.

e) A listing of recommended actions, such as changes in school capacities, new schools, revitalizations/expansions, program locations, and/or the service area of the schools. Supplements to the CIP may be published to provide more information on issues when deemed advisable by the superintendent of schools.

f) A line item summary of Capital Budget appropriation recommendations of the superintendent of schools.

3. The superintendent of schools' recommended CIP is posted on the MCPS website. Copies of the document are provided to Board members and Board staff, MCPS executive staff, and the MCCPTA president, area MCCPTA vice presidents, and cluster coordinators. In addition, notification of the CIP's publication and availability online is sent to principals, PTA leadership, municipalities, and civic groups. This notification includes the Board schedule for work sessions, public hearings, and action on the CIP.

4. The Board timeline for review and action on the CIP consists of a work session in early November, followed by a public hearing in mid-November, and action in mid- to late November of each year. (See Section IX.E. for the public hearing process and Section X for the annual calendar.)

5. The superintendent of schools' recommendations on any deferred planning issues and/or amendments to the CIP are made in mid-February. The Board timeline for these items consists of a work session in late February to early March, a public hearing in mid-March, and action in late March. If necessary, the timeline for deferred planning issues may be modified by the superintendent of schools to allow more time for community input processes.

6. In cases where the Board determines an unusual circumstance exists, the superintendent of schools may develop an alternative time schedule for making recommendations regarding the CIP, facility planning activities, school boundary changes, or geographic student choice assignment plans.

7. After review and Board action, the Board-requested CIP—including official Project Description Forms (PDFs) for all requested capital projects—is submitted to the County Council and county executive for their review and for County Council action. The Board-requested CIP also is sent for information purposes to M-NCPPC, the Maryland State Department of Education, and the State Interagency Coordinating Committee.

8. The county executive's recommendations are forwarded to the County Council in mid-January for inclusion in the overall county CIP. The County Council timeline for review and action on the Board-requested CIP is from February to May.

9. The County Council adopts the biennial six-year CIP, and amendments to the CIP, in late May.

B. Master Plan

By June 30 of each year, the superintendent of schools publishes a summary of all County Council-adopted capital and Board-adopted non-capital facilities actions. This document, the Educational Facilities Master Plan, is required under the rules and regulations of the State Public School Construction Program.

1. The Master Plan incorporates the projected impact of all capital projects approved for funding by the County Council and any non-capital facilities actions approved by the Board.

2. Similar to the CIP, the Master Plan includes the following:

   a) The following standards:

      (1) Preferred range of school enrollments

      (2) Program capacity and facility utilization calculations

      (3) School site size

b) Background information on the enrollment forecasting methodology.

c) Current enrollment figures, school demographic profiles, and facility profiles.

d) Program capacity and facility utilization calculations.

e) School enrollment forecasts for each of the next six years, and long-term forecasts for the 10th and 15th years. This information reflects projections made the previous fall with an updated one-year projection in the spring, and any changes in projected enrollment that result from boundary changes, geographic student choice assignment plans, or other changes adopted by the Board.

f) County Council-adopted PDFs for all capital projects with schedules, estimated costs, and funding sources.

VII. COMMUNITY INVOLVEMENT PROCESSES

A. Community Involvement

School and community involvement in MCPS facility planning is important to the success of the plans. Stakeholders and interested members of the community have several opportunities for input in facilities planning through processes that are in accordance with Board Policy ABA, *Community Involvement*.

1. Parents, staff, and students are the primary stakeholders in the planning process. MCCPTA, local PTAs, or other parent or student representatives along with appropriate MCPS staff members are involved in the following planning processes:

a) Site selection for new schools

b) Facility design (architect selection and architectural design) for new schools, additions, or revitalizations/expansions of existing schools

c) School boundary changes and geographic student choice assignment plans

d) Facility-related focus groups, task forces, work groups, advisory committees, and roundtable discussion groups

e) School closures and consolidations

2. Additionally, MCPS employees, municipalities, local government agencies, civic groups, and countywide organizations may contribute to planning processes.

B. Cluster Comments

1. In June, cluster representatives may submit to the superintendent of schools any facility-based concerns, priorities, or proposals that they have identified for their schools in consultation with local PTA leadership, principals, and the community.

2. Cluster comments are to be considered in the development of facilities recommendations made by the superintendent of schools in the CIP.

C. Community Involvement Methods

The superintendent of schools will solicit community input on school facility-related issues, including boundary changes and geographic student choice assignment plans, through any one or more of the following methods: focus groups, task forces, work groups, advisory committees, roundtable discussion groups, public forums, surveys, and/or technologically facilitated communications.

1. Focus groups, task forces, work groups, advisory committees (committees) or roundtable discussion groups (roundtables):

a) The superintendent of schools develops a charge for the focus group, task force, work group, advisory committee, or roundtable to follow:

(1) If the facility-related issue involves a boundary change or geographic student choice assignment plan, the superintendent of schools shall ensure that the potentially affected areas are represented on any focus group, task force, work group, advisory committee, or roundtable and that there are outreach efforts to promote racial, ethnic, and socioeconomic diversity within the group.

(2) If the facility-related issue involves site selection for a new school, the superintendent of schools shall ensure that civic groups with candidate sites in their area and appropriate municipal, county government, and Montgomery County Planning Department and Montgomery County Parks Department staff have an opportunity to participate.

b) Except as otherwise provided herein, the focus group, task force, work group, advisory committee or roundtable members identify criteria to assist staff in the development of approaches to address the facility-related issue. The superintendent of schools and the Board also will consider these criteria in their review of approaches to address the facility-related issue.

c) MCPS staff members will develop a range of approaches for the focus group, task force, work group, advisory committee, or roundtable to consider, with the number of approaches dependent on the nature of the facility-related issue. However, the total number of approaches developed for the group usually will not exceed 10.

d) Representatives, who are liaisons between the focus group, task force, work group, advisory committee, or roundtable, and the community they represent share relevant information with their community through PTA meetings, and other forums, such as civic group meetings, as appropriate. Input received from the community is then presented by representatives at subsequent meetings. Community input also is factored into evaluations of approaches by representatives and in optional PTA or cluster position papers.

e) The focus group, task force, work group, advisory committee or roundtable develops a report for the superintendent of schools that includes evaluations of the approaches by members. For selection of a new school site, members will identify the most favorably scored site and the second most favorably scored site based on the evaluation criteria. In addition, as appropriate, the superintendent of schools will consider any individual PTA or cluster position papers. Unless otherwise provided herein, the criteria developed at the outset of the process are the basis for assessing the approaches.

2. Public forums, surveys, and technologically facilitated communications

a) At any point in the process the superintendent of schools may direct MCPS staff and/or any facility-related focus group, task force, work group, advisory committee, or roundtable to use a public forum, survey, or technologically facilitated communication to obtain community input in conjunction with or in lieu of other methods for community input.

b) If the facility-related issue involves a boundary change or geographic student choice assignment plan, the superintendent of schools shall ensure that the potentially affected areas are notified of the public forum, survey, or technologically facilitated communication and have an opportunity to participate.

c) If the facility-related issue involves site selection for a new school, the superintendent of schools shall notify civic groups with candidate sites in their area; and appropriate municipal, county government, and Montgomery County Planning Department and Montgomery County Parks Department staff and provide an opportunity to participate.

VIII. SPECIFIC EVALUATION CRITERIA

A. School Boundary Changes and Geographic Student Choice Assignment Plans

The following factors are considered when evaluating changes to school boundaries and in geographic student choice assignment plans:

1. Facility Utilization

a) School boundary and geographic student choice assignment plans should result in facility utilizations in the 80 percent to 100 percent efficient range whenever possible.

b) Plans should be fiscally responsible to minimize capital and operating costs whenever feasible. The geographic scope of the studies should be broad enough to realize economies in costs and provide long-range plans to address facility issues while preserving as much stability in school assignments as possible.

c) Shared use of a facility by more than one cluster may be the most feasible facility plan in some cases. In these cases, it is desirable for 25 percent or more of articulating enrollment to move on to each of the assigned upper-level schools.

2. Demographic Characteristics of Student Population

a) School boundary and geographic student choice assignment plans should consider the impact of various options on the overall populations of affected schools. A school population consists of students assigned from a specific geographic attendance area.

b) Where reasonable, school boundaries or geographic student choice assignment plans should promote the creation of a diverse student body in each of the affected schools. Data showing the impact of various options include the following factors:

(i) The racial/ethnic composition of the student population

(ii) The socioeconomic composition of the student population as measured by participation in the federal FARMS program

(iii) The level of English language learners as measured by enrollment in the ESOL program

(iv) Other reliable demographic indicators, such as the mix of single family and multiple family dwellings, student mobility rates, and special education participation also may be considered where applicable and appropriate

3. Geographic Proximity of Communities to Schools

a) In most cases, the geographic scope of elementary school and middle school boundary studies and geographic student choice assignment plan studies should be limited to the high school cluster area. For high schools, more than one high school may be studied.

b) In accordance with MCPS' emphasis on community involvement in schools, boundary and student choice area plans should give consideration to the creation of service areas that are, as much as practical, made up of contiguous communities surrounding the school. Walking access to the school should be maximized and transportation distances minimized when other factors do not require otherwise.

4. Stability of School Assignments over Time

a) Boundaries and student choice assignment plans should result in stable assignments for as long a period as possible.

b) Student reassignments should consider recent boundary or geographic student choice assignment plan changes, and/or school closings and consolidations that may have affected the same students.

B. Selection of Sites for New Schools

When MCPS projections indicate a new school is required in the six-year CIP, the following factors are considered when evaluating potential new school sites, including those acquired through dedication or purchase and placed in the Board's inventory:

1. The geographic location relative to existing and future student populations and existing schools

2. Size in acreage

3. Topography and other environmental characteristics

4. Availability of utilities

5. Physical condition

6. Availability and timing to acquire

7. Cost to acquire if private property

C. Architect Selection and Facility Design

The following factors are considered when selecting an architect and evaluating facility design for classroom additions, revitalization/expansion for existing schools, and new school construction:

1. Educational specifications for school buildings as developed by MCPS staff members in consultation with instructional program staff and school-based administrators

2. Input from school administrators, school staff, and PTA representatives in selection of an architect

3. Input from adjacent property owners, if any

D. School Closures and Consolidations

The requirements of Maryland law are followed when evaluating school closures and consolidations.

IX. SUPERINTENDENT OF SCHOOLS RECOMMENDATION AND BOARD ACTION

A. The superintendent of schools develops recommendations on the six-year CIP after considering staff advice, any input from PTA cluster position papers or comments, task forces, work groups, advisory committees, roundtable reports, option or approach evaluations, public forums, surveys, and/or input from other organizations and individuals through avenues of community input.

B. The recommendations of the superintendent of schools are published no later than November 1, depending on the nature of the facility issues. Some recommendations may be published in mid-October or mid-February when necessary depending on the nature of the facility issues. In addition, recommendations may be made at other times of the year if the Board determines that an unusual circumstance exists that warrants a condensed schedule for recommendations and Board review and action.

C. Recommendations of the superintendent of schools are posted to the MCPS website, and affected school principals and PTAs are notified of their availability and the process for Board review and action.

D. The Board holds a work session to review the superintendent of schools' recommendations. The Board may request by majority vote that alternatives to the superintendent of schools' recommendation for boundary changes,

geographic student choice assignment plans, or closures or consolidations of schools be developed for Board consideration. Any significant modification to the superintendent of schools' recommendation requires an alternative supported by a majority of Board members. Any modification that impacts any or all of a school community that has not previously been included in the superintendent of schools' recommendation should be considered a significant modification.

1. Recommendations from the superintendent of schools and Board-requested alternatives are subject to a public hearing prior to final Board action.

2. The Board has the discretion to adopt minor modifications to the superintendent of schools' recommendation or Board-requested alternative(s) if this action will not have a significant impact on a plan that has received public review. Alternatives will not be considered after the Board work session without adequate notification and opportunity for comment by the affected communities.

E. Board Public Hearing Process

1. Public hearings are conducted annually following publication of the superintendent of schools' CIP recommendations. In addition, public hearings are conducted prior to actions affecting school boundaries, geographic student choice assignment plans, and closure or consolidation of schools.

   a) Public hearings are conducted in November following publication of the superintendent of schools' recommended Capital Budget and six-year CIP.

   b) Public hearings also may be conducted in March for any superintendent of schools' recommendations not previously subject to public hearings.

   c) Public hearings also may be conducted at other times during the year if the Board determines an unusual circumstance exists and the superintendent of schools has developed a different and/or condensed schedule for making recommendations.

   d) The PTA cluster coordinators and/or PTA area vice presidents in consultation with the PTA presidents coordinate testimony at the hearing on behalf of cluster schools and are encouraged to present a variety of opinions when scheduling testimony. Testimony time

for each cluster is scheduled and organized by the PTA organizational units ("quad-clusters") and/or consortium whenever possible.

e) Civic groups, municipalities, and countywide organizations also may testify at public hearings.

f) Individuals also may present public comments to the Board.

g) The Board office is responsible for scheduling those interested in testifying at public hearings.

2. In addition to other avenues of input, community members have opportunities to provide input to the superintendent of schools and the Board through written correspondence and public testimony. Written comments from the community are accepted at any point but, in order to be considered, comments must reach the Board at least 48 hours before action is scheduled by the Board.

X. CALENDAR

The long-range facilities planning process is conducted according to the county's biennial CIP process and adheres to the following calendar adjusted annually to account for holidays and other anomalies.

MCPS staff members meet with MCCPTA, area vice presidents, cluster coordinators, and PTA representatives to exchange information about the adopted CIP and consider issues for the upcoming CIP or amendments to the CIP.	Summer
MCPS staff members present enrollment trends and planning issues to the Board.	Mid-October
County Council adopts Spending Affordability Guidelines for the new CIP cycle, based on debt affordability.	Early-October of odd numbered fiscal years
Superintendent of schools publishes and sends to the Board any recommendations for school boundary, geographic student choice assignment plans, or other facility-related issues requiring more time for public review.	Mid-October
Superintendent of schools publishes and sends to the Board recommendations for the annual Capital Budget and the six-year CIP or amendments to the CIP.	By November 1

Board holds a work session on the CIP and to consider alternatives to superintendent of schools' recommended boundary changes, geographic student choice assignment plans, or other facility-related issues.	Early-November
Board holds a public hearing on the recommended CIP and boundary, geographic student choice assignment plans, and other facility-related recommendations and any alternatives identified by the Board at its work session.	Mid-November
Board acts on Capital Budget, CIP, amendments, and any boundary changes, geographic student choice assignment plans, or other facility-related issues.	Late November
County executive and County Council receive Board-requested capital budget and CIP for review.	December 1
County executive transmits recommended Capital Budget and CIP or amendments to County Council.	January 15
County Council holds public hearings on CIP.	February - March
County Council reviews Board requested and county executive recommended Capital Budget and CIP.	March - April
Superintendent of schools' recommendations on any deferred planning issues, boundary changes, geographic student choice assignment plans, and other facility-related issues, and/or recommended amendment(s) to the CIP are published for Board review, if needed.	Mid-February*
Board holds work session and identifies any alternatives to boundary changes, or geographic student choice assignment plans, or other facility-related recommendations, if needed.	Late-February/ early-March*
Board holds public hearing if needed.	Mid-March*
Board acts on deferred CIP recommendations and/or boundary changes, geographic student choice assignment plans or other facility-related issues, if needed.	Late-March*
County Council approves six-year Capital Budget and CIP.	Late-May
Cluster PTA representatives submit comments to the superintendent of schools about issues affecting their schools for the upcoming CIP or amendments to the CIP.	June
Superintendent of schools publishes a summary of all actions to date affecting schools (Educational Facilities Master Plan) and identifies future needs.	By June 30

*If necessary the timeline for deferred planning issues may be modified to allow more time for community input processes.

Regulation History: Interim Regulation, June 1, 2005; revised March 21, 2006; revised October 17, 2006; revised June 8, 2008; revised June 6, 2015.

Appendix U

POLICY BOARD OF EDUCATION OF MONTGOMERY COUNTY

Related Entries: ABA-RA, ABA-EA, ABC, ACA, BMA, IOD, IOD-RA
Responsible Office: Chief Engagement and Partnership Officer

Community Involvement

A. PURPOSE

The Montgomery County Board of Education (Board) is committed to fostering and supporting community interest and involvement in Montgomery County Public Schools (MCPS), because citizen support of the schools is essential to student success. The Board will ensure that the ideas, interests, and concerns of its stakeholders are considered and valued in decision-making processes and that input and involvement is sought and encouraged from a broad spectrum of our diverse community. The Board is committed to the maintenance and monitoring of ongoing collaborative and productive communication processes with the community.

B. ISSUE

Creating processes for community involvement in a large, diverse community such as Montgomery County presents challenges and opportunities. Ensuring that the members of the community are encouraged, supported, and recruited to contribute time, knowledge, skills, and ideas to the public school system is both challenging and essential. Commitment and resources are required to design, maintain, and monitor processes for productive collaboration and communication between MCPS and the community. These processes must create an environment where diverse views may be heard and considered in an atmosphere of respect.

C. DEFINITIONS

1. *Community Involvement* seeks to ensure that the breadth of interests and values from across the community are heard and considered by the Board , superintendent of schools, principals, and other educational leaders, thereby enhancing the decision-making process.

2. *Community* is comprised of numerous constituents with a vested interest in the education of children. Some of these constituents may include, but are not limited to, Montgomery County residents, advocacy, nonprofit, parent or community-based organizations; business, civic and nongovernment organizations; local postsecondary educational institutions; state, local, and federal agencies; and cultural, ethnic, racial, and religious groups.

D. POSITION

1. As part of its responsibility as a community member, the Board will:

   a. Develop its role as an advocate, using the best interest of the students as a guiding principle

   b. Engage community members in building an organizational culture of respect

   c. Establish processes designed to obtain input by engaging in a discussion among a broad variety of stakeholders and utilizing opportunities for input from the public and relevant staff members through any appropriate method such as, but not limited to:

      (1) Focus groups
      (2) Task forces
      (3) Work groups
      (4) Technologically facilitated communication
      (5) Advisory groups
      (6) Public forums
      (7) Surveys

   d. Solicit and consider community comments and concerns regarding the development of MCPS policies and other decisions

   e. Seek to engage members of our diverse community, particularly organizations representing new or traditionally underrepresented communities, in a committed, productive partnership to support the MCPS strategic plan

   f. Advocate for the MCPS student population and their families through engagement with local, state, and federal government agencies

2. As part of its responsibility as a community member, the school system offices will:

a. Integrate resources and services from the community to strengthen school programs, family practices, and student learning and development

b. Seek collaboration with a broad range of community members and organizations that reflect the diverse citizenry and interests of Montgomery County

c. Seek and support the involvement of local organizations, particularly organizations representing new or traditionally underrepresented communities, in the school system

d. Provide access and opportunity for broad segments of the community, representing the wide variety of interests within the community, to participate in decision-making processes

e. Provide, to the extent possible, interpretation services and translations of important information about school system programs, services, policies, or issues

3. As part of its responsibility as a community member, each school will:

a. Seek involvement from the community and provide opportunities to strengthen the home/school connection

b. Establish and maintain regular and ongoing two-way communication with families and the community to provide information and solicit feedback about school progress, resources, policies, and issues

c. Provide, to the extent possible, information in the native languages of members of the school community

d. Access community services to support and foster academic achievement and positive development for all students

e. Participate actively and responsibly in the life and social fabric of the local community

E. DESIRED OUTCOME

There will be an actively engaged community that is reflective of all residents. The system will benefit from the community's contribution of its skills, knowledge, ideas, and time to support the success of all students in partnership with MCPS.

F. IMPLEMENTATION STRATEGIES

1. The superintendent of schools will assess the status of community involvement, review existing policies and procedures, revise necessary regulations and procedures to support this policy, and make periodic reports to the Board regarding the status of community involvement.

2. The Board will seek community input on school system policies, including curriculum, facilities, and funding issues from a broad spectrum of our culturally and linguistically diverse community.

G. REVIEW AND REPORTING

This policy will be reviewed in accordance with the Board policy review process.

Policy History: Adopted by Resolution No. 287-74, May 28, 1974; amended by Resolution No. 268-76, May 11, 1976; amended by Resolution No. 346-06, July 18, 2006; amended by Resolution No. 327-13, June 13, 2013.

Appendix V

POLICY BOARD OF EDUCATION OF MONTGOMERY COUNTY

Related Entries: FAA, FAA-RA
Responsible Office: Chief Operating Officer
Facilities Management

Sustaining and Modernizing Montgomery County Public Schools (MCPS) Facilities

A. PURPOSE

To affirm the Board of Education's (Board) commitment to maintain all school facilities in conditions that maximize learning opportunities for every student in the county. Sustaining Montgomery County Public Schools (MCPS) facilities is accomplished by pursuing systematic maintenance programs that renew facilities on a life cycle replacement basis. Modernizing MCPS facilities is accomplished by pursuing the systematic assessment of older facilities that have reached the end of their useful lifecycle, and placing these schools in a queue for modernization based on their relative condition.

To establish a systematic approach for replacement of building systems and facilities for MCPS. The approach is intended to address changing educational program standards and aging of building systems at reasonable cost while providing appropriate spaces for educational programs and services and maintaining a safe, secure, and healthy physical environment for students and staff.

Many schools were built in the decades between 1950 and 1980. Since that time many code requirements have changed and construction methods have been improved, resulting in facilities that are capable of being sustained in good condition over a longer period of time than was the case with older school facilities. A rigorous maintenance program for well-built schools is critical to ensuring that the substantial taxpayer investment in school infrastructure is preserved. This policy recognizes that maintenance and systemic replacement activities need to serve as the primary means for keeping all schools in good condition over the extended life of a facility. At the same time, the policy recognizes that at some point the useful life-cycle of a facility has been reached and major modernization is necessary.

B. ISSUE

School facilities, building systems, and equipment all require various and continuing levels of attention to achieve their expected life-cycle. MCPS views facility maintenance as being on a continuum ranging from routine repairs to replacement of building systems to complete modernization of facilities.

The Board of Education (Board) should determine when funds will be spent on school facilities:

a) To sustain facilities through routine maintenance of building systems.

b) To replace building systems on a systematic schedule based on the anticipated life-cycle of these systems.

c) To modernize facilities in accordance with an established queue when overall physical limitations of the facility can no longer support the educational program or comply with applicable building codes and regulations.

C. POSITION

The pursuit of the systematic life-cycle replacement of building systems and facilities will:

1. Enable school facilities to remain in good condition for a long period of time through the coordinated scheduling of building system repairs and replacements. These activities are based on routine maintenance protocols and anticipated life expectancies of various building systems. Examples of the buildings systems that lend themselves to replacement include heating, ventilation and air conditioning systems (HVAC) and mechanical systems, roofs, restrooms, information technology systems, safe access to schools, and school security systems. In addition numerous other building systems, covered under the Planned Life-cycle Asset Replacement (PLAR) and Building Modifications with Program Improvements (BMPI) capital programs, lend themselves to replacement.

2. Allow the Board to dedicate appropriate levels of funding for systemic projects that ensure all MCPS facilities stay in good condition.

3. Allow the Board to dedicate appropriate levels of funding to complete modernization of school facilities on an established queue when overall physical limitations of the facility can no longer support the educational program or current building codes.

4. Determine when a facility needs to be modernized based on the ability of systemic projects to sustain the facility in good condition. If it is determined that systemic maintenance is no longer viable for a school, then it will be added to the next group of schools to be assessed for modernization using the Facilities Assessment with Criteria and Testing methodology.

5. Maintain all school facilities at consistently high operational levels and maximize the life-span of existing physical plant asset.

D. DESIRED OUTCOME

In order to support its educational programs, MCPS will sustain the life of MCPS facilities through a balanced approach of maintaining and replacing building systems, while also providing for modernization or replacement of facilities when physical limitations of a facility can no longer support the educational program. MCPS will provide sufficient holding facilities so as to allow modernization of facilities to be scheduled.

E. REVIEW AND REPORTING

The *Educational Facilities Master Plan* will constitute the official reporting on the annual funding of systematic life-cycle replacement of building systems and facilities. This document will reflect facilities actions taken by the Board, and funds approved by the County Council for systemic capital projects needed to sustain schools in good condition.

This policy will be reviewed in accordance with the Board of Education's policy review process.

Policy History: Adopted by Resolution No. 835-91, October 8, 1991; amended by Resolution No. 571-10, December 7, 2010.

Appendix W

POLICY BOARD OF EDUCATION OF MONTGOMERY COUNTY

Related Entries: JEE-RA
Responsible Office: Chief Operating Officer

Student Transfers

A. PURPOSE

To explain the limited circumstances under which students may be granted a transfer to attend a school other than their home school or the school assigned in accordance with their Individualized Education Program (IEP)

B. ISSUE

Students are expected to attend the school within the established area in which they reside (home school) or assigned in accordance with their IEP. Transfers from the home school or the school assigned through the IEP process may be permitted in cases of documented unique hardship.

C. POSITION

1. Transfers should be honored whenever there is a documented unique hardship circumstance. Problems that are common to large numbers of families do not constitute a unique hardship.

2. Exemptions

   The following circumstances are exempted from the student transfer process:

   a) An older sibling attends the requested school in the regular program. If the older sibling attends a magnet or special program, an exemption may be granted on a case-by-case basis, with consideration given to space needs or limitations at the requested school.

   b) Continuation at the articulation point from middle school to high school

   c) Students have met the criteria for and been admitted to countywide programs

3. A student who transfers to another school without a change in residence of his/her parents or legal guardian shall attend the new school for one calendar year in order to be able to participate in athletics. A waiver from this restriction may be requested.

4. Parents either accepting a hardship transfer or receiving an approved exemption under 2 a) or b) assume responsibility for transportation, and recognize that student parking is regulated on a school by school basis.

D. DESIRED OUTCOMES

To maintain the stability of school attendance boundaries by promoting home school attendance and respecting the space needs or limitations of the individual schools.

E. IMPLEMENTATION STRATEGIES

This policy is implemented through administrative regulation.

F. REVIEW AND REPORTING

This policy will be reviewed on an ongoing basis in accordance with the Board of Education policy review process.

Policy History: Resolution No. 288-72, April 11, 1972, amended by Resolution No. 825-72, December 12, 1972, reformatted in accordance with Resolution No. 333-86, June 12, 1986 and Resolution No. 458-86, August 12, 1986, accepted by Resolution No. 517-86, September 22, 1986; reviewed February, 1995; amended by Resolution No. 92-02, March 12, 2002; non-substantive modification, November 16, 2006.

REGULATION MONTGOMERY COUNTY PUBLIC SCHOOLS

Related Entries: ACD, JEE, FAA
Responsible Office: Chief Operating Officer
Deputy Superintendent of Teaching, Learning, and Programs

Transfer of Students

I. PURPOSE

To establish procedures concerning the within-county transfer of students

II. BACKGROUND

Students are expected to attend the school within the established attendance area in which they reside or are assigned in accordance with an Individualized Education Program (IEP). A request for a student to attend a school outside such attendance area may be initiated by the parent/guardian/eligible student (18 years of age or older), student services staff, or the principal.

III. DEFINITIONS

A. The *home school* is the school to which a student is assigned based upon the Montgomery County Board of Education (Board) geographical boundary decision. Should the student be reassigned through the transfer process, he or she may elect at any time to return to the home school.

B. The *assigned school* is the school to which the student has been assigned for a given school year. This is the home school in the absence of an approved Change of School Assignment (COSA). When a student is granted a COSA, the requested school becomes the assigned school.

IV. PROCEDURES

A. Only documented unique hardship situations will be considered for a COSA.

B. Exemptions

1. Except for a boundary change, an older sibling attending the requested school at the same time in the regular program.

2. The student is ready to move from middle school to high school, except for a boundary change.

3. The student has met the criteria for and been admitted to and attends a countywide program.

C. Timetables and Deadlines

1. COSA requests for the next school year will be accepted only between February 1 and April 1 for the following school year.

2. Every effort will be made to notify parents and students of the decision on their COSA request in May.

3. Some programs, such as elementary language immersion programs, may be based on attendance area, or admit students by lottery when there are more requests than available spaces.

4. COSA requests submitted after April 1 will not be accepted unless the student is a new resident of Montgomery County or there is a bona fide emergency or event that could not have been foreseen prior to April 1. Documentation supporting this situation must be supplied. Students must enroll in and attend their home school while a COSA request is being processed.

D. Process for COSA

1. General

a) Paired elementary schools are considered one school for COSA purposes. However, when a student on an approved COSA matriculates from the primary grades to the upper grades, a new form must be submitted. Each pairing has unique characteristics that can impact implementation of transfers.

b) High school students who receive an approved COSA are ineligible for athletic participation for one calendar year. A waiver may be

requested in writing from the director of Systemwide Athletics explaining the reason for the COSA.

c) Middle school students on an approved COSA, who wish to remain in that pattern for high school, will be required to reapply for a COSA at the end of middle school. The exemption will be approved and the athletic ineligibility will be waived.

d) Elementary school students on an approved COSA must reapply and meet the criteria in order to attend a middle school other than that serving their residence.

e) In unique circumstances, COSAs may be granted for one year only. Parents/guardians must reapply for a COSA or students must return to their home school for the next school year.

f) Students whose families have moved within the county who wish to continue attending their former home school should request a COSA from the school serving their new neighborhood to the school they have been attending. Such requests will be given preference for the remainder of the current school year only. Continuation in feeder pattern does not apply. Students in Grades 11 or 12 are exempt from this restriction and will be allowed to stay through graduation.

g) COSA or exemption requests for younger siblings of students, including step brothers and sisters and half brothers and sisters, for whom COSAs have been approved, will be approved for a COSA, absent a boundary change, provided that the older sibling still will be attending the requested school in the regular program.

h) COSA requests after an extended suspension will be addressed by staff in the Division of Pupil Personnel Services (DPPS) in consultation with the school principals involved. School changes for this reason are not generally approved.

i) Students who have been given permission to attend schools other than assigned may, with proper cause, such as poor attendance or behavior, have that permission rescinded. In addition, students whose COSAs were approved because they were attending a special/exempt program must return to their home school if they leave that program.

2. Initiated by Parent/Guardian/Eligible Student (18 years of age or older)

   a) If a COSA is desired, MCPS Form 335-45: *Request for Change of School Assignment* (COSA), must be obtained from the principal of the home school.

   b) This completed form must be submitted to the principal of the student's home school by the deadline. The principal's signature signifies verification of residency and knowledge of the request, but does not constitute agreement or disagreement with the request.

   c) Students receiving special education services available in all schools follow the regular COSA process. Students receiving all other special education services should *not* use the COSA form, but should submit their request in writing to the Department of Special Education Services at 850 Hungerford Drive, Room 230, Rockville, Maryland 20850.

   d) The COSA may be approved or denied after considering the reason(s) for the COSA and, for students receiving special education services, whether the IEP can be implemented, considering staffing and services available at the requested school.

   e) Parents accepting an approved COSA or exemption assume responsibility for transportation.

   f) The parent/guardian will receive written notification of approval or disapproval of a COSA or exemption request from DPPS. The student must enroll in and attend the home school while the appeal of a denial is in process. The home and requested schools will be notified that the request has been approved or denied.

3. Initiated by the Principal

   a) Prior to initiating a request for an administrative change of assignment of a student, the principal and the pupil personnel worker assigned to the student's home school will:

      (1) Review the student's educational, medical, and behavioral record and consider alternative programs

(2) Schedule a conference with the parent/guardian and the student

b) If a COSA is indicated, the following steps are implemented:

(1) After consulting with the principal and the appropriate associate superintendent as to the reason(s) for the COSA, the director of DPPS will identify an appropriate school placement for the student.

(2) The pupil personnel worker will arrange any necessary conferences with the parent/guardian, student, principal of the receiving school, and Department of Student Services staff, as well as supply written confirmation of the placement, athletic eligibility, and athletic waiver process.

c) Department of Student Services staff members are responsible for monitoring the academic progress and social adjustment of the student whose COSA was initiated by the principal.

4. Initiated by the Department of Student Services

A COSA may be initiated by Department of Student Services staff, in concert with the parent/guardian and the home school's staff, at any time for special circumstances. The approval or denial of Department of Student Services initiated COSAs is the responsibility of the director of DPPS.

a) Students transferred and assigned under this provision [IV.D.4.a] based on their behavior that raised concerns about the health and/or safety of others in the school setting must attend the assigned school for one calendar year in order to be eligible to participate in athletics. Parents may request a waiver by writing to the director of Systemwide Athletics, explaining the reason for the COSA.

b) Students transferred and assigned under this provision [IV.D.4.b] based on concerns about their health and/or safety in the school setting must attend the assigned school for one calendar year in order to be eligible to participate in athletics. Parents may request a waiver by writing to the director of Systemwide Athletics, explaining the reason for the COSA. In these cases, a waiver will be granted.

E. Appeals

1. Superintendent of Schools

If a COSA is denied by the director of DPPS, the parent/guardian may appeal the decision to the superintendent of schools. Appeals must be made in writing and must be received by the Office of the Chief Operating Officer (the chief operating officer serves as the superintendent of schools' designee) within 15 calendar days of the date of the decision letter. The appeal should state the reason(s) for seeking review of the decision. It is not necessary to provide additional information in order to appeal, but the appellant should include any additional information in order for it to be considered. The superintendent of schools, or the chief operating officer as his/her designee, will review all available information before issuing a decision. Although the matter is usually considered on the basis of the documents and telephone conferences, personal conferences may be arranged by the chief operating officer's hearing officer. Decisions will be made promptly given the number, complexity, and timing of appeals being handled at the same time. Appeals received by the chief operating officer before June 30 will be decided prior to the beginning of school.

2. Board of Education

An appeal of the decision of the superintendent of schools or his/her designee must be made in writing and received by the Board within 30 calendar days of the date on the superintendent of schools' decision letter. Appellants are strongly encouraged to note any appeal as soon as possible. The superintendent of schools will be given the opportunity to respond, with a copy sent to the appellant, before the Board considers the appeal. The Board's decision will be rendered in writing.

Regulation History: Formerly Regulation 265-2, February 22, 1980, revised January 23, 1992, revised April 25, 1994; revised December 23, 1994; revised December 30, 1997; revised July 20, 1998; revised December 2, 1999; updated office titles June 1, 2000; revised December 6, 2000; revised January 7, 2002; revised January 10, 2003; revised November 29, 2006; non-substantive revision, November 27, 2007; non-substantive revision, November 17, 2008; revised January 04, 2010; revised November 18, 2010; revised .December 12, 2011; revised December 20, 2012; revised November 6, 2013; revised December 13, 2013.

Appendix X

POLICY BOARD OF EDUCATION OF MONTGOMERY COUNTY

Related Entries: EEA-RA, EBH-RA, JEE, JEE-RA, JFA-RA, KLA

Related Sources: *Annotated Code of Maryland, Education Article, §3-903(c); Code of Maryland Regulations* §13A.06.07.09 *Instructional Content Requirements*; *Montgomery County Code,* Article II, §44-7 *Denominational and parochial school students entitled to transportation;* and *Montgomery County Code,* Article II, §44-8, *Cost of transportation of students; levy and appropriation; charge to students.*

Responsible Office: Chief Operating Officer
Department of Transportation

Student Transportation

A. PURPOSE

To establish safe, responsive, and accountable operation of the Montgomery County Public Schools (MCPS) student transportation system, in partnership with parents and students, and to delineate the services provided.

B. ISSUE

MCPS is authorized by the regulations of the State of Maryland to provide safe and efficient transportation to the students residing within Montgomery County. The Montgomery County Board of Education is responsible for establishing the operational expectations and eligibility criteria for its student transportation services. It is the responsibility of the Montgomery County Board of Education to work with other agencies when needed and to consider the safety of students when designing school site plans including pedestrian and vehicular traffic patterns; assessing routes for walking to and from school and school bus stops; and, establishing bus routes and locations of school bus stops.

C. POSITION

1. Eligibility for Transportation

    a) The Board of Education adopted attendance areas for each school are the basis upon which transported areas are defined. Students attending their home school who reside beyond the distances defined below will receive transportation services.

(1) Transported areas surrounding MCPS schools are as follows:

Elementary Schools—beyond 1 mile
Middle Schools—beyond 1.5 miles
High Schools—beyond 2.0 miles

(2) The superintendent of schools is authorized to extend these distances by one-tenth of a mile to establish a reasonable line of demarcation between transported and non-transported areas.

(3) Transportation may be provided for distances less than that authorized by Board policy if a condition is considered hazardous to the safety of students walking to or from school, or to establish a reasonable boundary consistent with the safety criteria outlined in C.2.

b) The Board of Education may establish transportation services for certain consortia schools, magnet, gifted and talented, International Baccalaureate, language immersion, alternative, or other programs based on the purposes of the programs, attendance areas, and available funding.

c) Enhanced levels of transportation services will be provided to those students, such as special education students, who meet the eligibility requirements of federal and state laws. Commercial carriers may be used to provide required services.

d) Students who attend denominational and parochial schools may be transported as specified under provisions of the Montgomery County Code. This service will be provided only on a space-available basis along established bus routes designed to serve public schools in keeping with the terms and conditions as set forth in this policy.

e) Under special circumstances, students may ride established bus routes across attendance boundaries for valid educational reasons.

f) Mixed grade/age level student loads are permitted.

g) Every effort is made to balance ride times and resources.

h) Buses may be used for educationally valuable purposes other than transporting students to and from the regular school day, such as field trips, extracurricular events, interscholastic sports, and outdoor education or

academic programs. Unless otherwise approved by the superintendent or his or her designee, use of MCPS buses is limited to MCPS and other governmental agencies. MCPS will establish criteria and rates for the use of MCPS transportation services for purposes other than transporting students to and from school on the regular school day.

i) In exigent circumstances, the superintendent may apply to the Board of Education for a waiver to temporarily adjust transported distances. Board action on the waiver request can be taken after allowing at least 21 days for public comment following publication of the waiver request. If the Board deems an emergency exists, this notification provision may be waived without notice if all Board members are present and there is unanimous agreement.

2. Student Safety

a) MCPS is responsible for routing buses in a manner that maximizes safety and efficiency.

b) MCPS buses will not cross a main line railroad at grade crossing while in Montgomery County.

c) MCPS is responsible for designing traffic control patterns for new and renovated schools prior to the completion of construction. MCPS will assess the safety of proposed traffic control patterns taking into consideration safe approaches by pedestrians, bicyclists, and motorists.

d) MCPS is responsible for conducting safety evaluations of bus stops and recommended walking routes. The following criteria will apply to students walking to schools or school bus stops:

(1) Students are expected to walk in residential areas along and across streets, with or without sidewalks.

(2) Students are expected to walk along primary roadways with sidewalks or shoulders of sufficient width to allow walking off the main road.

(3) Middle and high school students are expected to cross all controlled intersections where traffic signals, lined crosswalks, or other traffic control devices are available.

(4) Elementary school students may be required to cross primary roadways where an adult crossing guard is present.

(5) Elementary and middle school students are not expected to cross mainline railroad tracks unless a pedestrian underpass, overpass or adult crossing guard is present.

(6) Students are expected to walk along public or private pathways or other pedestrian routes.

e) MCPS will follow an effective process for handling and investigating accidents so that injured students and staff are cared for promptly, further injury is prevented, and correct and timely information is disseminated to all necessary parties.

f) Student safety, security, and comfort depend on appropriate behavior on MCPS buses identical to that expected of students in school. The Board of Education affirms that, while riding the bus, students are on school property, and disciplinary infractions are handled in accordance with Regulation JFA-RA: *Student Rights and Responsibilities* and other related policies and regulations.

3. Community Partnerships

a) MCPS will encourage a partnership of students, parents, and school staff to teach and enforce safe transportation practices.

(1) MCPS will implement a systemwide outreach and education program to teach safe walking practices en route to and from school, encourage safe bus-riding behavior, and reinforce appropriate student conduct while riding the bus.

(2) School staffs will encourage parents to teach their students safe walking practices en route to and from school.

(3) Bus operators and attendants are responsible for maintaining safe conditions for students boarding, riding, and exiting the bus. MCPS will provide preservice and in-service instruction to bus operators and attendants, consistent with COMAR 13A.06.07.09.

(4) Parents will be responsible for their child's safety along their walking route and at the bus stop. While waiting at bus stops, students should

observe safe practices, respect persons and private property, and stand well off the traveled portion of the road.

b) Principals and the leadership of PTAs or parent teacher organizations at special programs located at special centers that operate in lieu of nationally affiliated PTAs will be notified in advance of routing changes that involve reductions of service, as described in Regulation EEA-RA.

4. Identification and Resolution of Transportation and Safety Issues

Members of the public are encouraged to address inquiries, concerns, or complaints regarding student transportation as set forth in Policy KLA: *Responding to Inquiries and Complaints from the Public.* Complaints not resolved through the cluster transportation supervisor or other department staff, including the director of transportation may be appealed to the chief operating officer who will render a decision on behalf of the superintendent of schools, advising the appellant of the right to further appeal to the Board of Education consistent with the Education Article, *Annotated Code of Maryland*, Section 3-903(c).

5. Environmental and Economic Considerations

MCPS will balance environmental and economic factors when operating and maintaining its vehicles.

D. DESIRED OUTCOME

MCPS will have an efficient system of student transportation that provides an appropriate means of travel to and from school, is responsive to community input, and, in partnership with parents and students, coordinates effective community participation in the safe movement of students on a daily basis.

E. IMPLEMENTATION STRATEGIES

The superintendent will develop regulations to implement this policy as needed.

F. REVIEW AND REPORTING

This policy will be reviewed on an ongoing basis in accordance with the Board of Education policy review process.

***Policy History**:* Adopted by Resolution No. 89-78, February 13, 1978; amended by Resolution No. 219-78, March 14, 1978, Resolution No. 718-78, October 10, 1978, and Resolution No. 725-79, August 20, 1979; amended by Resolution No. 403-84, July 23, 1984; reformatted in accordance with Resolution No. 333-86, June 12, 1986, and Resolution No. 438-86, August 12, 1986, and accepted by Resolution No. 147-87, February 25, 1987; amended by Resolution No. 284-97, May 13, 1997; amended by Resolution No. 616-01, November 13, 2001; amended by Resolution No. 252-08, June 23, 2008.

2014–2015

MCPS

Rockville, MD

Montgomery County Public Schools

www.montgomeryschoolsmd.org

May 2015

ELEMENTARY SCHOOLS

No.	Name and Address	Principal	Telephone
790	**Arcola,** 1820 Franwall Ave., Silver Spring 20902	Emmanuel J. Jean-Philippe	301-649-8590
425	**Ashburton,** 6314 Lone Oak Dr., Bethesda 20817	Charlene E. Garran	301-571-6959
420	**Bannockburn,** 6520 Dalroy Lane, Bethesda 20817	Kathryn D. Bradley	301-320-6555
505	**Lucy V. Barnsley,** 14516 Nadine Dr., Rockville 20853	Andrew J. Winter	301-460-2121
207	**Beall,** 451 Beall Ave., Rockville 20850	Elliot M. Alter	301-279-8460
780	**Bel Pre,** 13801 Rippling Brook Dr., Silver Spring 20906	Carmen L. Van Zutphen	301-460-2145
607	**Bells Mill,** 8225 Bells Mill Rd., Potomac 20854	Jerri L. Oglesby	301-469-1046
513	**Belmont,** 19528 Olney Mill Rd., Olney 20832	Evan J. Pinkowitz	301-924-3140
401	**Bethesda,** 7600 Arlington Rd., Bethesda 20814	Lisa S. Seymour	301-657-4979
226	**Beverly Farms,** 8501 Postoak Rd., Potomac 20854	Dr. Beth L. Brown	301-469-1050
410	**Bradley Hills,** 8701 Hartsdale Ave., Bethesda 20817	Sandra S. Reece	301-571-6966
518	**Brooke Grove,** 2700 Spartan Rd., Olney 20832	Gail M. West	301-924-3154
807	**Brookhaven,** 4610 Renn St., Rockville 20853	Shahid A. Muhammad	301-460-2140
559	**Brown Station,** 851 Quince Orchard Blvd., Gaithersburg 20878	Mary Jo Powell	301-840-7172
419	**Burning Tree,** 7900 Beech Tree Rd., Bethesda 20817	Dr. Judith F. Lewis	301-320-6510
309	**Burnt Mills,** 11211 Childs St., Silver Spring 20901	Dr. Stacy A. Ashton	301-649-8192
302	**Burtonsville,** 15516 Old Columbia Pike, Burtonsville 20866	Kimberly L. Kimber	301-989-5654
508	**Candlewood,** 7210 Osprey Dr., Rockville 20855	Dr. Linda B. Sheppard	301-840-7167
310	**Cannon Road,** 901 Cannon Rd., Silver Spring 20904	Norman L. Coleman	301-989-5662
604	**Carderock Springs,** 7401 Persimmon Tree Lane, Bethesda 20817	Rock A. Palmisano	301-469-1034
159	**Rachel Carson,** 100 Tschiffely Square Rd., Gaithersburg 20878	Lawrence D. Chep	301-840-5333
511	**Cashell,** 17101 Cashell Rd., Rockville 20853	Maureen Ahern	301-924-3130
703	**Cedar Grove,** 24001 Ridge Rd., Germantown 20876	Lee F. Derby	301-253-7000
403	**Chevy Chase,** 4015 Rosemary St., Chevy Chase 20815	Jody L. Smith	301-657-4994
101	**Clarksburg,** 13530 Redgrave Pl., Clarksburg 20871	Kwang-Ja Lee	301-353-8060
706	**Clearspring,** 9930 Moyer Rd., Damascus 20872	Holly A. Steel	301-253-7004
100	**Clopper Mill,** 18501 Cinnamon Dr., Germantown 20874	Dr. Ocheze Joseph	301-353-8065
308	**Cloverly,** 800 Briggs Chaney Rd., Silver Spring 20905	Melissa A. Brunson	301-989-5770
238	**Cold Spring,** 9201 Falls Chapel Way, Potomac 20854	Martin J. Barnett	301-279-8480
229	**College Gardens,** 1700 Yale Pl., Rockville 20850	Stacey F. Rogovoy	301-279-8470
808	**Cresthaven,** 1234 Cresthaven Dr., Silver Spring 20903	Sherri A. Gorden	301-431-7622
111	**Capt. James E. Daly,** 20301 Brandermill Dr., Germantown 20876	Nora G. Dietz	301-353-0939
702	**Damascus,** 10201 Bethesda Church Rd., Damascus 20872	William J. Collins	301-253-7080
351	**Darnestown,** 15030 Turkey Foot Rd., Gaithersburg 20878	Laura S. Colgary	301-840-7157
570	**Diamond,** 4 Marquis Dr., Gaithersburg 20878	Daniel Walder	301-840-7177
747	**Dr. Charles R. Drew,** 1200 Swingingdale Dr., Silver Spring 20905	Wanda L. Means Harris	301-989-6030
241	**DuFief,** 15001 DuFief Dr., Gaithersburg 20878	Brent T. Mascott	301-279-4980
756	**East Silver Spring,** 631 Silver Spring Ave., Silver Spring 20910	Dr. Adrienne L. Morrow	301-650-6420
303	**Fairland,** 14315 Fairdale Rd., Silver Spring 20905	Lakeisha D. Lashley	301-989-5658
233	**Fallsmead,** 1800 Greenplace Terr., Rockville 20850	Roni S. Silverstein	301-279-4984
219	**Farmland,** 7000 Old Gate Rd., Rockville 20852	Mary E. Bliss	301-230-5919
566	**Fields Road,** One School Dr., Gaithersburg 20878	Kathryn S. Rupp	301-840-7131
549	**Flower Hill,** 18425 Flower Hill Way, Gaithersburg 20879	Lamar Whitmore	301-840-7161
506	**Flower Valley,** 4615 Sunflower Dr., Rockville 20853	Gay E. Melnick	301-924-3135
803	**Forest Knolls,** 10830 Eastwood Ave., Silver Spring 20901	Evan H. Bernstein	301-649-8060
106	**Fox Chapel,** 19315 Archdale Rd., Germantown 20874	Diana L. Zabetakis	301-353-8055
553	**Gaithersburg,** 35 North Summit Ave., Gaithersburg 20877	Stephanie D. Brant	301-840-7136
313	**Galway,** 12612 Galway Dr., Silver Spring 20904	Dorothea A. Fuller	301-595-2930
204	**Garrett Park,** 4810 Oxford St., Kensington 20895	Elaine L. Chang-Baxter	301-929-2170
786	**Georgian Forest,** 3100 Regina Dr., Silver Spring 20906	Kimberly D. Rogers	301-460-2170
102	**Germantown,** 19110 Liberty Mill Rd., Germantown 20874	Amy D. Bryant	301-353-8050
337	**William B. Gibbs, Jr.** 12615 Royal Crown Dr., Germantown 20876	Kimberly B. Bosnic	301-353-0800
767	**Glen Haven,** 10900 Inwood Ave., Silver Spring 20902	Dr. Jane Q. Ennis	301-649-8051
817	**Glenallan,** 12520 Heurich Rd., Silver Spring 20902	Peter O. Moran	301-929-2014
546	**Goshen,** 8701 Warfield Rd., Gaithersburg 20882	Yolanda R. Allen	301-840-8165
340	**Great Seneca Creek,** 13010 Dairymaid Dr., Germantown 20874	Scott T. Curry	301-353-8500
334	**Greencastle,** 13611 Robey Rd., Silver Spring 20904	Dr. Ayesha M. McArthur Moore	301-595-2940
512	**Greenwood,** 3336 Gold Mine Rd., Brookeville 20833	Cheryl A. Bunyan	301-924-3145

No.	Name and Address	Principal	Telephone
797	**Harmony Hills,** 13407 Lydia St., Silver Spring 20906	Dr. Carole E. Rawlison	301-929-2157
774	**Highland,** 3100 Medway St., Silver Spring 20902	Scott R. Steffan	301-929-2040
784	**Highland View,** 9010 Providence Ave., Silver Spring 20901	Anne M. Dardarian	301-650-6426
305	**Jackson Road,** 900 Jackson Rd., Silver Spring 20904	Sally Ann Macias	301-989-5650
360	**Jones Lane,** 15110 Jones Lane, Gaithersburg 20878	Carole A. Sample	301-840-8160
805	**Kemp Mill,** 411 Sisson St., Silver Spring 20902	Floyd D. Starnes	301-649-8046
783	**Kensington Parkwood,** 4710 Saul Rd., Kensington 20895	Barbara A. Liess	301-571-6949
108	**Lake Seneca,** 13600 Wanegarden Dr., Germantown 20874	Teri D. Johnson	301-353-0929
209	**Lakewood,** 2534 Lindley Terr., Rockville 20850	Robin L. Malcotti	301-279-8465
051	**Laytonsville,** 21401 Laytonsville Rd., Gaithersburg 20882	Donna M. Sagona	301-840-7145
304	**JoAnn Leleck ES at Broad Acres,** 710 Beacon Rd., Silver Spring 20903	Dr. Peter H. Bray	301-431-7616
336	**Little Bennett,** 23930 Burdette Forest Rd., Clarksburg 20871	Shawn D. Miller	301-540-5535
220	**Luxmanor,** 6201 Tilden Lane, Rockville 20852	Ryan D. Forkert	301-230-5914
244	**Thurgood Marshall,** 12260 McDonald Chapel Dr., Gaithersburg 20878	Pamela S. Nazzaro	301-670-8282
210	**Maryvale,** 1000 First St., Rockville 20850	Karen Gregory	301-279-4990
523	**Spark M. Matsunaga,** 13902 Bromfield Rd., Germantown 20874	Judy K. Brubaker	301-601-4350
110	**S. Christa McAuliffe,** 12500 Wisteria Dr., Germantown 20874	Wanda P. Coates	301-353-0910
158	**Ronald McNair,** 13881 Hopkins Rd., Germantown 20874	Sherilyn R. Moses	301-353-0854
212	**Meadow Hall,** 951 Twinbrook Pkwy., Rockville 20851	Cabell W. Lloyd	301-279-4988
556	**Mill Creek Towne,** 17700 Park Mill Dr., Rockville 20855	Kenneth L. Marcus	301-840-7149
652	**Monocacy,** 18801 Barnesville Rd., Dickerson 20842	Cynthia R. Duranko	301-972-7990
776	**Montgomery Knolls,** 807 Daleview Dr., Silver Spring 20901	Bertram B. Generlette	301-431-7667
791	**New Hampshire Estates,** 8720 Carroll Ave., Silver Spring 20903	Zoraida E. Brown *(Acting)*	301-431-7607
307	**Roscoe R. Nix,** 1100 Corliss St., Silver Spring 20903	Annette M. Ffolkes	301-422-5070
415	**North Chevy Chase,** 3700 Jones Bridge Rd., Chevy Chase 20815	Renee D. Wallace-Stevens	301-657-4950
766	**Oak View,** 400 East Wayne Ave., Silver Spring 20901	Peggy E. Salazar	301-650-6434
769	**Oakland Terrace,** 2720 Plyers Mill Rd., Silver Spring 20902	Cheryl D. Pulliam	301-929-2161
502	**Olney,** 3401 Queen Mary Dr., Olney 20832	Carla Glawe	301-924-3126
312	**William Tyler Page,** 13400 Tamarack Rd., Silver Spring 20904	Raushann Austin	301-989-5672
761	**Pine Crest,** 201 Woodmoor Dr., Silver Spring 20901	Cynthia A. Houston	301-649-8066
749	**Piney Branch,** 7510 Maple Ave., Takoma Park 20912	Rachel C. DuBois	301-891-8000
153	**Poolesville,** 19565 Fisher Ave., Poolesville 20837	Douglas M. Robbins	301-972-7960
601	**Potomac,** 10311 River Rd., Potomac 20854	Linda Z. Goldberg	301-469-1042
514	**Judith A. Resnik,** 7301 Hadley Farms Dr., Gaithersburg 20879	Latricia D. Thomas	301-670-8200
242	**Dr. Sally K. Ride,** 21301 Seneca Crossing Dr., Germantown 20876	Christopher A. Wynne	301-353-0994
227	**Ritchie Park,** 1514 Dunster Rd., Rockville 20854	M. Catherine Long	301-279-8475
773	**Rock Creek Forest,** 8330 Grubb Rd., Chevy Chase 20815	Jennifer H. Lowndes	301-650-6410
819	**Rock Creek Valley,** 5121 Russett Rd., Rockville 20853	Catherine A. Jasperse	301-460-2195
795	**Rock View,** 3901 Denfeld Ave., Kensington 20895	Kristine A. Alexander	301-929-2002
156	**Lois P. Rockwell,** 24555 Cutsail Dr., Damascus 20872	Cheryl Ann Clark	301-253-7088
771	**Rolling Terrace,** 705 Bayfield St., Takoma Park 20912	Jennifer L. Connors	301-431-7600
794	**Rosemary Hills,** 2111 Porter Rd., Silver Spring 20910	Deborah C. Ryan	301-650-6400
555	**Rosemont,** 16400 Alden Ave., Gaithersburg 20877	James A. Sweeney	301-840-7123
565	**Sequoyah,** 17301 Bowie Mill Rd., Derwood 20855	Dr. Barbara A. Jasper	301-840-5335
603	**Seven Locks,** 9500 Seven Locks Rd., Bethesda 20817	Carl R. Bencal	301-469-1038
501	**Sherwood,** 1401 Olney-Sandy Spring Rd., Sandy Spring 20860	Dina E. Brewer	301-924-3195
779	**Sargent Shriver,** 12518 Greenly Dr., Silver Spring 20906	Tamisha L. Sampson	301-929-4426
770	**Flora M. Singer,** 2600 Hayden Dr., Silver Spring 20902	Kyle J. Heatwole	301-649-8000
517	**Sligo Creek,** 500 Schuyler Rd., Silver Spring 20910	Diantha R. Swift	301-562-2722
405	**Somerset,** 5811 Warwick Pl., Chevy Chase 20815	Kelly Morris	301-657-4985
564	**South Lake,** 18201 Contour Rd., Gaithersburg 20877	Celeste D. King	301-840-7141
568	**Stedwick,** 10631 Stedwick Rd., Gaithersburg 20886	Dr. Margaret Pastor	301-840-7187
653	**Stone Mill,** 14323 Stonebridge View Dr., North Potomac 20878	Kimberly A. Williams	301-279-4975
316	**Stonegate,** 14811 Notley Rd., Silver Spring 20905	Linda M. Jones	301-989-5668
822	**Strathmore,** 3200 Beaverwood Lane, Silver Spring 20906	Tivinia G. Nelson	301-460-2135
569	**Strawberry Knoll,** 18820 Strawberry Knoll Rd., Gaithersburg 20879	E. Frank Kaplan	301-840-7112
563	**Summit Hall,** 101 West Deer Park Rd., Gaithersburg 20877	Keith R. Jones	301-840-7127
754	**Takoma Park,** 7511 Holly Ave., Takoma Park 20912	Zadia T. Gadsden	301-650-6414
216	**Travilah,** 13801 DuFief Mill Rd., North Potomac 20878	Susan Shenk	301-840-7153
206	**Twinbrook,** 5911 Ridgeway Ave., Rockville 20851	Karen P. Johnson	301-230-5925
772	**Viers Mill,** 11711 Joseph Mill Rd., Silver Spring 20906	Patrick E. Scott *(Acting)*	301-929-2165
552	**Washington Grove,** 8712 Oakmont St., Gaithersburg 20877	Susan B. Barranger	301-840-7120
109	**Waters Landing,** 13100 Waters Landing Dr., Germantown 20877	Tina W. Shrewsbury	301-353-0915
561	**Watkins Mill,** 19001 Watkins Mill Rd., Montgomery Village 20886	Dr. Harold A. Barber	301-840-7181
235	**Wayside,** 10011 Glen Rd., Potomac 20854	Donna E. Michela	301-279-8484
777	**Weller Road,** 3301 Weller Rd., Silver Spring 20906	Michaele O. Simmons	301-929-2010
408	**Westbrook,** 5110 Allan Terr., Bethesda 20816	Jennifer S. Lane	301-320-6506
504	**Westover,** 401 Hawkesbury Lane, Silver Spring 20904	Dr. Patricia A. Kelly	301-989-5676
788	**Wheaton Woods,** 4510 Faroe Pl., Rockville 20853	David T. Chia	301-929-2018
558	**Whetstone,** 19201 Thomas Farm Rd., Gaithersburg 20879	Victoria (Vicky) A. Casey	301-840-7191
341	**Wilson Wims,** 12520 Blue Sky Dr., Clarksburg 20871	Sean P. McGee	301-601-4921
417	**Wood Acres,** 5800 Cromwell Dr., Bethesda 20816	Marita R. Sherburne	301-320-6502

Located at Radnor Center, 7000 Radnor Rd., Bethesda 20817

No.	Name and Address	Principal	Telephone
704	**Woodfield,** 24200 Woodfield Rd., Gaithersburg 20882	Gayle J. Starr	301-253-7085
764	**Woodlin,** 2101 Luzerne Ave., Silver Spring 20910	Shoua F. Moua	301-650-6440
422	**Wyngate,** 9300 Wadsworth Dr., Bethesda 20817	Barbara J. Leister	301-571-6979

MIDDLE SCHOOLS

823	**Argyle,** 2400 Bel Pre Rd., Silver Spring 20906	Robert W. Dodd	301-460-2400
705	**John T. Baker,** 25400 Oak Dr., Damascus 20872	Dr. Louise J. Worthington	301-253-7010
333	**Benjamin Banneker,** 14800 Perrywood Dr., Burtonsville 20866	James K. Allrich *(Acting)*	301-989-5747
335	**Briggs Chaney,** 1901 Rainbow Dr., Silver Spring 20904	Dr. Tamitha F. Campbell	301-989-6000
606	**Cabin John,** 10701 Gainsborough Rd., Potomac 20854	Dr. Paulette L. Smith	301-469-1150
157	**Roberto W. Clemente,** 18808 Waring Station Rd., Germantown 20874	Khadija F. Barkley	301-601-0344
775	**Eastern,** 300 University Blvd. East, Silver Spring 20901	Casey B. Crouse	301-650-6650
507	**William H. Farquhar,** 16915 Batchellors Forest Rd., Olney 20832	Joel L. Beidleman	301-924-3100
248	**Forest Oak,** 651 Saybrooke Oaks Blvd., Gaithersburg 20877	Dr. Arthur Williams	301-670-8242
237	**Robert Frost,** 9201 Scott Dr., Rockville 20850	Dr. Joey N. Jones	301-279-3949
554	**Gaithersburg,** 2 Teachers' Way, Gaithersburg 20877	Carol L. Goddard	301-840-4554
228	**Herbert Hoover,** 8810 Postoak Rd., Potomac 20854	Dr. Yong-Mi Kim	301-469-1010
311	**Francis Scott Key,** 910 Schindler Dr., Silver Spring 20903	Yolanda Stanislaus	301-422-5600
107	**Dr. Martin Luther King, Jr.,** 13737 Wisteria Dr., Germantown 20874	Dana E. Davison	301-353-8080
708	**Kingsview,** 18909 Kingsview Rd., Germantown 20874	James N. D'Andrea	301-601-4611
522	**Lakelands Park,** 1200 Main St., Gaithersburg 20878	Deborah R. Higdon	301-670-1400
818	**Col. E. Brooke Lee,** 11800 Monticello Ave., Silver Spring 20902	Kimberly N. Hayden Williams	301-649-8100
787	**A. Mario Loiederman,** 12701 Goodhill Rd., Silver Spring 20906	Nicole A. Sosik	301-929-2282
557	**Montgomery Village,** 19300 Watkins Mill Rd., Montgomery Village 20886	Dr. Edgar E. Malker	301-840-4660
115	**Neelsville,** 11700 Neelsville Church Rd., Germantown 20876	L. Victoria (Vicky) Lake-Parcan	301-353-8064
792	**Newport Mill,** 11311 Newport Mill Rd., Kensington 20895	Panagiota (Penny) K. Tsonis	301-929-2244
413	**North Bethesda,** 8935 Bradmoor Dr., Bethesda 20817	Alton E. Sumner	301-571-3883
812	**Parkland,** 4610 West Frankfort Dr., Rockville 20853	Dr. Benjamin T. OuYang	301-438-5700
155	**Rosa M. Parks,** 19200 Olney Mill Rd., Olney 20832	Dr. Donna R. Jones	301-924-3180
247	**John Poole,** 17014 Tom Fox Ave., Poolesville 20837	Robert Sinclair, Jr.	301-972-7979
428	**Thomas W. Pyle,** 6311 Wilson Lane, Bethesda 20817	Christopher B. Nardi	301-320-6540
562	**Redland,** 6505 Muncaster Mill Rd., Rockville 20855	Everett M. Davis	301-840-4680
105	**Ridgeview,** 16600 Raven Rock Dr., Gaithersburg 20878	Monifa B. McKnight	240-406-1300
707	**Rocky Hill,** 22401 Brick Haven Way, Clarksburg 20871	Dr. Cynthia Eldridge	301-353-8282
521	**Shady Grove,** 8100 Midcounty Hwy., Gaithersburg 20877	Edward K. Owusu	301-548-7540
647	**Silver Spring International,** 313 Wayne Ave., Silver Spring 20910	John W. Haas	301-650-6544
778	**Sligo,** 1401 Dennis Ave., Silver Spring 20902	Eric A. Wilson	301-649-8121
755	**Takoma Park,** 7611 Piney Branch Rd., Silver Spring 20910	Alicia M. Deeny	301-650-6444
232	**Tilden,** 11211 Old Georgetown Rd., Rockville 20852	Irina LaGrange	301-230-5930
211	**Julius West,** 651 Great Falls Rd., Rockville 20850	Craig W. Staton	301-279-3979
412	**Westland,** 5511 Massachusetts Ave., Bethesda 20816	Alison L. Serino	301-320-6515
811	**White Oak,** 12201 New Hampshire Ave., Silver Spring 20904	Virginia A. de los Santos	301-989-5780
820	**Earle B. Wood,** 14615 Bauer Dr., Rockville 20853	Dr. Traci L. Townsend	301-460-2150

HIGH SCHOOLS

406	**Bethesda-Chevy Chase,** 4301 East-West Hwy., Bethesda 20814	Karen L. Lockard	240-497-6300
757	**Montgomery Blair,** 51 University Blvd., East, Silver Spring 20901	Renay C. Johnson	301-649-2800
321	**James Hubert Blake,** 300 Norwood Rd., Silver Spring 20905	Christopher S. Berry	301-879-1300
602	**Winston Churchill,** 11300 Gainsborough Rd., Potomac 20854	Dr. Joan L. Benz	301-469-1200
249	**Clarksburg,** 22500 Wims Rd., Clarksburg 20871	Stephen C. Whiting	301-444-3000
701	**Damascus,** 25921 Ridge Rd., Damascus 20872	Jennifer L. Webster	301-253-7030
789	**Albert Einstein,** 11135 Newport Mill Rd., Kensington 20895	James G. Fernandez	301-929-2200
551	**Gaithersburg,** 101 Education Boulevard, Gaithersburg 20877	Dr. Christine C. Handy-Collins	301-284-4500
424	**Walter Johnson,** 6400 Rock Spring Dr., Bethesda 20814	Jennifer A. Baker	301-803-7100
815	**John F. Kennedy,** 1901 Randolph Rd., Silver Spring 20902	Joe L. Rubens, Jr.	301-929-2100
510	**Col. Zadok Magruder,** 5939 Muncaster Mill Rd., Rockville 20855	Leroy C. Evans	301-840-4600
201	**Richard Montgomery,** 250 Richard Montgomery Dr., Rockville 20852	Damon A. Monteleone	301-610-8000
246	**Northwest,** 13501 Richter Farm Rd., Germantown 20874	E. Lancellotti (Lance) Dempsey	301-601-4660
796	**Northwood,** 919 University Blvd. West, Silver Spring 20901	Mildred L. Charley-Greene	301-649-8088
315	**Paint Branch,** 14121 Old Columbia Pike, Burtonsville 20866	Dr. Myriam A. Rogers	301-388-9901
152	**Poolesville,** 17501 Willard Rd., Poolesville 20837	Deena Levine	301-972-7900
125	**Quince Orchard,** 15800 Quince Orchard Rd., Gaithersburg 20878	Carole A. Working	301-840-4686
230	**Rockville,** 2100 Baltimore Rd., Rockville 20851	Billie-Jean Bensen	301-517-8105
104	**Seneca Valley,** 19401 Crystal Rock Dr., Germantown 20874	Marc J. Cohen	301-353-8000
503	**Sherwood,** 300 Olney-Sandy Spring Rd., Sandy Spring 20860	William M. Gregory	301-924-3200
798	**Springbrook,** 201 Valleybrook Dr., Silver Spring 20904	Samuel A. Rivera	301-989-5700
545	**Watkins Mill,** 10301 Apple Ridge Rd., Gaithersburg 20879	Scott W. Murphy	301-840-3959
782	**Wheaton,** 12601 Dalewood Dr., Silver Spring 20906	Dr. Debra K. Mugge	301-929-2050
427	**Walt Whitman,** 7100 Whittier Blvd., Bethesda 20817	Dr. Alan S. Goodwin	301-320-6600
234	**Thomas S. Wootton,** 2100 Wootton Pkwy., Rockville 20850	Dr. Michael J. Doran	301-279-8550

No.	Name and Address	Principal	Telephone
	TECHNICAL CAREER HIGH SCHOOL		
748	**Thomas Edison High School of Technology** **12501 Dalewood Dr.,** Silver Spring 20906	Dr. Ursula A. Hermann (Acting)	301-929-2175
	ENVIRONMENTAL EDUCATION CENTER		
990	**Lathrop E. Smith Environmental Education Center** 5110 Meadowside Lane, Rockville 20855	Laurie C. Jenkins	301-924-3123
	SPECIAL SCHOOLS		
951	**Longview School,** 13900 Bromfield Rd., Germantown 20874	Michelle M. Mach	301-601-4830
965	**John L. Gildner Regional Institute for Children and Adolescents (RICA)** **15000 Broschart Rd.,** Rockville 20850	Michelle E. Schultze	301-251-6900
916	**Rock Terrace School,** 390 Martins Lane, Rockville 20850	Katherine W. Lertora	301-279-4940
215	**Carl Sandburg Learning Center,** 451 Meadow Hall Dr., Rockville 20851	Marlene R. Kenny	301-279-8490
799	**Stephen Knolls School,** 10731 St. Margaret's Way, Kensington 20895	Kim M. Redgrave	301-929-2151
	ALTERNATIVE EDUCATION PROGRAMS		
239	**Alternative Education Programs,** Blair Ewing Center, 14501 Avery Rd., Rockville 20853	Dr. Ira K. Thomas	301-279-4920
	CENTERS, FACILITIES, AND OFFICES		
	45 West Gude Drive, 45 West Gude Drive, Rockville 20850		
	Construction (Suite 4300)		240-314-1000
	Consulting Teachers Team (Suite 2400)		301-217-5120
	Controller (Suite 3200)		301-279-3115
	Employee and Retiree Service Center (Suite 1200)		301-517-8100
	Facilities Management, Department of (Suite 4000)		240-314-1060
	Human Resources and Development (Suite 1100)		301-279-3270
	Long-range Planning (Suite 4100)		240-314-4700
	Procurement Unit(Suite 3100)		301-279-3555
	Pupil Personnel Services (Terrace Level)		301-315-7335
	School Plant Operations (Suite 4200)		240-314-1075
	SERT Program (Suite 4000)		240-314-1090
	Systemwide Safety Programs (Suite 4000)		240-314-1070
	Carver Educational Services Center, 850 Hungerford Dr., Rockville 20850		301-309-6277
	Association Relations		301-279-3511
	Board of Education		301-279-3617
	Chief Academic Officer		301-279-3474
	Chief Operating Officer		301-279-3626
	Communications		301-279-3145
	Community Engagement and Partnerships		301-279-3074
	Curriculum and Instructional Programs		301-279-3411
	Deputy Superintendent of School Support and Improvement		301-315-7377
	Editorial, Graphics & Publishing Services		301-279-3640
	Public Information and Web Services		301-279-3853
	School Safety and Security		301-279-3066
	Shared Accountability		301-279-3553
	Special Education Services		301-279-3135
	Student Services		301-279-3912
	Superintendent		301-279-3381
	Technology		301-279-3581
	Center for Technology Innovation, 4 Choke Cherry Rd., Rockville 20850		240-314-2250
	Central Records, Concord Center, 7210 Hidden Creek Rd., Bethesda 20817		301-320-7301
	County Service Park, 16651 Crabbs Branch Way, Rockville 20855		
	Maintenance		301-840-8100
	Transportation		301-840-8130
	Festival Center at Muddy Branch, 283 Muddy Branch Rd., Gaithersburg 20878		301-840-6740
	Food and Nutrition Services, 8401 Turkey Thicket Drive, Gaithersburg 20879		301-284-4900
	Lincoln Center, 580 North Stonestreet Ave., Rockville 20850		
	Department of Materials Management		301-279-3348
	Library and Media Programs		301-279-3272
	Lynnbrook Center, 8001 Lynnbrook Dr., Bethesda 20814		
	High Incidence Accessible Technology Services		301-657-4959
	InterACT		301-657-4929
	Physical Disabilities Program		301-657-4959
	Professional Library—USG, 9636 Gudelsky Dr., Education Bldg. III., Rm. 1200, Rockville 20850		301-279-3227
	Rocking Horse Road Center, 4910 Macon Rd., Rockville 20852		
	Academic Support, Federal and State Programs (Suite 202)		301-230-0660
	Child Find/Early Childhood Disabilities Unit (Suite 207)		301-230-5966
	Early Childhood Programs and Services (Suite 200)		301-230-0691
	ESOL/Bilingual Programs (Suite 115)		301-230-0670
	International Student Admissions Office (Suite 148–153)		301-230-0686
	Prekindergarten and Head Start (Suite 141)		301-230-0676
	Spring Mill Offices, 11721 Kemp Mill Rd., Silver Spring 20902		
	Autism Services		301-593-3720
	Transition Services		301-649-8008
	Consortia Choice and Application Program Services		301-592-2040
	Speech and Language Services		301-649-8085
	Taylor Science Materials Center, 19501 White Ground Rd., Boyds 20841		301-353-0866
	Upcounty Regional Services Center, 12900 Middlebrook Rd., Germantown 20874		301-601-0300
	Student Affairs		301-444-8620
	Transportation Support Services		301-444-8580

Planning Calendar

The following is the planning calendar for the FY 2017–2022 Capital Improvements Program (CIP).

Date	Activity
June 1, 2015	Cluster PTAs submit comments and proposals about issues for consideration in the CIP to superintendent
June 30, 2015	Superintendent publishes a summary of all actions to date that have affected schools (Educational Facilities Master Plan)
Summer 2015	Division of Long-range Planning staff meets with cluster representatives to discuss issues related to the upcoming CIP development
October 5, 2015	MCPS FY 2017 State CIP request to the Interagency Committee (IAC) on Public School Construction
October 13, 2015	Board of Education presentation on enrollment trends and facility planning issues
October 15, 2015	Superintendent releases recommendations on boundary and/or planning studies conducted in spring 2015
October 28, 2015	Six-year enrollment projections are revised and published
October 28, 2015	Superintendent publishes recommendations for the FY 2017–2022 CIP
October 29, 2015	MCPS/MCCPTA CIP Forum provides overview of recommendations to PTA leaders
November 5, 2015	Board of Education work session on superintendent's recommendations on spring 2015 boundary and/ or planning studies (if any) and the FY 2017 Capital Budget and the FY 2017–2022 CIP
November 12, 2015	IAC staff recommendations on FY 2017 State CIP
November 9 and 12, 2015	Public hearings on the superintendent's recommendations on spring 2015 boundary and/or planning studies (if any) and the FY 2017 Capital Budget and Amendments to the FY 2017–2022 CIP
November 16, 2015	Board of Education action on spring 2015 boundary and/or planning studies (if any) and the FY 2017 Capital Budget and the FY 2017–2022 CIP
November 23, 2015	Final revisions on FY 2017 state aid request due to IAC
December 1, 2015	Board of Education submits Requested FY 2017 Capital Budget and the FY 2017–2022 CIP to the County Executive
December 3, 2015	IAC appeal hearing on FY 2017 State CIP
Mid-January 2016	County executive publishes recommendations for the FY 2017 Capital Budget and the FY 2017–2022 CIP
Mid-January, 2016	Board of Public Works hearing on the FY 2017 State CIP
February–May 2016	County Council reviews requested FY 2017 Capital Budget and the FY 2017–2022 CIP
February 2016	Superintendent releases recommendations on winter boundary and/or planning studies (if any) and CIP recommendations for deferred CIP items (if any)
February 22, 2016	Board of Education facilities work session for winter boundary and/or planning studies (if any) and deferred CIP items (if any)
March 10, 2016	Public hearing on superintendent's recommendations for winter boundary and/or planning studies (if any) and deferred CIP items (if any)
March 21, 2016	Board of Education action on winter boundary and/or planning studies (if any) and deferred CIP items (if any)
May 2016	Board of Public Works decisions on FY 2017 State CIP
Late May 2016	County Council approves the FY 2017 Capital Budget and the FY 2017–2022 CIP

All CIP and Master Plan documents are accessible on the MCPS website at:
http://www.montgomeryschoolsmd.org/departments/planning/CIPMaster_Current2.shtml

MONTGOMERY COUNTY PUBLIC SCHOOLS

ROCKVILLE, MARYLAND







Published by the Department of Materials Management
for the Division of Long-range Planning
1369.15 • Editorial, Graphics & Publishing Services • 6/15 • 350
Copyright © 2015 Montgomery County Public Schools, Rockville, Maryland

PRODUCED BY SEIU LOCAL 500 MEMBERS
